

Initial Environmental Examination

PUBLIC

Document Stage: Updated
Project Number: 42267-034
January 2024

India: Rajasthan Secondary Towns Development
Sector Project – Additional Financing (PART A)

Dungarpur Town Water Supply and Sewerage Works

Prepared by Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited-
External Aided Project (RUDSICO-EAP) for the Asian Development Bank (ADB). This is an
updated version of the draft originally posted in July 2023 available on
<https://www.adb.org/projects/documents/ind-42267-034-iee-17>

CURRENCY EQUIVALENTS

(as of 31st March 2022)

Currency unit	–	Indian rupee (₹)
₹ 1.00	=	\$0.0120
\$1.00	=	₹83.14

ABBREVIATIONS

ADB	–	Asian Development Bank
BOCW	–	Building and Other Construction Workers
CGWB	–	Central Ground Water Board
CLC	–	City Level Committee
CPCB	–	Central Pollution Control Board
CPHEEO	–	Central Public Health and Environmental Engineering Organization
CTE	–	Consent To Establish
CTO	–	Consent To Operate
CWR	–	Clear Water Reservoir
DBO	–	Design-Build-Operate
DPR	–	Detailed Project Report
EHS	–	Environmental Health and Safety
EIA	–	Environmental Impact Assessment
EMP	–	Environmental Management Plan
FAO	–	Food and Agricultural Organization
FCO	–	Fertilizer Control Ordinance
FSSM	–	Faecal Sludge and Septage Management
IEE	–	Initial Environmental Examination
IFC	–	International Finance Corporation
LSGD	–	Local Self Government Department
MOEFCC	–	Ministry Of Environment, Forest and Climate Change
OHSR	–	Overhead Service Reservoir
PHED	–	Public Health Engineering Department
PIU	–	Project Implementation Unit
PMU	–	Project Management Unit
PWD	–	Public Works Department
REA	–	Rapid Environmental Assessment
ROW	–	Right-Of-Way
RSPCB	–	Rajasthan State Pollution Control Board
RSTDSP	–	Rajasthan Secondary Towns Development Sector Project
RUDSICO-EAP	–	Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited-Externally Aided Projects
RUDSICO	–	Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation
SCADA	–	Supervisory Control and Data Acquisition
SBR	–	Sequential Batch Reactor
SEIAA	–	State Environmental Impact Assessment Authority
SPS	–	Safeguard Policy Statement, 2009
STP	–	Sewage Treatment Plant
TEER	–	Treated Effluent Elevated Reservoir
TESR	–	Treated Effluent Storage Reservoir

ULB	–	Urban Local Body
WHO	–	World Health Organization
WTP	–	Water Treatment Plant

WEIGHTS AND MEASURES

m ³	–	cubic meter
dB	–	decibels
°C	–	degree centigrade
dia	–	diameter
kg	–	kilogram
kl	–	kiloliter
km	–	kilometer
kmph	–	kilometer per hour
KLD	–	kiloliters per day
ha	–	hectare
HP	–	horsepower
LPCD	–	liters per capita per day
lps	–	liters per second
m	–	meter
mg	–	milligram
mm	–	millimeter
MCM	–	million cubic meter
MLD	–	million liters per day
km ²	–	square kilometer

NOTE

In this report, "\$" refers to United States dollars.

This updated initial environmental examination is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or Staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area.

CONTENTS

EXECUTIVE SUMMARY	i
I. INTRODUCTION	1
A. Rajasthan Secondary Town Development Section Project – Additional Financing	1
B. Purpose of Initial Environmental Examination Report	2
C. Scope of IEE	2
D. Report Structure	2
II. DESCRIPTION OF PROJECT	3
A. Dungarpur Town	3
B. Proposed Water Supply and Sewerage Infrastructure in Dungarpur under RSTDSP	5
C. Proposed Source for Subproject	6
D. Implementation Schedule	18
III. ANALYSIS OF ALTERNATIVES	38
IV. POLICY, LEGAL AND ADMINISTRATIVE FRAMEWORKS	44
A. ADB Safeguard Policy	44
B. National Laws	47
C. Environmental Regulatory Compliance	48
V. DESCRIPTION OF ENVIRONMENT	61
A. Physical Resources	61
B. Ecological Resources	72
C. Other Infrastructure	78
D. Socio Cultural Resources	78
E. Environmental Settings of Investment Program Component Sites	79
VI. ANTICIPATED ENVIRONMENTAL IMPACTS AND MITIGATION MEASURES	87
A. Introduction	87
B. Pre-Construction Impacts– Design and Location	88
C. Environmental Audit of Existing Water Supply Infrastructure	105
D. construction Impacts	112
E. Operation and Maintenance Impacts	126
VII. PUBLIC CONSULTATION AND INFORMATION DISCLOSURE	131
A. Overview	131
B. Public Consultation	132
C. Information Disclosure	133
VIII. GRIEVANCE REDRESS MECHANISM	134
A. Project Specific Grievance Redress Mechanism	134
B. Grievance Redress Process	135
IX. ENVIRONMENTAL MANAGEMENT PLAN	138
A. Environmental Management Plan	138
B. Institutional Requirements	179
C. EMP Implementation Cost	188
X. CONCLUSION AND RECOMMENDATION	191

APPENDICES

Appendix 1: REA Check list	195
Appendix 2: Compliance with Environmental Criteria for Subproject Selection	201
Appendix 3: Audit report of existing water supply system in Dungarpur	210
Appendix 4: Source Sustainability Report of Dhungarpur Water Supply Scheme	247
Appendix 5: Letter for Allotment of Water for Dungarpur Town Water Supply Project of Dungarpur	281
Appendix 6: Stakeholders and Public Consultation Consultations Conducted During Project Preparation and implementation	288
Appendix 7: Integrated Biodiversity Assessment Tool World Bank Group Biodiversity Risk Screen DUNGARPUR STP	317
Appendix 8: Photographs of Proposed Component Locations and Existing components	325
Appendix 9: Water Test Report of PHED Lab	327
Appendix :10 Lab Test Report of Environment Monitoring	322
Appendix 11: Safety training and orientation programme at Dungarpur town	362
Appendix 12: Biodiversity assessment of Dimiya Dam Dungarpur with special reference to presence of Marsh Crocodile and its mitigation measures.....	374
Appendix 13: Letter of Municipal Council Dungarpur to WRD for NOC.....	402
Appendix 14: Bathymetric survey conducted for Vijay Chakra Sagar Dam.....	403

Appendix C1 – C25 – common appendices, attached separately, provide statutory standards, guidelines, reporting templates etc. are applicable to all subproject IEEs.

List of common Appendices

Appendix C-1: Drinking Water Standards
Appendix C-2: Ambient Air Quality Standards
Appendix C-3: Emission limits for New DG sets up to 800 KW
Appendix C-4: Stack Height Requirement of DG set
Appendix C-5: Vehicle Exhaust Emission Norms
Appendix C-6: Ambient Noise Quality Standards
Appendix C-7: Noise Limits for DG Set
Appendix C-8: Effluent Discharge Standards for Sewage Treatment Plant
Appendix C-9: Pages from Rajasthan State Sewerage and Wastewater Policy for reuse of treated effluent and sludge
Appendix C-10: Guidelines for Reuse of Treated Effluent and Sludge from STP for Beneficial Purposes
Appendix C-11: Guidelines for compensatory tree plantation in RUIDP works.
Appendix C-12: Salient Features of Laws applicable to Construction Works including Labor Laws
Appendix C-13: Sample Outline Spoil Management Plan
Appendix C-14: Sample Outline Traffic Management Plan
Appendix C-15: Sample Six Monthly Reporting Format
Appendix C-16: Sample Environmental Site Inspection Report
Appendix C-17: Sample Grievance Registration Form
Appendix C-18: Management Plan for Night works at Project Sites
Appendix C-19: Guidelines for Safety during Monsoon/Heavy rainfall
Appendix C-20: Sample ACM Management Plan
Appendix C-21: Guidelines for Workers Camps
Appendix C-22: Guidelines for Safety in Chlorine Usage
Appendix C-23: Guidelines for Prevention and Control of COVID-19

Appendix C-24: RUDSICO-EAP Guidelines for implementation of Prevention and Control Measures for COVID-19

Appendix C-25: Management of Work Plan during Festivals and Melas

EXECUTIVE SUMMARY

ADB approved a loan for the Rajasthan Secondary Towns Development Sector Project (RSTDSP, Loan 3972: IND) in September 2020. This is currently under implementation and will close by May 2028. The additional financing (the project) will expand the improved access to WSS services in at least ten urban local bodies (ULBs), benefiting 1.2 million people. Important value addition of the proposed project to the ongoing project is that it will provide innovative solutions to address climate change to respond to the growing climate risks and vulnerability and also to improve livability and prosperity through enhancing natural and/or built heritage at least ten ULBs in Rajasthan, benefiting 1.0 million people. The overall project is aligned with the following impacts: (i) access to potable, affordable, reliable, equitable, environmentally sustainable drinking water supply in all urban areas of Rajasthan improved, (ii) health status of urban population, especially the poor and under-privileged improved, and (iii) productivity, livability and prosperity for the citizens in Rajasthan cities and towns enhanced. Reflecting the additional measures to enhance climate resilience and heritage-sensitive urban development of the project, impact statement (iii) was added; the outcome statement is modified as quality, reliability, equity, and sustainability of urban assets and services in project towns of Rajasthan improved; and additional output was also added, resulting in four outputs.

Dungarpur is one of the project towns, and improvement of water supply and sewerage system in Dungarpur is proposed under the RSTDSP-AF. Following are the proposed components:

- **Water supply.** (i) Installation of SCDA system, refurbishment of existing intake structure at existing intake well, (ii) Raw water pump house-01 no (ii) clear Water Pump House (5 nos.) (iii) (iv) Clear Water Reservoir (2 nos., 550 KL & 600 KL) (v) Raw water rising main of approximately 10.082 km and clear water rising main of 14.95 km (vi) Distribution networks of 160.29 km (vii) House service connection-12067 nos. (viii) Refurbishment of pump house (7 nos.), RWR (235 KL), WTPs- 2 nos. (4.54 MLD and 3.25 MLD), CWRs (2nos.), OHSRs (8nos.), GLSRs (4 nos.), (ix) Rehabilitation of 2 TWs and 2 open wells, (x) Construction of CRMC (2 nos.) and MCC (1no.).
- **Sewerage.** (i) Laying of 51.48 km sewer (ii) Construction of 3 nos. Sewage pumping stations (SPS) of capacities of 3MLD, 3MLD and 0.25 MLD (iii) Construction of 4.0 MLD Sewage Treatment Plant (STP) near Do River on Udaipurroad along with 380 KL capacity TESR & 760 KL of TEER (iv) Rising main of 7.3 km (v) 6460 nos. of House Sewer Connections inside the property boundary (vi) FSSM work including procurement of desludging tank of 4000 lit capacity.

Screening and Categorization. assessment of potential impacts. Dungarpur Water Supply & Sewerage subproject is classified as environmental category B per ADB's Safeguard Policy Statement (SPS), 2009, and accordingly this initial environmental examination (IEE) assesses the environmental impacts and provides mitigation and monitoring measures to ensure that there are no significant impacts as a result of the subproject. Per Government of India environmental impact assessment (EIA) Notification, 2006, subproject do not require environmental clearance.

Description of the Environment. Subproject components are in Dungarpur City and in its immediate surroundings which were converted into urban use for many years ago, and there is no natural habitat left at the proposed subproject sites. The subproject sites are located in existing road right of way (RoW) and government-owned lands. The proposed sewerage components like STP and, SPS will be constructed on vacant government land. There are no trees on the site and is surrounded mostly by agricultural areas. The nearest built-up structures are to STP site are 3

cattle sheds about 150 m and nearest habitation is 200 m away from the proposed STP site. The selected STP site is in government owned site in on riverbank of Do River. The selected site is also had sufficient area for future expansion of the STP, area available 28173 sqm against 3600 sqm required. The treated waste will be reused by nearby farmers and overflow from STP will be discharged in Do River. Kheria Magra and Gumanpua Protected Forest at 3 km & 2.6 km respectively far from proposed STP site.

Under water supply, refurbishment of existing intake well at Dimiya dam is proposed which is owned by water resources department, government of Rajasthan. The nearest forest block to existing intake well is at an aerial distance of 670 meters. Clear water reservoirs will be constructed in government vacant land one at Chandpole and another at PHED campus at new colony. The nearest forest block to these locations is at 1.5 km and 3.2 km, respectively. The water supply rising mains and network will traverse through existing road right of way (RoW). The nearest wildlife sanctuary is Sita Mata Sanctuary located 86 km from project town. The nearest ASI protected monument in Dungarpur district are Deo Somnath temples about 35 km and Jain Temple Inscription in Baroda village about 16 km from Dungarpur town.

Potential Environmental Impacts and Mitigation measures. In this draft IEE, negative impacts were identified in relation to location, design, construction and operation of the improved infrastructure. Environmental impacts as being due to the project design or location were not significant as various measures are already included in site planning and preliminary design. No impacts on forests or archaeological resources envisaged. Temporary measures suggested to avoid any disturbance / damage to buildings during laying of water lines in nearby roads. Source of water for town is surface water from Edward Samand Dam (4.54 MLD), Vijay Chakra Sagar dam (3.20 MLD) and Somkamla Amba dam (4.361 MLD). Along these surface water sources additionally 4 existing ground water sources including 2 tube wells and 2 open wells, proposed for lean season when surface water source have less amount of water. The PHED has recorded yearly water level data of Edward Samand Dam, Vijay Chakra Sagar dam dams and as per water level data of past 12-year, the two dams was filled fully up to its storage capacity in all 12 years. New proposed Som Kamala Amba (SKA) Dam on Som River. The allotted water for Dungarpur is on 4.36 MLD (1.59 MCM) which is only 5.09 % of total drinking water available in dam.

Ground Water Source: At present there are 7 Nos Tube wells and 15 Nos Dug Wells / Open wells are supplies 3.0 MLD water to Dungarpur, out of these existing wells, 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desilting, with re commissioning work. Based on the design consideration, it was proposed to consider 1.5 MLD of water from ground water sources in case of emergency situations like repair and maintenance works in surface water sources and during lean seasons when water availability in surface water sources in less.

Assessment confirms the source sustainability to provide drinking water, and no water sharing conflicts or downstream impacts envisaged. New STP of 4 MLD will employ sequential batch reactor (SBR) technology to meet stipulated discharge standards. SBR will involve aerobic treatment, with minimum odour potential. Sludge management is included in the STP, properly dried sludge will be reused as manure.

Potential impacts during construction are considered significant but temporary and are common impacts of construction in urban areas, and there are well developed methods to mitigate the same. Except for laying water pipelines, all other construction activities will be confined to the selected sites and the interference with the general public and community around is minimal. In these works, the temporary negative impacts arise mainly from construction dust and noise, hauling of construction material, waste and equipment on local roads (traffic, dust, safety etc.), mining of construction material, occupational health and safety (OHS) aspects. Pipe laying works

will be conducted along public roads in an urban area congested with people, activities and traffic. Therefore, these works may have adverse, but temporary impacts arising mainly from the disturbance of residents, businesses and traffic due to construction work; safety risk to workers, public and nearby buildings due to deep trench excavations in the road; access impediment to houses and business, disposal of large quantities of construction waste etc. Trenchless method will be adopted for pipeline deeper than 3.5 m and also at main road crossings in traffic areas.

Environmental Management. An environmental management plan (EMP) has been developed to provide mitigation measures to reduce all negative impacts to acceptable levels, along with the delegation of responsibility to appropriate agency. Various design related measures are already included in the project design. During construction, the EMP includes mitigation measures such as (i) proper planning and scheduling of water line and sewer works to minimize public inconvenience; (ii) measures to avoid impacts on heritage building and chance find procedures (iii) barricading, dust suppression and noise control measures; (iv) traffic management measures for works along the roads and for hauling activities; (v) occupational and community health and safety, labour welfare, (vi) provision of walkways and planks over trenches to ensure access will not be impeded; (vii) reuse of excavated materials to extent possible, (viii) spill and sediment control measures to avoid water and soil pollution, etc.,. EMP will guide the environmentally-sound construction of the subproject. EMP includes a monitoring program to measure the effectiveness of EMP implementation and include observations on- and off-site, document checks, and interviews with workers and beneficiaries. A copy of the updated EMP/ site environmental management plan (SEMP) shall be always kept on-site during the construction period. The EMP was included in bids and contracts, and implementation shall be binding on contractors.

Implementation Arrangements. The executing and implementing agencies will remain unchanged from the current project, which are Government of Rajasthan's Local Self Government Department (LSGD) and Rajasthan Urban Drinking Water, Sewerage and Infrastructure Corporation (RUDSICO), respectively. The AF project retains the project management unit (PMU) at the implementing agency, as well as the two Zonal Offices in Jaipur and Jodhpur. Project implementation units (PIUs) have been established in project towns. A total of eight PIUs will manage 18 ULBs under the AF Project. Consultants will support the PMU and PIUs. Project Officer (Environment) at PMU and Safeguard and Safety Officer at each of the PIUs will be responsible for environment management and monitoring activities and will be supported by Safeguard support staff from Supervision Consultant, town staff/team and Environment Safeguard Specialist of Supervision Consultants. Contractor personnel will also include an Environment, Health and Safety (EHS) Engineer in the project construction team.

Consultation, Disclosure and Grievance Redress. The stakeholders were involved in developing the IEE. Informal and formal consultation are conducted with local population of the area at 8 places along with proposed alignment with about 66 persons in month of March and April 2022. A City Level Committee (CLC) was held and CLC has appreciated and approved the subproject. The draft IEE was made available at public locations; and this updated IEE will also be disclosed to a wider audience via the ADB and RUDSICO websites. Consultation process will continue during project implementation. A grievance redress mechanism (GRM) is established to redress public grievances.

Monitoring and Reporting. The PMU, PIU and consultants will be responsible for monitoring and reporting. During construction, results from internal monitoring by the DBO contractor will be reflected in their monthly EMP implementation reports to the PIU. PIU with the assistance of CMSC, will monitor the compliance of contractor, prepare a quarterly environmental monitoring

report (QEMR) and submit to PMU. The PMU will oversee the implementation and compliance and will submit semi-annual environmental monitoring reports (SEMR) to ADB. SEMRs will be disclosed on ADB and RUDSICO websites.

Conclusions. The proposed project is unlikely to cause significant adverse impacts, and potential impacts are mainly due to construction and can be mitigated or minimized to acceptable levels through measures included in the EMP. The citizens of Dungarpur will be the major beneficiaries. The subproject is primarily designed to improve environmental quality and living conditions of Dungarpur Town through provision of water supply and sewerage. The benefits arising from this subproject include: (i) increased availability of potable water to all households including urban poor; (ii) reduced time and costs in accessing alternative sources of water; (iii) better public health particularly reduction in waterborne and infectious diseases; (iv) reduced risk of groundwater contamination; (v) reduced risk of contamination of treated water supplies; (vi) reduced dependence on fresh water resource due to reuse of treated wastewater, and (vii) improvement in quality of water bodies due to disposal of treated effluent meeting disposal standards.

Based on the findings of the IEE, the classification of the project as Category “B” is confirmed. No further special study or detailed environmental impact assessment (EIA) needs to be undertaken to comply with ADB SPS (2009) or GoI EIA Notification (2006). To conform to government guidelines, the existing WTP and STP require consent to establishment (CTE) and consent to operate (CTO) from Rajasthan Pollution Control Board. CTE will be obtained prior to construction, as the detailed designs are being undertaken by contractor. Draft IEE of this subproject was prepared and approved by ADB based on feasibility / preliminary design and included in bid and contract of DBO package. The IEE is now updated to reflect updated and final design of sewer networks in Zone-1, Zone-3, Zone-4, and Zone -5, water supply networks in Zone – 7 and Zone – 9. The additional scope involves refurbishment and installation of the SCDA system at the existing intake point in Dimiya dam. The construction of a raw water reservoir (550 kl) has also been undertaken by PHED and removed from the original scope. The proposed new intake has been removed from the scope as well, resulting in a reduction of the length of the raw water rising mains from 13.75 km to 10.08 km. The length of distribution networks increased from 153.39 km to 160.29 km. This will be further updated to reflect final design of Clear water pump house, Clear water Reservoir (CWR), STP-4 MLD, Sewer Pumping Stations -2, and any change in project design or location.

I. INTRODUCTION

A. Rajasthan Secondary Town Development Section Project – Additional Financing

1. Sector Project (RSTDSP, Loan 3972: IND) from its regular ordinary capital resources on 25 September 2020 and became effective on 4 January 2021. The closing date of the current project is 31 May 2028. This project is on track and has performed well consistently since the first quarter of 2021. Under this project, water supply systems are being improved in eight urban local body (ULB) towns (Output 1), and sanitation systems in 13 ULBs (Output 2). During the implementation, an additional 13 ULBs were added to the project for fecal sludge and septage management system development. Under Output 3, capacity building and training activities on sustainable and resilient water supply and sanitation (WSS) operations, hygiene, gender equality and social inclusion conducted.

2. The additional financing (the project) will expand the improved access to WSS services in at least ten urban local bodies (ULBs), benefiting 1.2 million people. Important value addition of the proposed project to the ongoing project is that it will provide innovative solutions to address climate change to respond to the growing climate risks and vulnerability and also to improve livability and prosperity through enhancing natural and/or built heritage at least ten ULBs in Rajasthan, benefiting 1.0 million people. The overall project is aligned with the following impacts: (i) access to potable, affordable, reliable, equitable, environmentally sustainable drinking water supply in all urban areas of Rajasthan improved, (ii) health status of urban population, especially the poor and under-privileged improved, and (iii) productivity, livability and prosperity for the citizens in Rajasthan cities and towns enhanced. Reflecting the additional measures to enhance climate resilience and heritage-sensitive urban development of the project, impact statement (iii) was added; the outcome statement is modified as quality, reliability, equity, and sustainability of urban assets and services in project towns of Rajasthan improved; and additional output was also added, resulting in four outputs.

- (i) **Output 1: Resilient water supply systems developed or improved.** By 2028, the project will (i) At least 1,300 km of water supply pipelines will be commissioned through a district-metered area approach for effective non-revenue water (NRW) management, (ii) at least 79,000 households will be connected to an improved water supply system, including at least 95% below poverty line households, with 100% functional meters allowing for the introduction of volumetric billing, (iii) three new water treatment plants (WTPs) will be commissioned with a total capacity of at least 24 million liters per day (MLD).
- (ii) **Output 2: Resilient and inclusive sanitation systems developed or improved.** By 2028, (i) at least 500 km of sewers will be constructed; (ii) seven sewage treatment plants (STPs) with co-treatment of wastewater and fecal sludge and with a total capacity of at least 30 mld will be commissioned and one existing STP with 10 mld capacity will be upgraded to meet current effluent standards; and (iii) at least 54,000 new household connections (including at least 95% below poverty line households) to the sewer system will be installed.
- (iii) **Output 3: Urban assets to enhance climate resilience and heritage living developed or improved.** By 2028, (i) at least 50 km of drainage networks will be constructed in five ULBs; (ii) at least five either Kunds or Baories rehabilitated and/or reconstructed in three ULBs that were heritage structures built for drainage, rainwater harvesting, and reuse, but currently are not properly functioning; (iii) five water parks rehabilitated in one ULB to enhance water retention and storage capacity and/or to improve people's well-being, both residents and visitors; and (iv)

at least four heritage structures are refurbished in five ULBs to improve the living environment and attract more tourists.

- (iv) **Output 4: Institutional and human capacities strengthened for sustainable service delivery, gender equality, and improved public health.**

3. The executing and implementing agencies will remain unchanged. GOR's Local Self Government Department (LSGD) is executing agency and the Rajasthan Urban Drinking Water, Sewerage and Infrastructure Corporation (RUDSICO) is implementing agency.

4. **Dungarpur water supply and sewerage subproject.** This is one of the subprojects proposed under RSTDSP-AF. It will improve water supply and sewerage systems in the town.

B. Purpose of Initial Environmental Examination Report

5. Per ADB's Safeguards Policy Statement, 2009, ADB requires the consideration of environmental issues in all aspects of the Bank's operations. Using rapid environmental assessment (REA) checklist (Appendix 1), subproject is unlikely to cause significant adverse impacts, and classified as category B and per ADB SPS requirements this IEE is conducted.

C. Scope of IEE

6. The subproject will be implemented under the design-build-operate (DBO) modality. Thus, this IEE is based on the preliminary project design report. The IEE is conducted mainly based on field reconnaissance surveys and secondary sources of information. Stakeholder consultation was an integral part of the IEE. Draft IEE of this subproject was prepared and approved by ADB based on feasibility / preliminary design and included in bid and contract of DBO package. The IEE is updated to reflect updated and final design of sewer networks in Zone-1, Zone-3, Zone-4, and Zone -5, water supply networks in Zone – 7 and Zone – 9. This will be further updated to reflect the final design of Clear water pump house, Clear water Reservoir (CWR), STP-4 MLD, Sewer Pumping Stations -2. The additional scope involves refurbishment and installation of the SCDA system at the existing intake point in Dimiya dam. The construction of a raw water reservoir (550 kl) has also been undertaken by PHED and removed from the original scope. The proposed new intake has been removed from the scope as well, resulting in a reduction of the length of the raw water rising mains from 13.75 km to 10.08 km. The length of distribution networks increased for 153.39 km to 160.29 km. This will be further updated as needed to reflect any change in project design or location. Updated IEE will supersede the earlier version.

D. Report Structure

7. This Report contains the following sections:

- Executive summary;
- (i) Introduction;
- (ii) Description of the project;
- (iii) Analysis of alternatives;
- (iv) Policy, legal and administrative framework;
- (v) Description of the environment;
- (vi) Anticipated environmental impacts and mitigation measures;
- (vii) Public consultation and information disclosure;
- (viii) Grievance redress mechanism;
- (ix) Environmental management plan; and

- (x) Conclusions and recommendations.

II. DESCRIPTION OF PROJECT

A. Dungarpur Town

8. Location, Area and Connectivity: Dungarpur Town is a municipal council situated in the southern part of Rajasthan state of India. It is the administrative headquarters of Dungarpur District. The district is roughly triangular in shape. In East and North its borders on Banswara and Udaipur District respectively while it adjoins the State of Gujarat in South & West. The Mahi river runs along the western edge of the district, forming the boundary with Banswara district. The Som River, a tributary of the Mahi, runs along the northern edge of the district, largely forming the boundary with Udaipur district. The rail line between Udaipur and Ahmadabad in Gujarat runs through the town, shortest distance to the National Highway 8 from Dungarpur town is 20 km. Dungarpur is located in the southern part of Rajasthan between 23° 20' and 24° 01' North latitude and 73° 21' and 74° 01' east longitude. In East and North it has common borders with Banswara and Udaipur districts respectively, while it adjoins the State of Gujarat in South and West. The most of the part of the district is hilly. The avg. elevation is 225 m (738 ft) above MSL. The municipal area of the town is about 13.20 Sq. Km.

1. Existing Conditions

(a) Water Supply

9. At present an intermittent water supply system is running in the town. The present production of clear water is 6.4 MLD but in fact due to system losses only 3.840 MLD of treated water is being reached to the consumers giving a service level of supply is only ~70 LPCD against the desired service of 135 LPCD. Thus, there is 35- 40% NRW in the system. The frequency of supply is once in a day for the average duration of 1.00-1.5 hours. The total present water supply 6.4 MLD includes 2.4 MLD from Edward Samand dam, 1.0 MLD from Vijay Chakra dam, 1.0 MLD from tube wells and remaining 2.0 MLD from open wells. Detail discussions on existing water supply system in Dungarpur town is given in **Appendix 3**.

10. **Source:** At present water supply of the town is dependent on two local surface water Reservoirs viz Edward Samand and Vijay Chakra Sagar (Dimiya) dam, in addition to these, some sub surface sources (7 tube wells and 15 nos. open well) have also been connected with the system, but due to rocky terrain the yield of these ground water sources is very less and as the water table is regularly depleting fast therefore these would not sustain for longer. Vijay Chakra Sagar (Dimiya) dam was constructed in 60th decade in constituency of Maharawal Laxmansingh for the full fill the requirement of drinking water of Dungarpur.

(b) Water Treatment Plants

11. There are two rapid gravity water treatment plants of capacity of 4.54 MLD and 3.25 MLD with the existing system. Thus, there is a total capacity of WTP is 7.79 MLD.

12. **Raw Water Conveyance.** The raw water from Edward Samand is carried out to raw water Sump at Bori H/Ws (WTP) by means of DI pipeline (by gravity flow) from there raw water is being pumped to WTP (3.25 MLD) at the same H/Ws for treatment. Balance 1.29 MLD me raw water is also carried out to Udaivilas H/Ws where another WTP (4.54 MLD) exists. Similarly, 3.25 raw

water from Vijay Chakra Sagar (Dimiya) is carried out to Udaivilas H/Ws (WTP-3.25+1.29= 4.54 MLD) by means of DI pipeline through inter mediate pumping at Taraghati pumping station. The details of these raw water conveyance pipelines are given below in Table 1.

Table 1: Details of raw Water conveyance in Dungarpur

S.N.	Source	To	Details of raw water pipeline			Utility for this project
			Material	Dia in mm	Length In Mtr.	
1	Edward Samand	RW Sump at Bori H/Ws (WTP)	DI K-7	(a) 400 (b) 350	1490 7510	Useful, shall be utilised for this project
2	RW Sump at Bori H/Ws	Udaivilas H/Ws (WTP)	DI K-9	200	5950	Useful, shall be utilised for this project
3	Vijay Chakra Sagar (Dimiya)	Udaivilas H/Ws (WTP) Via Intermediate pumping station at Taraghati	DI K-9	200	10082	Replacement by 250 mm dia to accommodate flow and change of alignment along road.
		Total			25,030	

2. Details of Head Works and CWRs

13. There was Five Head works in the system with the six CWRs & pump houses but at present only four Head works are in use in the system, as one Head Works has now been closed due to ruined & unusable condition of CWR and pump house.

(a) Existing service reservoirs

14. At present from water supply distribution point of view, the entire town has been divided into 20 zones. In these zones 23 Service Reservoirs (13 ESRs and 10 GLSRs) of various capacities are available in the respective zone areas; from this clear water is being supplied to the consumers.

15. For completed details and existing conditions of various existing water supply components are given in Audit report of existing water supply system in Dungarpur town in **Appendix 3** in this IEE.

16. **Area Coverage:** Presently about 70-80% area of municipality limit is covered under the drinking water supply scheme by ULB. Remaining area which is newly developed and newly added to the municipality area is remain unconnected with piped scheme and will be considered under this proposal.

(b) Sewerage

17. Dungarpur Municipal Council does not have any sewerage system. Presently the wastewater from kitchens & bathrooms is discharged into storm water drains culminating finally to the Nallah or on ground, which pollutes the environment and contaminates the ground water. Most of the residential, commercial buildings and educational institutions have on-site septic tanks and soak pits. The effluents from the septic tanks directly drain into the open drains. In the absence of safe disposal system of sewage, the people of town are exposed to unhealthy and

unhygienic environment. Therefore, public representatives are also demanding for the facilities of sewerage system on priority basis.

(c) Sewage Flows for Different Horizon Years

18. As per CPHEEO Sewerage Manual, 80% of the water may be expected to reach the sewers unless there is data available to the contrary. In Dungarpur, it is proposed to supply the water at the rate of 135 LPCD. The expected flow of sewage be 108 LPCD, 5% provision is added over this to account for ground water infiltration and any other unaccounted for nondomestic addition. Estimated Sewage Generation for Dungarpur town (under RUIDP Phase-IV) is given below:

Population (number)			Sewage Generation (MLD)		
2025	2040	2055	2025	2040	2055
32256	34041	35288	3.66	3.86	4.00

19. Zone wise coverage (under RUIDP Phase-IV coverage) including ward wise projected population and zone wise coverage are given **Table 2**.

Table 2: Zone wise coverage (under RUIDP Phase-IV coverage)

Zone No.	Zone Population (Total Town)			Zone Population (RUIDP Phase-IV)			Zone Population (FSM Area)			Zone Wise % Coverage of Town		
	2025	2040	2055	2025	2040	2055	2025	2040	2055	Total Area	RUIDP Phase-IV	FSM Area
1	21293	21891	22310	21293	21891	22310				100%	100%	
2	12012	13601	14711	9273	10267	10962	2739	3334	3749	100%	77%	23%
3	1766	1958	2093	1438	1594	1704	328	364	389	100%	81%	19%
4	9704	10918	11766				9704	10918	11766	100%		100%
5	1336	1567	1728				1336	1567	1728	100%		100%
6	2199	3093	3717				2199	3093	3717	100%		100%
7	3141	3781	4228	253	288	312	2887	3493	3915	100%	8%	92%
8	1517	1996	2330				1517	1996	2330	100%		100%
9	2663	3396	3908				2663	3396	3908	100%		100%
Total:	55630	62200	66790	32256	34041	35288	23374	28159	31502			

B. Proposed Water Supply and Sewerage Infrastructure in Dungarpur under RSTDSP

1. Water demand

20. Total projected clear water demand for various design years is given in **Table 3**. and ward wise population. The total ULB Population in 2025 is 55630 and base water demand is 7.51 MLD.

Table 3: Total Clear Water Demand for design years

SI No	Description	WATER DEMAND IN MLD		
		Year 2025	Year 2040	Year 2055
1	Total ULB Population	55630	62200	66790
2	Base demand @ 135 LPCD in MLD	7.51	8.40	9.02
3	Other demand, as for floating population, boarding schools reserve police line etc	0.674	0.674	0.674

SI No	Description	WATER DEMAND IN MLD		
		Year 2025	Year 2040	Year 2055
4	Total basic clear water Demand in MLD	8.18	9.07	9.69
5	Clear Water Demand including distribution Network Losses @ 10% in MLD (at distribution point)	8.34	9.33	10.02
6	Clear Water Demand including further rising lines Losses @ 2 % on demand at s.no.5 in MLD (at CWR)	9.28	10.28	10.99
7	Total clear water demand in MLD	9.28	10.28	10.99

C. Proposed Source for Subproject

21. **Proposed Water Sources:** There are 3 nos. surface water sources, proposed for water demand in this sub-project, and 4 nos. ground water sources including 2 nos. tube wells and 2 nos. open wells, proposed for emergency. Surface water source include Edward Samand Dam (availability of water 4.54 MLD), Vijay Chakra Sagar dam (availability of water 3.25 MLD) and Somkamla Amba dam (availability of water 4.361 MLD). Details on the need for refurbishment of existing components are given in **Appendix 3**. All four sources are already existing, and no new source will be developed for the project.

1. Proposed sources for water supply for Dungarpur

Table 4: Drinking water sources and water demand

Source	Existing water Demand	Proposed water demand	Change in usage
Edward Samand	4.54 MLD	4.732 MLD	4.23% Increase
Vijay Chakra Sagar	3.25 MLD	3.103 MLD	4.52% Decrease
Som Kamla Amba	Nil	4.361 MLD	New source
Ground water	3.0 MLD	1.5 MLD	50 % decrease

Table 5: Water availability in sources

Source	Total yearly storage capacity	Abstraction of water	Percentage of Abstraction	Government Allocation available PHED dam is or
Edward Samand	137 mcft = 3.879 MCM (137/35.317)	Daily - 4.54 MLD – Yearly - 1657.1 million Litre/Year = 1.66 MCM (yearly)	=1.66/3.879*100% =42.79%	4.54 MLD
Vijay Chakra Sagar	44.87mcft = 1.27 MCM (44.87/35.317)	3.25 MLD –Daily (1186.2 Million Litre/Year) 1.1862 MCM (yearly)	=1.1862/1.27*100% =93.40%	3.25 MLD (required water demand is 3.1 MLD)

Source	Total yearly storage capacity	Abstraction of water	Percentage of Abstraction	Government Allocation is or PHED dam
Som Kamla Amba	160 MCM total storage capacity and 8.01 MCM is reserved for drinking water	4.361 MLD - 1591.76 Million Liter/Year) 1.59 MCM /year	=8.01/ 1.59 *100% = 5.09 % of total drinking water available.	4.361 MLD

22. **Edward Sagar Dam (Durgapur reservoirs):** Situated on Do River, a seasonal river is a drinking water reservoir owned by PHED, GOR. Water of this reservoir is reserved only for drinking water for Dungarpur. Capacity of this dam is 137 MCFT (3.879 MCM) live storage. The PHED has allocated 4.54 MLD (1.66 MCM) water for Dungarpur water supply subproject, which is about only 42.79 % of total storage capacity of dam.

23. Total storage capacity of Edward Samand Dam is 137 MCFT but only 61 MCFT water quantity can be abstracted from this dam on gravity basis. About 11 feet of water storage is maintained as dead storage and only 61 MCFT water quantity will be used for this subproject. The intake and WTP are already existing on this dam. Water quantity is allocated for use is based on water abstractions from this dam on gravity basis and capacity of existing WTP. 11 feet water storage is maintained as dead storage.

24. The water from dam is not used for irrigation or any other activity. The PHED has recorded yearly water level data of dam and as per water level data of past 12-year, the dam was filled fully up to its storage capacity in all 12 years.

25. **Vijay Chakra Sagar Dam:** Situated on Moran River, tributary to Mahi river near Dimiya village, Dungarpur is a drinking water reservoir owned by WRD, GOR water of this reservoir is reserved only for drinking water supply for Dungarpur. Capacity of this dam is 44.87 MCFT including dead storage and 40 MCFT (1.27 MCM) is live storage. The PHED has allocated 3.1 MLD (1.18 MCM) water for Dungarpur water supply subproject (but currently only 1 MLD has been abstracted), which is about 93.40% of total water available in dam. The existing water abstraction of water from dam is 3.25 MLD and proposed capacity is 3.1 MLD. The water from dam is not used for irrigation or any other activity. The PHED has recorded yearly water level data of dam and as per water level data of past 12-year, the dam was filled fully up to its storage capacity in all 12 years. This project will take up installation of SCDA system and refurbishment of existing intake structure. Assessment of existing structures will be conducted. Based on the conditions identified during these assessments, the scope of refurbishment will be determined.

26. As per the subproject design, the abstraction from Vijay Chakra Sagar Dam will remain same and it will provide 3.1 MLD or 25.44 % of total design demand of 12.196 MLD (2040). There is also a proposal by PHED Dungarpur to increase this dam height by 1 m to increase water availability in future, however since it is only in proposal stage, the increase in water storage of dam is not considered in the subproject design. In original project proposal a new intake well was proposed near the embankment, however due to presence of *Crocodylus palustris* nests near dam bund area, possibility and feasibility of using the existing intake well was explored. Bathymetric survey of the dam was conducted, and it was found that the depth of proposed location is 2.67 m, while the depth at existing location is 2.01 m. There is a difference of only 0.66 meters in depth at proposed and existing locations which indicate minimal level differences in the

dam. During lean years, temporary shortage of water occurs during summers at the existing location. However, the bathymetric survey (attached as Appendix 14) reveals that at a close distance from existing intake point, the reservoir depth is 3.0 m. A channel can be dug manually in the dam between the existing intake point and the nearest deepest point so that the water availability is secured during summers in event of lean years. The manual excavation of trench shall be taken up during summers when water level in dam is low. In view of water availability and proposed trench from nearest deepest point to existing intake well will ensure the availability of water in existing intake well. Construction of a new intake well at the proposed location might disturb the biota, especially the crocodiles. While existing intake well can assure the water availability and after refurbishment it can be efficiently used, the proposal of new intake well is dropped and refurbishment is proposed. PHED, Gov. Rajasthan have already taken up the work of replacement of pumps in existing intake well. This proposal will save approximately 3 km of raw water rising main from intake to WTP.

27. **New proposed Som Kamala Amba (SKA) Dam on Som River:** This dam is located on Sam River in Ashpur Tehsil of Dungarpur District, to provide the Irrigation cum drinking water facilities. The dam supplies 8.1 MCM drinking water and irrigation supply to 26998.6 ha of Gross Command Area (GCA) and 19155.42 ha of Culturable Command Area (CCA).

28. Capacity of dam at FTL of 213.5 m is 172.75 MCM and live storage capacity 160 MCM MCM out of which 8.1 MCM is reserved for drinking water. The allotted water for Dungarpur is on 4.36 MLD (1.59 MCM) which is only 5.09 % of total drinking water available in dam.

29. To meet out the shortfall demand of the town Dungarpur, the state Government has sanctioned a public importance project namely Drinking Water Supply Project for 151 Villages and 1 town of District Dungarpur (Dungarpur town itself) based on Som Kamla Amba Dam under Jal Jivan Mission. Presently the project is under execution, transmission main from the Som Kamla Amba Dam to Dungarpur town has been laid and construction work of intake well and water treatment plant is under progress. As per PHED officials project will be commissioned up to December 2022.

30. **Ground Water Source:** At present there are 7 Nos tube wells, and 15 Nos Dug Wells / Open wells are supplies 3.0 MLD water to Dungarpur, out of these existing wells, 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desilting, with re commissioning work. Based on the design consideration, it was proposed to consider 1.5 MLD of water from ground water sources in case of emergency situations like repair and maintenance works in surface water sources and during lean seasons when water availability in surface water sources in less.

31. **Proposed works under Water Supply are-** (i) Installation of SCDA system, Refurbishment of existing intake structure at existing intake well. (ii) clear Water Pump House (5 nos.) (iii) Clear Water Reservoir (2 nos., 550 KL & 600 KL) (iv) Raw water rising main of 13.75 km and clear water rising main of 14.95 km (v) Distribution networks of 160.29 km (vi) House service connection- 12067 nos. (vi) Refurbishment of pump house (7 nos.), RWR (235 KL), WTPs- 2 nos. (4.54 MLD and 3.25 MLD), CWRs (2nos.), OHSRs (8nos.), GLSRs (4 nos.), (viii) Rehabilitation of 2 TWs and 2 open wells, (ix) Construction of CRMC (2 nos.) and MCC (1no.).

2. Availability of clear water from proposed sources

32. As total production from Edward Samand dam is 4.54 MLD. 4.54 MLD raw water will be collected to Bori RWR by gravity. From Bori RWR 3.25 MLD water pumped to Bori WTP of

capacity 3.25 MLD and balance 1.29 MLD raw water is transferred to Udai villas WTP (of capacity 4.54 MLD). Production from Dimiya Dam will be 3.1 MLD, therefore total water proposed to be treated at Udai villas WTP is 3.25 MLD + 1.29 MLD = 4.54 MLD. Presently the existing intake well for pumping raw water from Dimiya dam is in back water of dam, during the summer season water is to be brought near existing pump house by the centrifugal submersible pumps.

33. PHED ensured vide letter No EE/ DPR/2021-22/ 1596 dated 12-08-2021 for allocation of clear water from proposed sources (Letter is attached as **appendix 5** in IEE)

3. Associated projects:

34. **New Water Source** Som Kamla Amba Dam on Som River is proposed as new sustainable source for the subproject by PHED. Som Kamla Amba dam is located on Som River in the Dungarpur district. The construction of this dam was started in 1992 and completed in 2000 for irrigation and drinking purposes. At the Somkamla Amba Dam, a new WTP, Intake and Rising Main upto CWR in new colony (Dungarpur) are proposed under PHED Jal Jivan Mission project which will completed by 2024 through PHED Dungarpur. Supporting details given by Chief Engineer PHED Jaipur through the letter **No. CE(SP)/PHED/Dungarpur/DPR/2018-19/2630-2431 dated 26.07.2018. Letter and Summary of DPR are given in Appendix 4. In this project** At initial phase WTP of 21.29 MLD is proposed for demand of 2036 upgradable upto 29.01 MLD for future demand.

35. **Sewerage works.** Under RSTDSP, it is proposed to develop a sewerage system in Dungarpur Town to collect, treat, and dispose/reuse the domestic wastewater safely. The objectives of the proposed sewerage works are:

- (i) Construction of sewerage network, including house sewer connection and collection of wastewaters from point of generation;
- (ii) Construction of energy efficient and mechanized STP and electromechanical machinery;
- (iii) Septage management and decentralized wastewater treatment systems in suitable areas;
- (iv) Provision for reuse of treated effluent etc.;
- (v) To ensure 100 % house service connections for wastewater collection; and
- (vi) To ensure sustainability of the project by implementing a comprehensive asset management plan focusing on an integrated approach to O&M to minimize lifecycle costs.

35. **Proposed works under Sewerage are-** (i) Laying of 63.79 km sewer (ii) Construction of 2 nos. Sewage pumping stations (SPS) of capacities of 3MLD, 3MLD and one number of MWPS of 0.25 MLD (iii) Construction of 4.0 MLD Sewage Treatment Plant (STP) near Do River on Udaipur road Provide 12440 nos. (iv) Rising main of 7.3 km (v) 6460 nos. of House Sever Connections inside the property boundary (vi) FSSM work including procurement of desludging tank of 4000 lit capacity.

36. **Sewage treatment Plant.** It is proposed to develop sequential batch reactor (SBR) based sewage treatment facility that will treat the incoming sewage to stringent discharge standards specified in this IEE and included in the bid documents. SBR is a cyclic activated sludge treatment process and provides highest treatment efficiency possible in a single step biological process. One STP of 4.0 MLD Capacity along with 380 KL capacity TESR & 760 KL of TEER, is proposed as part of the project in Dungarpur Town to meet the sewage generation.

The proposed location of STP and its associated components is in north-west direction of Dungarpur town. Land ownership of the proposed STP and treated effluent discharge point is under Nagar Parishad of Dungarpur town. The nearest habitation of the proposed STP site is Bhilwata colony at 300 m distance. There is no direct impact on human being lived in surrounding areas from STP and its treated effluent discharge. Land for proposed STP and treated effluent discharge is under ownership of Municipal Cooperation of Dungarpur

37. **Disposal of Treated Wastewater:** After Treatment of wastewater at proposed 4 MLD STP, is proposed to dispose by gravity nearby river located about 50 metre away from STP site into the Do River the disposal site is just outside the STP premises. Do River is the tributary river of Som River. Do River is associated with Dungarpur city through the natural drain in which local city drainage and outfall of Gap Sagar and Sabela Lake is discharged. Do river is seasonal river therefore impact of treated effluent discharge into this river is negligible. Proposed STP location and final discharge point of treated effluent are shown in Google Map and Toposheet Map in **Figure 1 and 2.**

38. The disposal of treated water will be at downstream of Khandeshwar Mahadev temple. The temple has its own tube well for it own water use. Temple is not using any water from river. STP is proposed at a sufficient distance from the temple thus there is no negative impact is envisaged on temple.

39. **Faecal Sludge and Septage Management.** It is proposed to provide FSSM system in areas where the population density is low (less than 100 persons per hectare) and will not generate sewage in adequate quantity to convey by sewer network. FSSM will provide low-cost sanitation in areas where sewer network is not an immediate requirement/not feasible at present, will make septage collection, treatment and effluent management environment- friendly. Total 40 nos. Wards in Dungarpur are taken in the sewerage project. Out of 40 wards, 12 wards are considered under FSSM. These wards having the low density, unfavourable topographical conditions and other wards which will be covered under upcoming schemes as per available funding in future.

Table 6: ward wise population and habitation details at Dungarpur town

Ward No.	Total Area	Habitation Area*	Other than Habitation Area	Census Population	Projected Population		
	Ha.			2011	2025	2040	2055
10 Year O & M							
1	137.93	61.47	76.46	1246	2482	3507	4223
2	18.98	11.01	7.97	889	1199	1457	1636
3	58.11	18.46	39.65	915	1420	1840	2132
4	127.04	40.08	86.96	1670	2271	2770	3118
5	245.89	47.64	198.25	1107	2185	3079	3704
Total					9557	12653	14813
3 Year O&M / Till laying of sewer network under other scheme or 10 Year which is minimum							
17	5.53	3.10	2.43	1117	1117	1117	1117
18	3.03	1.91	1.12	1284	1284	1284	1284
19	21.30	4.97	16.33	1289	1386	1466	1522
23	43.73	8.75	34.98	909	1150	1350	1490
26	98.51	9.11	89.40	1058	1274	1452	1577
31	44.15	8.08	36.07	1142	1319	1466	1569


Ward No.	Total Area	Habitation Area*	Other than Habitation Area	Census Population	Projected Population		
40	19.83	9.41	10.42	1018	1250	1442	1576
Total					8779	9577	10135

40. Under the FSSM, faecal sludge / septage will be collected from the household level septic tanks using truck mounted mobile desludging equipment and transported to STP for treatment. STP will have necessary provisions to receive and treat the septage along with the wastewater received via sewer network. STP will be designed accordingly by the successful bidder during the detailed design phase to comply with the treated effluent discharge standards specified in the bidding documents.

Figure 1: Location of STP and discharge point



Figure 2: Location of STP and discharge point on Toposheet

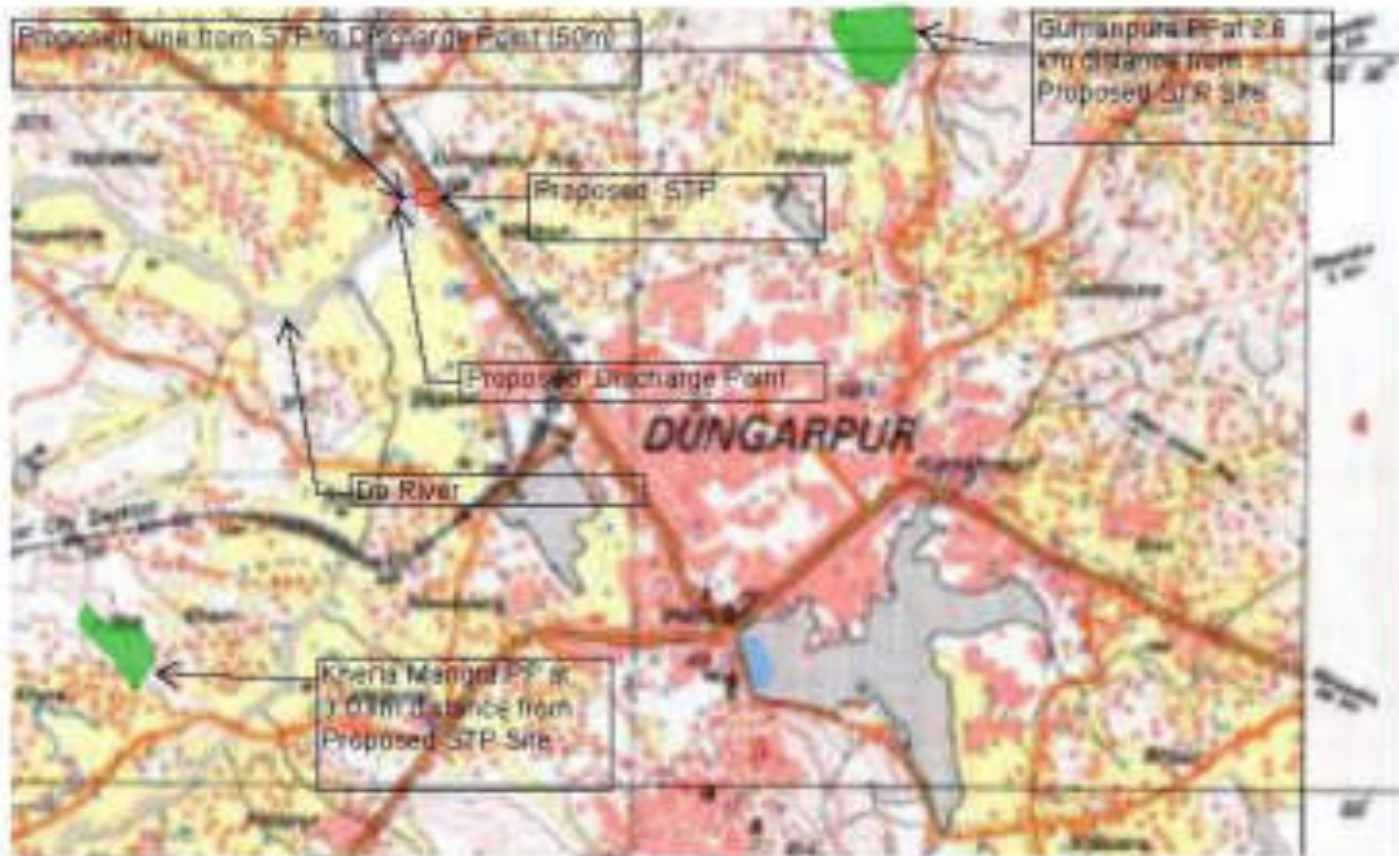

41. **Table 7** shows the nature and size of the various civil works components of this water supply and sewerage subproject in Dungarpur Town. Google Coordinates of proposed work sites are given in **Table 8**. Locations of project sites in google map are shown in **Figures 3 to 9**, conceptual layout plans and alignments are shown in **Figures 10 to 13** and approved layout plan of water supply and sewerage network are depicted in **Figures 14 to 21**.

Table 7: Details of Proposed Project components

Table 7.1: Details of Proposed Project Components				
Component	Function	Description	Location & Ownership	
Water Supply				
Intake – cum – raw water pump house for year 2036	Water extraction from source	Refurbishment • Installation of SCDA system • Refurbishment of existing intake structure. • Assessment of existing structures will be conducted. Based on the conditions identified during these assessments, the scope of refurbishment will be determined.	Location- Existing intake point at Vijay Chakra Sagar (Dimiya) Dam south-east of Dungarpur Town Ownership- WRD.	
Tube Wells	Water extraction from ground	Rehabilitation: 02 nos. of existing tube wells and 2 nos of existing open well	Location	Nos.
			Patrakar colony TW	1
			Darji wada TW	1
			Rani Bao OW	1
			Kela bao OW	1
			Total	4 (2 TW & 2 OW)
New Raw water pump house	Pumping the raw water	New Raw water pump house including complete pumping system to feed H/Ws	Location- Existing Bori WTP Campus Ownership- PHED	
Raw water Rising mains	Pumping of water	New 10.082 km	Location: Within ROW Ownership: Municipal Council	
WTPs	Treatment of raw water	Refurbishment Udaivilas - 4.54 MLD and Bori RGF (3.25MLD)	existing WTP campus Udaivilas existing WTP campus Bori RGF (3.25MLD)	
Pump houses		Refurbishment: Existing 7 Pump houses,	Vijay Chakra Sagar (Dimiya) PH-1 for Raw water, Udai vilas RGF (I), Bori RGF (I), Bori RGF (II), Nai Abadi CWR-PH-1, Main pump house at AEn PHED office, and Chandpole pump house	

Component	Function	Description	Location & Ownership																																																			
Clear Water Pump Houses with Chlorination system	Post chlorination / disinfection of water prior to supply	New 5 nos. of clear water pump houses with chlorination system	Locations: - Bori Campus - Chandpole Campus - Main PHED Campus - New Colony Campus - Udai Vilas Campus, Ownership: PHED																																																			
Clear water Rising mains	Pumping of water	New - 14.95 km	Location: Within ROW Ownership: Municipal Council																																																			
CWRs	Storage and pumping of clear water for supply	New 2 nos of CWRs of capacities of 550 KL and 600 KL	Location: - Chandpole (550 KL) - New Colony (600 KL) Ownership: PHED																																																			
OHSRs, CWRs,		Refurbishment: Existing raw water storage (235 KL), Existing 4.54 MLD (RGF) & 3.25 MLD (RGF) WTPs, Existing 4 nos. CWRs of 325, 325, 263 and 272 KL capacity, Existing SRs (8nos. ESRs & 4 nos. GLSRs)	Locations: Raw Water Storage: At Bori (Masonry) CWRs: <table><tr><th>Location of Head Works</th><th>Type of CWR</th><th>Capacity of existing CWR (kl)</th></tr><tr><td>Udaivilas</td><td>RCC CWR</td><td>325</td></tr><tr><td>Bori</td><td>RCC CWR</td><td>325</td></tr><tr><td>AEn Office</td><td>Masonry CWR</td><td>263</td></tr><tr><td>New colony / Nai Abadi</td><td>RCC CWR</td><td>272</td></tr></table> OHSRs and GLSRs- <table><tr><th>Location of OHSR/GLSR /VFD PUMPS</th><th>Capacity of OHSR(KL)</th><th>OHSR Staging</th></tr><tr><td>New Rajpura OHSR</td><td>150</td><td>18</td></tr><tr><td>Navadera OHSR</td><td>325</td><td>15</td></tr><tr><td>Meera Dungari GLSR</td><td>225</td><td>GLSR</td></tr><tr><td>Khantwara GLSR</td><td>225</td><td>GLSR</td></tr><tr><td>Ghati GLSR new</td><td>368</td><td>GLSR</td></tr><tr><td>Ghati (II) GLSR (</td><td>450</td><td>GLSR</td></tr><tr><td>Shastri Colony OHSR</td><td>100</td><td>15</td></tr><tr><td>Ptrakar Colony OHSR</td><td>140</td><td>18</td></tr><tr><td>Sindhi Colony OHSR</td><td>325</td><td>18</td></tr><tr><td>Pratap Nagar OHSR</td><td>75</td><td>15</td></tr><tr><td>Mordern School OHSR</td><td>210</td><td>18</td></tr></table>	Location of Head Works	Type of CWR	Capacity of existing CWR (kl)	Udaivilas	RCC CWR	325	Bori	RCC CWR	325	AEn Office	Masonry CWR	263	New colony / Nai Abadi	RCC CWR	272	Location of OHSR/GLSR /VFD PUMPS	Capacity of OHSR(KL)	OHSR Staging	New Rajpura OHSR	150	18	Navadera OHSR	325	15	Meera Dungari GLSR	225	GLSR	Khantwara GLSR	225	GLSR	Ghati GLSR new	368	GLSR	Ghati (II) GLSR (	450	GLSR	Shastri Colony OHSR	100	15	Ptrakar Colony OHSR	140	18	Sindhi Colony OHSR	325	18	Pratap Nagar OHSR	75	15	Mordern School OHSR	210	18
Location of Head Works	Type of CWR	Capacity of existing CWR (kl)																																																				
Udaivilas	RCC CWR	325																																																				
Bori	RCC CWR	325																																																				
AEn Office	Masonry CWR	263																																																				
New colony / Nai Abadi	RCC CWR	272																																																				
Location of OHSR/GLSR /VFD PUMPS	Capacity of OHSR(KL)	OHSR Staging																																																				
New Rajpura OHSR	150	18																																																				
Navadera OHSR	325	15																																																				
Meera Dungari GLSR	225	GLSR																																																				
Khantwara GLSR	225	GLSR																																																				
Ghati GLSR new	368	GLSR																																																				
Ghati (II) GLSR (	450	GLSR																																																				
Shastri Colony OHSR	100	15																																																				
Ptrakar Colony OHSR	140	18																																																				
Sindhi Colony OHSR	325	18																																																				
Pratap Nagar OHSR	75	15																																																				
Mordern School OHSR	210	18																																																				

Component	Function	Description	Location & Ownership		
			Ashok nagar OHSR	113	18
Distribution Network	Water distribution	New 160.29 km Length	Location: Entire Town, within ROW Ownership: Municipal Council		
House Service Connections		New 12067 nos.	Houses		
CRMCs and MCC	Consumer relations and SCADA system control for entire water supply system	New: CRMC- 2 nos. MCC- 1 no.	Location- On Govt. Lands (to be decided) Ownership- Govt. Land		
Sewerage					
House Sewer Connections		New 6460 nos.	Individual houses		
Sewer Collection networks	Collect wastewater from houses and convey by a combination of gravity and pressure pumping to pumping station and ultimately to the STP	New Sewer Collection networks: 63.79 km 1. RCC pipes– 2.50 Kms. 2. HDPE DWC SN 8 pipe – 46.80 Kms. 3. HDPE pipes– 2.18 Kms	Location: within existing ROW Ownership: Municipal Council Dungarpur		
Sewage Pumping Station (for ultimate design year 2055)	Sewer pumping stations are used to move wastewater to higher elevations in order to allow transport by gravity flow until the sewage reaches treatment plant.	New Two numbers of SPS of 3 3.0, 3.0 and one MWPS of 0.25 MLD capacities	Location and capacity of SPS		Ownership
			Near Padambhusan Shri Bhogi Lal Pandya Circle (3.0MLD). Location of SPS is in south direction of Dungarpur Town.	Rajasthan state Govt.	
			Near Ashram Vatika (3.0 MLD) Location of SPS is in west direction of Dungarpur Town.	Municipal Council, Dungarpur	

Component	Function	Description	Location & Ownership	
			Between RICCO & Gap Sagar (0.25 MLD). Location of SPS is in north-east of Dungarpur Town.	Rajasthan state Govt.
Rising mains	pumping from pumping station to STP	Rising mains for pumping sewers- 7300 m (DI K-9 pipes of following details- 400 mm dia- 2700 m 400 mm dia- 800 m 150 mm dia- 3800 m)	Location: within existing ROW Ownership: Municipal Council Dungarpur	
Sewage Treatment plants (for intermediate year 2040)	Treatment of collected wastewater to meet stipulated discharge standards	New 4 MLD STP	Location: Zone-6 near Do river on Udaipur road. Ownership: Rajasthan State Government The location of proposed STP is in north-west direction.	
Faecal sludge and septage management (FSSM) works	Desludging of septage from household pits/ septic tanks, transportation & discharge to STP	New Procurement of desludging equipment with 4000 ltr (1 nos.) tanks capacity for collection of faecal sludge and septage from 5 wards	Proposed wards for collection of faecal sludge and septage from houses- 1, 2, 3, 4 and 5.	

Table 8: Coordinates of Sub Project Locations

COMPONENTS	Latitude	Longitude
Proposed STP 4.0 MLD site, Near Do River on Udaipur Road	23°51'47.51"N	73°41'33.06"E
Proposed SPS site 1 at Near Padambhusan Shri Bhogi Lal Pandya Circle	23°50'24.33"N	73°42'40.44"E
Proposed SPS site 2 Near Ashram Vatika	23°51'7.38"N	73°42'14.09"E
Proposed SPS site 3 Between RICCO & Gap Sagar	23°50'59.09"N	73°43'37.55"E
Proposed CWR at Chandpole	23°50'6.18"N	23°50'6.18"N
Proposed CWR at New Colony	23°50'52.30"N	73°42'38.67"E
Proposed Raw Water Sump Storage near Existing WTP in Bori, Dungarpur	23°50'2.62"N	73°41'2.64"E

Subproject Benefits

42. The subproject is primarily designed to improve environmental quality and living conditions of Dungarpur Town through provision of water supply and sewerage. The benefits arising from this subproject include: (i) increased availability of potable water at appropriate pressure to all

households including urban poor; (ii) reduced time and costs in accessing alternative sources of water. (iii) collection of sewage from houses, appropriate treatment and safe disposal of sewage in scientific manner (iv) better public health particularly reduction in waterborne and infectious diseases; (v) reduced risk of groundwater contamination; (vi) reduced risk of contamination of treated water supplies; and (vii) improvement in quality of water bodies due to disposal of treated effluent meeting disposal standards.

D. Implementation Schedule

43. Subproject is proposed for implementation under DBO modality, wherein which the successful bidder will design the water supply and sewerage systems and components (based on the feasibility/preliminary design/standards/guidelines provided in the bid document), construct, commission, and operate for 10 years, after which it will be transferred to Dungarpur Municipal Council. The draft IEE was further updated and approved by ADB and this IEE is being updated due to change in scope (deletion of intake well and raw water pump house) from scope and inclusion of comprehensive biodiversity report prepared in view of sighting of crocodiles in the reservoir. This updated IEE will also be disclosed to a wider audience via the ADB and RUDSICO websites. The consultation process will continue during project implementation. A grievance redress mechanism (GRM) is established to redress public grievance. The updated IEE will supersede the previous version of IEE and will be binding to the contractor.

44. After the completion of preliminary designs, bids were invited in May 2022 for the subproject to be implemented under the DBO modality. After evaluation of Bids LOA was issued on 14 December 2022 and thereafter work is awarded. Project duration of Design Build is 36 months. After completion of construction and commissioning, scheme will be operated by DBO contractor for 10 years, and after which the O&M will be carried out by ULB and/or PHED.

Figure 3: Line diagram for water supply project, Dungarpur in Google Earth imagery



Figure 4: Schematic Layout of Proposed Water Supply Networks

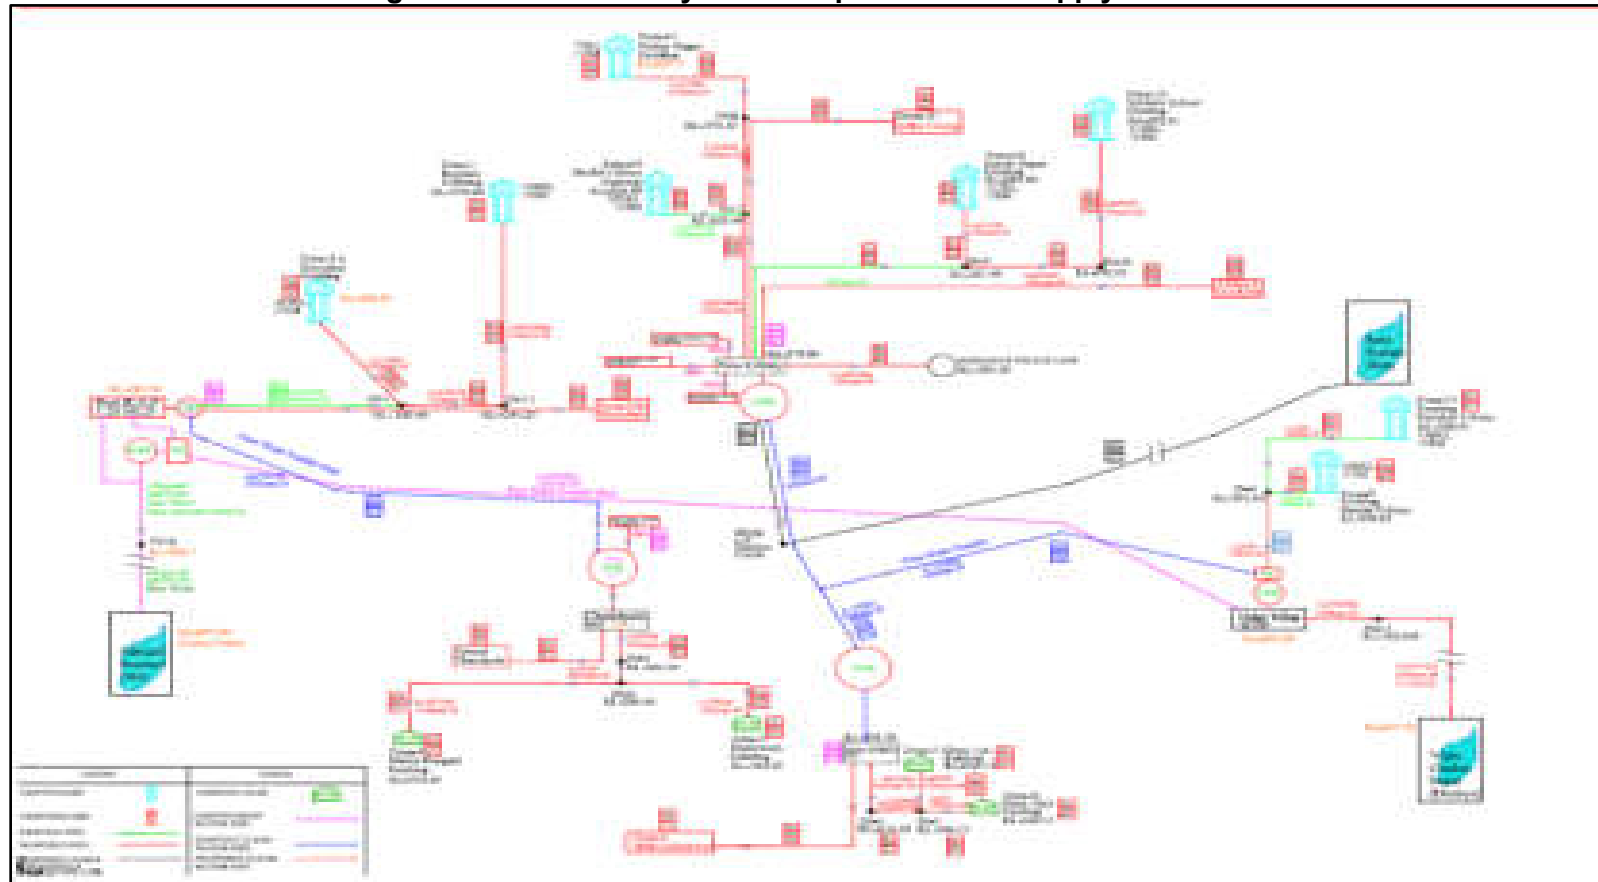


Figure 5: Location of Proposed Raw Water Sump Storage near Existing WTP in Bori, Dungarpur in Google Earth



Figure 6: Location of Proposed CWR1 location in Chandpole Colony, Dungarpur in Google Map

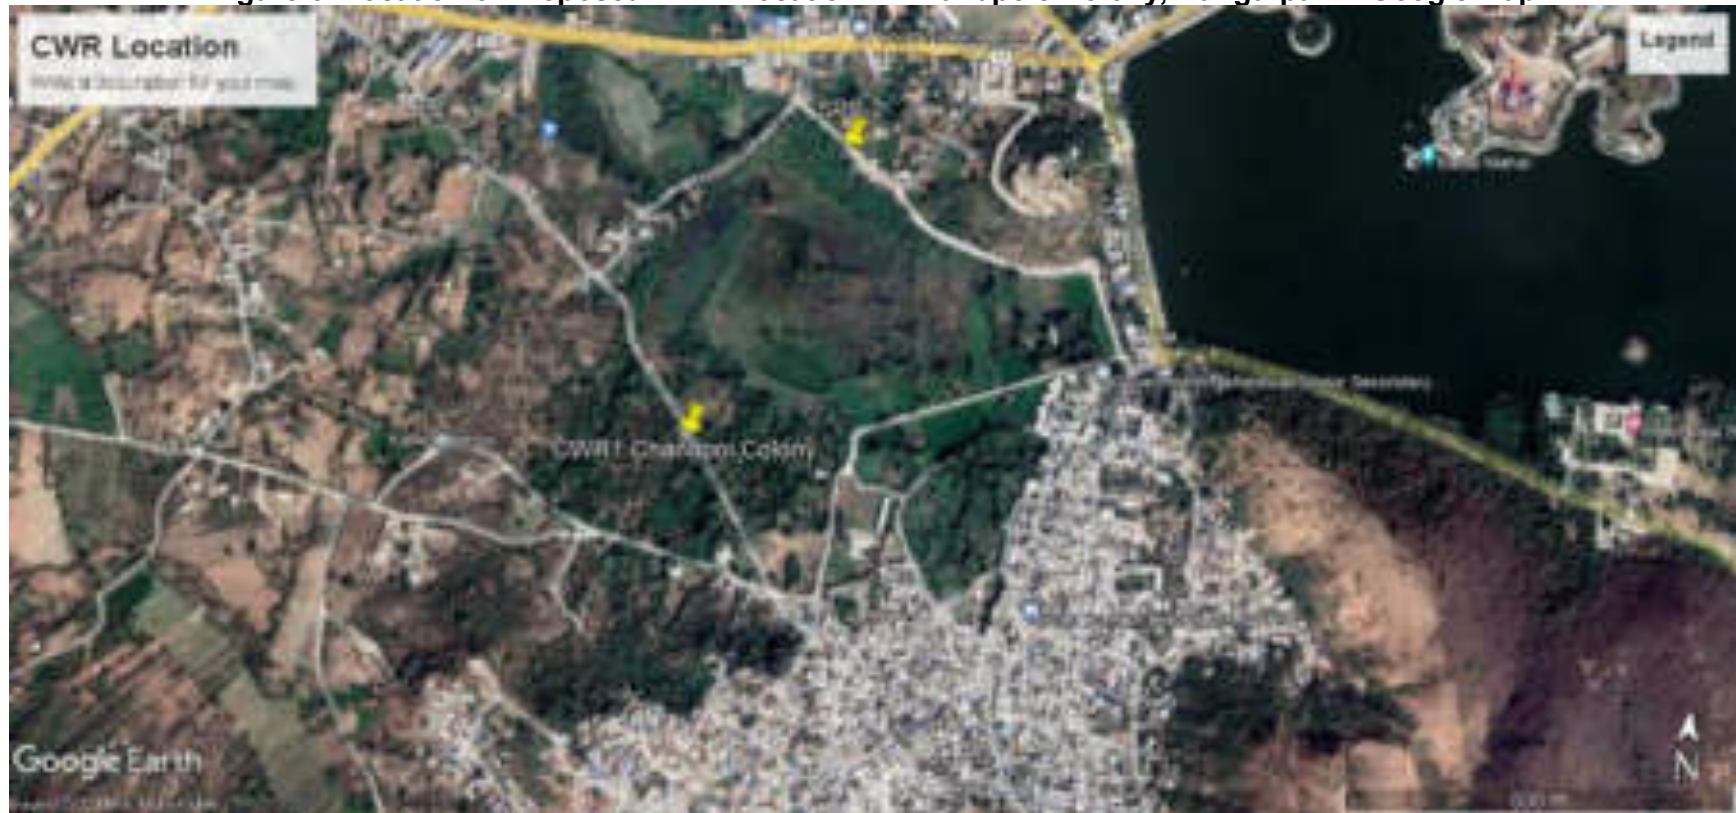


Figure 7: Location of Proposed CWR2 location in New Colony, Dungarpur in Google Map



Figure 8: Location of Proposed STP near Do River on Udaipur Road in Google Earth



Figure 9: Location of Proposed SPS1 locations Near Ashram Vatika, Dungarpur in Google Earth



Figure 10: Location of Proposed SPS2 location Near near Bhogi Lal Pandya Circle in Google Earth Map



Figure 11: Location of Proposed SPS3 location Between RICCO & Gap Sagar, Dungarpur in Google Map



Figure 12: Layout of Proposed Sewer Networks and FSSM areas


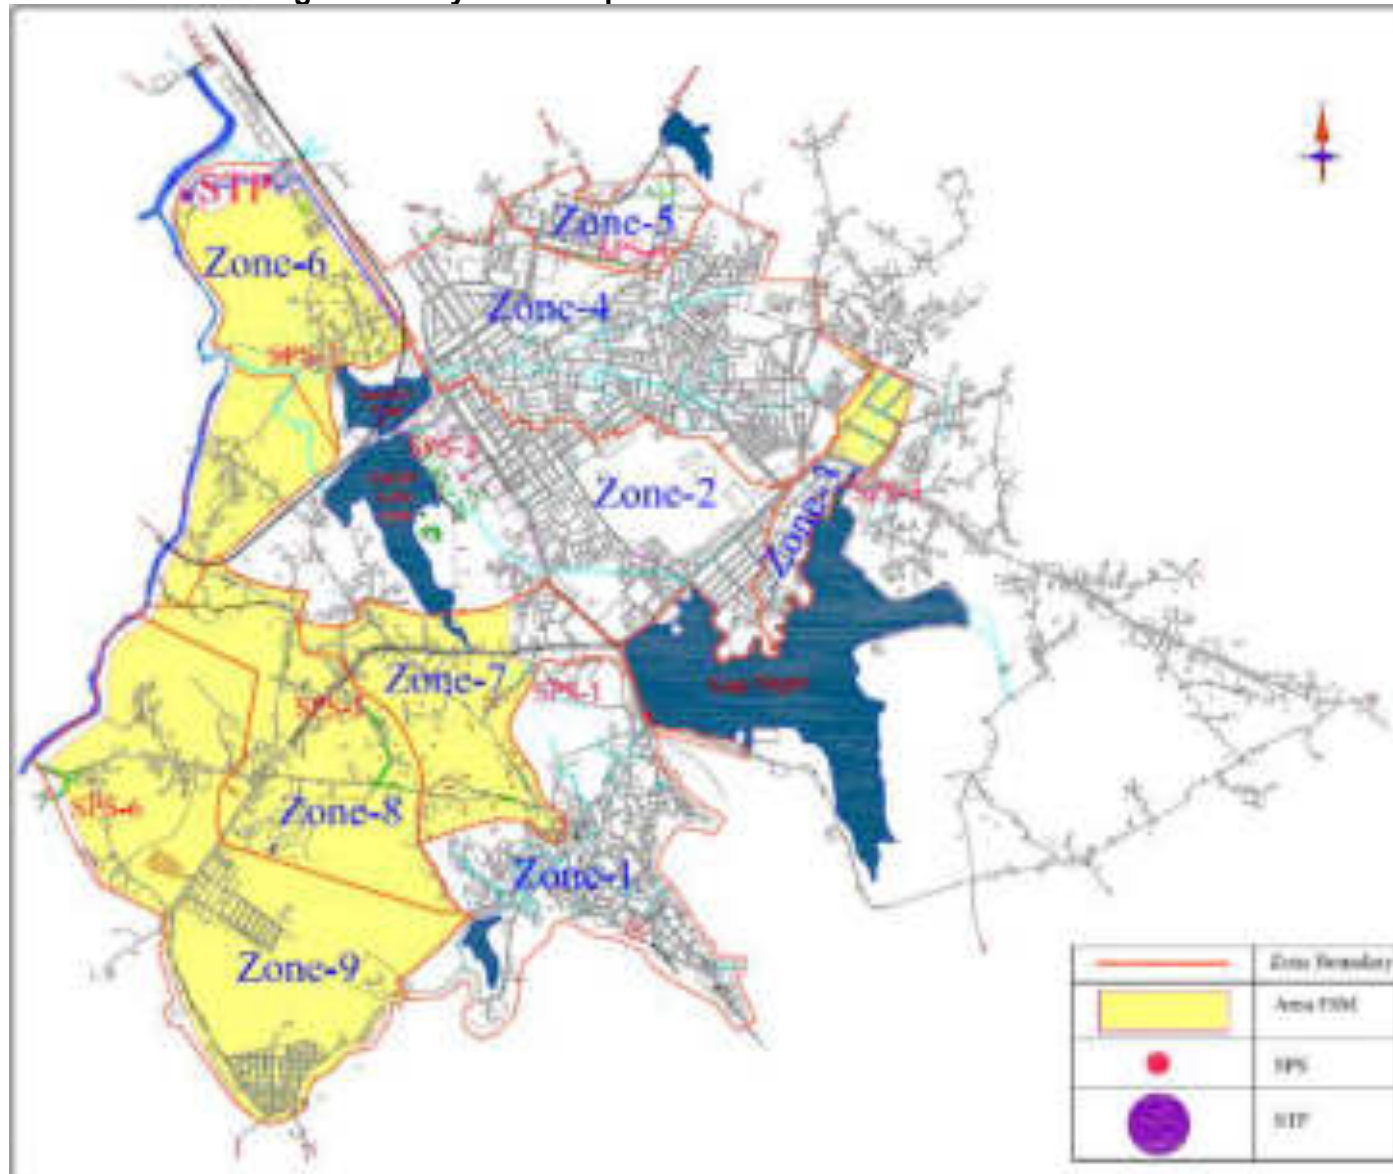


Figure 13: Typical Layout of Proposed STP

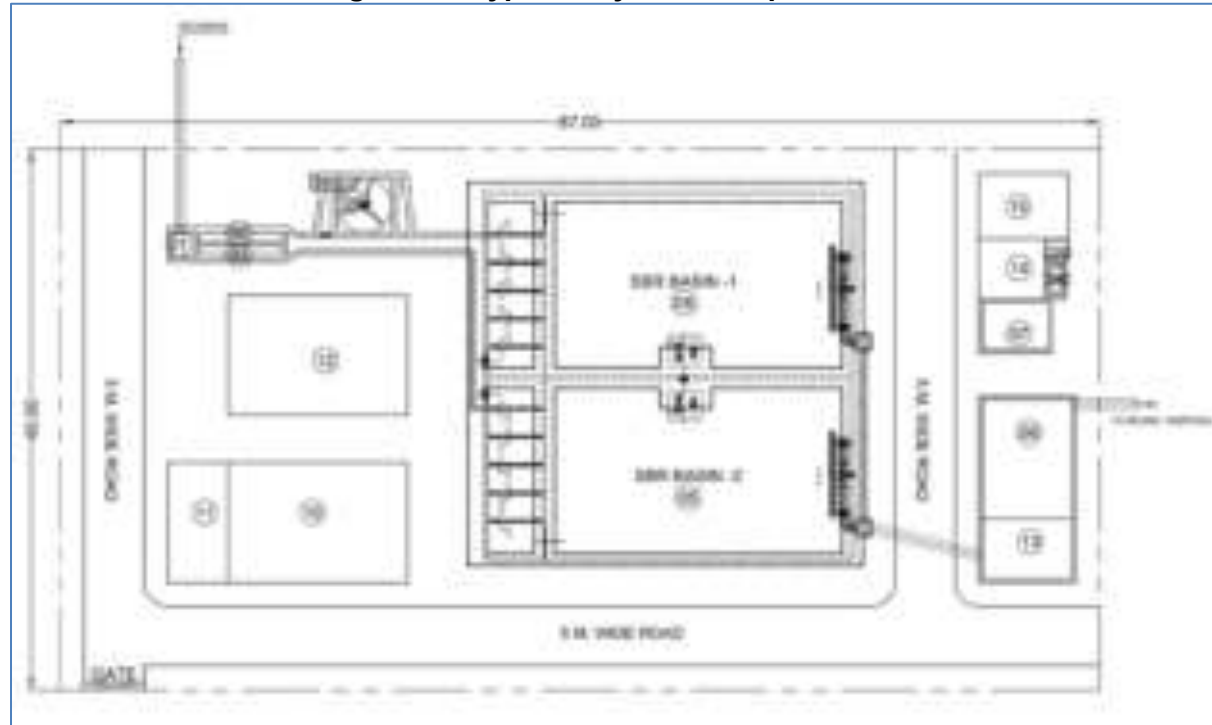

SL.NO	PROCESS UNIT	SIZE/CAPACITY	QTY.	REMARKS
01	Bar Screens	1000 x 750 x 550 SMC	01	
02	Bar Screens	1000 x 750 x 550 SMC	01	
03	Grassed Channel-Mechanical	4000 x 4000 x 300 SMC	01	
04	Grassed Channel-Mechanical	4000 x 4000 x 300 SMC	01	
05	Sewage Bay	10000 x 10000 x 3000 SMC	01	
06	Sewage Bay	10000 x 10000 x 3000 SMC	01	
07	Chlorination Tank	1000 x 1000 x 4000 SMC	01	
08	Sludge Slap	1000 x 1000 x 1000 SMC	01	
09	Particulate Solids Slab	1000 x 1000 x 1000 SMC	01	
10	Chlorination Tank	1000 x 1000 x 4000 SMC	01	

SL.NO	PROCESS UNIT	SIZE/CAPACITY	QTY.	REMARKS
10	Bar Screens	1000 x 750 x 550 SMC	01	
11	Grassed Channel-Mechanical	4000 x 4000 x 300 SMC	01	
12	Grassed Channel-Mechanical	4000 x 4000 x 300 SMC	01	
13	Sewage Bay	10000 x 10000 x 3000 SMC	01	
14	Sewage Bay	10000 x 10000 x 3000 SMC	01	
15	Chlorination Tank	1000 x 1000 x 4000 SMC	01	
16	Sludge Slap	1000 x 1000 x 1000 SMC	01	
17	Particulate Solids Slab	1000 x 1000 x 1000 SMC	01	
18	Chlorination Tank	1000 x 1000 x 4000 SMC	01	
19	Sludge Slap	1000 x 1000 x 1000 SMC	01	
20	Particulate Solids Slab	1000 x 1000 x 1000 SMC	01	

Figure 14: Layout plan of water supply network in ZoneZ-7 in Dungarpur

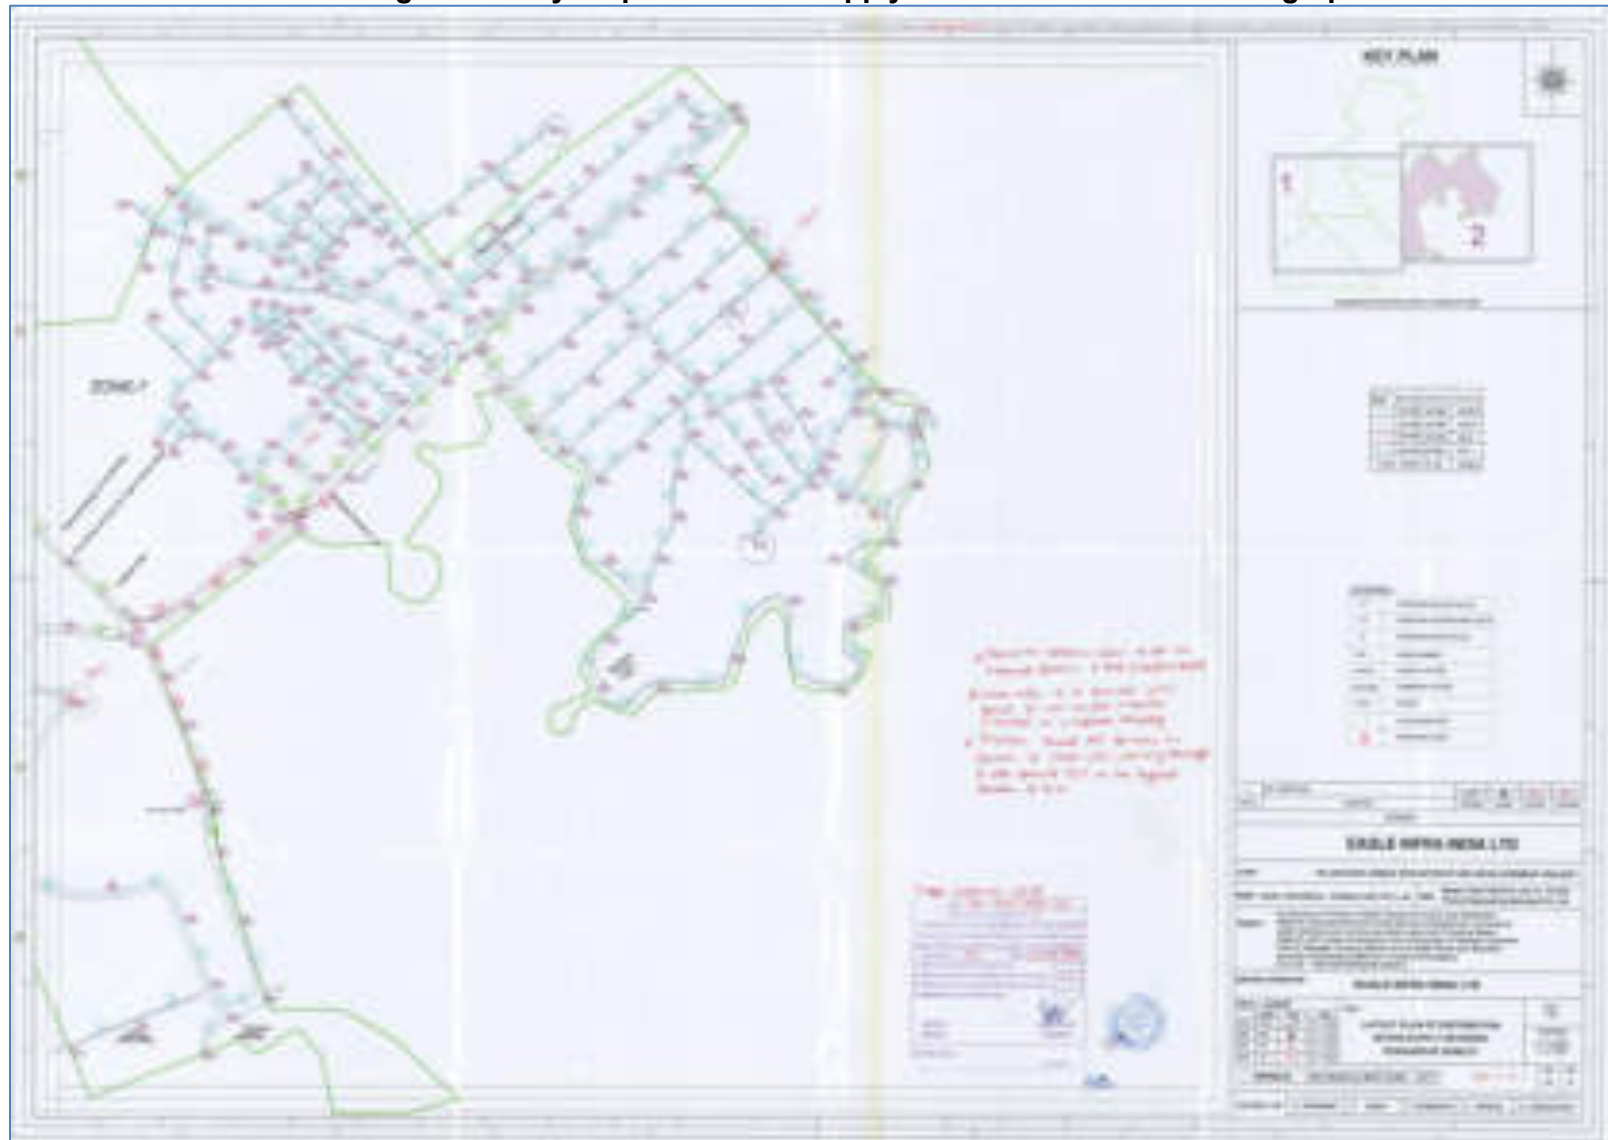


Figure 15: Layout plan of water supply network in Zone Z-7 in Dungarpur



Figure 16: Layout plan of water supply network in Zone Z-9 in Dungarpur

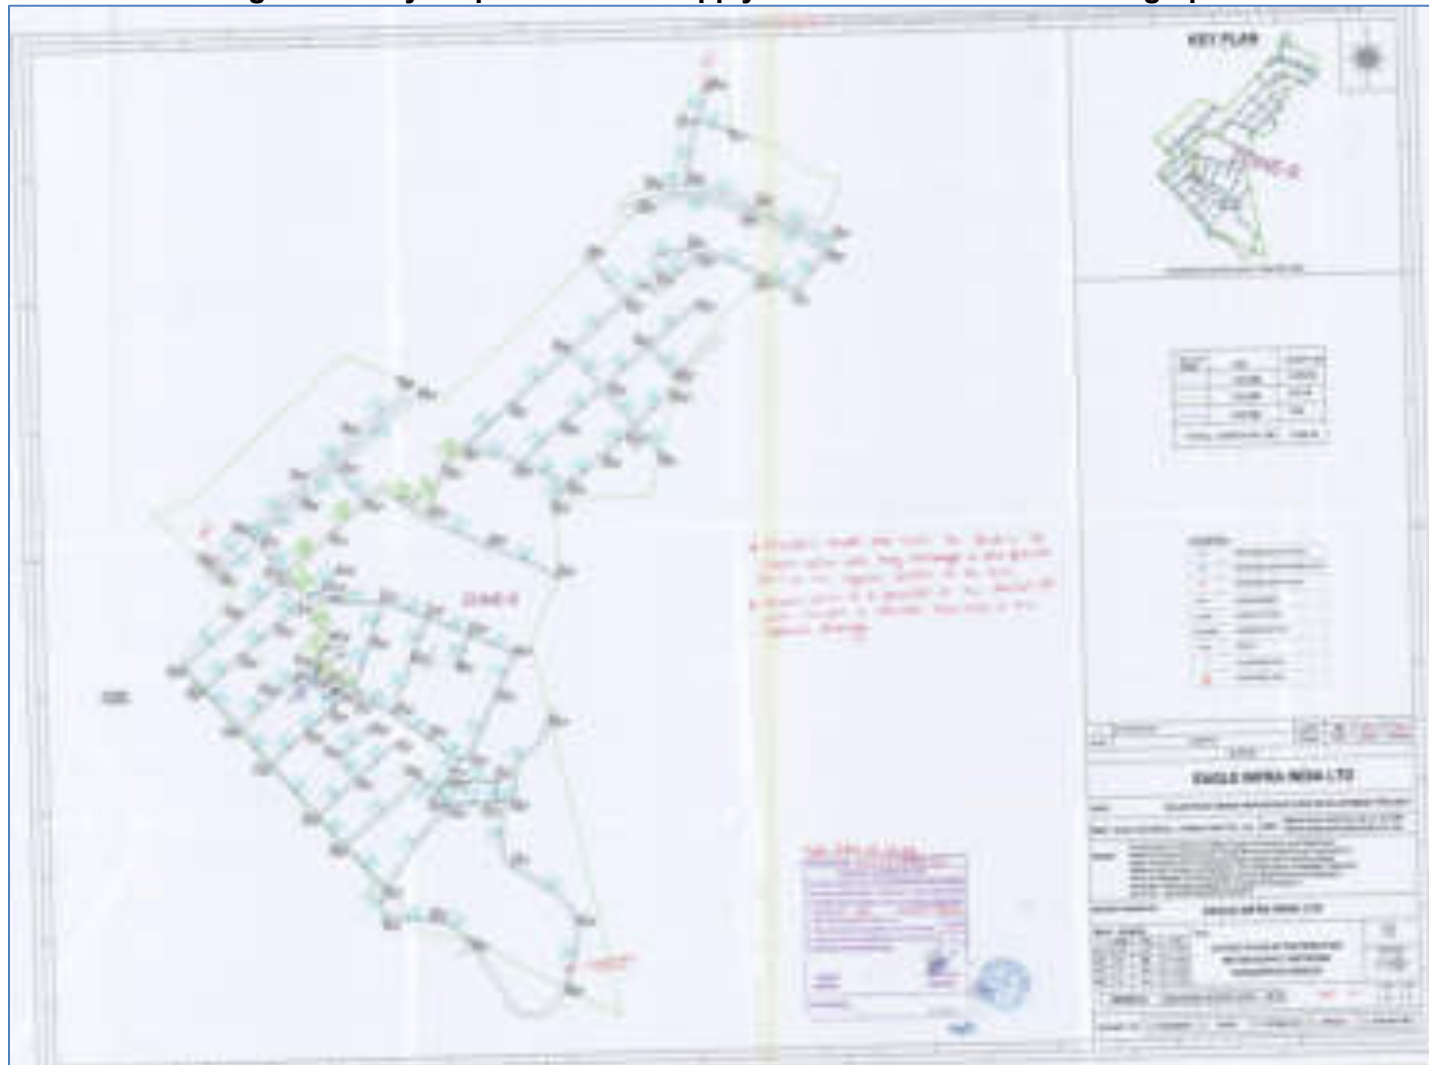


Figure 17: Layout plan of sewerage network in Zone -1 in Dungarpur



Figure 18: Layout plan of sewerage network in Zone -3 in Dungarpur

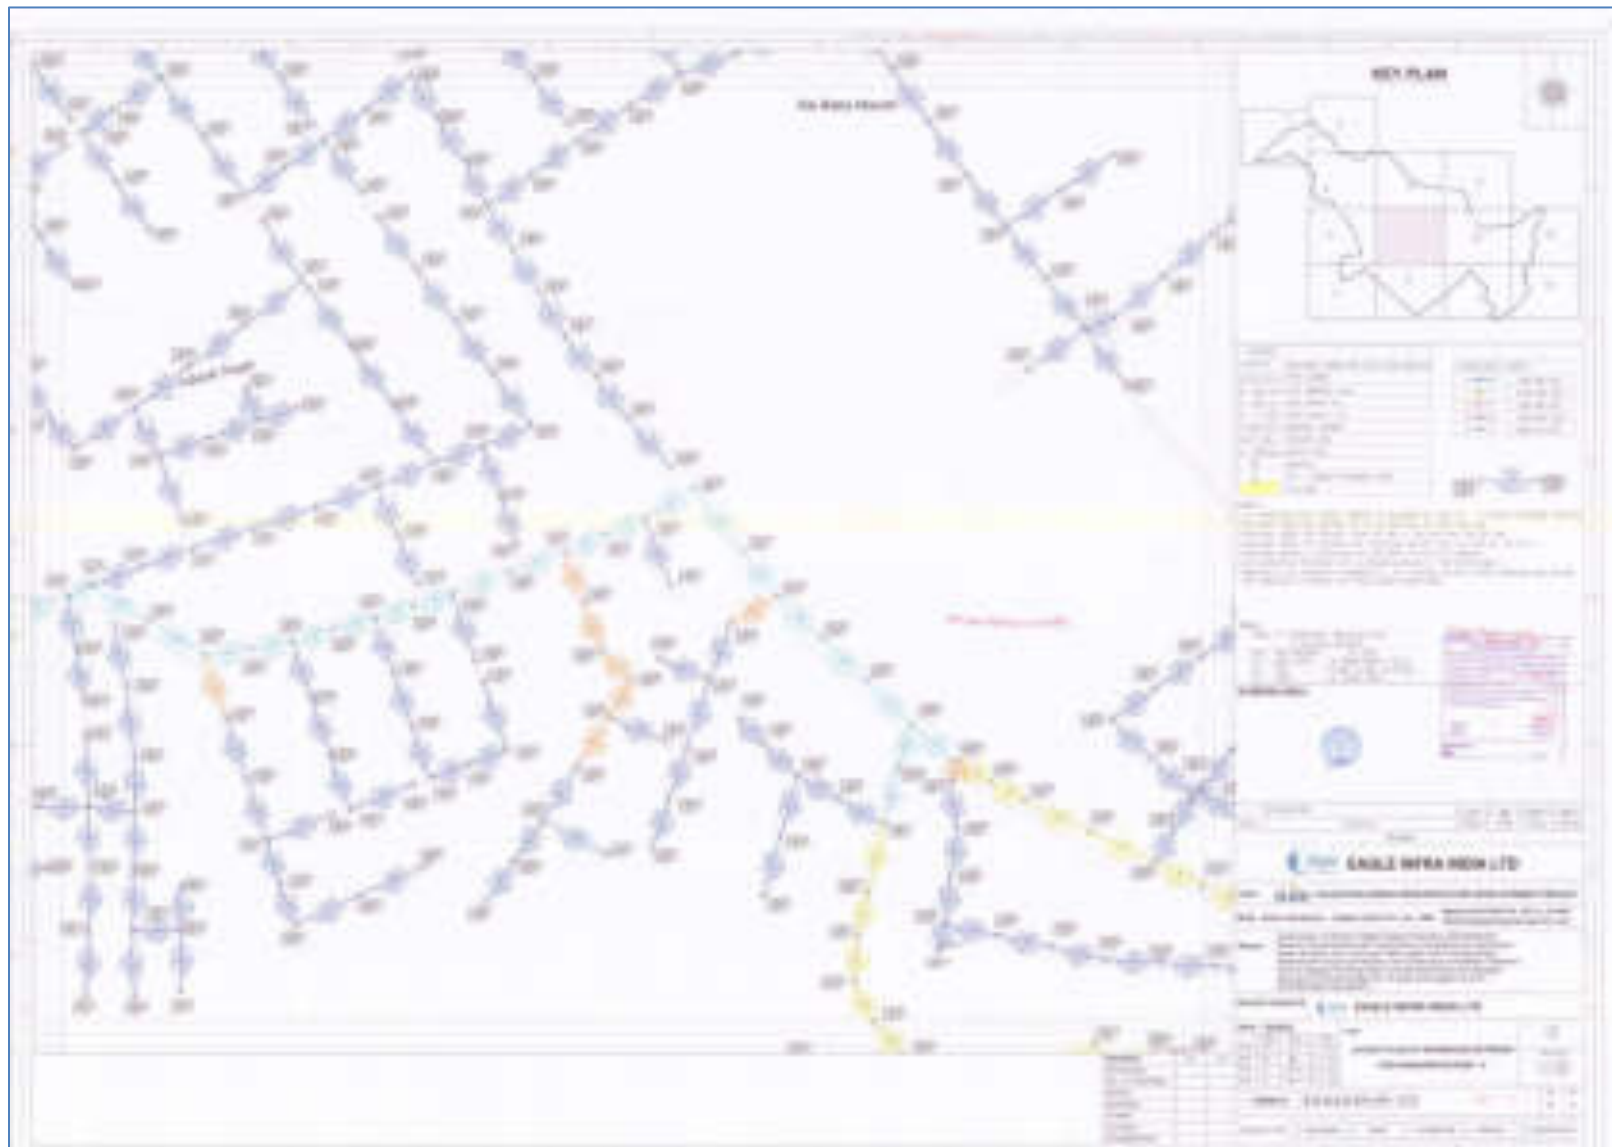


Figure 19: Layout plan of sewerage network in Zone -3 in Dungarpur



Figure 20: Layout plan of sewerage network in Zone -4 in Dungarpur


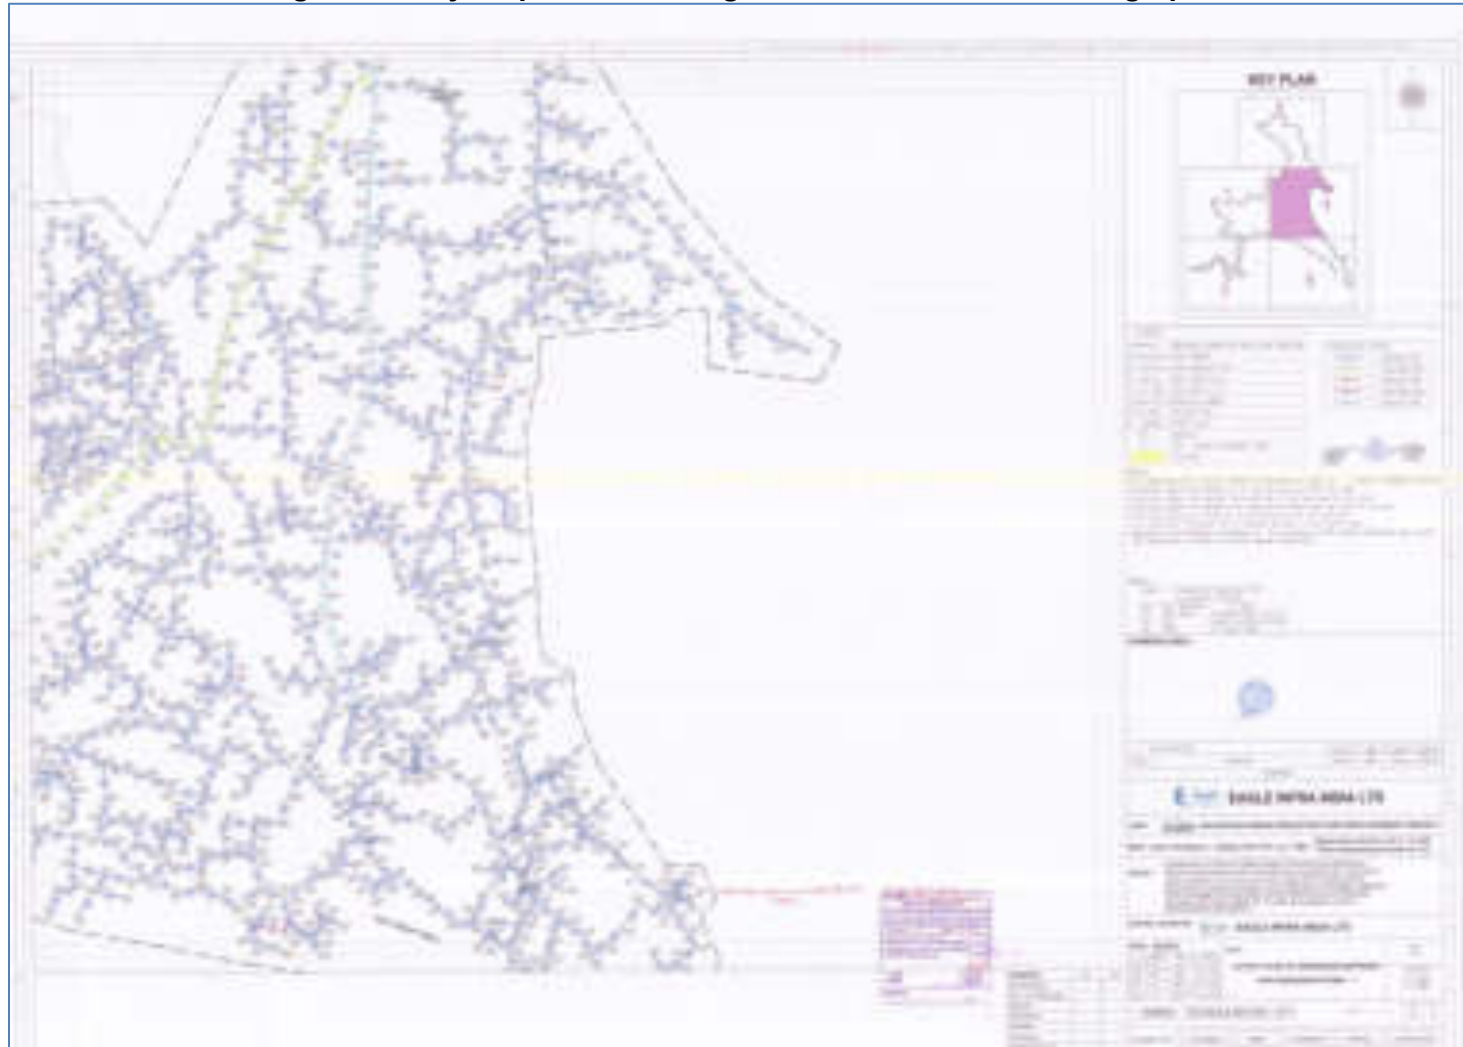


Figure 21: Layout plan of sewerage network in Zone -5 in Dungarpur

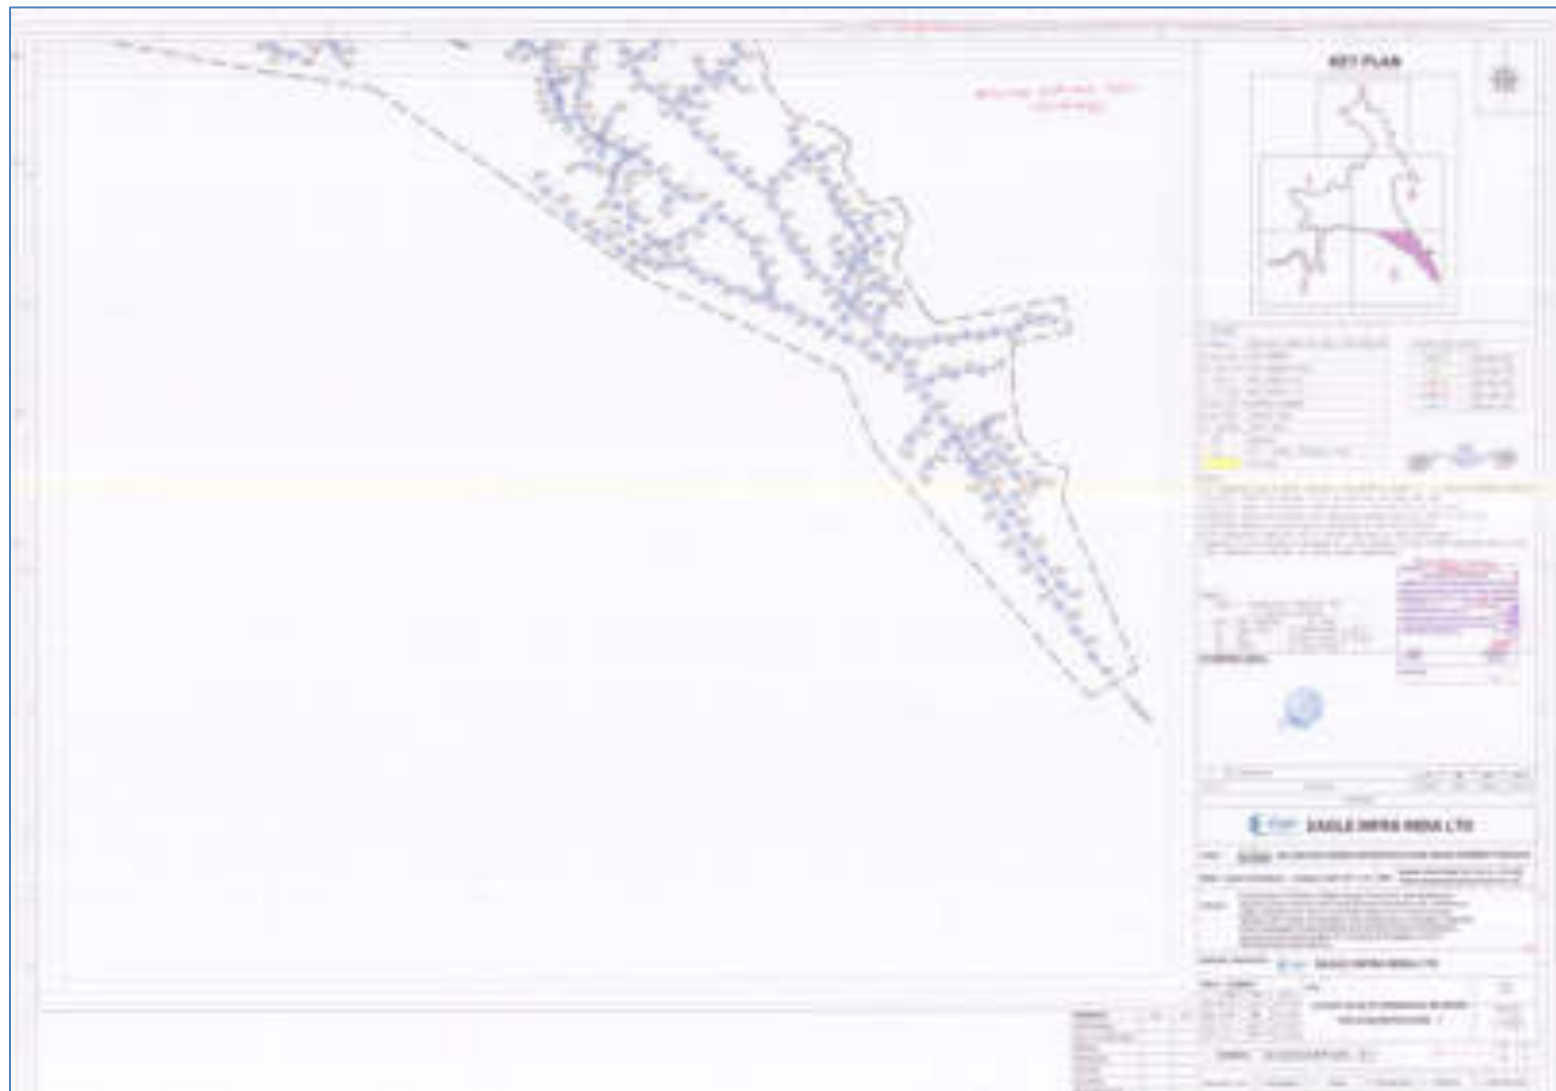

III. ANALYSIS OF ALTERNATIVES

45. The ADB SPS requires an analysis of project alternatives to determine the best method of achieving project objectives (which is providing potable water to people, and safely collecting and disposing the human waste generated, in Dungarpur town, in this case) while minimizing environmental impacts. Alternative analysis provides opportunity to integrate environmental considerations into early stages of project (i.e., pre-feasibility or feasibility study), so that adverse environmental impacts can be avoided or minimized by various alternatives. It also provides opportunity to study various options vis a vis costs, provides a logical base, via transparent process, assist in decision making, gaining public support and ultimately in project approvals and timely implementation.

46. The proposed water supply subproject component in Dungarpur include treated water conveyance, storage and distribution. Similarly, the sewerage component includes sewage collection network, transmission, treatment and treated wastewater reuse and disposal. Descriptions of various alternatives considered for critical components such as water source, sewage treatment, treated wastewater disposal etc., are presented in the following **Table 9**.

Table 9: Analysis of Alternatives

1.	Project Need – No Project Alternative
Type of alternative	'No project' alternative
Description of alternatives	Dungarpur subproject is proposed to improve the service levels of basic infrastructure – water supply and sewerage At present, residents of Dungarpur suffer from inadequate, intermittent and low-pressure supply. Presently, an intermittent water supply system is running in the town with actual service level of ~70 LPCD (once in a day for the average duration of 1-1.5 hours) at consumers' end, which is less than standard of 135 LPCD. The supply duration is about 1 to 1.5 hours with low pressure. System is old, inefficient, and leakages are frequent in water pipes, and consequently water losses are high. At present, no sewer system is existing in Dungarpur Town. Living conditions due to lack of proper water supply and sewerage, are poor, unhealthy, unhygienic. Lack of sewerage treatment and disposal system infrastructure in town is also causing environmental pollution, overall poor quality of life. Poor environmental quality affects the urban poor more. The project intends to provide following benefits to the town population, and the "no project" alternative will deprive people of these benefits: (i) increased availability of potable water at appropriate pressure to all households including urban poor; (ii) reduced time and costs in accessing alternative sources of water. (iii) better public health particularly reduction in waterborne and infectious diseases; (iv) reduced risk of groundwater contamination; (v) reduced risk of contamination of treated water supplies; and, (vi) improvement in quality of water bodies due to disposal of treated effluent meeting disposal standards
Selected Alternative	Without subproject would yield the town to be continuously under-serviced that puts the health of the general public at an increasing risk and could potentially worsen the living environment. This 'no project' scenario would impede further social and economic development of the town and the defer commitments to improve the proportion of the population with sustainable access to clean water and basic sanitation. Given the large-scale benefits to the population and environment, 'no project' alternative is considered inappropriate.

2	Alternative source of water																																																								
Type of alternative	'Water source'																																																								
Description of alternatives	Water Demand Total projected clear water demand for various design years is given below (including losses in the system) 2025 : 9.28 MLD 2040 : 10.28 MLD 2055 : 10.99 MLD																																																								
	Present source: At present water supply of the town at present the main sources of water are Edward Samand and Vijay Chakra Sagar dam. Beside these earlier some small quantity of water was also being obtained from nearby small Mandawa Khapeda anicut near to Taraghati, but now it has been closed as there is no sufficient water in this anicut. In addition to these, some sub surface sources (2 T/Ws and 2 O/Ws) are also at present running with the system. Therefore existing water supply in town is dependent on two local surface water Reservoirs viz Edward Samand and Vijay Chakra Sagar Dimiya dam, constructed exclusively for water supply needs, in addition to these, some sub surface sources (T/Ws and O/Ws) have also been connected with the system, but due to rocky terrain the yield of these ground water sources is very less and as the water table is regularly depleting fast therefore these would not sustain for longer. The details of surface sources together with the running tube wells & open wells and production details of water from these are given below in the table-																																																								
<table><tr><th rowspan="2">S. No.</th><th rowspan="2">Source</th><th rowspan="2">Net Capacity of Reservoir (mcft)</th><th rowspan="2">Present production MLD</th><th colspan="3">Anticipated production in MLD for the year</th><th rowspan="2">Utility for this project</th></tr><tr><th>2025</th><th>2040</th><th>2055</th></tr><tr><td>1</td><td>Edward Samand</td><td>134</td><td>2.4</td><td>4.54</td><td>4.54</td><td>4.54</td><td>Proposed to keep continue for this project</td></tr><tr><td>2</td><td>Vijay Chakra Sagar</td><td>40</td><td>1.0</td><td>3.1</td><td>3.1</td><td>3.1</td><td>Proposed to keep continue for this project.</td></tr><tr><td>3</td><td>Tube wells</td><td>-</td><td>1.0</td><td>1.0</td><td>1.0</td><td>1.0</td><td rowspan="2">Proposed to keep continue for this project, after augmentation and will be used in case of lean Season and repair maintenance of surface water infrastructure</td></tr><tr><td>4</td><td>Open Wells</td><td>-</td><td>2.0</td><td>2.0</td><td>2.0</td><td>2.0</td></tr><tr><td>5</td><td>SKA</td><td></td><td>-</td><td>0.59</td><td>2.46</td><td>4.36</td><td>New Source for</td></tr></table>								S. No.	Source	Net Capacity of Reservoir (mcft)	Present production MLD	Anticipated production in MLD for the year			Utility for this project	2025	2040	2055	1	Edward Samand	134	2.4	4.54	4.54	4.54	Proposed to keep continue for this project	2	Vijay Chakra Sagar	40	1.0	3.1	3.1	3.1	Proposed to keep continue for this project.	3	Tube wells	-	1.0	1.0	1.0	1.0	Proposed to keep continue for this project, after augmentation and will be used in case of lean Season and repair maintenance of surface water infrastructure	4	Open Wells	-	2.0	2.0	2.0	2.0	5	SKA		-	0.59	2.46	4.36	New Source for
S. No.	Source	Net Capacity of Reservoir (mcft)	Present production MLD	Anticipated production in MLD for the year			Utility for this project																																																		
				2025	2040	2055																																																			
1	Edward Samand	134	2.4	4.54	4.54	4.54	Proposed to keep continue for this project																																																		
2	Vijay Chakra Sagar	40	1.0	3.1	3.1	3.1	Proposed to keep continue for this project.																																																		
3	Tube wells	-	1.0	1.0	1.0	1.0	Proposed to keep continue for this project, after augmentation and will be used in case of lean Season and repair maintenance of surface water infrastructure																																																		
4	Open Wells	-	2.0	2.0	2.0	2.0																																																			
5	SKA		-	0.59	2.46	4.36	New Source for																																																		

Description of alternatives	Various secondary treatment technologies have been considered in the sewage treatment process after the primary treatment consisting of screening and grit removal. Secondary treatment is the critical process that removes the organic putrescible organic matters and brings down the BOD of the effluent to meet the discharge standards. Following process technologies considered: Waste Stabilization Ponds; Aerated Lagoons; Up Flow Anaerobic Sludge Blanket (UASB) + FAL; Conventional Activated Sludge Process (ASP); and Cyclic Activated Sludge Process/Sequential Batch Reactor (SBR)				
	A comparison of various treatment technologies is presented below in terms pf merits of the process over key parameters like quality characteristics and land requirement:				
	Item	Conventional Activated Sludge	Extended Aeration	UASB followed by Facultative Aerobic Lagoon	Cyclic Activated Sludge Process / SBR
	Performance (Typical)	Mostly stable	Mostly stable	Varying with temperature variations	Complete Stable
	BOD	<30 ppm	<30 ppm	<30 ppm	<10 ppm
	COD	<250 ppm	<250 ppm	<250 ppm	<50 ppm
	Suspended solids	<50 ppm	<50 ppm	<100 ppm	<10 ppm
	Total Nitrogen	No Treatment	No Treatment	No Treatment	<10 ppm
	Total Phosphorous	No Treatment	No Treatment	No Treatment	<2 ppm
	Coliform removal, %	60-90	60-90	-	99.99%
	Re-use Options	can only be used for low end usages like flushing and gardening tertiary treatment required for high and usages like construction water, industrial usages, cooling water etc.	can only be used for low end usages like flushing and gardening tertiary treatment required for high and usages like construction water, industrial usages, cooling water etc.	can only be used for low end usages like flushing and gardening tertiary treatment required for high and usages like construction water, industrial usages, cooling water etc.	Can be used for low end usages as well as for high end usages without any tertiary treatment.
	Land requirement (m2/person)	0.1-0.18	0.08-0.15	0.2-0.25	0.035-0.07
	Process Power requirement (kWh/person/year)	12-15	16-19	4-5	6-8
	Sludge handling	Sludge needs digestion prior to drying on beds or use mech. devices	Digested sludge, dry on beds or use mech. devices	Digested sludge, dry on beds or use mech. Devices	Digested sludge, dry on beds or use mech. devices
	Equipment requirement (excluding screening and grit removal)	Aerators, recycle pumps, scrapers, thickeners, digester, dryers, gas equipment	Aerators, recycle pumps, sludge scrapers, (for large settlers)	Nil (gas collection optional)	Diffuse aeration system, recycle sludge and waste sludge pumps, decanters
	Operational characteristics	Skilled Operation required	Simpler than activated sludge	Simpler than activated sludge	Complete automatic operation by computer and

					PLC. Negligible manpower Intervention required													
	Special features	Considerable equipment and skilled operation required especially if gas collection and usage involved. Method considered mainly for large sized plants	BOD removal high, effluent nitrified relatively high power requirement, favoured for small and medium sized plants	Minimal to negligible power requirement of the system makes it an economical alternative if gas revenue is neglected land requirement is also relatively small but depends on type of past treatment adopted	Highest treatment efficiency with crystal quality power requirement is 50% of conventional technologies land requirement is less than 50% of conventional technologies													
Selected Alternative	Selected processes: Sequential batch reactor (SBR) The genesis of selecting a suitable treatment process is primarily correlated with degree of treatment aimed to be achieved. In India, the latest court Order of April 2019 (NGT Order dated 30 April 2019) mandates all the civic authorities to adopt the treated sewage characteristics applicable are as shown in table below:																	
	<table><tr><td>Parameter</td><td>Standards</td></tr><tr><td>BOD, mg/l</td><td>10</td></tr><tr><td>TSS, mg/l</td><td>20</td></tr><tr><td>COD, mg/l</td><td>50</td></tr><tr><td>Nitrogen-Total, mg/l</td><td>10</td></tr><tr><td>Phosphorus- Total, mg/l</td><td>1</td></tr><tr><td>Fecal Coliform (MPN/ 100 ml)</td><td>100 (permissible 230)</td></tr></table> SBR provides highest treatment efficiency possible in a single step biological process. The system is operated in a batch reactor mode this eliminates all the inefficiencies of the continuous processes. A batch reactor is a perfect reactor, which ensures 100% treatment. Separate modules are provided to ensure continuous treatment. The complete process takes place in a single reactor, within which all biological treatment steps take place sequence. The complete biological operation is divided into cycles. Each cycle is of 3 – 5-hour duration, during which all treatment steps take place.					Parameter	Standards	BOD, mg/l	10	TSS, mg/l	20	COD, mg/l	50	Nitrogen-Total, mg/l	10	Phosphorus- Total, mg/l	1	Fecal Coliform (MPN/ 100 ml)
Parameter	Standards																	
BOD, mg/l	10																	
TSS, mg/l	20																	
COD, mg/l	50																	
Nitrogen-Total, mg/l	10																	
Phosphorus- Total, mg/l	1																	
Fecal Coliform (MPN/ 100 ml)	100 (permissible 230)																	
4	Treated wastewater disposal																	
Type of alternative	Treated wastewater disposal – reuse applications																	
Description of alternatives	Discharge of treated wastewater into Water body (ii) Reuse the treated wastewater in non-potable uses																	
	Rajasthan is a water scarce region and receives low rainfall. Recognizing the importance of treated wastewater in reducing the demand on water, Sewerage and Wastewater Policy, 2016, of Rajasthan promotes the reuse of treated sewage for non-potable applications, and also to make sewerage projects environmentally sustainable. This policy prioritizes reuse in irrigation (agriculture, forestry, and landscaping), followed by fish farming, industry and non-potable domestic reuse. Policy suggests construction of storage tanks to store treated wastewater to facilitate reuse. Policy prescribes that the detailed project report (DPR) should clearly define the best reuse option specific to the town and prepare a Reuse Action Plan part of the DPR following water quality norms and legal implications.																	

	Accordingly, it is proposed to utilize the treated wastewater for non-potable uses. There are vast agricultural practices near the STP sites, where there is scarcity of water for irrigation, due to which mostly rain fed agriculture is being practiced. A detailed Reuse Action Plan will be prepared during the detailed design phase, and, implemented. It is also proposed that the excess / surplus treated wastewater which is not being utilized in reuse will be discharge into natural drain located near STP, and necessary facilities – pipelines and pumping facilities, will be developed.
Selected Alternative	Reuse in non-potable applications and discharge excess/surplus into natural stream located near STP site
5	Project Locations
Description of alternatives	Intake Well and Pump house. Option 1- new intake at.. Option 2- existing intake As per the subproject design, the abstraction from Vijay Chakra Sagar Dam will remain same and it will provide 3.1 MLD or 25.44 % of total design demand of 12.196 MLD (2040). In original project proposal a new intake well was proposed near the embankment, however due to presence of <i>Crocodylus palustris</i> in the reservoir, possibility and feasibility of using the existing intake well was explored. Bathometric survey of the dam was conducted and it was found that the depth of proposed location is 2.67 m, while the depth at existing location is 2.01 m. There is a difference of 0.66 meters in depth at proposed and existing locations which indicate minimal level differences in the dam (Bathometric survey is attached as appendix 14). During lean years, temporary shortage of water occurs during summers at the existing location. However, the bathymetric survey reveals that at a close distance from existing intake point, the reservoir depth is 3.0 m. A channel can be dug manually in the dam between the existing intake point and the nearest deepest point so that the water availability is secured during summers in event of lean years. The manual excavation of trench shall be taken up during peak summers when water level in dam is low. In view of water availability and proposed trench from nearest deepest point to existing intake well will ensure the availability of water in existing intake well. Construction of a new intake well at the proposed location might disturb the biota, especially the crocodiles. While existing intake well can assure the water availability and after refurbishment it can be efficiently used, the proposal of new intake well is dropped and refurbishment is proposed. PHED, Gov. Rajasthan have already taken up the work of replacement of pumps in existing intake well. . Since the water allocation from the Vijay Chakra Sagar dam is 3.1 MLD till the design year, the need of 3.1 MLD is fulfilled by existing intake well after refurbishment. Since the proposed new intake was proposed in southern part which is farthest from the WTP and dropping the new intake will further reduce the length of raw water rising main. Therefore, considering all the possible alternatives the refurbishment of existing intake well is considered which is feasible. Location of RWR, CWRs and pump houses. All the 5 proposed clear water pump houses, one Raw water pump house, Raw water reservoirs (1 no.) and Clear water reservoirs (2 nos.) are proposed within the existing PHED campuses as per Table-2). There are sufficient vacant lands available for the construction of these structures at these locations. Therefore no alternative locations are required to be considered for construction of these structures. SPS Locations- all the three SPSs are proposed in Rajasthan Govt. Lands to avoid any impact on livelihood of any person. Sewage pumping station are proposed in vacant

	government lands on the basis of drainage pattern of town, availability of government land with no any other use, adequate land parcel, site away from habitation etc. Out of 3 SPS location one location is located in market area. This location has been selected on the basis of its natural gravity flow of house discharge without any additional mechanical flow. There is no alternative govt. land in nearby location so this location has been selected to avoid any land acquisition and gravity flow and requirement of minimum electricity in sewer collection. STP location. Based on the technical feasibility of gravity flow system, sewerage system in Dungarpur is designed and optimized with one sewage treatment plants (4MLD). Site selection is guided by technical suitability, availability of government owned vacant land, adequate land parcel, site away from habitation, and where there is a channel to discharge the treated wastewater. The selected site of STP is away from habitations and surrounded by agricultural lands (no habitations within 100 mts from STP sites proposed at Do river on Udaipur Road, Dungarpur). As far as possible a 100 m distance from proposed STPs from habitation is desirable, and also considering the selected superior and compact sewage treatment technology (SBR), the proposed site for construction of WTP is suitable for the construction of STP and therefore no site alternative is considered. Proposed STP location is located in Malpur village at north direction from city area of Dungarpur. The allocated for the STP is approx. 11.14 ha from Khasra No. 312 and 313. Water distribution and sewer lines. Sewer and water supply pipes are proposed along the roads/streets in the town within the road right-of-way (ROW). In wider roads water pipes will be laid in the road shoulder beside the tarmac, and in narrow roads, where there is no space, pipes will be laid in the road carriage way by break opening the tarmac. Sewers will be mostly laid in the center of the road, away from water pipes. There are existing asbestos cement pipes underground in the existing water supply networks, the alignment will be fine-tuned during the detailed design, to avoid existing AC pipe alignments as far as possible.

IV. POLICY, LEGAL AND ADMINISTRATIVE FRAMEWORKS

A. ADB Safeguard Policy

47. ADB SPS Requires that during the design, construction, and operation of the project necessary compliance to all applicable laws and international conventions / treaties along with pollution prevention and control technologies and practices consistent with international good practice, are ensured.

48. ADB uses a classification system to reflect the significance of a project's potential environmental impacts. A project's category is determined by the category of its most environmentally sensitive component, including direct, indirect, cumulative, and induced impacts in the project's area of influence. Each proposed project is scrutinized as to its type, location, scale, and sensitivity and the magnitude of its potential environmental impacts. Projects are assigned to one of the following four categories:

- (i) **Category A.** A proposed project is classified as category A if it is likely to have significant adverse environmental impacts that are irreversible, diverse, or unprecedented. These impacts may affect an area larger than the sites or facilities subject to physical works. An Environmental Impact Assessment (EIA) is required.
- (ii) **Category B.** A proposed project is classified as category B if its potential adverse environmental impacts are less adverse than those of category A projects. These impacts are site-specific, few if any of them are irreversible, and in most cases

mitigation measures can be designed more readily than for category A projects. An initial environmental examination (IEE) is required.

- (iii) **Category C.** A proposed project is classified as category C if it is likely to have minimal or no adverse environmental impacts. No environmental assessment is required although environmental implications need to be reviewed.
- (iv) **Category FI.** A proposed project is classified as category FI if it involves investment of ADB funds to or through a FI.

49. The environmental impacts of Dungarpur water supply and sewerage subproject have been identified and assessed as part of the planning and design process. An environmental assessment using ADB's REA checklist for water supply and sewerage (see **Appendix 1**) was conducted, and results of the assessment show that the subproject is unlikely to cause significant adverse impacts. Thus, this IEE has been prepared in accordance with ADB SPS's requirements for environment category B projects.

50. **Environmental Management Plan.** An EMP which addresses the potential impacts and risks identified by the environmental assessment shall be prepared. The level of detail and complexity of the EMP and the priority of the identified measures and actions will be commensurate with the Project's impact and risks.

51. **Environmental Audit of Existing Facilities.** ADB SPS, 2009 requires an environmental audit, if a subproject involves facilities and/or business activities that already exist or are under construction, including an on-site assessment to identify past or present concerns related to impacts on the environment. The objective of this compliance audit is to determine whether actions were in accordance with ADB's safeguard principles and requirements for borrowers/clients, and to identify and plan appropriate measures to address outstanding compliance issues.

52. **Public Disclosure.** The IEE will be put in an accessible place (e.g., local government offices, libraries, community centers, etc.), and a summary translated into local language for the project affected people and other stakeholders. The following safeguard documents will be put up in ADB's website so that the affected people, other stakeholders, and the public can provide meaningful inputs into the project design and implementation:

- (i) For environmental category A projects, a draft EIA report at least 120 days before Board consideration;
- (ii) Final or updated EIA and/or IEE upon receipt; and
- (iii) Environmental monitoring reports submitted by the PMU during project implementation upon receipt.

53. **Consultation and Participation.** ADB SPS, 2009 require borrower to conduct meaningful consultation¹ with affected people and other concerned stakeholders, including civil society, and facilitate their informed participation. The consultation process and its results are to be documented and reflected in the environmental assessment report.

¹ Per ADB SPS, 2009, meaningful consultation means a process that (i) begins early in the project preparation stage and is carried out on an ongoing basis throughout the project cycle 1; (ii) provides timely disclosure of relevant and adequate information that is understandable and readily accessible to affected people; (iii) is undertaken in an atmosphere free of intimidation or coercion; (iv) is gender inclusive and responsive, and tailored to the needs of disadvantaged and vulnerable groups; and (v) enables the incorporation of all relevant views of affected people and other stakeholders into decision making, such as project design, mitigation measures, the sharing of development benefits and opportunities, and implementation issues.

54. **Grievance Redress Mechanism.** ADB SPS, 2009 require borrowers to establish a mechanism to receive and facilitate resolution of affected people's concerns, complaints, and grievances about the subproject's performance. The grievance mechanism shall be scaled to the risks and adverse impacts of the subproject.

55. **Monitoring and Reporting.** Borrower shall monitor, measure and document the implementation progress of the EMP. If necessary, the borrower shall identify the necessary corrective actions, and reflect them in a corrective action plan. Borrower shall prepare and submit to ADB semi-annual environmental monitoring reports that describe progress with implementation of the EMP and compliance issues and corrective actions, if any. For subprojects likely to have significant adverse environmental impacts during operation, reporting will continue at the minimum on an annual basis until ADB issues a project completion report.

56. **Unanticipated Environmental Impacts.** Where unanticipated environmental impacts become apparent during subproject implementation, ADB SPS, 2009 requires the borrower to update the environmental assessment and EMP or prepare a new environmental assessment and EMP to assess the potential impacts, evaluate the alternatives, and outline mitigation measures and resources to address those impacts.

57. **Occupational Health and Safety.** ADB SPS, 2009 requires the borrower² to ensure that workers³ are provided with a safe and healthy working environment, taking into account risks inherent to the sector and specific classes of hazards in the subproject work areas, including physical, chemical, biological, and radiological hazards. Borrower shall take steps to prevent accidents, injury, and disease arising from, associated with, or occurring during the course of work, including: (i) identifying and minimizing, so far as reasonably practicable, the causes of potential hazards to workers; (ii) providing preventive and protective measures, including modification, substitution or elimination of hazardous conditions or substances; (iii) providing appropriate equipment to minimize risks and requiring and enforcing its use; (iv) training workers and providing them with appropriate incentives to use and comply with health and safety procedures and protective equipment; (v) documenting and reporting occupational accidents, diseases, and incidents; and (vi) having emergency prevention, preparedness, and response arrangements in place.

58. **Community Health and Safety.** ADB SPS, 2009 requires the borrower to identify and assess risks to, and potential impacts on, the safety of affected communities during the design, construction, operation, and decommissioning of the subproject, and shall establish preventive measures and plans to address them in a manner commensurate with the identified risks and impacts.

59. **Physical Cultural Resources.** Borrower is responsible for siting and designing the subproject to avoid significant damage to physical cultural resources. ADB SPS, 2009 requires that such resources likely to be affected by the subproject are identified, and qualified and experienced experts assess the subproject's potential impacts on these resources using field-based surveys as an integral part of the environmental assessment process. When the proposed location of a subproject component is in areas where physical cultural resources are expected to be found as determined during the environmental assessment process, chance finds procedures

² In case where responsibility is delegated to subproject contractors during construction phase, borrower shall ensure that the responsibilities on occupational health and safety are included in the contract documents.

³ Including nonemployee workers engaged by the borrower/client through contractors or other intermediaries to work on project sites or perform work directly related to the project's core functions.

shall be included in the EMP.

60. **ADB SPS International Best Practice Requirements.** ADB SPS, 2009 requires that, during the design, construction, and operation of the project, the executing agency shall apply pollution prevention and control technologies and practices that are consistent with international good practice, as reflected in internationally recognized standards such as the World Bank Group's Environment, Health and Safety (EHS) Guidelines. (IFC's General EHS Guidelines⁴ and Sector Specific [Water and Sanitation] Guidelines⁵). These standards contain performance levels and measures that are normally acceptable and applicable to projects. These standards contain performance levels and measures that are normally acceptable and applicable to projects. When Government of India regulations differ from these levels and measures, the PMU and PIUs will achieve whichever is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the PMU and PIUs will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in ADB SPS, 2009.

B. National Laws

61. The implementation of the subprojects will be governed by Government of India and State of Rajasthan and other applicable environmental acts, rules, regulations, and standards. These regulations impose restrictions on the activities to minimize or mitigate likely impacts on the environment. It is the responsibility of the project executing and implementing agencies to ensure subprojects are consistent with the legal framework, whether applicable international, national, state or municipal or local. Key standards include those related to drinking water quality, air quality, effluent discharge, and protected areas. Compliance is required in all stages of the subprojects including design, construction, and operation and maintenance.

62. **Environmental assessment.** The Government of India EIA Notification of 2006 (replacing the EIA Notification of 1994) sets out the requirement for environmental assessment in India. This states that environmental clearance is required for specified activities/projects, and this must be obtained before any construction work or land preparation (except land acquisition) may commence. Projects are categorized as A or B depending on the scale of the project and the nature of its impacts.

63. **Category A** projects require environmental clearance from the central Ministry of Environment, Forests and Climate Change (MOEFCC). The proponent is required to provide preliminary details of the project in the prescribed manner with all requisite details, after which an Expert Appraisal Committee (EAC) of the MOEFCC prepares comprehensive terms of reference (TOR) for the EIA study. On completion of the study and review of the report by the EAC, MOEFCC considers the recommendation of the EAC and provides the environmental clearance if appropriate.

64. **Category B** projects require environmental clearance from the State Environment Impact Assessment Authority (SEIAA). The State level EAC categorizes the project as either B1 (requiring EIA study) or B2 (no EIA study) and prepares TOR for B1 projects within 60 days. On completion of the study and review of the report by the EAC, the SEIAA issues the environmental clearance based on the EAC recommendation. The Notification also provides that any project or

⁴ <https://www.ifc.org/wps/wcm/connect/554e8d80488658e4b76af76a6515bb18/Final%2B%2BGeneral%2BEHS%2BGuidelines.pdf?MOD=AJPERES>

⁵ <https://www.ifc.org/wps/wcm/connect/e22c050048855ae0875cd76a6515bb18/Final%2B%2BWater%2Band%2BSanitation.pdf?MOD=AJPERES>

activity classified as category B will be treated as category A, if it is located in whole or in part within 10 km from the boundary of protected areas, notified areas or inter-state or international boundaries.

65. None of the components of this water supply and sewerage subproject falls under the ambit of the EIA Notification 2006, and therefore EIA Study or environmental clearance is not required for the subproject.

66. **Applicable environmental regulations.** Besides EIA Notification 2006, there are various other acts, rules, policies and regulations currently in force in India that deal with environmental issues that could apply to infrastructure development. The specific regulatory compliance requirements of the subproject are shown in **Table 10**.

C. Environmental Regulatory Compliance

67. Table 10 presents a summary of environmental regulations and mandatory requirements applicable to Dungarpur Town water supply and sewerage subproject.

Table 10: Applicable Environmental Regulations

Law	Description	Requirement	Relevance to Project Phase
National Environment Policy (NEP), 2006.	NEP is a comprehensive guiding document in India for all environmental conservation programs and legislations by Central, State and Local Government. The dominant theme of this policy is to promote betterment of livelihoods without compromising or degrading the environmental resources. The policy also advocates collaboration method of different stakeholders to harness potential resources and strengthen environmental management.	RSTDSP should adhere to NEP principle of “enhancing and conservation of environmental resources and abatement of pollution”.	All phases of project
Rajasthan State Environment Policy, 2010 And Rajasthan Environment Mission and Climate Change Agenda for Rajasthan (2010-14)	Follows the National Environment Policy, 2006 and core objectives and policies are: -Conserve and enhance environmental resources; assure environmental sustainability of key economic sectors; and, improve environmental governance and capacity building - it recommends specific strategies and actions to address the key environmental issues: water resources,	Project implementation should adhere to the policy aims of: conservation and enhancement of environmental resources, integration of environmental concerns into projects/plans, and capacity building in environmental management. Under water sector, major concerns, as the policy notes, are huge water losses and wastage, declining water availability, pollution.	All phases of project

Law	Description	Requirement	Relevance to Project Phase
	desertification and land degradation, forest and biodiversity, air quality, climate change: adoption and mitigation, mining, industry, tourism, energy, urban development, etc. - Establishment of Environment Mission under the chairpersonship of the Chief Minister and a Steering Committee under the chairpersonship of Chief Secretary, Government of Rajasthan Tasks force set up for six key areas	Relevant recommendations for the project include control of losses, integrated water resources management, control of raw water pollution¹⁸, reuse and recycling. Avoid/minimize use of forest lands. With reference to climate change adoption and mitigation following should be considered in the project: (i) diminishing flows in surface water bodies, and groundwater depletion, and revival traditional water bodies as water sources (lakes/tanks); (ii) equal stress on demand side management in water; and (iii) minimize energy use - design energy efficiency systems.	
EIA Notification, 2006	Projects indicated in the schedule of this notification requires EIA study and environmental clearance.	None of the components of this subproject falls under the ambit of the notification; no EIA study or environmental clearance required	-
Central Ground Water Authority Public Notice 2/100	Public Notice specifies districts and areas where there are restrictions on the construction and installation of any new structure for extraction of groundwater resources without specific approval from the CGWA	Subprojects belonging to the Notified Areas in the Public Notice and will require new structures on extracting groundwater should seek the permission from the Central Groundwater Authority	Not applicable
Public Health Engineering Department Office Order P5 (1) PHE-2010 dated July 14 2020	PHED Office Order states that the State Government is instructed that permits for any new tube wells, bore wells or any structures extracting ground water shall be secured from the District Collector	Subprojects with components shall secure permits from the District Collector for components that include any new tube wells, bore wells or structures extracting groundwater	Not applicable
Water (Prevention and Control of Pollution) Act of 1974, Rules of 1975, and amendments (1987)	Act was enacted to provide for the prevention and control of water pollution and the maintaining or restoring of wholesomeness of water, by Central and State Pollution Control Boards and for conferring on and assigning to CPCB/SPCBs powers and functions relating to water	Proposed STP will require CTE (prior to start of construction works) and CTO (prior to start of operation) from Rajasthan State Pollution Control Board (RSPCB) For the refurbishment of 2 existing WTPs, CTE and CTO will also be required as per	Construction and Operation

Law	Description	Requirement	Relevance to Project Phase
	pollution control. Control of water pollution is achieved through administering conditions imposed in consent issued under provision of the Water (Prevention and Control of Pollution) Act of 1974. These conditions regulate the quantity and quantity of effluent, the location of discharge and the frequency of monitoring of effluents. Any component of the subproject having the potential to generate sewage or trade effluent will come under its purview. Such projects have to obtain Consent to establish (CTE) under Section 25 of the Act from Rajasthan State Pollution Control Board (RSPCB) before starting implementation and Consent to Operate (CTO) before commissioning.	requirement of RSPCB All relevant forms, prescribed fees and procedures to obtain the CTE and CTO can be found in the RSPCB website. (http://environment.rajasthan.gov.in)	
Air (Prevention and Control of Pollution) Act of 1981, Rules of 1982 and amendments.	This Act was enacted to achieve prevention, control and abatement of air pollution activities by assigning regulatory powers to Central and State boards for all such functions. The Act also establishes ambient air quality standards. The projects having potential to emit air pollutants into the atmosphere have to obtain CTE and CTO under Section 21 of the Act from RSPCB. The occupier of the project/facility has the responsibility to adopt necessary air pollution control measures for abating air pollution.	The following will require CTE and CTO from RSPCB: (i) Diesel generators (more than 15 KVA); (ii) Batching Plant hot mix plants; and (iii) stone crushers, if installed for construction. All relevant forms, prescribed fees and procedures to obtain the CTE and CTO can be found in the RSPCB website (http://environment.rajasthan.gov.in) If ready mix concrete and hot mix bitumen is procured from third party, contractor has to ensure that the plants, from where material is being purchased is having CTE/CTO and copy should be collected from third party and submitted in PIU	Construction and operation
Biodiversity Act of 2002	This Act primarily addresses access to genetic resources and associated knowledge by foreign individuals, institutions or companies, to ensure	Not Applicable	-

Law	Description	Requirement	Relevance to Project Phase
	equitable sharing of benefits arising out of the use of these resources and knowledge to the country and the people.		
Wildlife Protection Act, 1972 and amendment 1991	This overarching Act provides protection to wild animals, birds, plants and matters connected with habitat protection, processes to declare protected areas, regulation of wildlife trade, constitution of state and national board for wildlife, zoo authority, tiger conservation authority, penalty clauses and other important regulations.	None of the components of the subproject are located within the protected Area. Therefore, this act is not applicable.	Not Applicable
Forest (Conservation) Act, 1980	The Forest (Conservation) Act prohibits the use of forest land for non-forest purposes without the approval of Ministry of Environment Forests & Climate Change (MoEFCC), Government of India	Most of the proposed components are within municipal boundary of Dungarpur where no forest areas are present. Rising mains of water supply are away from municipal limits. Confirmation of presence of any forest areas in the alignment of rising main will be required during confirmatory survey	Pre-construction and construction
Environmental (Protection) Act, 1986 amended in 1991 and the following rules/notifications:	This is an “umbrella” legislation that empowers the Central Government to take all necessary measures to protect and improve the quality of the environment and prevent, control and abate environmental pollution. Empowers central government to enact various rules to regulate environmental pollution, including standards for quality of air, water, noise, soil; discharge standards or allowable concentration limits for environmental pollutants, handling of hazardous substances, locating/prohibiting industries, etc.,	There are rules / notifications that have been brought out under this Act, which are relevant to RSTDSP, and are listed below	Construction and operation
Environmental Standards (ambient and discharge).	Emissions and discharges from the facilities to be created or refurbished or augmented shall comply with the notified standards	Appendix C-2 provides ambient air quality standards, emission limits and Appendix C-3 emission stack height requirements for diesel generators.	Construction and operation

Law	Description	Requirement	Relevance to Project Phase
		Appendix C-8 provides STP discharge standards	
Noise Pollution (Regulation and Control) Rules, 2000 amended up to 2010.	Rule 3 of the Act specifies ambient air quality standards in respect of noise for different areas/zones.	Appendix C-7 provides applicable noise standards	Construction and operation
Indian Drinking Water Standards	Gives details of the permissible and desirable limits of various parameters in drinking water as per the Bureau of Indian Standards	Appendix C-1 provides drinking water standards.	Construction and operation
Solid Waste Management Rules 2016	Responsibility of Solid Waste Generator segregate and store the waste generated in three separate streams namely bio-degradable, non-biodegradable and domestic hazardous wastes in suitable bins and handover segregated wastes to authorized waste pickers or waste collectors as per the direction or notification by the local authorities from time to time; store separately construction and demolition waste, as and when generated, in his own premises and shall dispose off as per the Construction and Demolition Waste Management Rules, 2016; (iii) No waste generator shall throw, burn or bury the solid waste generated by him, on streets, open public spaces outside his premises or in the drain or water bodies.	Contractor to follow all the rules during construction works	Construction and operation
Construction and Demolition Waste Management Rules 2016	(i) Every waste generator shall segregate construction and demolition waste and deposit at collection centre or handover it to the authorized processing facilities. (ii) Shall ensure that there is no littering or deposition so as to prevent obstruction to the traffic or the public or drains. (iii) Large generators (who generate more than 20 tons or more in one day or 300 tons per project in a month) shall submit	Construction waste shall be collected at stockpile area for 8-10 days and will be sent to disposal site. Disposal site shall be identified and allotted by Municipal Council after mobilization of contractor (during SIP period) and can't be mentioned at this time. Contractor to follow all the rules during construction works. Sludge or any material if classified as hazardous waste / material is to be handled and	Construction

Law	Description	Requirement	Relevance to Project Phase
	waste management plan and get appropriate approvals from the local authority before starting construction or demolition or remodelling work, (iv) Large generators shall have environment management plan to address the likely environmental issues from construction, demolition, storage, transportation process and disposal / reuse of C & D Waste. (v) Large generators shall segregate the waste into four streams such as concrete, soil, steel, wood and plastics, bricks and mortar, (vi) Large generators shall pay relevant charges for collection, transportation, processing and disposal as notified by the concerned authorities;	disposed according to this Rules	
Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016,	Responsibilities of the occupier for management of hazardous and other wastes. - (1) For the management of hazardous and other wastes, an occupier shall follow the following steps, namely:- (a) prevention; (b) minimization; (c) reuse, (d) recycling; (e) recovery, utilization including co-processing; (f) safe disposal. (2) The occupier shall be responsible for safe and environmentally sound management of hazardous and other wastes. (3) The hazardous and other wastes generated in the establishment of an occupier shall be sent or sold to an authorized actual user or shall be disposed of in an authorized disposal facility. (4) The hazardous and other wastes shall be transported from an occupier's establishment to an authorized actual user or to an authorized disposal facility in accordance with the provisions of these	Contractor to comply all the requirements of this Act during construction works.	Construction and operation

Law	Description	Requirement	Relevance to Project Phase
	rules. (5) The occupier who intends to get its hazardous and other wastes treated and disposed of by the operator of a treatment, storage and disposal facility shall give to the operator of that facility, such specific information as may be needed for safe storage and disposal. (6) The occupier shall take all the steps while managing hazardous and other wastes to- 6 (a) contain contaminants and prevent accidents and limit their consequences on human beings and the environment; and (b) provide persons working in the site with appropriate training, equipment and the information necessary to ensure their safety.		
Wetlands (Conservation and Management) Rules, 2017	The Rules specify activities which are harmful and prohibited in the wetlands such as industrialization, construction, dumping of untreated waste and effluents, and reclamation. The Central Government may permit any of the prohibited activities on the recommendation of Central Wetlands Regulatory Authority.	Not applicable as subprojects components are not located in or near to designated wetland area.	Not applicable
Ancient Monuments and Archaeological Sites and Remains Act, 1958 and Ancient Monuments and Archaeological Sites and Remains (Amendment and Validation) Act, 2010.	The Act designates areas within 100 meters (m) of the "protected monument/area" as "prohibited area" and beyond that up to 200 m as "regulated area" respectively. No "construction" is permitted in the "prohibited area" and any construction activity in the "regulated area" requires prior permission of the Archaeological Survey of India (ASI).	Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments.	Not Applicable
The Rajasthan Monuments, Archaeological Sites and Antiquities Act, 1961; the Rajasthan	Any construction/excavation work in the 'protected area' (as declared by GoR under the Act) requires priori permission of Department of Archaeology & Museums -Application under the Rules shall be submitted to Director,	Not applicable - there are no state protected monuments in the town	Not applicable

Law	Description	Requirement	Relevance to Project Phase
Monuments, Archaeological Sites and Antiquities (amendment) Act 2007	State Archaeological Department, at least 3 months prior to the work. Department provides conditional permission, including time for completion, procedures to be followed during the work and for chance finds et-.		
The Building and Other Construction Workers (BOCW) Act 1996 and Rajasthan Building and Construction Workers Rules 2009	Employer shall- • Provide and maintain, at suitable point, sufficient quantity of wholesome drinking water, such point shall be at least 6 meters away from any washing areas, urinals or toilets. • Provide sufficient urinals and latrines at convenient place, easily accessible by workers. • Provide free of charge, temporary living accommodations near to work sites with separate cooking place, bathing and lavatory facilities and restore the site as preconditions after completing the construction works. • Provide crèche with proper accommodation, ventilation, lighting, cleanliness and sanitation if more than fifty female workers are engaged. • Provide first aid facilities in all construction sites. For safety of workers employer shall provide- • Safe access to site and workplace • Safety in demolition works. • Safety in use of explosives • Safety in operation of transporting equipment and appoint competent person to drive or operate such vehicles and equipment. • Safety in lifting appliance, hoist and lifting	Contractors are required to follow all the provisions of BOCW Act and Rajasthan BOCW Rules. Salient features of Rajasthan BOCW Rules are- Chapter III, section 17- Registration of establishments Chapter VIII, section 61- Hours of works, intervals or rest and spread over, overtime. Section 62- weekly rest Section 63- night shift Section 67- registers of workers Section 68- Muster roll, wages register. Section 70- latrine and urinal facilities Chapter XI- Safety and Health Section 78- fire protection Section 79- emergency action plan Section 80- fencing of motors. Section 81- lifting and carrying of weight Section 82- H&S policy Section 83- dangerous and harmful environment Section 84- Overhead protection Section 88- eye protection Section 89- PPEs Section 90- electrical hazards Section 97- use of safety helmets and shoes Chapter XIII-lifting appliances and gears Chapter XV- transport and earth moving equipments Chapter XVI- concrete works Chapter XVII- demolition works Chapter XVIII-Excavation and tunnelling Chapter XX- ladders and step ladders	Construction

Law	Description	Requirement	Relevance to Project Phase
	gears. • Adequate and suitable lighting to every workplace and approach • Prevention of inhalation of dust, smoke, fumes, gases during construction works and provide adequate ventilation in workplace and confined space • Safety in material handling and stacking/unstacking. • Safeguarding the machinery with flywheel of moving parts • Safe handling and use of plants operated by compressed air • Fire safety • Limit of weight to be lifted by workers individually. • Safety in electric wires, apparatus, tools and equipment • Provide safety net, safety sheet, safety belts while working at height (more than 1.6 mtrs as per OSHA) • Providing scaffolding, ladders and stairs, lifting appliances, chains and accessories where required • Safety in pile works, concrete works, hot asphalt, tar, insulation, demolition works, excavation, underground construction and handling materials. • Provide and maintain medical facilities for workers. • Any other matters for the safety and health of workers	Chapter XXII- structural frame and formworks Chapter XXIV- medical facilities and first aid box	
Contract Labor (Regulation and Abolition) Act, 1970; The Inter-State Migrant Workmen (Regulation of	Provides for welfare measures to be provided by the Contractor to contract labor and in case the Contractor fails to provide, the same are required to be provided by the Principal Employer by Law. The principal employer is required to take	• Applicable to all construction works in the project. • Principle employer (RUDSICO-EAP) to obtain Certificate of Registration from Department of I, as principal employer	Construction and operation

Law	Description	Requirement	Relevance to Project Phase
Employment and Conditions of Service) Act, 1979	Certificate of Registration and the Contractor is required to take a License from the designated Officer. The Act is applicable to the establishments or Contractor of principal employer if they employ 20 or more contract labor. The inter-state migrant workmen, in an establishment to which this Act becomes applicable, are required to be provided certain facilities such as housing, medical aid, traveling expenses from home up to the establishment and back, etc.,	- Contractor to obtain license from designated labor officer. - Contractor shall register with Labor Department, if Inter-state migrant workmen are engaged - Adequate and appropriate amenities and facilities shall be provided to workers including housing, medical aid, traveling expenses from home and back, etc., Appendix C-12 provides applicable labor laws including amendments issued from time to time applicable to establishments engaged in construction of civil works.	
The Child Labour (Prohibition and Regulation) Act, 1986	Prohibits employment of children below 14 years of age in certain occupations and processes Employment of child labor is prohibited in building and construction Industry.	No child labour should be employed	Construction and operation
Minimum Wages Act, 1948	Minimum wages fixed by appropriate Government as per provisions of the Act if the employment is a scheduled employment. Construction of buildings, roads and runways are scheduled employment.	Applicable to all construction works in the project. All construction workers should be paid not less than the prescribed minimum wage	Construction and operation
Workmen Compensation Act, 1923	Provides for compensation in case of injury by accident arising out of and during the course of employment.	Compensation for workers in case of injury by accident	Construction and operation
Equal Remuneration Act, 1979	Provides for payment of equal wages for work of equal nature to male and female workers and not for making discrimination against female employees in the matters of transfers, training and promotions etc.	Equal wages for work of equal nature to male and female workers	Construction and operation
Rajasthan Forest Act, 1953 and Rajasthan Forest Rules, 1962	This Act makes the basis for declaration of Reserved Forests, constitution of village forest committees, management of reserved	Most of the proposed components are within municipal boundary of Dungarpur where no forest areas are present. Rising mains of water supply are away from	Pre-construction and construction

Law	Description	Requirement	Relevance to Project Phase
	forests and penalties and procedures.	municipal limits. Confirmation of presence of any forest areas in the alignment of rising main will be required during confirmatory survey	
IS 11768: 1986/2005: Recommendations for disposal of asbestos waste material	The standard emphasizes that every employer who undertakes work which is liable to generate asbestos containing waste, shall undertake adequate steps to prevent and/or reduce the generation of airborne dust during handling, storing, transportation and final disposal of final disposal of asbestos and asbestos containing products.	The crux is waste avoidance: the practice inculcated should focus on minimal waste generation. Waste Collection: In the project circumstance, the waste is referred to the damaged powered asbestos which will be collected in the Permissible plastic bags to be disposed to the nearest TSDF facilities.	Construction
IS 12081: Pictorial Warning to be implemented on equipment containing Asbestos Contaminated Products.	The objective of the caution is to make the person handling to take all pre-cautionary measures and make them aware of all the possible risk.	The following signs and personal protective equipment shall be used in handling ACM. 	Construction
IS 11451: Safety and Health Requirements related to Occupational Exposure to Asbestos contaminated Products.	These standard details the occupational exposure allowable and safety at work place to be enforced.	In the project the norms pertaining to limiting number of hours working with ACM will be 8.0 hrs/48 hrs a week and the medical examination has to be periodic; the environmental monitoring has to be done as per the protocol. The safety at workplace shall be enforced.	Construction

Law	Description	Requirement	Relevance to Project Phase
IS 11768: Waste Disposal Procedure for Asbestos Containing Products.	The protocol pertaining to disposal of the waste is emphasized.	The collection of ACM powered will be in permissible plastic bags, which will be twisted tight at the neck so that the wear and tear due to abrasion will be minimum and the transportation of the asbestos waste has to be done by the authorized vendor to the approved landfill site.	Construction
International conventions and treaties			
Ramsar Convention, 1971	The Ramsar Convention is an intergovernmental treaty that provides the framework for national action and international co-operation for the conservation and wise use of wetlands and their resources. India is one of the signatories to the treaty. The Ramsar convention made it mandatory for the signatory countries to include wetland conservation in their national land use plans.	There are no Ramsar sites in or near Durgapur Town. Not applicable to Durgapur Town water supply and sewerage subproject.	Not applicable
Convention on International Trade in Endangered Species of Wild Fauna and Flora (CITES), 1973	India is a signatory of this convention which aims to control international commercial trade in endangered species	Applicable in this project as endangered species of wild fauna and flora is found in project area (Dimiya Dam).	Applicable
Montreal Protocol 1992	India is a signatory of this convention which aims to reduction in the consumption and production of ozone-depleting substances (ODS), while recognizing differences in a nation's responsibilities. Ozone depleting substances are divided in two groups Chlorofluorocarbons (CFCs) and Hydrochlorofluoro carbons (HCFCs)	Not applicable in this project as no ODS are involved in construction works	Not applicable
Basel Convention on Trans-boundary Movement of Hazardous Wastes, 1989	India is a signatory of this convention which aims to reduce trans-boundary movement and creation of hazardous wastes	Contractor to follow the provisions of Hazardous Waste Rules 2016 for storage, handling, transport and disposal of hazardous waste emerged during construction works.	Not applicable

Law	Description	Requirement	Relevance to Project Phase
		Under this Convention, asbestos or asbestos waste in the form of dust and fibers is classified as hazardous waste.	
Convention on Migratory Species of Wild Animals (CMS), 1979 (Bonn convention)	CMS, also known as Bonn convention, was adopted in 1979 and entered into force on 1 November 1983, which recognizes that states must be the protectors of migratory species that live within or pass through their national jurisdictions, and aims to conserve terrestrial, marine and avian migratory species throughout their ranges. Migratory species threatened with extinction are listed on Appendix I of the Convention. CMS Parties strive towards strictly protecting these species, conserving or restoring the places where they live, mitigating obstacles to migration and controlling other factors that might endanger them. Migratory species that need or would significantly benefit from international cooperation are listed in Appendix II, and CMS encourages the Range States to conclude global or regional agreements.	Applicable to this project as migratory species of wild animals and birds are reported in the project areas.	Applicable

68. **Clearances / permissions to be obtained prior to start of construction.** Table 11 shows the list of clearances/permissions required for project construction. This list is indicative, and the contractor should ascertain the requirements prior to start of the construction and obtain all necessary clearances/permission prior to start of construction.

Table 11: Clearances and permissions required for Construction activities.

S. No	Construction Activity	Statute under which Clearance is Required	Implementation
1	Land for project activity	Allotment and approval for specific land use	ULB
2	Pipe laying works	Permission from Dungarpur Council and PWD (where applicable)	PIU
3	Establishment of construction camps	Allotment and approval for specific land use	Contractor
4	Construction of new STP	Consent to establish and consent to operate under Water Act, 1974 from RSPCB	PIU & Contractor
5	Tree Cutting	State forest department/Revenue (Tehsildar)	PIU

S. No	Construction Activity	Statute under which Clearance is Required	Implementation
6	Hot mix plants, Crushers, Batching plants and DG Set	Consent to establish and consent to operate under Air Act, 1981 from RSPCB	Contractor
7	Storage, handling and transport of hazardous materials	Hazardous Wastes (Management and Handling) Rules, 2016 Manufacturing, Storage and Import of Hazardous Chemicals Rules, 1989 from RSPCB	Contractor
8	Sand mining, quarries and borrow areas	Permission from District Collector/ State Department of Mines & Geology	Contractor
9	New quarries and borrow areas	Environmental clearance under EIA Notification 2006	Contractor
10	Use of vehicles and equipment	Pollution under control certificate (PUC) form RTO	Contractor
11	Temporary traffic diversion measures	Temporary traffic diversion measure including use of alternate road from District traffic police	Contractor
12	Use of Railways ROW for construction area/ crossing	Indian Railways	PIU
13	Use of highway ROW for construction area/ crossing	National Highway Authority of India	PIU

69. PMU will be overall responsible for supervision in getting all clearances and provide details to ADB through semi-annual report. PMU will ensure all necessary regulatory clearances and approvals are obtained prior to commencement of works. Respective PIUs, with support of project consultants and DBO contractors, are responsible for obtaining the clearances/permits and ensuring conditions/specifications/provisions are incorporated in the subproject design, costs, and implementation. The PIUs shall report to PMU the status of compliance to clearances/permits as part of the regular progress reporting.

V. DESCRIPTION OF ENVIRONMENT

A. Physical Resources

1. Location, Area & Connectivity

70. Dungarpur is a city in the southern part of Rajasthan state of India. It is the administrative headquarters of Dungarpur District. It was founded by Dungariya bheel king in the 13th century. The district is roughly triangular. In East and North it borders on Banswara and Udaipur District respectively while it adjoins the State of Gujrat in South & West.

71. The rail line between Udaipur and Ahmedabad in Gujarat runs through the town, shortest distance to the National Highway 8 from Dungarpur town is 20 km. It is located in the southern part of Rajasthan between 23° 20' and 24° 01' north latitude and 73° 21' and 74° 01' east longitude. In East and North its borders on Banswara and Udaipur districts respectively while it adjoins the State of Gujarat in South and West. Most of the part of district and town are hilly. The elevation is 225 m (738 ft) above MSL. The municipal area of the city is about 14.65 Sq. Km. Location of Dungarpur town in Rajasthan State map is shown in **Figure 22**.

Figure 22: Location of Dungarpur Town in Rajasthan State Map



2. Topography, Soils and Geology

72. **Topography.** The district is characterised by uneven topography with hills of Aravalli comprising of mainly quartzite and intrusive rocks alternating with low lying areas of phyllites, slates and schists. The district, though fairly open in the south is interspersed with stony hills covered with low jungle. In the north and east, the landscape is rugged and wild, but towards the southwestern border, the harsh features gradually become softer and finally merge in the topography of Gujarat region. The eastern part slopes towards the basin of Mahi river and consists of 3 plain area. Cultivated areas are mainly confined to valleys and low-lying ground between the hills.

73. The rugged and wild aspect of the region is attributed to the off shoots of the Aravalli. The country is broken and hilly, but none of the hills attain a great height. The highest peak which is in the extreme northwest is about 572 m above mean sea level and the other highest point 2 km north of Sagwara is 497 m above mean sea level. The lowest point in the district is about 90 m above mean sea level near Solakari village in the bed of Mahi River. Dungarpur town is also hilly undulating terrain.

74. **Soil.** There are pre-dominantly two types of soils in the district. Red loam soils are found in the south-eastern parts of the district, adjoining Gujarat border. These are soils of hilly plains (flats) i.e., brought down from nearby hills and deposited in low lying areas. They are characteristically shallow to moderately deep, reddish in colour medium in texture, sandy loam to loam in nature, non-calcareous, granular, well drained, free of salts and may have slight calcareous carbonates in lower layers. Hilly soils are found along the hill ranges of Aravalli in the northern and western parts of the district. These soils are very shallow with gravelly material, very near to the surface. These are in general, light in texture and reddish brown to greyish brown in colour, non-calcareous and freely drained. These extend in small patches on uneven terrain.

75. **Soil Quality:** For the study of baseline environment soil quality has been conducted by DBO contractor in February 2023.

76. Seven nos. soil samples were collected from different sites which are STP, SPS-1, SPS-2, SPS-3, CWR & Pumping Station at Udaipur office, CWR & Pumping Station at MPH Office Campus, and CWR & Pumping Station at New Colony. Test report of soil Sample result is given in **Table 12**. pH of soil samples is found in the range of 7.21 to 8.51. Nitrogen, Potassium and Phosphate are found in the range of 32.11 to 58.99 Kg/hect, 215.3 to 239.59 Kg/hect and 8.04 to 12.58 Kg/hect respectively. Laboratory test reports of soil quality are given in **Appendix 10**.

Table 12: Test Result of Soil Samples

S. No	Parameters	Unit of Measurements	Results and Locations						
			STP	SPS-1 Near Shree Padambhushan Bhogilal Circle	SPS-2 Near Ashram Vatika	SPS-3 Sagwara Road near Gap Sagar	CWR & Pumping Station at Udaipur office	CWR & Pumping Station at MPH Office Campus	CWR & Pumping Station at New Colony
1	pH (at 25°C)	-	7.81	7.21	7.51	7.91	8.11	8.21	8.51
2	Electrical Conductivity	mS/cm	0.286	0.279	0.289	0.295	0.311	0.327	0.411
3	Calcium (as Ca)	mg/kg	89.77	107.74	98.75	125.69	134.67	62.85	116.71
4	Magnesium (as Mg)	mg/kg	45.19	24.59	49.48	14.79	14.34	37.22	31.54
5	Sodium (as Na)	mg/kg	53.13	49.29	43.81	38.38	39.34	42.23	43.18
6	Potassium (as K)	Kg/hect.	228.35	215.30	224.0	234.32	227.87	239.59	217.12
7	Available Nitrogen (as N)	Kg/hect.	58.99	52.43	45.88	58.99	56.37	57.02	32.11
8	Soil Moisture content	%	1.11	0.91	0.96	0.93	1.37	2.35	1.36
9	Organic Matter	%	0.95	0.86	0.71	0.81	0.90	0.68	0.43

Source: Lab Test Report February 2023

Sampling and testing done by: SKS Test Labs Pvt. Ltd.


BLQ: Below Limit of Quantification

LOQ: Limit of Quantification

77. **Geology.** The district is underlain by mainly hard rock formations belonging to Bhilwara Supergroup and Aravalli Supergroup intruded by granite. Along the major river courses, localized patches of shallow alluvium occur overlying the compact basement.

78. **Seismology.** According to the Vulnerability Atlas of India, most of Dungarpur District, including Dungarpur Town, is in an area of low earthquake risk (Zone II). Although Rajasthan has not experienced a major earthquake in the recent past, there have been 37 events with a magnitude of 5-7 since 1720, with the most recent occurring in 2001. This measured 6.9 on the Richter Scale, but because the epicentre was in neighbouring Gujarat, there was only limited damage in Dungarpur.

Figure 23: Earthquake Zone Map of Rajasthan

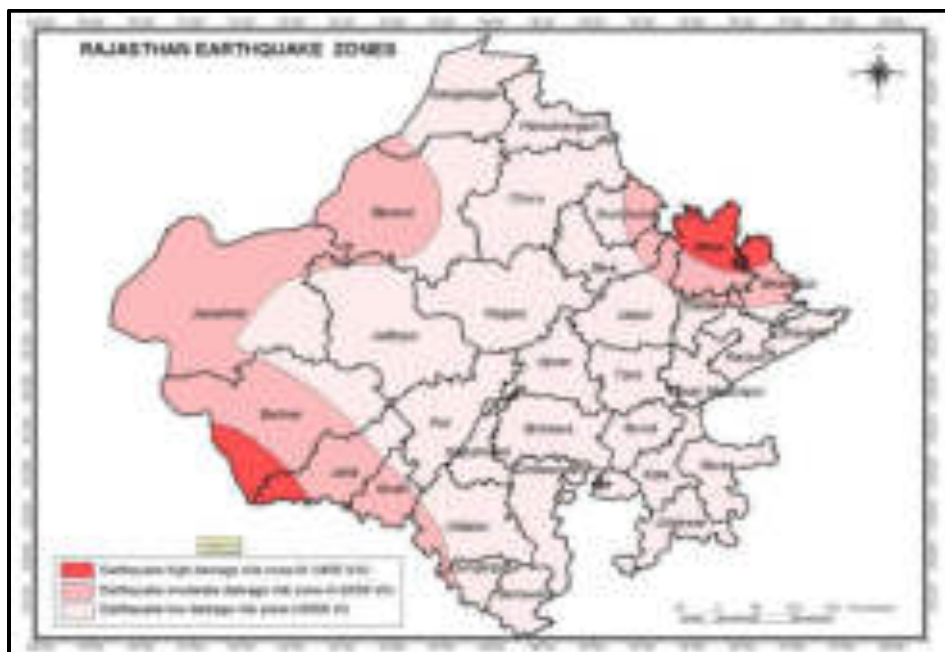

3. Climatic Conditions & Rainfall

79. Major part of the district enjoys sub humid type of climate. However, semi-arid type of climate is also experienced in a small area near northern boundary of the district. The summer season prevails from March to May, when peak temperatures are attained. Mean daily maximum temperature during May is 38.6°C and the mean daily minimum temperature is 24.9°C. Thereafter temperatures decrease with the onset of southwest monsoon. After the withdrawal of monsoon in September, the day temperature increases slightly, and a secondary maximum is attained in October. However, night temperature continues to fall. From November onwards both the day and night temperatures decrease rapidly till January, which is the coldest month with mean daily maximum temperature of 24.2°C and mean daily minimum temperature of 7.8°C. The annual potential evapotranspiration of the district is of the order of 1380mm with highest potential evapotranspiration (204.4mm) during the month of May and lowest (55.2mm) during the month of December. The highest average annual rainfall () has been recorded as 897.67mm and the lowest average annual rainfall has been recorded as 570.55mm.

4. Surface Water

80. The district is drained mainly by the rivers Som and Mahi. The former forms the natural boundary between Dungarpur and Udaipur districts and separates Dungarpur district from Banswara district. The Mahi River originates from the Mahi Kanta hills in the western part of Madhya Pradesh and enters Banswara and Dungarpur districts before entering Gujarat near

village Salakari. On an average, the riverbed is about 100m to 130 m in width and mostly rocky. Its banks are steep in many parts though not very high. Its length in Dungarpur district is about 110 km. The Som River flows southeast from hills near Bichhabhera in Udaipur district, till it meets the border of Dungarpur district. It then turns first to the east and then to the south forming the northern boundary. After meeting the Jhakham, it enters the Dungarpur district and after traversing for a few km down it meets river Mahi at Baneshwar. The river traverses through the district for a distance of about 84 km.

81. Moran a seasonal river emerges in the central part of the district and flows in the southeastern direction to find its way into the Mahi. There are various streams like Jhakham, Majhham, Vatrak, Bhader, Gangli, Sapan and Very Ganga. All these dry up during summer. The seasonal nallahs are Nagdari, Phallu, Padar, Mahaya and Kadva Bagaria. Samples of raw water and treated water at Udaivilas headworks were tested by PHED and test report shows that water quality of treated water is well within the permissible limits. Test Results are given in **Table 13**.

82. **Vijay Chakra Sagar Dam:** Situated near Dimiya village, Dungarpur and this earthen dam with masonry opening comes under control of Water Recourse Department, GoR. Dam was constructed in 60th decade in constituency of Maharawal Laxmansingh for the full fill the requirement of drinking water of Dungarpur. This dam is used for raw water source for urban water supply in Dungarpur. Capacity of this dam is 44.87 Mcft, the dam is not used of irrigation purposes at all. The dam is located on Moran River a tributary of mahi river. at the coordinate 23°46'44.82"N and 73°46'5.69"E.

83. **Edward Sagar Dam** is a drinking water Reservoir, owned by PHED and used for only for drinking water purpose, also known as Dungarpur Reservoir. This earthen dam with masonry opening has the total storage of 137 McFt excluding the dead storage of the dam. It is not used for irrigation purpose. Dam is located on do river at 23°47'19.78"N and 73°40'16.78"E.

84. **Som Kamla Amba Dam:** The construction of Som Kamla Amba Project across Som river, a tributary of Mahi river was completed in the year 2000 and its stated in 1992. The dam is located in Ashpur Tehsil of Dungarpur District, Rajasthan to provide the Irrigation cum drinking water facilities. The dam supplies drinking water to the tune of 8.1 MCM., besides irrigation supply to 26998.6 ha of Gross Command Area (GCA) and 19155.42 ha of Culturable Command Area (CCA).

85. Samples of water at Raw Water RGF Plant Udai Vilas, Filter Water RGF Plant Udai Vilas, CWR- Near RGF Plant Udai Vilas, CWR- Near RGF Plant Udai Vilas Tank, and Bori headworks filter house were collected on 05.04. 2021 and tested by PHED lab Dugarpur and test report shows that water quality of treated water is well within the desirable limits of National drinking water standards, except for TDS and hardness which was marginally on higher side. Test results are presented in table 13.

5. Groundwater

86. The principal source of ground water recharge is precipitation. Out of the total, rainfall received, a major part is lost as runoff and evapotranspiration through soil and vegetation. Only a small portion of rainfall infiltrates down to join the ground water body. Central Ground Water Board periodically monitors the National Hydrograph Network Stations (NHNS) stations in the Dungarpur district, four times a year i.e. in January, May (Pre-monsoon), August and November (Postmonsoon). Depth to water level during pre-monsoon (May 2011) varied from 1.7 to 55.32 mbgl. During post monsoon period (November 2011), the depth to water level varied from 0.46

mbgl. In general depth of water level varied from 5 to 20 mbgl. The overall stage of ground water development in the district is 77.56%.

87. Presently Dungarpur town is partially dependent on ground water. Samples of raw water from Wells at Patrakar Colony, Darjuwada, Fatehgari, Near Railway Puliya, Near New Colony pumphouse, Near Kabristan and Jalan Math were collected and tested in summers of 2021 and tested by PHED lab Dungarpur and test report shows that water quality of treated water is well within the desirable limits for all the parameters except TDS and total hardness, which is marginally higher than desired levels but is well below the maximum permissible limits of National drinking water standards. Test results are presented in Table 13.

88. After commission of subproject, during summer or during repair maintenance of systems when reduced flow will be available from dams. The ground water shall be used after blending with surface water. The blending with surface water will keep water quality within the permissible drinking water limits and water quality shall be monitored on regular basis before supplying it to the town.

Table 13: Test report of Surface water by PHED laboratory Dungarpur

Parameter	Unit	National Standards for Drinking Water ^a	WHO Guidelines for Drinking-Water Quality, 4 th Edition, 2011 ^b	Raw Water	Treated Water			
				Raw Water RGF Plant Udai Vilas	Filter Water RGF Plant Udai Vilas	CWR-Near RGF Plant Udai Vilas	CWR-Near RGF Plant Udai Vilas Tank	Bori headworks filter house
Date of Sample				05 April 2021				22 June 2021
Turbidity	NTU	1 (5)	-	16	0.2	0.2	0.2	8.5
pH		6.5 – 8.5	none	8	7.9	7.9	7.9	8.2
Color	Hazen units	5 (15)	none					none
Taste and Odor		Agreeable	-					
TDS	mg/l	500 (2,000)	-	480	550	550	550	330
Fluoride	mg/l	1 (1.5)	1.5	0.25	0.24	0.24	0.24	
Chloride	mg/l	250 (1,000)	none established	70	100	100	100	
Total Hardness	mg/l	200 (600)	-	200	230	230	230	

Source: PHED Regional Laboratory, Dungarpur, date of sample 04.02.2021 (Report copy attached as **Appendix 4**)

^a Bureau of India Standard 10500: 2012.; Figures in parenthesis are maximum limits allowed in the absence of alternate source

^b Health-based guideline values.

Table 14: Test report of Groundwater by PHED laboratory Dungarpur

National Standards for Drinking Water ^a			WHO Guidelines for Drinking-Water Quality, 4 th Edition, 2011 ^b							
Parameter	Unit	Max. Concentration Limits ^c		Patrakar Colony	Darjuwada	Fatehgari	Near Railway Puliya	Near New Colony pumphouse	Near Kabisran	Jalan Math
TDS	mg/l	500 (2,000)	-	777	660	752	545	550	547	550
Fluoride	mg/l	1 (1.5)	1.5	0.56	0.5	0.45	0.54	0.4	0.35	0.54
Chloride	mg/l	250 (1,000)	none established	110	130	155	132	100	150	120
Nitrate	mg/l	45	50	26	32	32	32	19	15	19

^a Bureau of India Standard 10500: 2012.; Figures in parenthesis are maximum limits allowed in the absence of alternate source

^b Health-based guideline values.

89. For the baseline study, DBO contractor has conducted groundwater quality monitoring at 7 nos. location which are: STP, SPS-1, SPS-2, SPS-3, CWR & Pumping Station at Udaivilas office, CWR & Pumping Station at MPH Office Campus, and CWR & Pumping Station at New Colony. Laboratory test results are presented in the **Tables 15**. Test result are show that groundwater is slightly alkaline in nature with pH ranging from 7.35 to 8.07, and within the acceptable range of drinking water quality. TDS, Alkalinity, Chloride and Total Harness are found in excess limit of acceptable limits while some other parameters are found in limits of IS10500 (2012). Laboratory test reports of groundwater quality are given in Appendix 10. A comparison of test results with the national standards and WHO guidelines reveal that ground water quality at all the five locations is agreeable with national and WHO norms. However, the TDS, is slightly higher than the desired level but well below the maximum permissible levels at all the five test locations. Alkalinity and Total Hardness at STP, SPS-1, SPS-2 and SPS-3 is higher than the desired levels but well below the maximum permissible limits. Chlorides at STP, SPS-1 and SPS-3 are higher than the desired levels but bellow the maximum permissible limits, as depicted in Table 15. Appendix 10. A comparison of test results with the national standards and WHO guidelines reveal that ground water quality at all the five locations is agreeable with national and WHO norms. However, the TDS, is slightly higher than the desired level but well below the maximum permissible levels at all the five test locations. Alkalinity and Total Hardness at STP, SPS-1, SPS-2 and SPS-3 is higher than the desired levels but well below the maximum permissible limits. Chlorides at STP, SPS-1 and SPS-3 are higher than the desired levels but bellow the maximum permissible limits, as depicted in Table 15.

Tables 16: Test Result of Ground Water Samples (Sampling date 01 February 2023)

S.No	Parameters	Units	National Standards for Drinking Water (Bureau of India Standard 10500: 2012) ^b	WHO Guidelines for Drinking-Water Quality, 4 th Edition, 2011 ^a	Results						
					Location						
					STP	SPS-1 Near Shree Padam Nhushan Bhogilal Circle	SPS-2 Near Ashram Vatika	SPS-3 Sagwara Road near Gap Sagar	CWR & Pumping Station at Udai vilash	CWR & Pumping Station at MPH Office Campus	CWR & Pumping Station at New Colony
1	pH	-	6.5 – 8.5	-	7.44	7.35	7.48	7.45	8.07	8.03	7.44
2	Total Dissolved solids	mg/l	500 (2,000)	-	959.0	1140.0	1678.0	1359.0	452.0	390.0	646.0
3	Alkalinity as CaCO ₃	mg/l	200 (600)	-	322.04	508.28	465.6	512.16	190.12	190.12	310.50
4	Total Hardness as CaCO ₃	mg/l	200 (600)	-	384.0	520.0	456.0	524.0	184.0	180.0	320.0
5	Nitrate as NO ₃	mg/l	<45	50	7.27	10.52	12.55	8.44	8.02	7.09	7.03
6	Chlorides as Cl	mg/l	250 (1000)	-	260.34	264.17	0.30	369.46	65.09	53.60	109.12
7	Sulphate as SO ₄	mg/l	200 (400)	-	83.05	91.98	152.78	127.5	86.11	52.78	72.22
8	Fluorides (as F)	mg/l	1 (1.5)	1.5	0.31	0.21	0.30	0.33	0.25	0.26	0.23
9	Iron as Fe	mg/l	0.3	-	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	0.11	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)
10	Arsenic (as As)	mg/l	0.01 (0.05)	0.01	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)	*BLQ (**LOQ 0.005)
11	Mercury (as Hg)	mg/l	0.001	0.006	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)	*BLQ (**LOQ 0.0005)
12	Lead (as Pb)	mg/l	0.01	0.01	*BLQ (**LOQ 0.05)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.05)	*BLQ (**LOQ 0.05)	*BLQ (**LOQ 0.05)	*BLQ (**LOQ 0.05)	*BLQ (**LOQ 0.05)
13	Cadmium (as Cd)	mg/l	0.003	0.003	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)	*BLQ (**LOQ 0.002)
14	Copper as Cu	mg/l	0.05 (1.5)	2.0	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)	*BLQ (**LOQ 0.02)
15	Zinc as Zn	mg/l	5 (15)	-	*BLQ (**LOQ 0.20)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.20)	*BLQ (**LOQ 0.20)	*BLQ (**LOQ 0.20)	*BLQ (**LOQ 0.20)	*BLQ (**LOQ 0.20)

16	Manganese as Mn	mg/l	0.1 (0.3)	-	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)	*BLQ (**LOQ-0.05)
17	Phenolic compounds	mg/l	0.001	-	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.001)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)	*BLQ (**LOQ 0.1)
18	Dissolved Oxygen (DO)	mg/l	-	-	4.82	4.82	4.72	4.11	4.8	5.1	4.5
19	Phosphate as PO ₄	mg/l	-	-	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)	*BLQ (**LOQ 0.2)
20	Hexavalent Chromium as Cr ⁺⁶)	mg/l	-	-	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)	*BLQ (**LOQ-0.02)

Sampling and testing done by: SKS Test Labs Pvt. Ltd.

BLQ: Below the Limit of Quantification; LoQ : Limit of Quantitation

Note-

^a Health-based guideline values.

Per ADB SPS, the government shall achieve whichever of the standards is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the executing agency of the government will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in ADB SPS.

^b Figures in parenthesis are maximum limits allowed in the absence of alternate source.

6. Air Quality

In Dungarpur town there are no major polluting industries and therefore level of pollution of gases like CO, NO_x and SO_x is not high. But particulate matters (PM₁₀ and PM_{2.5}) are above the WHO standards but within the Indian standards due to presence of dust from sand. Transport also add pollution load in air in city.

90. Air quality monitoring has been conducted in February 2023 at 7 locations. Test report of ambient air quality is shown in **Table 16** and details of test report are shown in **Appendix 10**. Baseline ambient air quality test report shows that all tested parameters are found within the permissible limit of CPCB 2009 but PM₁₀, PM_{2.5}, NO₂ are recorded higher at all the sampling locations and air quality with regard to SO₂ and CO is below the set levels of Air Quality Guidelines level (WHO 2021).

Table 16: Ambient Air Quality Test Result (Date of Sampling 06 February 2023- 24 hrs sampling)

Sr. No	Location	Results				
		PM ₁₀ (µg/m ³)	PM _{2.5} (µg/m ³)	SO ₂ (µg/m ³)	NO ₂ (µg/m ³)	CO (mg/m ³)
1.	Shastri Colony	69.37	53.17	8.07	15.29	0.56
2.	SPS-1 (Near Shree Padhambhusan Bhogilal Circle)	64.21	22.9	11.99	23.87	0.55
3.	SPS-2 (Near Ashrarm Vatica)	62.68	21.95	11.07	23.78	0.52
4.	SPS -3(Gap Sagar)	63.27	26.79	12.39	24.93	0.55
5.	STP (Do Nadi)	61.25	28.01	12.01	24.89	0.54
6.	CWR & Pumping Station at Udai villas	66.12	25.88	10.91	21.39	0.55
7.	CWR & Pumping Station at MPH Office Campus	62.03	29.74	11.29	22.42	0.50
8.	CWR & Pumping Station at New Colony	60.21	26.83	11.58	22.47	0.56
9.	Intake well Dimiya Vijay Sagar Dam	65.28	29.79	13.13	24.95	0.57
10	Old City Manakchok	59.35	23.82	9.97	17.46	0.47
Prescribes Limit (CPCB 2009) - 24 hours**		100	60	80	80	4
WHO Air Quality Guidelines (µg/m ³)		45	15	40	10	4

Sampling and testing done by: SKS Test Labs Pvt. Ltd. in month of February 2023

7. Noise Quality

91. There are no industrial or heavy development activities in the municipal areas of Dungarpur town, therefore noise quality in town is almost good though due to vehicular movements noise is increased as compared to prescribed limits. Ambient Noise Level Monitoring has been conducted by DBO Contractor in February 2023 at seven locations and ambient noise level values are given in **Table 17** and details are given in **Appendix 10**. At all locations daytime ambient noise level was observed higher than national level and WHO guidelines and night time levels are recorded within prescribed limits.

Table 17: Ambient Noise Level Quality Test Result (Date of monitoring 31 Jan 23 to 1 Feb 23)

S. No.	Parameters	Unit of Measurement	Location Results						
			STP near Do river	SPS-1 Near Shree Padhambhusan Bhogilal Circle)	SPS-2 Near Ashrarm Vatica	SPS-3 near Gap Sagar	CWR & Pumping Station at Udai vilash	CWR & Pumping Station at MPH Office Campus	CWR & Pumping Station at New Colony
1	Ambient Noise Level (Day Time)	dB(A)	63.21	60.51	64.91	63.22	65.82	62.42	64.40
2	Ambient Noise Level (Nighttime)	dB(A)	42.60	40.09	45.69	41.69	44.19	43.22	46.39
Noise Level Standards									
Receptor/ Source		India National Noise Level Standards ^a (dBA)		WHO Guidelines Value For Noise Levels Measured Out Doors ^b (One Hour LA _q in dBA)					
		Day	Night	07:00 – 22:00	22:00 – 07:00				
Industrial area		75	70	70	70				
Commercial area		65	55	70	70				
Residential Area		55	45	55	45				
Silent Zone		50	40	55	45				

Source: Lab Test Report February 2023

B. Ecological Resources

92. **Protected areas.** The nearest wildlife sanctuary is Sita Mata Sanctuary located 86 km from project town. The nearest forest area is Gumanpua protected forest block in North-East direction which having 4 km distance from Dungarpur town. The nearest protected area is Sita Mata sanctuary at 86 km distance in east direction. IBAT results show no key biodiversity area within 10 km of project boundary, Jaisamand Lake and Wildlife Sanctuary and Phulwari Wildlife Sanctuary are located at 50 km from project boundary. There is no notified breeding or nesting bird site/ecological sensitive area/Ramsar convention site/Area notified under Wild Protection Act-1972 in these forest blocks as well as in town. In the project Town “Dundarpur” area no wildlife sanctuary or other protected area are existed.

93. **Wildlife.** In the forest blocks especially in Gumanpua, Ghatol and Pipalkhut forest block, some wild animals are observed which are blue bull, sambar, Jackal, jungle cat, deer, wild boar, monkey, wild dogs etc. Our experts were told by locals that reptiles like common garden lizard (*Chameleon zeylanicaul*), common Indian monitor (*Varanus beagalansis*), Indian Cobra (*Najanaja*), and Krait (*Bungarusc oerulens*) are rarely found in agriculture fields during rainy season. Common birds found in the region are Little egret (*Egretta garzetta*), Common Green Pigeon (*Treron phoenicoptera*), Blue Rock Pigeon (*Columba livia*), House swift (*Apus affinis*), Pheasant tailed Jacana (*Hydrophasianus chirurgus*) etc. No rare or migratory birds are reported in the project areas. *Crocodylus palustris* was observed in the Vijay Chakra Sagar Dam which is a vulnerable crocodile species as per IUCN and is protected under wild life conservation act.

94. On occurrence of *crocodylus palustris* in the reservoir, a detailed biodiversity survey was conducted in view of construction of a new intake well in the Vijay Chakra Sagar Dam. New intake well was proposed under the subproject as the existing intake well is located in shore of the reservoir and experience recede of water during summers, hence a new intake well in deeper part of reservoir was proposed downstream to existing one at about 1.5 km distance. In view of findings of biodiversity report and presence of probable nestling grounds in the shore of reservoir near the embankment, which is about 1.5 km away from the existing intake well, it was proposed not to construct new intake well and refurbish the existing intake well. The existing intake well is located in the lake shore and experience intermittent dryness during summer seasons and to address this issue it is proposed to dig a channel from nearest deepest area to the existing intake well. Meanwhile, PHED under a separate scheme have replaced the pumps (2 Nos) and DBO contractor is conducting survey and investigating to finalize the scope of work under refurbishment of existing intake well and the same will be incorporated in next IEE. Comprehensive Biodiversity report is appended in this IEE as Appendix 12. Mitigation measures, in view of presence of crocodiles in the reservoir are also included in EMP.

95. **Flora.** Major tree species in project area include Babul, Sagwan, Khakhra, *Terminalia belarica* (Behara), *Azadirachta indica* (Neem), Khejri- *Prosopis cineraria*, Lasura or Lehsua- *Cordia dichotoma*, Kair or Teat -*Capparis deciduas*, Pakori-*Ficusrumphii*, etc. There are no vulnerable, threatened and/or endangered species of flora and fauna is available in the project areas. Common shrub species found in the area are *Adhatodavasica*, *Calotropis procera*, *Ipomea carnea*, *Prosopis juliflora*, *Achyranthes aspera*, *Ageratum conyzoides*, Argemone etc. in the project areas. On the review of available information, no rare or endangered species of flora and fauna prescribed by IUCN or WPC, 1972 are found along the project areas.

96. Biodiversity Assessment has been carried out through online IBAT analysis tool for potential presence of critical habitat within the proposed projects potential area of influence. In addition, to the potential impacts on identified local biodiversity and ecosystems, ADB's SPS,

2009 requires demonstration that the project will not adversely affect the identified critical habitat. ADB SPS, 2009 states that projects should not be developed within critical habitat areas unless all of the below criterion are met (i) there are no measurable adverse impacts, or likelihood of such, on the critical habitat which could impair its high biodiversity value or the ability to function; (ii) the project is not anticipated to lead to a reduction in the population of any recognized endangered or critically endangered species or a loss in area of the habitat concerned such that the persistence of a viable and representative host ecosystem be compromised; and (iii) any lesser impacts are mitigated.

97. Biodiversity Assessment Report (IBAT Analysis) for Water Supply (CWR) and Sewerage system (STP located on Do River in Dungarpur town has been attached with this report as **Appendix 7**. The screening study for critical habitation indicates that within the area of analysis (AOA) there are no known species which would qualify the area as critical habitat under the set criteria (criterion 1–5, as presented in the report). As per IBAT report; within 50 km radius of STP. There are 14 species of concern fauna listed as IUCN Red list, most of which are wild species and not reported in urban areas of Dungarpur. The nearest wildlife sanctuary is Sita Mata Sanctuary located 86 km from project town. Proposed activities will not have impact on these species. There is no national or international protected area within the periphery of 50 km. There is no key bio-diversity areas within the buffer of 1-10 km, however there are two key biodiversity area Jaisamand Lake and Wildlife Sanctuary and Phulwari Wildlife Sanctuary are located at 50 km from project boundary.

98. **Field based biodiversity assessment:** In view of sighting of the *Crocodylus palustris* in the Vijay Chakra Sagar Dam, detailed biodiversity assessment was conducted by field biologist and visits were made during September, October and November months of year 2023. Following flora and fauna is recorded during the visit in and around Vijay Chakra Sagar Dam. Detailed report is attached at Appendix 12.

99. **Flora:** following species were observed in the field visit and are depicted in Table 18.

Table 18: Floral diversity of Vijay Chakra Sagar dam and its surroundings

S.No.	Scientific Name	Common Name
1.	<i>Tectona grandis</i>	Teak
2.	<i>Boswellia serrata</i>	Salai
3.	<i>Anogeissus pendula</i>	Dhawada
4.	<i>Acacia nilotica</i>	Babul
5.	<i>Acacia catechu</i>	Khair
6.	<i>Dendrocalamus strictus</i>	Bamboo
7.	<i>Tectona grandis</i>	Teak
8.	<i>Butea monosperma</i>	Khakhra
9.	<i>Acacia leucophloea</i>	Ronjh
10.	<i>Holoptelia integrifolia</i>	Papdi
11.	<i>Euphorbia sp.)</i>	Thoor
12.	<i>Phoenix sylvestris)</i>	Khajoor
13.	<i>Ailanthus excelsa</i>	Ardu
14.	<i>Acacia nilotica</i>	Babool
15.	<i>Azadirachta indica</i>	Neem
16.	<i>Prosopis cineraria</i>	Khejri
17.	<i>Ziziphus spp.</i>	Jujube

18.	<i>Mangifera indica</i>	Mango
19.	<i>Lantana camera</i>	
20.	<i>Polygonum glabra</i>	
21.	<i>Sterculia urens</i>	Kadaya
22.	<i>Datura metel</i>	Dhatura
23.	<i>Croton bonplandianus</i>	
24.	<i>Parthenium hysterophorus</i>	Congress grass
25.	<i>Tribulus terrestris</i>	Gokharu
26.	<i>Lindenbergia indica</i>	
27.	<i>Tridax procumbens</i>	
28.	<i>Evolvulus sps</i>	
29.	<i>Rungia sps</i>	
30.	<i>Ludwigia sedoides</i>	
31.	<i>Nymphoides indica</i>	
32.	<i>Nymphaea alba</i>	
33.	<i>Eclipta abla</i>	
34.	<i>Ipomoea aquatica</i>	

100. Some of the plant species observed are very important in view of supporting avifauna and are described below:

- (i) **Teak (*Tectona grandis*):** While teak may not directly provide food for birds, its large canopy and sturdy branches can offer perching and nesting sites.
- (ii) **Khakhra (*Butea monosperma*):** The Flame-of-the-Forest produces bright orange to scarlet flowers, which can attract nectar-feeding birds like sunbirds. The tree also provides perching and nesting opportunities.
- (iii) **Ronjh (*Acacia leucophloea*):** Acacia trees, including *Acacia leucophloea*, are known for providing habitat and food for various bird species. Birds may use the branches for perching, and some species may feed on insects associated with the tree.
- (iv) **Papdi (*Holoptelia integrifolia*):** The Papdi tree may provide food and shelter for birds. Insects help in pollination and also attract insect-eating birds.
- (v) **Thoor (*Euphorbia sp.*):** birds may be attracted to the plant for shelter or potential nesting sites. However, many *Euphorbia* species are toxic and should be handled with care.
- (vi) **Khajoor (*Phoenix sylvestris*):** Date Palm trees produce dates, which can attract fruit-eating birds. Additionally, the palm fronds may offer nesting sites for certain bird species.
- (vii) **Ardu (*Ailanthus excelsa*):** Ailanthus trees may attract insects, and birds that feed on insects may be found in the vicinity. The tree's canopy can provide perching and nesting opportunities.
- (viii) **Babool (*Acacia nilotica*):** Acacia trees are known for their thorns, which can provide protection for birds nesting in their branches. Birds may also feed on insects associated with the tree.
- (ix) **Azadirachta indica (Neem):** Neem trees provide shelter and attract insects. Birds, especially insectivores, may feed on the insects found on neem trees. Some bird species may consume neem seeds.
- (x) **Prosopis cineraria (Khejri):** Khejri trees are a valuable resource for birds in arid regions. They provide shade, and the foliage is browsed by herbivorous birds. The seeds are also consumed by various bird species. Insects attracted to the tree can attract insectivorous birds.
- (xi) **Ziziphus spp. (Jujube):** Jujube trees produce small, edible fruits that are attractive

tobirds, including bulbuls and barbets. The dense foliage provides shelter and nesting sites for birds.

- (xii) **Mangifera indica** (Mango): Mango trees produce large, fleshy fruits that are attractive to a variety of birds, including Parrots, Mynas, and Bulbuls. The robust branches and thick foliage of mango trees can serve as nesting sites for birds.
- (xiii) **Lantana**: Lantana flowers attract butterflies and hummingbirds, contributing to the overall biodiversity in your garden.
- (xiv) **Polygonum glabra**: Birds may be attracted to this plant if it produces seeds or provides shelter for insects that birds feed on.

101. **Avifauna**: A total of 74 species of avifauna were observed in and around the Vijay Chakra Sagar dam as listed below in Table 19.

Table 19: Avifauna recorded in and around Vijay Chakra Sagar dam during site visit

S.No.	Scientific Name	Common Name	Red List Category	Movement Category
1.	<i>Sterna aurantia</i>	River Tern	VU	Not a Migrant
2.	<i>Threskiornis melanocephalus</i>	Black-headed Ibis	NT OR LR/NT	Not a Migrant
3.	<i>Ciconia episcopus</i>	Asian Woollyneck	NT OR LR/NT	Not a Migrant
4.	<i>Dendrocygna javanica</i>	Lesser Whistling-duck	LC OR LR/LC	Not a Migrant
5.	<i>Leiopicus mahrattensis</i>	Yellow-crowned Woodpecker	LC OR LR/LC	Not a Migrant
6.	<i>Alcedo atthis</i>	Common Kingfisher	LC OR LR/LC	Not a Migrant
7.	<i>Ceryle rudis</i>	Pied Kingfisher	LC OR LR/LC	Not a Migrant
8.	<i>Alexandrinus krameri</i>	Rose-ringed Parakeet	LC OR LR/LC	Not a Migrant
9.	<i>Spilopelia senegalensis</i>	Laughing Dove	LC OR LR/LC	Not a Migrant
10.	<i>Amauornis phoenicurus</i>	White-breasted Waterhen	LC OR LR/LC	Not a Migrant
11.	<i>Porphyrio porphyrio</i>	Purple Swampen	LC OR LR/LC	Not a Migrant
12.	<i>Tringa totanus</i>	Common Redshank	LC OR LR/LC	Full Migrant
13.	<i>Tringa ochropus</i>	Green Sandpiper	LC OR LR/LC	Full Migrant
14.	<i>Tringa glareola</i>	Wood Sandpiper	LC OR LR/LC	Full Migrant
15.	<i>Actitis hypoleucos</i>	Common Sandpiper	LC OR LR/LC	Full Migrant
16.	<i>Vanellus indicus</i>	Red-wattled Lapwing	LC OR LR/LC	Not a Migrant
17.	<i>Microcarbo niger</i>	Little Cormorant	LC OR LR/LC	Not a Migrant
18.	<i>Phalacrocorax fuscicollis</i>	Indian Cormorant	LC OR LR/LC	Not a Migrant
19.	<i>Ardea purpurea</i>	Purple Heron	LC OR LR/LC	Not a Migrant
20.	<i>Ardea alba</i>	Great White Egret	LC OR LR/LC	Not a Migrant
21.	<i>Bubulcus ibis</i>	Cattle Egret	LC OR LR/LC	Not a Migrant
22.	<i>Ardeola grayii</i>	Indian Pond-heron	LC OR LR/LC	Not a Migrant
23.	<i>Plegadis falcinellus</i>	Glossy Ibis	LC OR LR/LC	Not a Migrant
24.	<i>Pseudibis papillosa</i>	Red-naped Ibis	LC OR LR/LC	Not a Migrant
25.	<i>Anastomus oscitans</i>	Asian Openbill	LC OR LR/LC	Not a Migrant
26.	<i>Lanius schach</i>	Long-tailed Shrike	LC OR LR/LC	Not a Migrant
27.	<i>Hirundo smithii</i>	Wire-tailed Swallow	LC OR LR/LC	Not a Migrant
28.	<i>Prinia socialis</i>	Ashy Prinia	LC OR LR/LC	Not a Migrant
29.	<i>Prinia inornata</i>	Plain Prinia	LC OR LR/LC	Not a Migrant
30.	<i>Chrysomma sinense</i>	Yellow-eyed Babbler	LC OR LR/LC	Not a Migrant
31.	<i>Cinnyris asiaticus</i>	Purple Sunbird	LC OR LR/LC	Not a Migrant
32.	<i>Ploceus philippinus</i>	Baya Weave	LC OR LR/LC	Not a Migrant

33.	<i>Halcyon smyrnensis</i>	White-breasted Kingfisher	LC OR LR/LC	Not a Migrant
34.	<i>Merops orientalis</i>	Asian Green Bee-eater	LC OR LR/LC	Not a Migrant
35.	<i>Ardea intermedia</i>	Intermediate Egret	LC OR LR/LC	Not a Migrant
36.	<i>Himantopus himantopus</i>	Black-winged Stilt	LC OR LR/LC	Not a Migrant
37.	<i>Curruca curruca</i>	Lesser Whitethroat	LC OR LR/LC	Not a Migrant
38.	<i>Streptopelia chinensis</i>	Spotted Dove	LC OR LR/LC	Not a Migrant
39.	<i>Gallinula chloropus</i>	Common Moorhen	LC OR LR/LC	Not a Migrant
40.	<i>Egretta garzetta</i>	Little Egret	LC OR LR/LC	Not a Migrant
41.	<i>Passer domesticus</i>	House Sparrow	LC OR LR/LC	Not a Migrant
42.	<i>Copsychus saularis</i>	Oriental Magpie-robin	LC OR LR/LC	Not a Migrant
43.	<i>Palaeornis eupatria</i>	Alexandrine Parakeet	NT OR LR/NT	Nomadic resident
44.	<i>Francolinus pondicerianus</i>	Grey Francolin	LC OR LR/LC	Not a Migrant
45.	<i>Pavo cristatus</i>	Indian Peafow	LC OR LR/LC	Not a Migrant
46.	<i>Ocyrceros birostris</i>	Indian Grey Hornbill	LC OR LR/LC	Not a Migrant
47.	<i>Upupa epops</i>	Common Hoopoe	LC OR LR/LC	Full Migrant
48.	<i>Hierococcyx varius</i>	Common Hawk-cuckoo	LC OR LR/LC	Full Migrant
49.	<i>Treron phoenicopterus</i>	Yellow-footed Green-pigeon	LC OR LR/LC	Not a Migrant
50.	<i>Accipiter badius</i>	Shikra	LC OR LR/LC	Not a Migrant
51.	<i>Dendrocitta vagabunda</i>	Rufous Treepie	LC OR LR/LC	Not a Migrant
52.	<i>Corvus splendens</i>	House Crow	LC OR LR/LC	Not a Migrant
53.	<i>Pericrocotus cinnamomeus</i>	Small Minivet	LC OR LR/LC	Not a Migrant
54.	<i>Rhipidura aureola</i>	White-browed Fantail	LC OR LR/LC	Not a Migrant
55.	<i>Dicrurus macrocercus</i>	Black Drongo	LC OR LR/LC	Not a Migrant
56.	<i>Dicrurus caerulescens</i>	White-bellied Drongo	LC OR LR/LC	Not a Migrant
57.	<i>Aegithina tiphia</i>	Common Iora	LC OR LR/LC	Not a Migrant
58.	<i>Eumyias thalassinus</i>	Verditer Flycatcher	LC OR LR/LC	Full Migrant
59.	<i>Saxicoloides fulicatus</i>	Indian Robin	LC OR LR/LC	Not a Migrant
60.	<i>Phoenicurus ochruros</i>	Black Redstart	LC OR LR/LC	Full Migrant
61.	<i>Stumia pagodarum</i>	Brahminy Starling	LC OR LR/LC	Not a Migrant
62.	<i>Acridotheres tristis</i>	Common Myna	LC OR LR/LC	Not a Migrant
63.	<i>Ptyonoprogne concolor</i>	Dusky Crag Martin	LC OR LR/LC	Not a Migrant
64.	<i>Pycnonotus cafer</i>	Red-vented Bulbul	LC OR LR/LC	Not a Migrant
65.	<i>Prinia hodgsonii</i>	Grey-breasted Prinia	LC OR LR/LC	Not a Migrant
66.	<i>Orthotomus sutorius</i>	Common Tailorbird	LC OR LR/LC	Not a Migrant
67.	<i>Eremopterix griseus</i>	Ashy-crowned Sparrow-lark	LC OR LR/LC	Not a Migrant
68.	<i>Streptopelia decaocto</i>	Eurasian Collared-dove	LC OR LR/LC	Not a Migrant
69.	<i>Parus major</i>	Great Tit	LC OR LR/LC	Not a Migrant
70.	<i>Burhinus indicus</i>	Indian Thick-knee	LC OR LR/LC	Not a Migrant
71.	<i>Tephrodornis pondicerianus</i>	Common Woodshrike	LC OR LR/LC	Not a Migrant
72.	<i>Terpsiphone paradisi</i>	Indian Paradise-flycatcher	LC OR LR/LC	Not a Migrant
73.	<i>Argya striata</i>	Jungle Babbler	LC OR LR/LC	Not a Migrant
74.	<i>Zosterops palpebrosus</i>	Indian White-eye	LC OR LR/LC	Not a Migrant

102. **Reptiles:** A species of reptile - Marsh crocodile , *Crocodylus palustris* was observed during field visit in Vijaya Chakra Sagar Dam. Post observation of Marsh crocodile, a field biologist was engaged for detailed biodiversity assessment in and around the dam. A total of 74 bird species and 34 floral species were observed and documented in Appendix 12. Some inactive crocodile nests were also observed towards the southern extremity of the dam. This warranted to explore alternatives and possibility of refurbishment of existing intake well which is well away from inactive crocodile nests. After the bathometric survey and other feasibility options, refurbishment of new intake well was chosen, where in PHED, Government of Rajasthan already taken up the work of replacement of pumps. Remaining works of refurbishment will be taken up under the present proposal, for which details will be submitted by DBO contractor after detailed survey and investigation.

8. Economic Development

(a) Land use

103. Dungarpur Master Plan provides land use details of the town. Out of total 947.0 acre area, 81.1 % is developed urban area. Rest of the land is underwater body, vacant and agricultural land and government reserved land. Details of the land use is provided in **Table 20** below-

Table 20: Existing Land Use of Dungarpur

S. No.	Land Use	Area (in Acres)	Percentage of Developed area (%)	Percentage of Urban area (%)
1	Residential	259.0	33.8	27.3
2	Commercial	44.0	5.6	4.7
3	Industrial	66.0	8.6	7.0
4	Govt. / Semi Govt.	26.0	3.3	2.7
	Public and Semi Public	120.0	15.6	12.7
5	Recreational	8.0	1.1	0.8
6	Circulation	245.0	32.0	25.9
	Developed Area	768.0	100%	81.1
7	Water body	20.0	-	2.1
8	Vacant and Agricultural land	84.0	-	8.9
9	Government Reserved	75.0	-	7.9
	Total Urban area	947.0	-	100%

*Source: Master Plan Dungarpur 2011-2031

104. In the Dungarpur town approx. 81.1 % area is developed area, 2.1 % is water bodies 7.9 % is govt. land and 8.9% is vacant and agriculture land.

(b) Commerce, Industry & Agriculture

105. **Industries.** There are 22 small and medium industries functioning in the town out of which

15 industries are running in RIICO industrial area rest are scattered all over the town. Traditional 353 cottage and small-scale service industries have been functioning within residential and commercial areas. These industries mainly comprises of repair workshops, engineering works handicrafts, gold smith etc.

106. **Agriculture.** The agriculture in the district is characterized by recurrent droughts, sloppy lands, dominance of low value and low demand crops, inadequate infrastructure, small size of land holding, poor irrigation sources, poor livestock productivity, lack of off farm employment opportunities, poor market support, non-availability of credit and high rate of illiteracy. The major crops of the Kharif season are maize, rice, black gram, soybean and cotton, while wheat, gram and barley are major Rabi crops. Area under Zaid green gram cultivation is increasing. Cereal crops (maize, wheat and rice) constitute 88.12% of gross cultivated area followed by pulses (black gram, pigeon pea, gram and green gram) 11.45% and oilseeds 0.23 % (soybean).

C. Other Infrastructure

107. **Storm Water Drainage.** Dungarpur town is facing severe drainage problem resulting water logging on roads and low lined areas during the rainy season, even though the rain is moderate. The surface runoff from the town finally gets accumulated in every monsoon season in the outskirts of town in low lying areas.

108. **Power Supply.** Distribution of power in the town is the responsibility of the Rajasthan State Electricity Board. Power is generated and supplied from Mahi Hydal Project, Banswara. Main electricity line is 81 kms away from the town. The major sector for electric consumption is domestic which constitute 14.53% small scale industries consume 2.48% of power.

109. **Transport.** Transport in the city is mainly by personal vehicles (motorcycles and bicycles) and auto- and private taxis. The Rajasthan State Road Transport Corporation (RSRTC) runs public buses to neighbouring villages and towns and to larger towns farther afield, such as Banswara, Udaipur, with which there are good road connections. The rail line between Udaipur and Ahmadabad in Gujarat runs through the town, shortest distance to the National Highway 8 from Dungarpur town is 20 km which connects Dungarpur with all the major districts of Rajasthan.

D. Socio Cultural Resources

110. **Demography.** As of 2011 India census, Dungarpur had a population of 47,706 people. The population consists of 52% males and 48% females. Dungarpur has an average literacy rate of 76%, higher than the national average of 59.5%. The male literacy rate is 83%, and the female literacy rate is 69%. In Dungarpur, 13% of the population is under 6 years of age.

111. **History, Culture and Tourism.** The town of Dungarpur, was founded near the end of the 14th century by Rawal Bir Singh, the sixth descendant of Sawant Singh of Mewar, who named it after Dungaria, an independent Bhil chieftain who was assassinated. After the death of Rawal Udai Singh of Bagar at the Battle of Khanwa in 1527, where he fought alongside Rana Sanga against Babar, his territories were divided into the states of Dungarpur and Banswara. Successively under Mughal, Maratha, and British Raj control by treaty in 1818, it remained a 15-gun salute state. Dungarpur was founded by Raja Dungaria Bhil in the 13th century. Rawal Veer Singh defeated the Bhil chief Dungaria after whom the place was named Dungarpur. It was taken over by the East India Company in 1818. This place was the capital of Dungarpur Princely State. Holi is the most important festival for them, drums are played before the holy day of Holi. On the day of Holi, boys and girls dance, which is known as Gair. Gaib sagar Lake, Dev Somnath Temple,

Museum, Juna Palace, Beneshwar dham, Galiyakot are the nearest tourist places of Dungarpur town. However, there are no any historical, cultural or important tourist places in Dungarpur Municipal areas. Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments.

E. Environmental Settings of Investment Program Component Sites

112. Sewers and water supply pipes will be laid along the roads/streets in the town within the road right of way (ROW). In wider roads pipes/sewers will be laid in the road shoulder beside the tarmac, and in narrow roads, where there is no space, sewers will be laid in the road carriage way by break opening the tarmac. Roads in some parts of the town are narrow. Roads are lined both sides with open drains. In narrow roads sewers will be laid in the middle of the road, which may affect the traffic. Bigger diameter trunk sewers will be laid along the main roads, which are wide and have adequate space. No tree cutting is anticipated as there is adequate space to lay the water & sewer pipeline in those roads. Pipe networks for water supply will be laid in the entire town within the existing RoW. There is sufficient space available for laying of pipeline. These works will require advance permission from concerned authority for road cutting and traffic diversion etc. If any tree cutting will be required during execution mitigation measures shall be adopted.

113. STP (4.0 MLD) is proposed near Do river on Udaipur road in Zone-6, Durgapur on vacant government land under Municipal Council in Malpur village. Total area of allocated land is 11.14 ha and Khasra no. of proposed land are 312 & 313. There are no trees present at site, which may be required to cut for construction of STP. There are only agricultural activities in the periphery of this site. Khandeshwar Mahadev Temple at upstream of STP site at about 200 m distance, Indrakhet residential colony at 350 m distance and Do river along the proposed STP site at 50 m distance. No wildlife is reported in this area. There is no sensitive receptor and habitation in 100m periphery, Therefore, there will be no adverse impacts on habitation.

114. 3 nos. SPS are proposed at Padambhusan Shri Bhogi Lal Pandya Circle, Ashram Vatika, and between RICCO & Gap Sagar. All the sites are Govt. of Rajasthan lands. There are few habitations within 100-200 mtr area of the SPS except SPS between RICCO & Gap Sagar where market area is existed on LHS & RHS side but due the close circuit of SPS, there will be minimum odour nuisance. Adequate mitigation measures will be required during construction works.

115. CWRs and pump houses are proposed in existing PHED campus at Chandpole and New Colony, Dungarpur. There is no habitation near the proposed CWR in Chandpole area, but new colony CWR is surrounded by habitation.

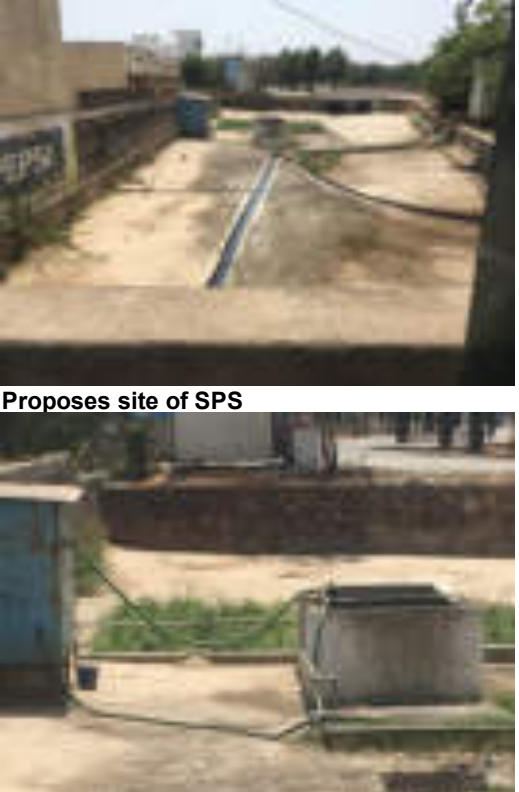
116. Site environmental features of all subproject sites and photographs are presented in the following Table 21.

Table 21: Environmental Features of Project sites

Proposed Structure	Environmental Features	Photo
Refurbishment of existing Intake – cum – raw water pump house at Vijay Chakra Dam	- There is no plantation at the location of intake and pump house. - There is no forest or protected areas near existing intake and pump house. - Nearest forest area is Raajdhani unclassified forest area at 670 m in north-east direction. - Land is owned by water resource department, Municipal Council, Dungarpur have already written letter to WRD for No-objection certificate (Appendix 13) The same will be obtained prior to refurbishment works. - Access to existing intake and pump house is through PMJSY BT road. - The nearest habitant (2 nos.) at aerial distance of 120 m in South direction.	 Existing pump house and intake point
Proposed New Water Source: WTP at Somkamla Amba Dam. Note: This is part associated project	- It is under construction phase at nearby location of Dam. - The Nearest forest area is Rajdhani protected forest block in east side and having approx. 500m distance - WTP at Somkamla Amba is having connectivity with 2 lane SH 54 and a single lane village road. - Available area is 15000 sq.m. and required area 5000 sq.m.	
CWR Location in Chandpole, Dungarpur Latitude- 23°50'6.18"N Longitude- 73°42'35.80"E	- This proposed location is existed on Navadera Road, Dungarpur. - There are outdated existing water reservoirs structures. - There is Dargah Mastan Baba at 40-meter distance, - There is dense habitation of Chanpole area in south-east direction of proposed CWR site. - These are Muslim Graveyards at adjoining of proposed site.	

Proposed Structure	Environmental Features	Photo
	- No tree and wildlife will be impacted. - The Nearest forest area is Rajdhani protected forest block in south-east side and having approx. 1.5 km distance. - CWR is connected with bituminous concrete road - Nearest Household at 50 meters distance from CWR. - Required land is only 235 sqm against available land of 700 sqm.	 Proposes site of CWR
CWR in PHED Campus new colony Latitude- 23°50'52.30"N Longitude- 73°42'38.67"E	- This site is located behind PHED office on Udaipur Road in new colony, Dundarpur. - One Neem tree will be impacted. - This site is located in the residential area. - CWR in PHED is connected with 2 lane cement concrete road. - Nearest Household at 50 meter distance. - The Nearest forest area is Rajdhani protected forest block in south-east side and having approx. 3.2 km distance - Required land is only 235 sqm against available land of 650 sqm.	 Proposes site of CWR

Proposed Structure	Environmental Features	Photo
Existing WTP site in Uday Vilas, Dungarpur Latitude- 23°49'59.18"N Longitude- 73°43'32.52"E	• This Existing WTP site is existed near Udai Place on Gap Sagar Lake bank. • There is no habitation but Raajdhani protected forest block is at 150 m distance. • Hilly area and dense tree cover are observed behind the site. • WTP at Uday Vilas is connected with a 2 lane City Road. • Nearest Household at 190.74 meters distance. • No new land is required.	
SPS Site at Ashram Vatika on Sabla Bypass Road, Dungarpur Latitude- 23°51'7.38"N Longitude- 73°42'14.09"E	• This proposed SPS site is located between Suneria lake and Sabla lake on Sabla bypass road. • There is Pit Composting Unit at adjoining of this site. • A small Tejaji Temple is existed in the proposed area but it will not be affected. • Surrounded by waterlogged area • The Nearest forest area is Rajdhani protected forest block	 Proposes site of SPS

Proposed Structure	Environmental Features	Photo
	in north-east side and having approx. 2.8 km distance. • The SPS Ashram is connected to 2 lane Dungarpur bypass road. • Nearest Household present at 65.01 meters distance. • Required land is only 1500 sqm against available land of 5159 sqm.	
SPS Site on Sagwara Road near Gap Sagar, Dungarpur Latitude- 23°50'59.09"N Longitude- 73°43'37.55"E	• This proposed SPS site is existed in market area on Sagwara Road near Gap Sagar, Dungarpur. • A small treatment is existed in the proposed site. • There is no tree observed in the proposed site. • No wildlife and no forest area will be impacted. • Govt. bus stand and bus depot are existed at 400 m distance. • Gap Sagar is existed behind the proposed site at 100m distance. • SPS on Sagwara road is in the middle of Gap Sagar and RIICO which is connected to them via 4 lane NH 927A. • Nearest Household at 20 meters distance. • Required land is only 400 sqm against available land of 4636 sqm.	 Proposes site of SPS

Proposed Structure	Environmental Features	Photo
MWPS Site Uttam Marg near Bhogilal Pandiya Circle, Dungarpur. Latitude- 23°50'24.33"N Longitude- 73°42'40.44"E	• This proposed SPS site is existed on Uttam Marg near Bhogilal Pandiya Circle, Dungarpur. • In the proposed site no tree is observed but behind the site open land area is observed dense tree cover is present. • There is no major habitation near the proposed site. • No wildlife and no forest area will be impacted. • A Municipal Council Depot is present at adjoining of this site. • The Nearest forest area is Rajdhani protected forest block at more than 1500m • MWPS Site Uttam Marg is connected to city through 2 lane city road. • Nearest household at 52 meters distance. • Required land is only 1500 sqm against available land of 4425 sqm.	
Proposed STP at Do River near the Railway Quarter Colony, Dungarpur Latitude- 23°52'6.32"N Longitude- 73°41'37.57"E	• The Proposed STP Site is existed on riverbank of Do River • In the proposed site no tree is observed. • Do riverbed is spread in the valley side/lower side of the proposed site. • In the 1-2 km radius, agriculture fields are observed in which treated effluent can be used for irrigation. • The Nearest forest area is Gumanpura forest block in north-east side and having approx. 2.6 km distance • STP at Do river is connected to 4 lane 927A National Highway. • There is no habitation within the range of 150-250 of Proposed STP location, however 3 nos. cattle shed are existed at 160 m distance and the nearest habitant at 210m distance. • Required land is only 3600 sqm against available land of 28173 sqm.	 Proposes site of STP

Proposed Structure	Environmental Features	Photo
		
Proposed CRMC-1 in Dungarpur at Latitude- 23.836939° Longitude- 73.702243°E	• This CRMC building is proposed in Superintending Engineer Office PHED campus. • No tree will be impacted. • Total required area is 60 sq. m. that is available in PHED campus.	
Proposed MCC Building in Dungarpur at Latitude- 23.833208° Longitude- 73.725841°E	• This MCC building is proposed in Udaivilas PHED campus filter plant Dungarpur. • NO tree will be impacted. • Total required area is 90 sq. m. that is available in PHED campus.	

Proposed Structure	Environmental Features	Photo
Proposed CRMC-2 in Dungarpur at Latitude- 23.836972° Longitude- 73.716226°E	• This CRMC building is proposed in PHED AEN campus. • No tree will be impacted. • Total required area is 60 sq. m. that is available in PHED campus.	

VI. ANTICIPATED ENVIRONMENTAL IMPACTS AND MITIGATION MEASURES

A. Introduction

117. Potential environmental impacts of the proposed infrastructure components are presented in this section. Mitigation measures to minimize/mitigate negative impacts, if any, are recommended along with the agency responsible for implementation. Monitoring actions to be conducted during the implementation phase is also recommended to reduce the impact.

118. Screening of potential environmental impacts are categorized into four categories considering subproject phases: location impacts and design impacts (pre-construction phase), construction phase impacts and operations and maintenance phase impacts.

- i. **Location impacts** include impacts associated with site selection and include loss of on-site biophysical array and encroachment either directly or indirectly on adjacent environments. It also includes impacts on people who will lose their livelihood or any other structures by the development of that site.
- ii. **Design impacts** include impacts arising from Investment Program design, including technology used, scale of operation/throughput, waste production, discharge specifications, pollution sources and ancillary services.
- iii. **Pre-construction impacts** include impacts which are anticipated during construction works but planning are required for proposed mitigation measures before start of construction works i.e. during SIP period such as taking consents from various departments, planning for construction and workers camps, deployment of safety officer, arrangement of required barricades and caution boards etc.
- iv. **Construction impacts** include impacts caused by site clearing, earthworks, machinery, vehicles and workers. Construction site impacts include erosion, dust, noise, traffic congestion and waste production.
- v. **O&M impacts** include impacts arising from the operation and maintenance activities of the infrastructure facility. These include routine management of operational waste streams, and occupational health and safety issues.

119. Screening of environmental impacts has been based on the impact magnitude (negligible/moderate/severe - in the order of increasing degree) and impact duration (temporary/permanent).

120. This section of the IEE reviews possible project-related impacts, in order to identify issues requiring further attention and screen out issues of no relevance. ADB SPS (2009) require that impacts and risks will be analyzed during pre-construction, construction, and operational stages in the context of the project's area of influence. The ADB Rapid Environmental Assessment Checklist has been used to screen the project for environmental impacts and to determine the scope of the IEE.

121. In the case of this project (i) most of the individual elements are relatively small and involve straight forward construction and operation, so impacts will be mainly localized and not greatly significant; (ii) most of the predicted impacts are associated with the construction process, and are produced because that process is invasive, involving excavation and earth movements; and (iii) being located in an urban area, will not cause direct impact on biodiversity values. The project will be in properties held by the local government body and access to the project location is through public rights-of-way and existing roads hence, land acquisition and encroachment on

private property will not occur.

B. Pre-Construction Impacts– Design and Location

1. Location Impacts

122. **Location Impacts of Sewage Treatment Plants.** STP (4.0 MLD) is proposed near Do river on Udaipur road in Zone-6, on vacant government land under Municipal Council. There are no trees present at site, which may be required to cut for construction of STP. There is neither agriculture nor other activities on the proposed land. No wildlife is reported in this area. Agricultural activities are observed at 150m distance around this site. Treated effluent and sludge from STP are proposed for utilized in agricultural and tree plantation purposes. Do river flows near the site and unused/excess treated effluent can be disposed in it. There is no residential or sensitive area within 100 m radius.

123. **Odor Nuisance from STPs.** As presented in the baseline profile, the proposed STP site is currently vacant, and do not have any notable sensitive environmental features. STP site is located near the habitation. The proposed treatment technology, SBR, being an aerobic process and conducted in a compacted and a closed system with automated operation, odor nuisance will be very minimal. Limited bad odors may be generated from wet well, primary treatment units and sludge treatment. Also, to account for future development potential around the sites, and to enhance the environmental benefits following measures should be included in the STP site planning and design:

- (i) Provide a green buffer zone of 10-20 m wide all around the STP with trees in multi-rows. This will act as a barrier, visual screen around the facility and will improve the aesthetic appearance. Treated wastewater shall be used for plantation.
- (ii) Sludge generated from the STP will be used in construction work as block or other purposes.
- (iii) Develop layout plan of STP such that odor generating units (such as sludge/ solids handling facilities) are located away from the residences and in surrounding area with future development potential.

124. **Reuse/discharge of treated effluent.** It is proposed to reuse the treated effluent for irrigation in agriculture, horticulture, development of urban forestry etc. Provision for ground water reservoir and elevated reservoir is made in the contract for the ease of getting required head for reuse in nearby agricultural activities. Although priority is given to reuse of treated wastewater for beneficial purposes following the Sewerage and Wastewater Policy of Government of Rajasthan, discharge point is necessary to provide for excess/surplus or when it is not reused. Therefore it is proposed for discharge of excess treated effluent in to adjacent Do River, when it is not being used.

125. **Location Impacts of proposed SPS sites:** 3 nos. SPS are proposed at Padambhusan Shri Bhogi Lal Pandya Circle, Ashram Vatika and Between RICCO & Gap Sagar. There are some residential areas, Some water bodies and some religious structures near proposed SPS sites. As per preliminary survey, no tree cutting is required for SPSs, If any tree cutting is required for construction works, prior permission from local administration for tree cutting will be required and compensatory plantation as per RUDSICO-EAP policy will also be required. All the precautions should be taken during construction and operation to minimize the impacts on nearby residents and water bodies. Additionally, public consultations should be held near the SPS location to provide project information, type of anticipated disturbances and gain the consent of the nearby

residents for the construction of the proposed SPS.

126. 0.25 MLD MWPS is proposed between RICCO & Gap Sagar location in the govt. land on highway where some market activities like shops are observed. Although there are some shops within the 50 m radius but there is natural gravity flow of sewerage for collection and there is no other alternative site for the gravity flow collection of sewerage, required land for construction of SPS is only 400 sqm against available land of 4636 sqm. Enough land is available for plantation and construction barrier wall between nearby household and SPS. Considering the gravity flow and negative impact of land acquisition, this site was selected.

127. **Locations impacts of Water Supply and Sewerage Networks:** The water supply and sewerage collection networks will traverse through different city roads within ROW. There are no trees coming in the alignment of proposed pipeline works. Therefore, no significant impacts shall be envisaged regarding location; though some temporary disturbances are expected, and mitigation measures will be required to minimize these impacts. Location of intake has been selected to ensure water availability throughout the year and avoid/minimize impact on wildlife species (i.e. crocodiles). These, works will require advance permission from concerned authority for road cutting and traffic diversion etc. If any tree cutting will be required during execution mitigation measures shall be adopted.

128. **Physical Cultural Resources.** There are no notable or significant archaeological places or protected monuments or areas in Dungarpur project area. Therefore, no impacts envisaged but risk of uncovering archaeological remains, given the long history of town, during the excavations cannot be ruled out completely. Construction contractors therefore should follow the below measures in conducting any excavation work:

- (i) Create awareness among the workers, supervisors and engineers about the chance finds during excavation work;
- (ii) Stop work immediately to allow further investigation if any finds are suspected;
- (iii) Inform local Archaeological Department / Museum office if a find is suspected and take any action, they require to ensure its removal or protection in situ; and prepare a chance find protocol.

129. **Tree cutting at project sites.** There is one mango tree (girth size of about 1m) at proposed CWR site at Bori headworks and one neem tree (girth size of about 1m) at proposed site of CWR at PHED campus, New Colony, which may be impacted/required to be cut during construction works. Water pipelines and sewers will be laid along the road within road ROW. There are no notable trees in the alignment; therefore, no major tree cutting is envisaged. Following measures need to be implemented to minimize and/or compensate for the loss of tree cover.

- (i) Minimize removal of trees by adopting to site condition and with appropriate layout design of STP, SPS, CWR or any other site with trees;
- (ii) Obtain prior permission for tree cutting at any site that may require tree cutting finalized during detailed design; and
- (iii) Plant and maintain 3 trees for each tree that is removed.

130. In preliminary design stage, 2 trees may be required to cut. During detail design DBO contractor confirmed cutting of two trees is required (one Mango tree and one Neem tree) at CWR and RWR construction sites. No tree cutting requirement for pipeline works. At this stage higher side of tree cutting numbers are taken as 5 trees. As per RUDSICO-EAP policy; compensatory plantation in the ratio of 1:3 is to be followed during construction works. Therefore 15 numbers of

trees are taken as compensatory plantation. 15 numbers of trees are taken for plantation around STP as mitigation measures to reduce foul smell and 15 numbers of trees are taken for plantation around 3 SPSs.

131. **Design of the Proposed Components.** The Central Public Health and Environmental Engineering Organization (CPHEEO) manual suggests a design period of 15/30 years⁶ in general while designing the systems for water supply and sewerage components. It is proposed to consider 2055 as the design year for all the components in order to maintain unanimity in the design period and design population. Accordingly, 2025 shall be the base year and 2040 the intermediate year to cross check the designs pertaining to intermediate demand. The rate of water supply has been taken as 135 lpcd for 100% population. Sewage generation is 85% of water supply (including 5% to account for infiltration).

132. One of the critical aspects in sewerage system operation is, change in raw sewage characteristics at inlet of sewage treatment plant may affect the process and output quality. STPs are designed for municipal wastewater, which does not include industrial effluent. Characteristics of industrial effluent widely vary depending on the type of industry, and therefore disposal of effluent into sewers may greatly vary the inlet quality at STP and will upset process and affect the efficiency. Although legally the disposal of effluent meeting certain standards is allowed into municipal sewers (refer **Appendix C-8**), the monitoring of the same is not-practical.

133. To prohibit the industrial discharge into municipal sewers following measures should be considered:

- (i) No industrial wastewater shall be allowed to dispose into municipal sewers.
- (ii) No domestic wastewater from industrial units shall be allowed into municipal sewers.
- (iii) Ensure that there is no illegal discharge through manholes or inspection chambers.
- (iv) Conduct public awareness programs; in coordination with RSPCB, issue notice to all industries for compliance.
- (v) Conduct regular wastewater quality monitoring (at inlet and at outlet of STP) to ensure that the treated wastewater quality complies with the national effluent standards.

134. **Design of Sewage Treatment Plant.** One 4.0 MLD STP is proposed to be constructed at the identified site to treat the sewage generated from Dungarpur Town. It is proposed to establish STP based on SBR (sequential batch reactor) process, followed by disinfection by chlorine. As the bid is DBO type, detailed design of the STP will be carried out by the contractor to the following specific discharge standards. Currently for STPs in India, the standards notified by Ministry of Environment, Forests and Climate Change (MOEFCC) in 2017 are applicable. However, under RSTDSP, PMU has decided to base the STP design on discharge standards for STPs suggested National Green Tribunal (NGT) in one of its orders directed MOEFCC in April 2019, which are more stringent. The strident standards also facilitate maximum utilization of treated wastewater for reuse in various purposes following the Sewerage and Wastewater Policy, 2016 of Rajasthan.⁷

⁶ As per CPHEEO, pumps, motors, STP, storage reservoirs are to be designed for a life of 15 years.

⁷ "The use of treated wastewater in irrigation and industrial application shall be given the highest priority and shall be pursued with care. Effluent quality standards shall be defined based on the best attainable treatment technologies, and calibrated to support or improve ambient receiving conditions, and to meet public health standards for end users".

Table 22: Proposed Raw and Treated Wastewater Characteristics for STP Design

S. No	Parameter	Proposed Discharge Standards for Dungarpur STP NGT 2019	MOEFCC STP Discharge Standards, 2017	CPCB discharge standards, 2015	IFC Guideline value for sewage discharge	WHO Guideline Value for safe use in agriculture
(1)	(2)	(3)	(4)	(5)	(6)	(7)
1	pH	6.5 – 9.0	6 – 9	6.0-9.0	6 – 9	6 – 9
2	BOD5, mg/l	≤10	<30	≤10	30	-
3	COD, mg/l	≤50		≤50	125	-
4	TSS, mg/l	≤20	<100	≤10	50	-
5	NH4-N, mg/l	<25	-	≤5	-	
6	Total nitrogen, mg/l	<10	-	≤10	10	-
7	Oil & grease, mg/l	-	-	-	10	-
8	Total phosphorus, mg/l	-	-	-	2	-
9	Fecal Coliform,	<1000	<1000	≤100	-	<1,000
10	Nematodes, number of eggs per litre	-	-	-	-	1

BOD = Biochemical Oxygen Demand; COD = Chemical Oxygen Demand; CPCB = Central Pollution Control Board; IFC = International Finance Corporation, the World Bank Group; TSS = Total Suspended Solids.

135. **Treated wastewater Reuse/disposal.** Rajasthan is a water scarce region and receives low rainfall. Recognizing the importance of treated wastewater in reducing the demand on water, Sewerage and Wastewater Policy, 2016, of Rajasthan promotes the reuse of treated sewage for non-potable applications, and also to make sewerage projects environmentally sustainable. Government of Rajasthan adopted this policy to ensure “improved health status of urban population, specially the poor and under privileged, through the provision of sustainable sanitation services and protection of environment”. To further promote the reuse and provide guidance, Policy prioritized reuse in irrigation (agriculture, forestry, and landscaping), followed by fish farming, industry and non-potable domestic reuse. Policy requires monitoring of treated wastewater quality, soil quality etc. Policy prohibits artificial recharge of aquifers using treated wastewater and promotes construction of storage tanks to store treated wastewater to facilitate reuse. Policy prescribes that the detailed project report (DPR) should clearly define the best reuse option specific to the town and prepare a Reuse Action Plan part of the DPR following water quality norms and legal implications. LSGD is currently in the process of publishing Guidelines for Reuse of Treated Wastewater in Rajasthan 2019 to promote the reuse and provide guidance to the stakeholders. Guidelines promotes the use the treated wastewater and envisages to maximize the collection and treatment of sewage generated and reuse of treated wastewater on a sustainable basis, thereby reducing dependency on freshwater resources.

136. Policy provided priority to reuse in agricultural for unrestricted irrigation. It suggests blending of treated wastewater with fresh water to improve quality where possible, and crops to

be irrigated shall be selected to suit the irrigation water, soil type and chemistry. Policy requires monitoring of accumulation of heavy metals and salinity. It encourages farmers to use modern and efficient irrigation technologies, and to ensure protection of on-farm workers and crops. As a contingency measure, policy requires regular monitoring of treated water quality, and emergency alerts to users in any event of deterioration of quality. Policy prohibits use of treated wastewater for artificial recharge (excerpts from Policy on Reuse is provided in **Appendix C-9**).

137. Reuse Options. Following the Sewerage and Wastewater Policy, 2016, the draft Guidelines on Reuse provides the following reuse applications:

- (i) Agriculture, horticulture, irrigation;
- (ii) Gardening in park;
- (iii) Road washing and water sprinkling to reduce fugitive dust;
- (iv) Industries including mining;
- (v) Recreational ponds and lakes;
- (vi) Social forestry;
- (vii) Construction activities;
- (viii) Firefighting and other municipal uses;
- (ix) Railway;
- (x) Thermal power plants;
- (xi) Cantonments; and
- (xii) Individual users.

138. Allocation of treated wastewater for reuse. City Level Committee (CLC) headed by the district collector will allocate the water for most appropriate uses. According to the proposed procedure, agencies/individuals that require treated wastewater shall apply to the district collector. CLC will allocate water to users. In case of supply is more than the demand of the town, the treated wastewater can be allocated to users within 25 km of STP by the CLC. It may also be made mandatory to industries to use treated wastewater under certain conditions. Memorandum of understanding between ULB and the users of the treated water.

139. Reuse Plan. The State Policy requires the sewerage detailed project report provide reuse options and strategy to implement reuse, and detailed reuse action plan. As the Dungarpur subproject is proposed under DBO, the reuse plan will be prepared by the DBO contractor during the detailed design phase in consultation with the stakeholders in Dungarpur and reuse modalities will be firmed up. Following needs to be considered in the preparation of reuse plan:

- (i) As part of the plan, identify potential reuse application in Dungarpur, and establish quality criteria for each of the use;
- (ii) For applications that use treated wastewater directly (e.g. agriculture), the quality required for such application in safe manner considering health, environment and crop yield concerns shall be ensured;
- (iii) Prepare a reuse plan for agriculture, if that is the priority use or one of the applications as per the CLC in Dungarpur, clearly indicating the limits (geographical/crops/type of application/type of soils etc.); adopt international good practice suggested by agencies like World Health Organization (WHO), Food and Agricultural Organization (FAO) of the United Nations;
- (iv) Plan should include awareness and training provisions and responsibilities; these can be conducted by concerned department (e.g., Agricultural Department, District Collectorate); and
- (v) Carryout regular/online monitoring of critical quality parameters of treated wastewater to ensure that they meet the preset standards established for reuse.

140. **Use of treated wastewater for irrigation.** Use of wastewater for irrigation is associated with some health risks – from germs in wastewater, which may contaminate food and spread disease, health risk to farm workers from worms (helminths) and nematodes and chemical risk is associated if industrial wastewater enters the sewers. If the wastewater with bacteriological contaminants is used for food crops like lettuce, tomato, which are eaten without peeling or cooking, it will present a greater health risk if precaution such as such washing with chlorinated water or storing for adequate time in normal temperature before use (at least 10 days). According to the WHO, effluent which is used to irrigate trees, industrial/commercial (not food, like cotton) and fodder crops, fruit trees, and pasture should have less than one viable nematode egg per liter. Effluent used for the irrigation of food crops, sports fields, public parks, should have and less than one viable nematode egg per liter and less than 1,000 faecal coliforms per 100 millilitres (ml). These shall be considered in the reuse plan that will be prepared during the detailed design and complied accordingly.

141. **Disposal of treated wastewater.** As the wastewater shall be treated to stringent disposal standards, no notable impacts envisaged. The disposal of treated wastewater meeting the set quality standards, in fact, will improve the quality of water by dilution. Proper systems should be put in place at the proposed STP to ensure that treated wastewater at all times meet the stipulated standards prior to its disposal into river. Baseline water quality monitoring of the discharge point should be conducted during the detailed design phase (monsoon flow). Any change/lowering of treatment efficiency during operation may lead to poor quality of wastewater and may further pollute the water body. It is therefore critical that STP treats the sewage as designed. O&M of STP and change in incoming sewage quality will have impact on the treatment efficiency. This therefore requires to:

- (i) Obtain of consent of RSPCB for discharge of treated wastewater into water body;
- (ii) Conduct a baseline water quality assessment of receiving water body ;
- (iii) Regularly monitor the treated wastewater quality at STP and ensure that it meets the discharge standards; and
- (iv) Monitor water quality periodically during operation phase as per the EMP.

142. **Sludge treatment and disposal.** Sewage sludge generally consists of organic matter, pathogens, metals and micro pollutants. The concentration of parameters such as metals can be influenced by input to the sewers system from industry. Since no industrial wastewater is allowed into sewers, it is unlikely that sludge contains heavy metals. Heavy metal concentration may not be ruled out completely as the chemicals used in treatment may potentially contain heavy metals, which will then leach into the sludge.

143. Subproject includes sludge management infrastructure in STP, including system for sludge collection, thickening, solar drying, and disposal at landfill/identified site. This includes a sludge sump to collect sludge from SBR basins; returning arrangement for supernatant from the sump to inlet/equalization tank for treatment; pumping sludge to sludge thickener and pumping thickened to mechanical sludge dewatering system (such as centrifuge). It also requires contractor to establish a shed where the dewatered sludge cake can be further air dried for 15 days. This is indicative sludge management system, and DBO contractor will design the system meeting these requirements. Bid indicates that “the sludge produced from the treatment process would be processed so it may be used as fertilizer and soil conditioner” and it requires DBO contractor “to conform to the regulations of public health and environment protection norms”. This follows the Sewerage and Wastewater Policy, 2016, which suggests “use of sludge produced from the treatment as fertilizer and soil conditioner after processing”. Other solid waste materials from sludge treatment should be covered by an environmentally compliant disposal management plan. Disposal to vacant lot (even if government land) should not be allowed.

144. The treatment and drying processes kill enteric bacteria and pathogens, and because of its high content of nitrates, phosphates and other plant nutrients the sludge is an excellent organic fertilizer for application to the land. Adequate drying is however necessary to ensure maximum kill of enteric bacteria. To achieve adequate drying minimum drying period (15 days) shall be ensured. The drying period, which will be varying depending on the season will be determined during operation and be followed. A sludge management plan will be developed by the DBO contractor during the detailed design phase. Proper sludge handling methods should be employed. Personal protection equipment should be provided to the workers.

145. Contractor will propose the sludge management plan with best methods for reuse of sludge as per guidelines of CPHEEO (guidelines are attached as **Appendix C-10**) and best international practices in consultation with PMU and Municipal Council. Properly dried sludge can be used as soil conditioner. Periodic testing of dried sludge will be conducted to ensure that it does not contain heavy metals that make it unsuitable for food crops. Tests shall be conducted to confirm the concentrations below the following standards. As there are no specific standards notified for sludge reuse, the compost quality standards notified under the Solid Waste Management Rules, 2016 have been adopted here. Rules stipulate that “In order to ensure safe application of compost, the following specifications for compost quality shall be met”, given in **Table 23**.

Table 23: Standards for Sludge Reuse as Manure

Standards for Composting. As there are no specific standards notified for sludge reuse, the compost quality standards notified under the Solid Waste Management Rules, 2016 (Schedule II A, Standards for Composting) have been adopted here. According to the standards “In order to ensure safe application of compost, the following specifications for compost quality shall be met, namely:			
Parameters	Units	Organic Compost (FCO 2009)	Phosphate Rich Organic Manure (FCO 2013)
Arsenic	mg/kg	10	10
Cadmium	mg/kg	5	5
Chromium	mg/kg	50	50
Copper	mg/kg	300	300
Lead	mg/kg	100	100
Mercury	mg/kg	0.15	0.15
Nickel	mg/kg	50	50
Zinc	mg/kg	1000	1000
C/N ratio	-	<20	<20:1
pH	-	6.5 – 7.5	(1:5 solution) maximum 6.7
Moisture, percent by weight, maximum		15.0 – 25.0	25.0
Bulk density	g/cm ³	<1	Less than 1.6
Total Organic Carbon, per cent by weight, minimum	percent by weight	12	7.9
Total Nitrogen (as N), per cent by weight, minimum	percent by weight	0.8	0.4
Total Phosphate (as P ₂ O ₅) percent by weight, minimum	percent by weight	0.4	10.4
Total Potassium (as K ₂ O), percent by weight, minimum	percent by weight	0.4	-

Standards for Composting. As there are no specific standards notified for sludge reuse, the compost quality standards notified under the Solid Waste Management Rules, 2016 (Schedule II A, Standards for Composting) have been adopted here. According to the standards "In order to ensure safe application of compost, the following specifications for compost quality shall be met, namely:			
Parameters	Units	Organic Compost (FCO 2009)	Phosphate Rich Organic Manure (FCO 2013)
Colour			
Odour		Absence of foul Odor	
Particle size		minimum 90% material should pass through 4.0 mm is sieve	minimum 90% material should pass through 4.0 mm is sieve
Conductivity, not more than	dsm-1	4	8.2
* Compost (final product) exceeding the above stated concentration limits shall not be used for food crops. However, it may be utilized for purposes other than growing food crops. FCO = Fertilizer Control Order, Department of Agriculture, Government of India			

146. In order to ensure the safe use of dried sludge, following should be followed:

- (i) Prepare a dried Sludge utilization plan for Dungarpur within the help of Agriculture Department/CLC; plan should also include if any additional processing is required for sludge to use as soil conditioner;
- (ii) Plan should clearly include various potential uses and demand in town and surroundings;
- (iii) Establish usage limits, where required, (geographical/crops/type of application /type of soils etc.); adopt international good practice suggested by agencies like World Health Organization (WHO), Food and Agricultural Organization (FAO) of the United Nations;
- (iv) Identify a landfill/suitable site for disposal of surplus dried sludge;
- (v) Monitor sludge quality during operation phase as per the EMP, ensure that it meets the quality parameters established by FCO; and
- (vi) In case of sludge not meeting the quality parameters, it shall not be used as soil condition, and shall be disposed at appropriate disposal site (if it falls under hazardous category, it shall be disposed as per the Hazardous Waste Management Rules, 2016).

147. **Mixing of industrial effluent in wastewater.** One of the critical aspects in sewerage system operation is, change in raw sewage characteristics at inlet of sewage treatment plant may affect the process and output quality. STP is designed for municipal wastewater, which does not include industrial effluent. Characteristics of industrial effluent widely vary depending on the type of industry, and therefore disposal of effluent into sewers may greatly vary the inlet quality at STP and will upset process and affect the efficiency. While the project does not provide sewerage system in established industrial areas, there is a risk of industrial effluent joining municipal sewers from the small/household units established in town areas where sewers are being provided. Mixing of industrial effluent will severely deteriorate the quality of treated wastewater, and therefore the proposed reuse. Reuse of such water may have significant impact on public health, and on land and water. Following measures should be incorporated to safeguard the sewerage system and the intended reuse:

- (i) No industrial wastewater shall be allowed to dispose into municipal sewers;
- (ii) As there is a risk of potential mixing of industrial waste, no domestic wastewater from industrial units shall be allowed into municipal sewers;
- (iii) Ensure that there is no illegal discharge through manholes or inspection chambers;
- (iv) Conduct public awareness programs in coordination with RSPCB and CLC; and
- (v) Conduct regular wastewater quality monitoring (at inlet and at outlet of STP) to ensure

that the treated wastewater quality complies with the effluent standards.

148. **Design of Sewer system - collection & conveyance.** The sewerage system is designed as a separate system of sewage collection (i.e. caters only to domestic wastewater). There is considerable length of existing surface drains in the project area that can be used for disposal of storm runoff. The underground gravity sewers will carry sewage from households to trunk sewers and further to STP. To maximize the benefits as intended, Dungarpur Municipal Council should ensure that all existing septic tanks are phased out by bypassing the inlet and connecting the toilet discharge from each house directly to sewerage system.

149. Accumulation of silt in sewers in areas of low over time, overflows, blockages, power outages, harmful working conditions for the workers cleaning sewers etc. are some of the issues that needs to be critically looked into during the sewer system design. A properly designed system is a must for system sustainability.

150. Measures such as the following shall be included in sewer system design to ensure that the system provides the benefits as intended:

- Limit the sewer depth where possible
- Sewers shall be laid away from water supply lines and drains (at least 1 m, wherever possible);
- In all cases, the sewer line should be laid deeper than the water pipeline (the difference between top of the sewer and bottom of water pipeline should be at least 300 mm)
- If unavoidable, where sewers are to be laid close to storm water drains, appropriate pipe material shall be selected (stoneware pipes shall be avoided)
- For shallower sewers and especially in narrow roads, use small inspection chambers in lieu of manholes;
- Design manhole covers to withstand anticipated loads & ensure that the covers can be readily replace if broken to minimize silt/garbage entry.
- Ensure sufficient hydraulic capacity to accommodate peak flows & adequate slope in gravity mains to prevent build-up of solids and hydrogen sulfide generation.
- Take necessary precautionary measures to protect sewer network, and to avoid disposal of solid wastes, debris, wastewater into newly laid sewers from the time it is constructed to the start of operation phase.

151. **Faecal Sludge and Septage Management.** The proposed FSSM will help the ULB to cover entire population with safe disposal of human excreta by serving areas which are not feasible to be provided with a sewerage system. Under the FSSM, faecal sludge/septage will be collected from the household level septic tanks using truck mounted mobile desludging equipment and transported to STP for treatment. At this stage, the quantity of septage generated from this area is not available. This will be estimated during the detailed design phase, and number of mobile tankers required to collect the transport the septage to STP, frequency of collection depending on the size of septic tanks etc., will be worked out accordingly. Although handling, transportation and disposal into STP is completely mechanized, the system will however be operated by the workers, therefore proper precautions as workers will be dealing with highly harmful septage. Accessibility of septic tanks to mobile suction tankers to collect septage is critical for success of the septage management system. At STP, the septage will be mixed with the sewage and will be treated combined in the STP. Septage will be in concentrated and partially degraded form, and disposal of the same into STP inlet stream may upset the sewage treatment process, may generate bad odors, and may ultimately affect the quality of treated wastewater.

Treatment process needs to be properly designed. Following measures are suggested for implementation:

- (i) Conduct detailed survey of the households to be covered with FSSM to design the system to suit the local conditions, such as type of septic tanks and their location in the houses;
- (ii) Create awareness program on the FSSM from collection to treatment system that will be adopted;
- (iii) Design the sewage treatment process duly considering mixing of septage;
- (iv) Ensure that the FSSM system is completely mechanized no human touch, even accidentally, from collection at household to discharge into STP, and in periodic cleaning of tankers;
- (v) Demarcate a proper area for cleaning of mobile tankers in STP premises, and ensure that the wastewater shall be discharged into STP;
- (vi) Provide proper training to the workers, and staff in safe handling of FSSM tasks, provide all necessary personal protection equipment, eliminate any risks to the workers and the communities by providing proper training and necessary PPEs to workers. Safeguards induction prior to start of works will include detailed instructions handling, managing and protection from diseases and other biological hazards;
- (vii) Ensure proper facilities for workers including showers, wash areas, toilets, drinking water, eating and resting places;
- (viii) Conduct regular health checks; and
- (ix) Prepare health and safety plan for FSSM.

Design of Water supply components

152. Technical design of the **water supply components** (i) water treatment plants; (ii) raw water and clear water transmissions mains (iii) overhead tanks, and (iv) distribution network, connections, flow meters, etc., follows the relevant national planning and design guidelines, focusing on providing a robust system which is easy to operate, sustainable, efficient and economically viable. Besides, the project also included the following environmental considerations:

- (i) Discontinuation of current unsustainable groundwater wells and keeping only sustainable wells and creating a new comprehensive water supply system based on a nearest surface water sources. Ground water only in case of repair and maintenance of surface water infrastructure and lean season of water
- (ii) To the maximum extent possible nearest surface water source is adopted.
- (iii) Appropriate location of intake to ensure water availability throughout the year, and avoid/minimize impact on wildlife species (i.e. crocodiles)
- (vi) Recovering backwash water from treatment process.
- (vii) Treatment and disposal management of sludge from treatment process.
- (viii) Minimizing water losses from pipelines by perfect jointing and alignments using appropriate techniques (HDPE pipes up to 150 mm dia joined by electro fusion couplers using on-site electro fusion welding, and all higher dia pipes by on site butt welding)
- (ix) Designing the entire system to maintain optimal flow and terminal pressure, and optimising the overall energy usage
- (x) Reducing the incidence of water borne diseases by providing 100% population including urban poor with potable water supplies

(xi) Improve water use efficiency and reduce water wastage at household level by recording and monitoring the water usage, and charging the consumers as per usage; due consideration to urban poor

(xii) Minimize unaccounted for water (UFW) losses using district metered area approach with flow meter and pressure logging arrangements to identify and rectify the leaks, and unauthorized connections

(xiii) Using low-noise and energy efficient pumping systems

Construction near Dimiya dam

Following activities are proposed near Demiya dam

- Installation of SCDA system
- Refurbishment of existing intake structure.
- Replacement of raw water rising mains (Intake to WTP)

153. Construction activities near Demiya dam can have significant impacts on the resident crocodile populations. Understanding these impacts and implementing effective mitigation measures is crucial to ensure the coexistence of human development and wildlife conservation.

Impacts:

154. **Habitat Disruption:** Construction activities may lead to habitat disruption, affecting the natural nesting and basking sites of crocodiles. Excavation, dredging, land reclamation and use of heavy machinery can alter the shoreline and vegetation cover, impacting the crocodiles' habitat.

155. **Disturbance during Nesting Season:** Construction activities may coincide with the crocodile nesting season, causing disturbances that can lead to the abandonment of nests. Vibrations, noise, and human presence can be stressful for nesting females, potentially affecting egg viability.

156. **Increased Human-Crocodile Conflict:** Construction activities near lakes may attract crocodiles to new areas, increasing the potential for human-crocodile conflicts. Encounters between construction workers and crocodiles can pose risks to both parties.

Recommendations

a. **Seasonal Restrictions:** Schedule construction activities to avoid critical periods in the crocodile's life cycle, such as nesting and hatching seasons. Implement seasonal restrictions to minimize disturbances during sensitive times.

b. **Buffer Zones:** Establish buffer zones around known crocodile habitats where construction activities are restricted. This helps maintain undisturbed areas crucial for crocodile nesting and other essential behaviour.

c. **Maintain dead storage in dam :-** Do not utilize the dead storage of dam for supply; ensure that dead storage is always available in the dam all times; limit the abstraction to allowable limits

d. **Educational Programs:** Conduct educational programs for construction workers, local

communities, and relevant stakeholders. Raise awareness about the presence of crocodiles, their behaviour, and the importance of coexisting with these species.

e. **Secure Construction Sites:** Implement measures to secure construction sites, such as fencing and signage, to prevent crocodile ingress. Restrict access to areas where crocodile presence is likely, minimizing the risk of encounters.

f. **Wildlife Monitoring and Rescue Teams:** Establish wildlife monitoring teams to track crocodile movements during construction. Implement rescue teams trained to safely relocate crocodiles away from construction sites if necessary.

g. **Environmental Best Practices:** Adopt environmentally friendly construction practices to minimize habitat disturbance. Use silt fences and erosion control measures to prevent sedimentation in water bodies, maintaining water quality for crocodile habitats.

h. **Collaboration with Conservation Agencies:** Collaborate with local wildlife conservation agencies like forest department, NGOs to develop and implement effective mitigation measures. Engage in research and conservation efforts to better understand and protect crocodile populations in the area. Further this site can be developed as bird and Crocodile conservation and watching site

Selection of Source for water supply

35. To meet total water demand, there are 3 nos. surface water sources are proposed for town, Surface water source include Edward Samand Dam (4.54 MLD), Vijay Chakra Sagar dam (3.1 MLD) and Somkamla Amba dam (4.361 MLD). Along these surface water sources additionally 4 existing ground water sources including 2 tube wells and 2 open wells, proposed for lean season when surface water source have less amount of water. All these sources are already existing, and no new source development is required for the sub-project.

- **Vijay Chakra Sagar Dam:** The earthen dam with masonry opening is located on Moran River, a tributary of mahi river at the coordinate 23°46'44.82"N and 73°46'5.69"E near Dimiya village is a drinking water reservoir owned by WRD, GOR. The water of this reservoir is reserved only for drinking water for Dungarpur. Capacity of this dam is 44.87 MCFT including dead storage and 40 MCFT (1.27 MCM) is live storage. The PHED has allocated 3.1 MLD (1.18 MCM) water for Dungarpur water supply subproject, which is about 93.40% of total water available in dam. The existing water abstraction of water from dam is 3.25 MLD and proposed capacity is 3.1 MLD. The water from dam is not used for irrigation or any other activity.



a) **Selection of Site:** Dam already connected with the existing **water supply** system are sustainable sources with respect to quantity & quality; Presently the existing intake well for pumping raw water from Dimiya dam is in back water of dam, during the summer season water is to be brought near existing pump house by the centrifugal submersible pumps. So in order to get the maximum benefit in pumping the raw water during severe drought conditions a new intake was proposed near the spillway section of the Vijay Chakra Sagar dam (Dimiya dam), which is now dropped after findings of detailed bathometric survey report.

b) **Gauge level of Dam**

Since the construction of the Dimiya dam PHED has continuously maintained the daily water level and storage capacity details of the same are as follows: -

Table 24: Gauge Details of VIJAY CHAKRA SAGAR (DIMIYA) DAM

S.no.	Year	Gauge of Dam	Filling of Dam	Vol. of Dam	Remark
1	2010	29 Feet	29 Feet	40 McFt	Full
2	2011	29 Feet	29 Feet	40 McFt	Full
3	2012	29 Feet	29 Feet	40 McFt	Full
4	2013	29 Feet	29 Feet	40 McFt	Full
5	2014	29 Feet	29 Feet	40 McFt	Full
6	2015	29 Feet	29 Feet	40 McFt	Full
7	2016	29 Feet	29 Feet	40 McFt	Full
8	2017	29 Feet	29 Feet	40 McFt	Full
9	2018	29 Feet	29 Feet	40 McFt	Full
10	2019	29 Feet	29 Feet	40 McFt	Full
11	2020	29 Feet	29 Feet	40 McFt	Full
12	2021	29 Feet	29 Feet	40 McFt	Full

The existing production capacity of reservoir is 3.1 MLD, same will be continue for the subproject after proposed repair and maintenance works.

c) **Distance from STP**

4 MLD STP is proposed at Do River, Udaipur Road (Dungarpur) which is 18.4 km away from Vijay Chakra Sagar Dam. No direct drain from STP site is connected with Vijay Chara Sagar Dam.

36. **Edward Sagar Dam (Durgapur reservoirs):** Situated on Do river, a seasonal stream is a drinking water reservoir owned by PHED, GOR water of this reservoir is reserved only for drinking water for Dungarpur. Capacity of this dam is 137 MCFT (3.879 MCM) live storage. The PHED has allocated 4.54 MLD (1.66 MCM) water for Dungarpur water supply subproject, which is about only 42.79 % of total storage capacity of dam.

37. The water from dam is not used for irrigation or any other activity. The PHED has recorded yearly water level data of dam and as per water level data of past 12-year, the dam was filled fully up to its storage capacity in all 12 years. CWR, Pump house and WTP are already existing on dam and are connected with existing water supply system of Dugarpur town.

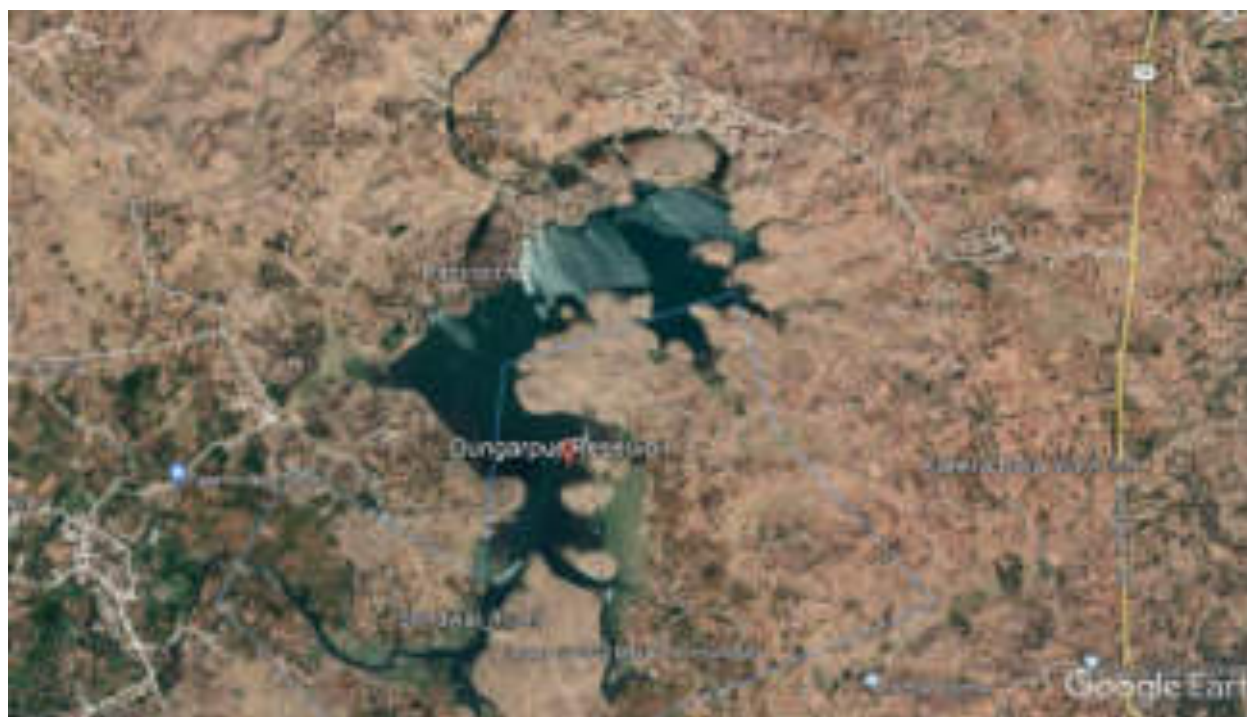


Table 25: Water Quantity Report of Edward Sagar Dam

Gauge Details of Edward Sagar Dam (Dungarpur reservoir)					
S.no.	Year	Gauge of Dam	Filling of Dam	Vol. of Dam	Remark
1	2010	29 Feet	29 Feet	134 McFt	Full
2	2011	29 Feet	29 Feet	134 McFt	Full
3	2012	29 Feet	29 Feet	134 McFt	Full
4	2013	29 Feet	29 Feet	134 McFt	Full
5	2014	29 Feet	29 Feet	134 McFt	Full
6	2015	29 Feet	29 Feet	134 McFt	Full
7	2016	29 Feet	29 Feet	134 McFt	Full
8	2017	29 Feet	29 Feet	134 McFt	Full
9	2018	29 Feet	29 Feet	134 McFt	Full
10	2019	29 Feet	29 Feet	134 McFt	Full

11	2020	29 Feet	29 Feet	134 McFt	Full
12	2021	29 Feet	29 Feet	134 McFt	Full

38. **Sustainability and environmental considerations of Edward Sagar Dam.** The Edward Samand dam has the total storage of 137 McFt excluding the dead storage of the dam. For proposed water supply project only 4.54 MLD i.e. about 61 McFt water is proposed to be drawn from the source. Water abstractions from this dam on gravity basis and capacity of existing WTP, 11 feet water storage is maintained as dead storage.

39. Given the small storage compared to the total volume of water available in the dam, no significant impacts envisaged on downstream. Given the small size of dam, there are no notable sensitive environmental features. There is no notable, protected or unique aquatic plant/creatures. The Aquatic life in the river is limited to local common species of fishes and aquatic plants and the fish is limited to local varieties (such as Rohu, Katla, and water snakes). There is no commercial fisherman activity take place in these dams.

40. No notable sensitive features are found. There is no forest area in the downstream of the proposed intake. Removal of trees and vegetation will not require during implementation phase as the work is confined to within dam site only.

Distance from STP

41. STP of 4 MLD is proposed at Do River, Udaipur Road which is 13 km away from Edward Sagar Dam. MSL of Proposed STP site and Edward Sagar Dam are 267m and 312 respectively. Proposed STP site and Edward Sagar Dam are corrected through a drain but runoff discharge is from Edward Sagar Dam to STP site therefore no adverse impact of STP to Dam.

Ground Water Source: Development of Ground Water sources. At present there are 7 Nos Tube wells and 15 Nos Dug Wells / Open wells, out of these existing TW/ OW, 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desilting, with re commissioning work. The ground water will be used in Lean Season or during repair maintenance works in infrastructures supplying surface water *and details of existing tube wells & open wells are as follows.* –

Table 26: Details of proposed wells

S. No.	Location	Type	No.	Production Per Day (In KL)
Tube Wells				
1.	Patrakar colony TW	Tube well	1	500
2.	Darjiwada TW	Tube well	1	500
	Total		2	1000
Open Wells				
1.	Rani Bao OW	Open well	1	1000
2.	Kelabao OW	Open well	1	1000
	Total		2	2000

Based on the reports, it was finalized that out of the complete water requirement for the project only 1.5 MLD water will be taken from the ground water source.

Sustainability and environmental considerations of Ground water sources. 1.5 MLD of the total requirement of the proposed project is planned to be taken from ground water sources. As

per the data available, a total of 3 MLD water is available in the ground water sources. 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desalting, with re commissioning work. The ground water will be used only in lean season and repair and maintenance works when less amount of surface water will be available.

42. **New proposed Som Kamala Amba (SKA) Dam on Som River:** The construction of Som Kamla Amba Dam was completed in the year 2000. This dam is located in Ashpur Tehsil of Dungarpur District, Rajasthan to provide the Irrigation cum drinking water facilities. The dam supplies 8.1 MCM drinking water and irrigation supply to 26998.6 ha of Gross Command Area (GCA) and 19155.42 ha of Culturable Command Area (CCA).



Table 27: Details of Sam Kamla Amba Dam

Project	Som Kamla Amba Project
River	Som river, a tributary of Mahi
Lat/Long	23° 58' 00" / 74° 02' 00"
GCA	26998.60 ha
CCA	19155.42 ha
Annual water supply	8.01 MCM
Catchment Area	5376 sq km
Main Dam	
Type	Earthen Dam
Length	620 m
Top elevation	217.50 m
Height of dam above lowest river bed level	27 m
Lowest river bed level	190.5 m
Reservoir	
Maximum water level	215.50 m
Full Reservoir Level	33.50 m
MDDL	200.50 m
Live storage	160.30 MCM
Gross storage	172.80 MCM

Reservoir spread area	36.18 sq km
Year of start of construction	1992
Date of completion	2000
Year of first impoundment	2004

43. To meet out the shortfall demand of surface water for the town Dungarpur, the state Government has sanctioned a public importance project namely Drinking Water Supply Project for 151 Villages and 1 town of District Dungarpur (Dungarpur town itself) based on Som Kamla Amba Dam on Som River. Presently the project is under execution, transmission main from the Som Kamla Amba Dam to Dungarpur town has been laid and construction work of intake well and water treatment plant is under progress. As per PHED officials project will be commissioned up to December 2022.

44. Som Kamla Amba Scheme: This is a scheme under PHED which proposes to take water from Som Kamla Amba Dam and supplies water to 151 villages and Dungarpur town itself. This project is under construction and the tentative date of completion is in December 2022.

45. Location: The dam is located at the coordinate 23°58'11.05"N and 73°58'56.77"E on Som River, tributary to Mahi River. The rising main of this scheme has already been laid and will supply water proposed for Dungarpur town at Bhogilal Pandya Circle.

Table 28 water availability in Somkamla Amba dam

S. No.	Year	Maximum live storage attained in the reservoir (MCM)	Designed live storage (MCM)	Reservoir storage efficiency
1	1999	82.9	160.3	52%
2	2000	47.2	160.3	30%
3	2001	163.8	160.3	100%
4	2002	69.8	160.3	44%
5	2003	157.5	160.3	98%
6	2004	172.8	160.3	100%
7	2005	172.8	160.3	100%
8	2006	172.8	160.3	100%
9	2007	172.8	160.3	100%
10	2008	100.6	160.3	100%
11	2009	133.4	160.3	100%
12	2010	170.1	160.3	100%
13	2011	171.3	160.3	100%
14	2012	172.8	160.3	100%
15	2013	172.6	160.3	100%
16	2014	152.6	160.3	100%
17	2015	172.8	160.3	100%
18	2016	172.8	160.3	100%
19	2017	172.8	160.3	100%
20	2018	172.8	160.3	100%
21	2019	172.8	160.3	100%
22	2020	172.8	160.3	100%
23	2021	172.8	160.3	100%

Maximum Live storage stained in the Som Kamla Amba Dam. (Source: WRD, 2021).

46. **Details of Dam:** - As per the report published by World Bank for Dam Rehabilitation and

Improvement Project (Drip II). The construction of Som Kamla Amba Project across Som river, a tributary of Mahi river was completed in the year 2000. The dam is located in Ashpur Tehsil of Dungarpur District, Rajasthan to provide the Irrigation cum drinking water facilities. This dam supplies drinking water to the town with the capacity of 8.1 MCM., besides irrigation supply to 26998.6 ha of Gross Command Area (GCA) and 19155.42 ha of Culturable Command Area (CCA). It is proposed to fulfil 4.36 MLD in the year 2055 and as this project is designed to fulfil the requirement of Dungarpur. Summary of DPR report for proposed works for Dungarpur water supply is provided in appendix 4.

47. **Sustainability and environmental considerations of Som Kamla Amba Dam** Capacity of dam at FTL of 213.5 is 172.75 MCM and live storage capacity 160 MCF there is 93.75 % dependability of required 47.33 MCF quantity for Dungarpur town on the basis of past 15-year record of storage of Sam Kamla Amba dam. The intake WPT and transmission lines from dam to down are already under construction by PHED and water will be available in town by December 2022.

48. **Proposed works** The DPR of the project was prepared by the PDCOR limited. Work has been awarded and under execution, under this project there is provision of Intake Structure at Som Kamla Dam levels of the proposed for different stages of intake structure are as below:-

- Top Bank Level of Dam 217.50 m
- F.T.L. of Dam 213.50 m
- Sill level of Dam 200.50 m
- Lowest level on upstream side of dam 193.00 m
- Maximum Water Depth 20.50 m
- Top level of Intake structure 217.50 m

49. Length of the approach bridge to access the Intake is approx. 75m. Raw water pumping main is 600 mm DI k-7 for a length of 850 m. RWPS is proposed at Som Kamla Amba dam to pump raw water received through intake structure to pump water to WTP located at Main Head Works near Aspur. Capacity of the WTP is 21.90 MLD for phase-I demand and will be upgraded to 29.01 MLD for upcoming village scheme. 3000 KL CWR with pump house is to be constructed at WTP campus to transfer water to Dungarpur town. 45 kms clear water pumping main under laying dia. varying from 650 mm to 300 mm. Status note of Som Kamla Amba Dam is attached received from EE,PHED, Project. Estimated time for completion of this project is end of 2022.

C. Environmental Audit of Existing Water Supply Infrastructure

50. It is designed to utilize existing water supply infrastructure like tube wells, clear water reservoirs, pump houses etc. with necessary improvements. As per the ADB SPS 2009, these are associated facilities and therefore the component operation shall comply with the ADB and applicable environmental laws of India. Besides, ADB SPS lays emphasis on impacts and risks on biodiversity and natural resources, pollution prevention abatement including hazardous waste, occupational health and safety, community health and safety, and physical cultural resources. A random environmental audit is conducted to (i) assess the compliance of the existing infrastructure with environmental legislations and (ii) improve environmental performance to minimize future potential liabilities. The preliminary audit note is given in **Appendix 3**. A more detailed environmental audit and risk assessment shall be carried out during detailed design stage and incorporated into the final IEE.

51. All the existing infrastructure facilities are located in Dungarpur town, which is an urban area

and where there are no protected or sensitive environmental areas such as forests, wildlife sanctuaries or archeologically protected areas. Therefore, there are no risks or impacts on biodiversity and natural resources. The designed project will optimally utilize the surface and groundwater sources. Due to nature of components, the existing infrastructure components do not fall under the ambit of any environmental related regulations, and therefore there is no requirement of permissions or clearances. Presence of Asbestos Containing Material (ACM) in the form of asbestos cement pipes in the existing water supply infrastructure is a cause of concern due to its potentially hazardous nature. Project, however, do not include rehabilitation or repair of AC pipes, and the project, in fact, designed to discontinue the use of AC pipes. Presence of AC pipes in the existing facilities may create hazardous conditions for the workers and surrounding community. Besides, the generation and disposal of debris and discarded materials, and construction phase health and safety need to be considered and mitigated to comply with the SPS provisions. Following **Table 29** provides component wise compliances and concerns. Corrective actions for the identified environmental concerns are discussed in the following section.

Table 29: Environmental Audit of Existing Facilities

Infrastructure	Details	Designed Rehabilitation	Compliance with environmental regulatory framework	Environmental Concerns
3.2 MLD WTP at Bori Head Works	Location: PHED Bori Head Works Year of Construction of RGF Units : 1: 2002 and Unit 2: 2007 Technology: RGF Total Area: 3500 sq.m Quantity of Sludge generated from WTP: 400 kg/month Disposal: For the plantation in nurseries	Repairing RGF units and replacement of pipes, submersible pumps, cables, panels, valves, flow meters and synchronization with SCADA enabled devices Depth of the tube wells will not be increased.	CTE will be taken before start the refurbishment work and CTO will be taken before start the operation.	Occupational health and safety, public safety during the construction works
4.54 MLD WTP at Udai Vilas Head Works.	Location: PHED Udai Vilas Head Works Year of Construction: 1990 Technology: RGF Total Area: 2800 sq.m Quantity of Sludge generated from WTP: 300 kg/month	Civil works, Cleaning, and replacement of pipes, submersible pumps, cables, panels, valves, flow meters and synchronization with SCADA enabled devices	CTE will be taken before start the refurbishment work and CTO will be taken before start the operation.	Occupational health and safety, public safety during the construction works

Infrastructure	Details	Designed Rehabilitation	Compliance with environmental regulatory framework	Environmental Concerns
	Disposal: For the plantation in nurseries			
2. Tube wells and 2. open wells	• Patrakar colony TW, • Darji wada TW • Rani Bao OW, • Kela bao OW,	Replacement of pipes, submersible pumps, cables, panels, valves, flow meters and synchronization with SCADA enabled devices	No requirements under existing laws	Occupational health and safety, public safety during the construction works Disposal of discarded material, debris There are no asbestos containing material / AC pipes noticed
1 Raw water Storage	Bori (RCC) 235 KL	Civil repairs and rehabilitation, replacement of pipes, connections, electrical and mechanicals parts as required Cleaning	No requirements under existing laws	Storage of AC pipes in existing campus Occupational health and safety, public safety during the construction works Disposal of discarded material, debris including AC pipes
4 Clear water reservoirs (CWRs)	1. Udaivilas, RCC CWR, 325 KL 2. Bori, RCC CWR, 325 KL 3. AEn, Office Masonry CWR, 263 KL	Civil repairs and rehabilitation, replacement of pipes, connections, electrical and mechanicals parts as required Cleaning	No requirements under existing laws	NO storage of AC pipes in existing campus Occupational health and safety, public

Infrastructure	Details	Designed Rehabilitation	Compliance with environmental regulatory framework	Environmental Concerns
	4. New colony / Nai Abadi, RCC CWR, 272 KL			safety during the construction works Disposal of discarded material, debris including AC pipes
04 GLSR and 08 OHSRs	- Meera Dungari GLSR (Zone 04) 225 KL - Khantwara GLSR (Zone 05) 225 KL - Ghati GLSR new (Zone 07) 368 KL - Ghati (II) GLSR (Zone 08) 450 KL - New Rajpura OHSR (Zone 01) 150 KL - Navadera OHSR (Zone 02 A) 325 KL - Shastri Colony OHSR (Zone 09) 100 KL - Ptrakar Colony OHSR (Zone 15) 140 KL - Sindhi Colony OHSR (Zone 10) 325 KL - Pratap Nagar OHSR (Zone 11) 75 KL - Mordern School OHSR (Zone 13) 210 KL - Ashok nagar OHSR (Zone 16) 113 KL	Civil repairs and rehabilitation, replacement of pipes, connections, electrical and mechanicals parts as required Cleaning	No requirements under existing laws	Presence of AC pipes in existing connections Occupational health and safety, public safety during the construction works Disposal of discarded material, debris including AC pipes
07 Pumping stations	- Udaivilas RGF PH-(I) (Size 7mX8m) - Main pump house (Size 5mX7m)	Civil works, all New pump houses are proposed and old will be phased put	No requirements under existing laws	Presence of AC pipes in existing connections Spillage of oils, lubricants etc.,

Infrastructure	Details	Designed Rehabilitation	Compliance with environmental regulatory framework	Environmental Concerns
	3. Chandpole pump house (Size 5mX7m) 4. Bori RGF (I) (Size 4mX5m) 5. Bori RGF (II) (Size 4mX5m) 6. Nai Abadi GLR-1 (Size 5mX10m)			Occupational health and safety, public safety during the construction works Disposal of discarded material, waste oils, mechanical and electrical parts, debris including AC pipes
Transmission and distribution	Water Collected in CWR (from 2 Dams and 2TWs) and is transferred through DI transmission line to each OHSR. DI transmission mains AC (27.79 Km), DI (21.37 Km), GI (0.09 Km) and CI (3.87 Km) which are functioning properly are proposed to be retained.	No works proposed All AC pipes will be replaced by new distribution lines	No requirements under existing laws	Exact location and condition of AC pipes not known; no maps available. Accidental disturbance / need to remove in narrow roads Occupational health and safety, public safety during trenching

52. Corrective Measures. As presented in the above table, there are no regulatory non-compliance issues in the existing infrastructure other WTP Plant where CTE and CTO are not taken. The environmental concerns are mainly related to occupational health and safety, public safety, disposal of debris, discarded materials etc. A work specific environmental management plan needs to be prepared for these aspects. The exact nature of rehabilitation and repair works will be known only during the detailed design phase as the detailed technical audit will be conducted by the DBO contractor and the required rehabilitation and repair measures will be designed accordingly. Therefore, a separate EMP will be prepared for rehabilitation works during the detailed design phase by the DBO contractor, and reviewed and approved by PMU/consultants, and the same will be implemented by the DBO contractor. These are included in the EMP.

53. **Asbestos Containing Materials (ACM) Management.** Presence of ACM, mainly asbestos cement pipes, in the existing infrastructure is the main concern. Asbestos is recognized as a cause of various diseases and is considered health hazard if inhaled.

54. The old existing underground water transmission and distribution system consists asbestos cement pipes. Most of the asbestos cement pipes in the existing water supply are old and all these AC pipes are planned to be phased out after laying the new water supply networks. Since use of AC pipes are banned all over the India, there is no use of new asbestos cement pipes but for repairing work in the existing network, and for replace the damaged sections, asbestos cement pipes are being used. There will be no use of any asbestos cement pipe in the future as under the present project, water supply network is being provided in the entire town with non-asbestos cement pipes. It is normal practice in Rajasthan that existing asbestos cement pipes are left as it is in the ground and new pipes will be laid in a new alignment. As per the discussion with the PHED staff in Durgapur, there are about 94 kms of AC pipes in existing water supply distribution networks. Existing asbestos cement pipes are laid long back, they are deep in ground, more than 2 m at many places, as the road level has risen considerably. In wider roads, there will be adequate space to lay the new pipelines, and therefore there is no need to remove the existing pipelines.

55. However, complete avoidance of handling and disposal of asbestos cement pipes may not be possible. There are narrow lanes, where asbestos cement pipes may be encountered during the laying of new pipes. Some connections/inlet/outlet pipes at the existing CWRs are also of asbestos cement pipes. These will be removed and replaced with new non-asbestos cement pipes. At present no maps available on the exact location/position of asbestos cement pipes.

56. A temporary storage area shall be provided in the project site by the PIU. Asbestos materials present and removed from the construction activities will be temporarily maintained at the identified area. The temporary storage area shall be constructed by the DBO contractor based on the specifications of the asbestos management service contractor.

57. Bureau of Indian Standards (BIS) Guidelines for Safe Use of Products containing asbestos states that “asbestos cement products (such as asbestos cement pipes) generally contain about 10-15% asbestos fibers in a cement matrix that comprises the rest of the materials and are termed as locked in asbestos products as these products have the asbestos fibers bound in cement. There is very little possibility of generation of airborne asbestos fibers during any reasonable handling, storage, and use of such products. However, during storing and installation, recommended work practices shall be followed to avoid harmful exposure”. According to Hazardous and other Wastes (Management and Transboundary Movement) Rules, 2016, any waste having asbestos concentration limit of 10,000 mg/kg (i.e. 1%), however this will apply only if the asbestos containing substances are in a friable, powdered or finely divided state. Under the Basel Convention,⁸ asbestos or asbestos waste in the form of dust and fibers is classified as hazardous waste.

58. Working with or handling asbestos cement pipes in a manner that produces dust, fibres, air borne particles etc., is very harmful and hazardous to the workers and general public around the work sites. The condition of existing underground asbestos cement pipes is not known, however, as these are old, pipes may be in deteriorated conditions. Condition needs to be assessed to

⁸ Basel Convention on the Control of Transboundary Movements of Hazardous Wastes and their Disposal, adopted in 1989.


check whether it is in friable form or in a condition in which it can release fibres before it is subjected any disturbance or removal.

59. As per above discussions, it is therefore obvious that specific measures are necessary to safeguard the health and safety of the project workers and nearby communities; consistent with the requirements of the ADB SPS, 2009. Activities such as clearing, transfer and disposal of asbestos cement pipes, work in narrow streets, and interventions in existing asbestos cement pipes may have adverse impacts on workers and surrounding population. Air borne asbestos if handled unsafely, cut, drilled or broken into pieces that may cause health issues such as Inflammation of the lungs, mesothelioma, peritoneal mesothelioma, pleural plaques, asbestosis and bronchogenic carcinoma. Following measures are to be implemented to avoid any impacts:

- (i) Develop and implement the ACM Management Plan (AMP) that includes identification of hazards, the use of proper safety gear and disposal methods. Sample AMP is provided in **Appendix C-20**. Adhere to the workflow process suggested in **Figure 24**;
- (ii) Conduct awareness program on safety during the construction work;
- (iii) Undertake the construction work stretch-wise; excavation, pipe laying and trench refilling should be completed on the same day;
- (iv) Provide barricades, and deploy security personnel to ensure safe movement of people and also to prevent unnecessary entry and to avoid accidental fall into open trenches;
- (v) Identify risk of intervention with existing asbestos cement pipes. If there is significant risk, implement the AMP strictly that includes identification of hazards, the use of proper safety gear and disposal methods;
- (vi) Appropriate actions as defined in the AMP will have to be adhered to; and
- (vii) Maintain records of asbestos cement pipes as per the AMP.

Figure 24: ACM Management Plan – Work Process Flow Chart

ANNEX 1 – ACM Management Plan

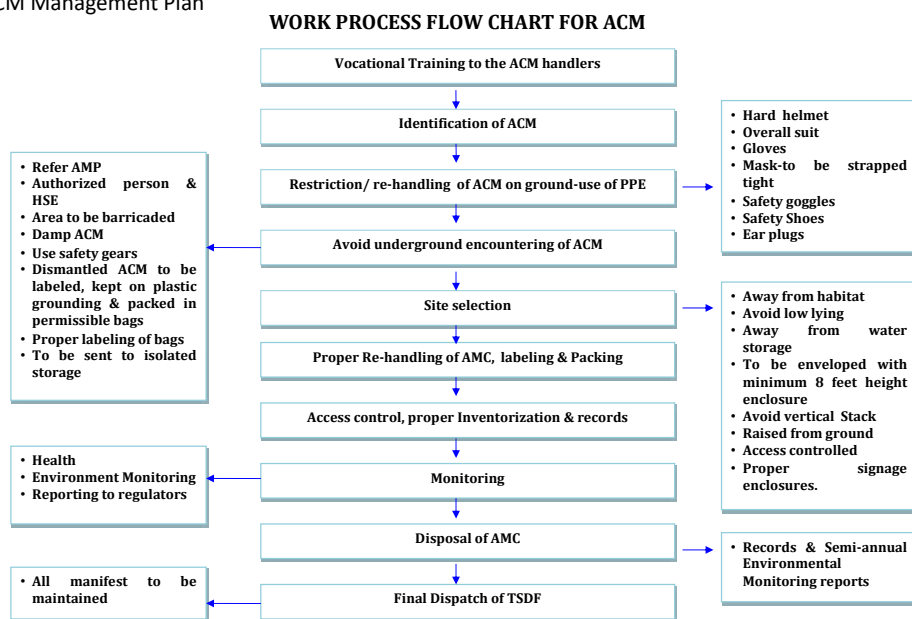

60. Requirement for the contractor and the subcontractor. The following are operational requirements related to works involving asbestos:

- (i) engaging certified and competent asbestos service provider to identify, handle and remove the asbestos materials present and encountered in the project sites;
- (ii) adopting good practices per EHS Guidelines⁹ to minimize the health risks associated with asbestos materials by avoiding their use in new construction and renovation, and, if installed asbestos-containing materials are encountered, by using internationally recognized standards and best practices to mitigate their impact;¹⁰
- (iii) training of workers and supervisors, possession of (or means of access to) adequate equipment and supplies for the scope of envisioned works, and a record of compliance with regulations on previous work;
- (iv) removal, repair, and disposal of ACM shall be carried out in a way that minimizes worker and community asbestos exposure, and require the selected contractor to develop and submit a plan, subject to the PMU and PIU's acceptance, before doing so;
- (v) providing adequate protection to its personnel handling asbestos, including respirators and disposable clothing; and
- (vi) notifying the Rajasthan State Pollution Control Board (RSPCB) of the removal and disposal according to applicable regulations as indicated in the technical requirements and cooperating fully with representatives of RSPCB during all inspections and inquiries.

61. PMU will engage an asbestos management specialist to provide training and awareness, and to coordinate with various stakeholders on the risks, management, and mitigation measures required for the identification, safe handling, transport and disposal of the asbestos materials.

D. Pre-construction Impacts

62. **Utilities.** Telephone lines, electric poles and wires, water lines within the proposed project locations may require to be shifted in few cases. To mitigate the adverse impacts due to relocation of the utilities, the contractor, in collaboration with ULB will

- identify the locations and operators of these utilities to prevent unnecessary disruption of services during construction phase; and
- (ii) instruct construction contractors to prepare a contingency plan to include actions to be done in case of unintentional interruption of services.

⁹ ADB SPS specifies application of pollution prevention and control technologies and practices consistent with international good practice, as reflected in internationally recognized standards such as the World Bank Group's *Environment, Health and Safety (EHS) Guidelines*. These standards contain performance levels and measures that are normally acceptable and applicable to projects. When host country regulations differ from these levels and measures, the borrower/client will achieve whichever is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the borrower/client will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in this document.

¹⁰ The EHS Guidelines specify that the use of ACM should be avoided in new buildings and construction or as a new material in remodeling or renovation activities. Existing facilities with ACM should develop an asbestos management plan that clearly identifies the locations where the ACM is present, its condition (e.g., whether it is in friable form or has the potential to release fibers), procedures for monitoring its condition, procedures to access the locations where ACM is present to avoid damage, and training of staff who can potentially come into contact with the material to avoid damage and prevent exposure. The plan should be made available to all persons involved in operations and maintenance activities. Repair or removal and disposal of existing ACM in buildings should be performed only by specially trained personnel following host country requirements or, if the country does not have its own requirements, internationally recognized procedures. Decommissioning sites may also pose a risk of exposure to asbestos that should be prevented by using specially trained personnel to identify and carefully remove asbestos insulation and structural building elements before dismantling or demolition.

63. Site selection of construction work camps, stockpile areas, storage areas, and disposal areas. Priority is to locate these near the project location. However, if it is deemed necessary to locate elsewhere, sites to be considered will not promote instability and result in destruction of property, vegetation, irrigation, and drinking water supply systems. Residential areas will not be considered for setting up construction camps to protect the human environment (i.e., to curb accident risks, health risks due to air and water pollution and dust and noise and to prevent social conflicts, shortages of amenities and crime). Extreme care will be taken to avoid disposals near forest areas, water bodies, swamps or in areas which will inconvenience the community. Construction sites will be selected by DBO contractor in compliance with these conditions and the same will be reflected in Site Environmental Management Plan (SEMP) which is to be prepared by DBO contractor prior to start of construction and approved by PIU.

64. Site selection of sources of materials. Extraction of materials can disrupt natural land contours and vegetation resulting in accelerated erosion, disturbance in natural drainage patterns, ponding and water logging, and water pollution. To mitigate the potential environmental impacts, locations of quarry site/s and borrow pit/s (for loose material other than stones) would be assessed by PIU. Priority would be sites already permitted by Mines and Geology Department. If new sites are necessary, these would be located away from population centers, drinking water intakes and streams, cultivable lands, and natural drainage systems; and in structurally stable areas. It will be the construction contractor's responsibility to verify the suitability of all material sources and to obtain the approval of Department of Mines & Geology and local revenue administration. If additional quarries will be required after construction is started, then the construction contractor shall use the mentioned criteria to select new quarry sites, with written approval of PIU. DBO contractor will identify sources of water for construction purposes and obtain necessary permissions as required, and approval of PIU before the use. Details of material sources and water sources will be provided in SEMP.

65. Debris disposal. Prior to the commencement of works, contractor shall identify a debris disposal site in consultation with the PIU and Consultant. Contractor will follow all the prescribed rules¹¹ during construction and adhering to following criteria (including but not limited to)-

- The site shall be selected preferably from barren, infertile lands. In case agricultural land needs to be selected, top-soil stripping, stacking and preservation should be undertaken prior to initiation of any activities.
- The local governing body and community shall be consulted while selecting the site.
- Contractor shall prepare a construction and demolition waste management plan in pre-construction phase for safe disposal of construction and demolition wastes as per applicable rules and submit to Municipal Council through PIU for approval
- Debris disposal site shall be at least 200 m away from surface water bodies¹².
- No residential areas shall be located within 100 m downwind side of the site.
- The site is minimum 250 m. away from sensitive locations like hospitals, religious places, ponds/lakes or other water bodies.

Construction Impacts

66. The civil works for the subproject include earth work excavation for sewer trenches, sewer

¹¹ Construction and Demolition Waste Management Rules 2016 (refer appendix 8)

¹² In the absence of site meeting the stipulated criteria, an alternate site can be selected specifying the reasons. In such a case, the construction camp management plan should incorporate additional measures specific to the site as suggested by the Construction Manager.

laying, construction manholes, shifting of public utilities and providing house service connections. Earth work excavation will be undertaken by machine (backhoe excavator) and include danger lighting and using sight rails and barricades at every 100 m., while sewer laying works will include laying sewer at required gradient, fixing collars, elbows, tees, bends and other fittings including conveying the material to work spot and testing for water tightness.

67. Refurbishment of existing intake. To avoid impacts on the local biodiversity in the Dimiya Dam, the following measures must be implemented:

Following mitigation measures are proposed;

- (i) Prepare Environment management plan before starting any work;
- (ii) All project related site staff, construction workers and supervisors, shall be made aware of the sensitive sites, and prevent any harm or damage or disturbance to trees, vegetation, wildlife, birds etc.;
- (iii) Schedule works during dry season to avoid contaminated runoff from the work sites entering lake; clear the sites of materials, debris, and consolidated the refilled trenches prior to onset of monsoon;
- (iv) No construction camps (workers accommodation, material / waste / soil storage) should be established within 200 m from the boundary of dam; camps should not be located close to drainage lines/streams that flow into dam;
- (v) Movement of workers and staff should be confined to work site, and not be allowed in dam area which may disturb the sensitive area; ensure via strict supervision no poaching, fishing, cutting / damaging trees/vegetation or wildlife, birds etc.;
- (vi) Proper accommodation and facilities shall be provided within the camps, and workers shall not use the lake or surroundings for open defecation, bathing, or fishing / hunting, collecting firewood etc. Contractor should put in place, a proper system to monitor the staff and workers to prevent damage/ disturbance;
- (vii) Implement sediment and erosion control measures to prevent soil erosion and sedimentation in the dam. Prevent entry of silt-laden / contaminated runoff into dam or drains leading to dam from the construction sites or construction camps. Soil stabilization measures should be taken to prevent soil erosion during construction, Construction near dam to be planned in dry seasons only;
- (viii) Place storage areas for fuels and lubricants away from any drainage leading to water bodies;
- (ix) Store fuel, construction chemicals etc., on an impervious floor, also avoid spillage by careful handling;
- (x) Do not use equipment that generate heavy noise, ground vibration, dust etc., (such as pneumatic drills), within 100 m of Dam;
- (xi) Construction sites often generate significant amounts of dust that can impact nearby habitats. Dust suppression measures, such as watering down exposed soil, can help to reduce dust levels;
- (xii) Dispose any wastes generated by construction activities in designated sites;
- (xiii) Monitor the project closely throughout construction to ensure that all mitigation measures are being implemented effectively and that any issues are identified and addressed promptly;
- (xiv) Conduct surface quality inspection according to the environmental management plan (EMP);
- (xv) Conduct continuous consultations with the local people during the works;
- (xvi) Schedule the works during low water level period – late winter months to pre monsoon (February – June/July); ensure that works are completed during the same period to prior to onset of monsoon;
- (xvii) Erect temporary barriers to form enclosed construction area with least disturbance;

- (xviii) Allow adequate time to settle the distributed solids to prior to pumping out water; only clear/clarified water shall be pumped back into the reservoir; any silt laden water should be pumped to a silt pond
- (xix) Clear the work site after completion at least to pre project conditions, ensure that there are no materials, debris, spills etc., and prior to removal of temporary barriers.
- (xx) Implement work site safety at works in water body and aware them for the presence of crocodile.
- (xxi) Erect temporary barriers to form enclosed construction area with least disturbance
- (xxii) Implement work site safety at works in water body.

68. Laying of Water Supply and Sewer Networks. Subproject include linear works (laying of water supply and sewage collection pipes). This covers almost entire project area of Dungarpur Town. Distribution lines/small sewers (tertiary sewers) will be laid in all streets and roads, the larger sewers and water mains will be laid mostly on wider main roads. Pipes/sewers will be laid by open cut method. Water pipes will be laid in the ground with or without a maximum cover of 1 m, so that depth of excavation will be up to 1.5 m-1.8 m. The maximum depth for sewers depends on the design, and in Dungarpur most of the sewers will be laid 1.2 m to 3.5 m below the ground, and some sewers will be laid deeper (>2 m) and maximum depth will be 6 m. As per the bid conditions, "the maximum depth of sewer is 3.5 m for open excavation; after 3.5 m sewer shall be laid by the trenchless method only. Trenchless method may also be used even where depth is less than 3.5 m for important roads in the city where traffic density is more, and in the streets where traffic diversion is not feasible etc. Sufficient care will be taken while laying so that existing utilities and cables are not damaged and pipes are not thrown into the trenches or dragged, but carefully laid in the trenches. Trenches deeper than 1.5 m will be protected by shoring/bracings to avoid collapse of trenches, and also to avoid any risk to surrounding buildings. Once they are laid, pipes will be joined as per specification and then tested for any cracks or leakages. The minimum working hours will be 8 hours daily, the total duration of each stage depends on the soil condition and other local features. Extraneous soil after backfilling of trenches shall be used for filling low lying area or stored/ dumped in approved debris disposal sites.

69. Although construction of these project components involves quite simple techniques of civil work, the invasive nature of excavation and the project locations in the built-up areas of the town where there are a variety of human activities, will result in impacts to the environment and sensitive receptors such as residents, businesses, and the community in general. The anticipated impacts are temporary and for short duration. A detail survey is needed after finalization of alignment to access the feasibility of the alignment for need of any tree cutting, demolition of any structure, road and railway crossings, pipe laying in any private land, presence of any sensitive receptor along alignment, disturbance to public or business etc. Mitigation measures have been prepared for potential adverse impacts. Prior consent from land owners (if pipe laying is required in private land) and NOC from concerned departments (for pipe laying in roads, road/railway crossings etc) prior to start of construction works, is required

70. Physical impacts will be reduced by the method of working and scheduling of work, whereby the project components will be (i) constructed by small teams working at a time; (ii) any excavation done near sensitive area like school, religious places and house will be protected as per standard norms etc (iii) finish excavation, pipe laying and back filling of trench in the same day (iv) provide adequate barricades and road safety signage during pipe laying works in traffic areas (v) Further if night works are required (however unlikely, applicable only in extreme conditions) all the mitigation measures to reduce impacts of disturbance to minimum level to nearby habitants and road users should be ensured by contractor.

71. Demolition works. In the initial stage of project planning it is accessed that there is no requirement of demolition of structures. If any demolition works are required, proper work plan and Mitigation measures will be required for demolition works. Structures to be demolished should be wetted through water sprinkling to reduce dust emission. Appropriate site for storage and disposal of demolished materials should be selected prior to start of demolition activities with prior permission/approval of PIU/ULB. All the safety measures should be adopted during demolition activities.

72. Storage and Disposal of excavated earth. A large quantity of soil will be excavated for pipe laying, construction of CWR, pump house and other. Some part of this excavated soil will be reused for backfilling and/or surface leveling; rest of the soil will need to be disposed in other locations. Proper storage and disposal plan from contractor is required before start of the work. Prior permission from land owner/concerned authority for storage and disposal of excess earth is required. Prior to the commencement of works, Contractor will follow all the prescribed rules¹³ and shall identify a debris disposal site in consultation with the PIU/ULB and adhering to following criteria:

- The site shall be selected preferably from barren, infertile lands. In case agricultural land needs to be selected, top-soil stripping, stacking and preservation should be undertaken prior to initiation of any activities.
- Debris disposal site shall be at least 200 m away from any surface water body.
- No residential areas shall be located within 200 m downwind side of the site.
- The site is minimum 250 m. away from sensitive locations like hospitals, religious places, ponds/lakes or other water bodies.
- The local governing body and community shall be consulted while selecting the site.
- Contractor is required to prepare plan for disposal of construction and demolition waste including excavated earth in the designated site/sites and submit the plan in PIU to be approved by Municipal Council as per Construction and Demolition Waste Rules 2016
- Soil storage site should be properly demarcated by fencing and information board should be placed at entrance
- At soil storage site soil should be covered by tarpaulin or regular water sprinkling should be done to reduce dust emission
- At soil disposal site the disposed soil should be levelled on daily basis and no heap or mound should be left at end of the day

73. Sources of Materials. Significant amount of gravel, sand, coarse aggregate, and cement will be required for this project. The construction contractor will be required to:

- Use material sources permitted by government¹⁴;
- Verify suitability of all material sources and obtain approval of PIU;
- Ensure that the loading and unloading of the materials and the transportation of the materials from source to construction site does not cause impact on health and safety of the workers and the community; and

¹³ Construction and Demolition Waste Management Rules 2016 and Solid Waste Management Rules (refer appendix 8)/ Table 1

¹⁴ CTE and CTO will be required for batching plant, hot mix plant, crushers etc. if specifically established for this project. If contractor is purchasing raw material or ready mix concrete, asphalt/macadam and aggregates from third party, he has to be assured that third party is having CTE/CTO from RSPCB and should collect the copy of these and submit to PIU/consultants. Quarry sites should also have the desired permissions.

- Submit to PIU on a monthly basis documentation of sources of materials.. If contractor is purchasing ready mix concrete, asphalt/macadam and aggregates from third party, contractor will assure that all the parties/ suppliers are having CTE/CTO from RSPCB and will collect the copy of these certificates and submit to PIU/consultants

74. **Air Quality.** Emissions from construction vehicles, equipment, and machinery used for excavation and construction will induce impacts on the air quality in the construction sites. Anticipated impacts include dusts and increase in concentration of vehicle-related pollutants such as carbon monoxide, sulphur oxides, particulate matter, nitrous oxides, and hydrocarbons. These however will be temporary limiting to construction activities only. To mitigate the impacts, construction contractors will be required to:

- Consult with PIU/on the designated areas for stockpiling of soils, gravel, and other construction materials;
- Damp down exposed soil and any stockpiled material on site by water sprinkling;
- Use tarpaulins to cover sand and other loose material when transported by trucks;
- Clean wheels and undercarriage of haul trucks prior to leaving construction site
- Don't allow access in the work area except workers to limit soil disturbance and prevent access by barricading and security personnel
- Fit all heavy equipment and machinery with air pollution control devices which are operating correctly, DGs should have proper stake height as per norms;
- Ensure all the equipment are having PUC certificates
- Do regular water sprinkling in dusty areas to reduce dust emission during works
- Damp down the structures before demolishing to reduce dust emission
- Damp down on regular basis all the access ways
- Maintain all the equipment and vehicles to reduce emission of smoke and keep pollution under control and keep records of periodic maintenance
- Conduct ambient air quality monitoring periodically as per Environmental Management Plan EMP

75. **Surface Water Quality.** Do River, Sabela Lake and Gap Sagar Kale are major surface water bodies near the proposed locations of SPS (1, 2 & 3) CWR (new Colony) and STP site. These water bodies may be contaminated from leakage of fuel oil and lubricants during construction phase from house sewerage during operation phase. These potential impacts are temporary and short-term duration only. However, to ensure that these are mitigated, construction contractor will be required to:

- Prepare and implement a spoils management plan;
- Avoid to construct any construction camps and labour camps near to any water body and do not allow to dispose any waste or sillage in to any water body;
- Avoid stockpiling of earth fill especially during the monsoon season unless covered by tarpaulins or plastic sheets;
- Prioritize re-use of excess spoils and materials in the construction works. If spoils will be disposed, consult with PIU on designated disposal areas;
- Install temporary silt traps or sedimentation basins along the drainage leading to the water bodies;
- Place storage areas for fuels and lubricants away from any drainage leading to water bodies and provide impermeable lining under the storage yard of fuels and lubricants;
- Dispose any wastes generated by construction activities in designated sites;

- Keep oil tray or pans under the DG set or during maintenance of mechanical equipment to avoid oil spillage resulting soil and water pollution, and
- Conduct surface water quality Monitoring according to the Environmental Management Plan (EMP).

76. Noise and Vibration Levels. Construction works will be conducted along the roads in Dungarpur urban area, where there are majorly houses, commercial activities, few religious places and small-scale businesses. The sensitive receptors are the schools, religious places, hospitals in these areas. Increase in noise level may be caused by excavation, particularly breaking of cement concrete or bitumen roads, operation of construction equipment like concrete mixers, and the transportation of equipment, materials, and people. Vibration generated from construction activity, for instance from the use of pneumatic drills, will have impact on nearby buildings. This impact is negative but short-term, and reversible by mitigation measures. The construction contractor will be required to:

- Plan activities in consultation with PIU so that activities with the greatest potential to generate noise are conducted during periods of the day which will result in least disturbance;
- Use road cutters instead of breaker/hammer for cutting the road before excavation for pipe laying on roads
- Horns should not be used unless it is necessary to warn other road users or animals of the vehicle's approach;
- Minimize noise from construction equipment by using vehicle silencers, fitting jackhammers with noise-reducing mufflers, and use portable street barriers to minimize sound impact to surrounding sensitive receptor;
- DGs being used at site should have sound reducing (acoustic) enclosures, preferably silent DGs should be used at site;
- Maintain maximum sound levels not exceeding 80 decibels (dBA) when measured at a distance of 10 m or more from the vehicle/s and equipment;
- Identify any buildings at risk from vibration damage and avoiding any use of pneumatic drills or heavy vehicles in the vicinity;
- Consult the custodians of important buildings, cultural and tourism authorities and local communities in advance of the work to identify and address key issues, and avoid working at sensitive times, such as religious and cultural festivals, exams of students etc.;
- Provide all workers appropriate PPEs like ear plug/muff, working in high noise conditions;
- Keep all vehicles and equipment in good conditions to avoid excessive noise generation;
- Provide noise barriers near sensitive receptors like schools, hospitals, temples, courts etc and consult in advance with sensitive receptors about the working hours (specially schools, hospitals, offices, courts etc) and avoid noisy works in those hours;
- Avoid noisy works in nights in inhabited areas to avoid any disturbance to habitants; and
- Consult in advance with habitants and inform them about the nature and duration of works
- Conduct noise monitoring according to the Environmental Management Plan (EMP)

77. Management Plan for Night works (if required). Following requirements should be fulfilled for construction works at night hours-

- Night works should be avoided at construction sites specially in residential areas and should be performed only when day works are not possible due to excessive

traffic/public/pedestrian movement, site of cultural or religious importance, where there is huge crowd during day hours or any other unavoidable circumstances.

- Contractor should plan for night works only after directions from PMU/PIU/CMSC
- Contractor should submit plan for night works for approval from PIU.
- PIU should ensure that prior written information should be given to local authorities such as district administration, Police/traffic police, line agencies concerned, residents welfare association/business association/vyapar of the affected areas and their consents/permissions should be taken prior to start of night works.
- PIU/CMSC engineers should check and ensure that all the preparation as per management plan is done by contractor and contractor is having all the necessary equipment and materials for night works.
- Contractor is required to have following equipment/arrangements for night works-
- Contractors should have hand held noise level meter for measurement of noise during night hours
- Contractors should have hand held lux meter for the measurement of illumination during night hours
- Preferably electrical connections is available for running equipment otherwise sound proof/super silent Diesel Generator set should be available
- Sound level should not increase as per following-

Type of area of work	Maximum noise level dB(A)
Industrial	70
Commercial	55
Residential	45
Silence zone	40

- Illumination should be as follows-

Minimum illumination (lx)	Areas to be illuminated	Type of work activity
54	Illumination throughout the work area	General work area lighting, and performance of visual tasks of large size, or medium contrast, or low require accuracy
108	Illumination of work area and areas adjacent to equipment	Performance of visual tasks of medium size, or low to medium contrast, or medium required accuracy
216	Illumination of task	Performance of visual tasks of small size, or low contrast or high required accuracy or fine finish

- As far as possible ready mix concrete from batching plant to be used, otherwise the concrete should be prepared away from residential areas and brought to the site
- All the noise activity like hammering, cutting, crushing, running of heavy equipment should be done in day time and avoided in night time
- Workers engaged in night works should have adequate rest/sleep in day time before start of night works
- Worker engaged for night works should have previous experience of night works and should be physically fit for such works including clear vision in night
- All the necessary provisions of traffic aids such as traffic signals, road signage, barricades, cautions boards, traffic diversion boards etc. should be available with fluorescent/retro-reflective arrangements.

- Workers should be trained before start of night works about risks and hazards of night works and their mitigation measures and should be provided all the protective aids (PPEs) including fluorescent/retro-reflective vests
- Horns should not be permitted by equipment and vehicles
- Workers should not shout and create noise
- First aid and emergency vehicles should be available at site
- Emergency preparedness plan should be operative during night works
- Old persons and pregnant women and women having small kids should not work in night time
- All the vehicles and equipment being used at night works should have adequate type of silencers/enclosures/mufflers to reduce noise
- All the vehicles should be checked for working head lamps, tail lamps, inner lights etc. before start of night works
- PIU/CMSC site engineers and contractors safety personnel should closely monitor the safety of works continuously and noise and illumination levels on hourly basis and maintain photographic and videographic records as well as register the observations
- Night works should be stopped early in the morning at least one hour before start of pedestrian/traffic movement.
- After completion of night works all the site should be cleaned and maintained obstruction free for day time movement of vehicles and pedestrians
- Drivers and workers should be alert and responsive during night works
- All the wages to workers working in night hours should be as per the applicable labour acts
- Avoid any nuisance which may create problems to nearby habitants and work peacefully during night hours
- Night works should not be conducted near hospitals and during peak seasons such as peak tourist season, students' exam times etc.

78. **Landscape and Aesthetics.** The construction works may require cutting of trees and also will produce excess excavated earth, excess construction materials, and solid waste such as removed concrete, wood, packaging materials, empty containers, spoils, oils, lubricants, and other similar items. Haphazard disposal of these will have negative impacts on Landscape and overall aesthetics. These impacts are negative but are of short-term and reversible by mitigation measures. The construction contractor will be required to:

- Prepare and implement spoils management plan;
- Avoid stockpiling of excess excavated soils;
- Coordinate with ULB for beneficial uses of excess excavated soils or immediately dispose to designated areas;
- Recover used oil and lubricants and reuse or remove from the sites;
- Manage solid waste according to the following preference hierarchy: reuse, recycling and disposal to designated areas;
- Minimize removal of vegetation and disallow cutting of trees;
- If tree-removal will be required, obtain tree-cutting permit from the Revenue Department; and
- Plant three native trees for every one that is removed.
- Remove all wreckage, rubbish, or temporary structures which are no longer required; and

- Request PIU to report in writing that the necessary environmental restoration work has been adequately performed before acceptance of work.

79. **Groundwater Quality.** Another physical impact that is often associated with excavation is the effect on drainage and the local water table if groundwater and surface water collect in the voids. Although, groundwater is much deeper than the proposed trenching depth, and rains are scarce and limited to very short duration during monsoon, to ensure that water will not pond in pits and voids near project location, the construction contractor will be required to conduct excavation works in non-monsoon season to the maximum extent possible. These potential impacts are temporary and short-term duration only. However, to ensure that these are mitigated, construction contractor will be required to:

- Prepare and implement a spoils management plan (**Appendix C-13**);
- Avoid stockpiling of earth fill especially during the monsoon season unless covered by tarpaulins or plastic sheets;
- Prioritize re-use of excess spoils and materials in the construction works. If spoils will be disposed, consult with PIU on designated disposal areas;
- Install temporary silt traps or sedimentation basins along the drainage leading to the water bodies;
- Place storage areas for fuels and lubricants away from any drainage leading to water bodies;
- Dispose any wastes generated by construction activities in designated sites; and
- Conduct periodical ground water quality monitoring according to the Environmental Management Plan (EMP).

80. **Accessibility.** Excavation along the roads, hauling of construction materials and operation of equipment on-site can cause traffic problems. Potential impact is negative but short term and reversible by mitigation measures. The construction contractor will be required to:

- Prepare and implement a Traffic Management Plan (**Appendix C-14**)
- Plan transportation routes so that heavy vehicles do not use narrow local roads, except in the immediate vicinity of delivery sites;
- Schedule transport and hauling activities during non-peak hours;
- Locate entry and exit points in areas where there is low potential for traffic congestion;
- Keep the site free from all unnecessary obstructions;
- Drive vehicles in a considerate manner;
- Coordinate with Traffic Police for temporary road diversions and for provision of traffic aids if transportation activities cannot be avoided during peak hours; and
- Notify affected sensitive receptors by providing sign boards informing nature and duration of construction works and contact numbers for concerns/complaints.

81. Wherever road width is minimal, there will be temporary loss of access to restrains and vehicular traffic (including 2-wheelers) during the laying of pipes. Under those circumstances, contractor shall adopt following measures:

- Inform the affected local population 1-week in advance about the work schedule
- Plan and execute the work in such a way that the period of disturbance/ loss of access is minimum.
- Provide pedestrian access in all the locations until normalcy is restored. Provide wooden/metal planks over the open trenches at each house to maintain the access.

82. **Socio-Economic - Income.** The project components will be located in government land and there is no requirement for land acquisition or any resettlement. Construction works will impede the access of residents to specific site in limited cases. The potential impacts are negative and moderate but short-term and temporary. The construction contractor will be required to:

- Prepare and implement spoils management plan (**Appendix C-13**);
- Leave spaces for access between mounds of soil;
- Provide walkways and metal sheets where required to maintain access across for people and vehicles;
- Increase workforce in the areas with predominantly institutions, place of worship, business establishment, hospitals, and schools;
- Consult businesses and institutions regarding operating hours and factoring this in work schedules; and
- Provide sign boards for pedestrians to inform nature and duration of construction works and contact numbers for concerns/complaints.
- Notify community/ water users in advance about likely interruptions in water supply.
- Provide alternate sources of clean water until water supply is restored.
- Provide all mitigation measures as given in resettlement plan (RP) prepared for the project to mitigate impacts on vendors and shopkeepers.

83. **Socio-Economic-Employment.** Manpower will be required during the 36-months construction stage. This can result in generation of temporary employment and increase in local revenue. Thus potential impact is positive and long-term. The construction contractor will be required to:

- Employ at least 50% of the labour force, or to the maximum extent, local persons within the 2-km immediate area if manpower is available; and
- Secure construction materials from local market.

84. **Occupational Health and Safety.** Workers need to be mindful of the occupational hazards which can arise from working on roads, in height and excavation (trenches and trenchless) works. Potential impacts are negative and long-term but reversible by mitigation measures. Construction contractor will depute experienced EHS personnel and will be required to:

- Comply with all national, state and local labor laws (see **Appendix C-12**);
- Develop and implement site-specific occupational health and safety (OH&S) Plan which will include measures such as: (a) excluding public from the site; (b) ensuring all workers are provided with and use personal protective equipment; (c) OH&S Training¹⁵ for all site personnel; (d) documented procedures to be followed for all site activities; and (e) documentation of work-related accidents;
- Ensure that qualified first-aid is provided at all times. Equipped first-aid stations shall be easily accessible throughout the site;

¹⁵ Some of the key areas that may be covered during training as they relate to the primary causes of accidents include (i) slips, trips and falls; (ii) personal protective equipment; (iii) ergonomics, repetitive motion, and manual handling; (iv) workplace transport; and (v) legislation and responsibilities. Training can provide the foundations of competence but it does not necessarily result in a competent worker. Therefore, it is essential to assess staff competence to ensure that the training provided is relevant and effective. Supervision and monitoring arrangements shall be in place to ensure that training has been effective and the worker is competent at their job. The level of supervision and monitoring required is a management decision that shall be based on the risks associated with the job, the level of competence required, the experience of the individual and whether the worker works as part of a team or is a lone worker.

- Provide medical insurance coverage for workers;
- Secure all installations from unauthorized intrusion and accident risks;
- The project area experiences extreme temperature during summer months of April and May, which may affect the health of workers engaged in construction work. Contractor should take necessary measures during summers including the following:
 - a. Work schedule should be adjusted to avoid peak temperature hours (12 -3 PM)
 - b. Provide appropriate shade near the work place; allow periodic resting and provide adequate water
 - c. Provide necessary medicine and facilities to take care of dehydration related health issues
- Provide supplies of potable drinking water;
- Provide clean eating areas where workers are not exposed to hazardous or noxious substances;
- Provide H&S orientation training to all new workers to ensure that they are apprised of the basic site rules of work at the site, personal protective protection, and preventing injuring to fellow workers;
- Provide visitor orientation if visitors to the site can gain access to areas where hazardous conditions or substances may be present. Ensure also that visitor/s do not enter hazard areas unescorted;
- Ensure the visibility of workers through their use of high visibility vests when working in or walking through heavy equipment operating areas;
- Ensure moving equipment is outfitted with audible back-up alarms;
- Mark and provide sign boards for hazardous areas such as energized electrical devices and lines, service rooms housing high voltage equipment, and areas for storage and disposal. Signage shall be in accordance with international standards and be well known to, and easily understood by workers, visitors, and the general public as appropriate; and
- Disallow worker exposure to noise level greater than 85 dBA for duration of more than 8 hours per day without hearing protection. The use of hearing protection shall be enforced actively.

85. **Asbestos Containing Materials.** No ACM is proposed to be used in the subproject construction. There are however ACM in the existing water supply infrastructure, which may be disturbed or come in contact with the workers and general public and may have serious health implications. This is already discussed under heading **Design Impacts**, and necessary measures are suggested.

86. **Community Health and Safety.** Hazards posed to the public, specifically in high-pedestrian areas may include traffic accidents and vehicle collision with pedestrians. Potential impact is negative but short-term and reversible by mitigation measures. The construction contractor will be required to:

- Plan routes to avoid times of peak-pedestrian activities.
- Liaise with PIU in identifying risk areas on route cards/maps.
- Maintain regularly the vehicles and use of manufacturer-approved parts to minimize potentially serious accidents caused by equipment malfunction or premature failure.
- Provide road signs and flag persons to warn of on-going trenching activities.

87. Some part of the town is characterized by narrow roads. Particularly, the areas located in old town have very narrow roads with dense habitation and heavy traffic and are accessible only to pedestrians. Besides impeding the access, the trench excavation and pipe laying will pose

safety risks to pedestrians, and the people living in these areas. Though the width (<500 mm) and depth (<750mm) of trench is minimal, it will pose safety risk, especially for children and elders the construction contractor will be required to:

- Trench excavation and pipeline works shall be conducted in a safe manner; if the allowing public movement along the work sites (pedestrians or vehicles as the case may be) is likely to cause safety risks, movement should be blocked temporarily and work shall be conducted; in such areas, conducting night work or working in small stretches to avoid blockage of traffic/movement no more than few hours in due consultation with the local community and ULB shall be planned;
- All trenches deeper than 1.5 m shall be provided with safety shoring/braces; and avoid open cutting method for trenches deeper than 3.5 m by adopting trenchless technology;
- Survey the surrounding vulnerable buildings for likely issues in structural stability/differential settlement during the excavation works;
- Provide prior information to the local people about the nature and duration of work;
- Conduct awareness program on safety during the construction work;
- Undertake the construction work stretch-wise; excavation, pipe laying, and trench refilling should be completed on the same day; and
- Provide hard barricades and deploy security personnel to ensure safe movement of people and also to prevent unnecessary entry and to avoid accidental fall into open trenches.

88. **Work Camps.** Operation of work camps can cause temporary air and noise pollution from machine operation, water pollution from storage and use of fuels, oils, solvents, and lubricants. Potential impacts are negative but short-term and reversible by mitigation measures. The construction contractor will be required to:

- Consult PIU before locating project offices, sheds, and construction plants;
- Minimize removal of vegetation and disallow cutting of trees;
- Provide drinking water, water for other uses, and sanitation facilities for employees;
- Provided temporary rest and eating area at all work sites;
- Ensure conditions of liveability at work camps are maintained at the highest standards possible at all times; living quarters and construction camps shall be provided with standard materials (as far as possible to use portable ready to fit-in reusable cabins with proper ventilation); thatched huts, and facilities constructed with materials like GI sheets, tarpaulins, etc., shall not be used as accommodation for workers; accommodation shall meet the IFC standards for workers accommodation¹⁶ which include: provision of safe housing, availability of electricity, plumbing, water and sanitation, adequate fire protection and dormitory/room facilities; accommodation shall be in the range from 10 to 12.5 cubic meter (m³) (volume) or 4 to 5.5 square meters (m²) (surface) per worker, a minimum ceiling height of 2.10 m; a reasonable number of workers are allowed to share the same room—(standards range from 2 to 8 workers); workers with accompanying families shall be provided with a proper and safe accommodation (Suggested guidelines based on IFC benchmark standards for workers accommodation is provided in **Appendix C-21**);
- Prohibit employees from poaching wildlife and cutting of trees for firewood;
- Train employees in the storage and handling of materials which can potentially cause soil contamination;

¹⁶

https://www.ifc.org/wps/wcm/connect/topics_ext_content/ifc_external_corporate_site/sustainability-at-ifc/publications/publications_gpn_workersaccommodation

- Recover used oil and lubricants and reuse or remove from the site;
- Manage solid waste according to the following preference hierarchy: reuse, recycling and disposal to designated areas;
- Remove all wreckage, rubbish, or temporary structures which are no longer required; and
- Report in writing that the camp has been vacated and restored to pre-project conditions before acceptance of work.

89. **Social and Cultural Resources.** For this project, excavation will occur at locations not known to have archaeological values, so there is no risk of such impacts. Religious places such as temples are present nearby the proposed pipeline works for water supply and contractor will require to follow the mitigation measures as given below-

- Consult with concerned religious authorities, nearby people and devotees in pre-construction phase and explain the work method and duration of proposed works, take their suggestions and comments and incorporate in design the mitigation measures required
- Adjacent to religious/social/historic sites, undertake excavation and construction work in such a way that no structural damage is caused to the religious building.
- Observe the local rituals and important dates of festivals, weekly/monthly/annual religious occasions in the religious places and do not make any disturbance/hindrance/obstacles during such time to the religious places,
- provide proper signage, barricades etc. to protect public and devotees from dangers of construction works.

90. **Traffic diversion and/or road closure-** If traffic diversion and/or road closure is required for the proposed works, prior consent from traffic department will be required and prior information to affected areas and public should be disseminated through consultations by CAPC. Proper road signage and traffic aids should be provided at site. Excavation along the roads, hauling of construction materials and operation of equipment on-site can cause traffic problems. Potential impact is negative but short term and reversible by mitigation measures. The construction contractor will be required to:

- Prepare and implement a Traffic Management Plan
- Plan transportation routes so that heavy vehicles do not use narrow local roads, except in the immediate vicinity of delivery sites;
- Schedule transport and hauling activities during non-peak hours Locate entry and exit points in areas where there is low potential for traffic congestion;
- Keep the site free from all unnecessary obstructions;
- Drive vehicles in a considerate manner;
- Coordinate with Traffic Police for temporary road diversions and for provision of traffic aids if transportation activities cannot be avoided during peak hours; and
- Notify affected sensitive receptors by providing sign boards informing nature and duration of construction works and contact numbers for concerns/complaints.
- Maintain sufficient access to houses and shopkeepers (commercial establishments) during pipe laying work through metal sheets and temporary bridges
- Locate entry and exit points in areas where there is low potential for traffic congestion;

91. Wherever road width is minimal, there will be temporary loss of access to pedestrians and vehicular traffic including two wheelers during the laying of pipes. Under those circumstances,

contractor shall adopt following measures:

- Inform the affected local population 1-week in advance about the work schedule
- Plan and execute the work in such a way that the period of disturbance/ loss of access are minimum.
- Provide pedestrian access in all the locations until normalcy is restored. Provide wooden/metal planks over the open trenches at each house to maintain the access
- Excavate only that stretch in a day that could be finished in the same day by laying of pipes and backfilling.

E. Operation and Maintenance Impacts

92. **Water Supply System.** O&M of the water supply system will be carried out by DBO contractor for 10 years and then by Dungarpur Municipal Council directly or through an external operator. The water supply system is intended to deliver potable water meeting drinking water standards (**Appendix C-1**) to the consumers at their homes. This must be ensured.

93. The system has a design life of 30 years, during which shall not require major repairs or refurbishments and should operate with little maintenance beyond routine actions required to keep the equipment in working order. The stability and integrity of the system will be monitored periodically to detect any problems and allow remedial action if required. Any repairs will be small-scale involving manual, temporary, and short-term works involving regular checking and recording of performance for signs of deterioration, servicing and replacement of parts.

94. Recurrence of pipe bursting and leakage problems in water supply system will be managed by the leak detection and water auditing surveys. The operating agency will be required to ensure that the leak detection and rectification time is minimized.

95. Since backwash water/wastewater from the process is recovered and recirculated in the WTP, no wastewater will be generated from water treatment process. Water treatment process will generate sludge from sedimentation of particulate matter in raw water, flocculated and precipitated material resulting from chemical coagulation, residuals of excess chemical dosage, plankton etc.; and waste from rinsing and back washing of filter media containing debris, chemical precipitates, straining of organic debris and plankton. The management and safe disposal of wastewater and sludge have already been considered in the design phase, and if these activities are implemented as intended will have no negative impacts.

96. It is proposed to use chlorine for disinfection of water, therefore there is a safety risk due to handling of large quantities of chlorine at the WTP. Likely impacts will be negligible if the various measures are suggested safety features and equipment to meet with any accidental eventuality are included in the design and development of the facility. During the operation phase, it is necessary that the facility is operated by trained staff as per the standard operating procedures.

97. Following measures are suggested for implementation/compliance during the operation phase:

- (i) Judiciously utilize the available surface water and groundwater resources by adapting conjunctive use; prepare a water utilization plan every year post monsoon season depending on the water storage in Dams;

- (ii) Ensure that dead storage is always maintained in Dams; utilize only available live storage for water supply;
- (iii) Prepare and implement contingency plan for low rainfall years that will result in low water levels in Dams; in such cases revise the water supply rate appropriately to ensure uninterrupted water supply throughout the year; provide prior information to stakeholders;
- (iv) Ensure that water supplied to the consumers at all times meet the drinking water standards; carry out regular sampling and testing, and disseminative information;
- (v) Ensure zero wastewater discharge from the water treatment process via collection and recirculation of process wastewater/backwash water;
- (vi) Implement sludge management plan; ensure collection, processing, drying, and safe disposal/reuse accordingly;
- (vii) Assess composition and characteristics of sludge from the first batch operation at the initial phases, and confirm the handling, management and disposal/reuse actions suggested in the management plan;
- (viii) Conduct periodic testing of sludge as per the EMP;
- (ix) Ensure valid consent to operate (CTO) from RPCB for operation of WTP;
- (x) Ensure that all conditions/standards prescribed by RPCB are complied duly;
- (xi) Ensure that chlorinator facility is operated only by trained staff and as per the standard operating procedures; in case of any accident and/or maintenance activity, ensure that the staff follows documented procedures only; and
- (xii) Implement emergency response system (ERS) for the chlorine leakage; Guidelines and Emergency plan for handling and storing chlorine is attached as Appendix C-22.

98. **Sewerage System.** O&M of the sewerage system will be carried out by DBO contractor for 10 years and then by Dungarpur Municipal Council directly or through an external operator. The sewerage system is intended to collect, convey, treat and dispose the sewage from the town areas safely. Operation will involve collection and conveyance of wastewater from houses to STP; treatment of sewage at STP to meet the disposal standards; and final disposal of treated wastewater, and treatment and disposal of sludge.

99. Treated wastewater is proposed to be utilized in reuse applications following the Sewerage and Wastewater Policy 2016 of Rajasthan, and accordingly reuse plan will be prepared by the DBO contractor during the detailed design phase. As stated previously, subproject will be implemented under DBO, and the successful bidder/DBO contractor will carry out detailed designs, therefore at present the subproject is designed in outline only. The treated wastewater if utilized for reuse purposes as per the reuse plan there will be no negative impacts, and in fact it will enhance environmental benefits in the form of water savings. Various measures to safeguard environment and health environment in utilizing the treated wastewater, including required quality for various process will be established in the reuse plan and will be implemented accordingly. All necessary safety, mitigation and monitoring measures as suggested in the reuse plan shall be implemented. Remaining treated effluent is proposed to be discharged in to the open space available in campus during rainy season. Mixing of industrial effluents in sewers may affect the inlet quality of sewage. It is therefore critical that STP receives the sewage with intended quality and treats the same to design discharge standards.

100. STP operational procedures will be firmed up during the detailed design phase, including the amount of automated or manual operation. It must be ensured that the facility is operated with standard operating procedures and only by trained staff. Ensuring uninterrupted power supply with back-up facility is a must. Standard operating procedures and operation manual will be

prepared by the DBO contractor. Besides routine operation, this should cover all necessary items such as preventive maintenance, periodic maintenance and emergency maintenance, replacement of pumps, motors, and other electro-mechanical parts as per the design life to optimize energy use and system efficiency etc. Adequate resources – technical and financial, has been taken into consideration in the project design. Manual will also include safety awareness and mock drills for worker safety.

101. Subproject includes sludge management infrastructure in STP, including system for sludge collection, thickening, solar drying, and disposal at landfill/identified site. This includes a sludge sump to collect sludge from SBR basins; returning arrangement for supernatant from the sump to inlet/equalization tank for treatment; pumping sludge to sludge thickener and pumping thickened to mechanical sludge dewatering system (such as centrifuge). It also requires contractor to establish a shed where the dewatered sludge cake can be further air dried for 15 days. This is indicative sludge management system, and DBO contractor will design the system meeting these requirements and prepare sludge management plan. Bid indicates that “the sludge produced from the treatment process would be processed so it may be used as fertilizer and soil conditioner” and it requires DBO contractor “to conform to the regulations of public health and environment protection norms”. The norms for safe use of processed sludge as fertilizer and soil conditioner are discussed earlier in this IEE. This follows the Sewerage and Wastewater Policy, 2016, which suggests “use of sludge produced from the treatment as fertilizer and soil conditioner after processing”. A sludge disposal site will be identified during the detailed design phase to dispose unutilized dried sludge in reuse applications. The updated IEE will include the details of disposal site. If the sludge is managed accordingly, there will no impacts.

102. During the operation phase, it is necessary that the facility is operated by trained staff as per the standard operating procedures. Following measures are suggested for implementation/compliance during the operation phase:

- Ensure that treated wastewater meets the established discharge standards all times; conduct regular wastewater quality monitoring (at inlet and at outlet of STP) to ensure that the treated effluent quality complies with design standards;
- Ensure implementation of reuse plan, and ensure intended quality for each direct reuse;
- Assess composition and characteristics of sludge from the first batch operation at the initial phases, and confirm the handling, management and disposal/reuse actions suggested in the management plan;
- Conduct periodic testing of dried sludge/compost to check presence of heavy metals and confirming the concentrations to use as compost as specified in the Standards for Composting, Schedule II A, Solid Waste Management Rules, 2016, Fertilizer Control Order (FCO), 1985, amendments in 2009 and 2013. It shall not be used for food crops;
- Ensure valid consent to operate (CTO) from RSPCB for operation of STP;
- Ensure that all conditions/standards prescribed by RSPCB are complied duly;
- Ensure that chlorinator facility is operated only by trained staff and as per the standard operating procedures; in case of any accident and/or maintenance activity, ensure that the staff follows documented procedures only;
- Implement emergency response system (ERS) for the chlorine leakage; Guidelines and Emergency plan for handling and storing chlorine is attached as **Appendix C-22**;
- Ensure proper knowledge transfer, hands-on training to municipal staff engaged in STP operation has been provided by contractor prior to handover of facility;
- Operate and maintain the facility following standard operating procedures of operational manual;
- Undertake preventive and periodic maintenance activities as required;

- Conduct periodic training to workers; ensure that all safety apparatus at STP including personal protection equipment are in good condition all times; and are at easily accessible and identifiable place; periodically check the equipment, and conduct mock drills to deal with emergency situations;
- No wastewater from industrial premises (including domestic wastewater) shall be allowed to dispose into municipal sewers; monitor regularly and ensure that there is no illegal discharge through manholes or inspection chambers; conduct public awareness programs; in coordination with RSPCB.

103. There are also certain environmental risks from the operation of the sewer system, most notably from leaking sewer pipes as untreated faecal material can damage human health and contaminate both soil and groundwater. It will be imperative therefore that the operating agency establishes a procedure to routinely check the operation and integrity of the sewers, and to implement rapid and effective repairs where necessary. There is an occupation health risk to workers engaged in sewer maintenance activities. Following measures should inter alia be followed:

- Establish regular maintenance program, including:
 - (a) Regular cleaning of grit chambers and sewer lines to remove grease, grit, and other debris that may lead to sewer backups. Cleaning should be conducted more frequently for problem areas;
 - (b) Inspection of the condition of sanitary sewer structures and identifying areas that need repair or maintenance. Items to note may include cracked/deteriorating pipes; leaking joints or seals at manhole; frequent line blockages; lines that generally flow at or near capacity; and suspected infiltration or exfiltration;
 - (c) Monitoring of sewer flow to identify potential inflows and outflows; and
 - (d) Conduct repairs on priority based on the nature and severity of the problem;
 - (e) Immediate clearing of blockage or repair is warranted where an overflow is currently occurring or for urgent problems that may cause an imminent overflow (e.g., pump station failures, sewer line ruptures, or sewer line blockages).
 - Review previous sewer maintenance records to help identify “hot spots” or areas with frequent maintenance problems and locations of potential system failure, and conduct preventative maintenance, rehabilitation, or replacement of lines as needed;
 - When a spill, leak, and/or overflow occurs, keep sewage from entering the storm drain system by covering or blocking storm drain inlets or by containing and diverting the sewage away from open channels and other storm drain facilities (using sandbags, inflatable dams, etc.). Remove the sewage using vacuum equipment or use other measures to divert it back to the sanitary sewer system;
 - Prohibit/prevent disposal of wastewater/effluent from industrial units in the sewers; ensure regular checking to ensure no illegal entry of industrial wastewater into sewers;
 - Develop an ERS for the sewerage system leaks, burst and overflows, etc.;
 - Provide necessary health & safety training to the staff;
 - Provide all necessary personnel protection equipment;
 - During cleaning/clearing of manholes and sewer lines great precautions should be taken for the safety of workers conducting such works:
- (f) As far as possible use remote/CCTV mechanism to identify/detect the problems in sewers and do not engage persons for this purpose;
 - (g) As far as possible use mechanized cleaning of manholes and sewers by using modern techniques and machines and do not engage persons for this purpose;
 - (h) Ensure that maintenance staff and supervisors understand the risks; provide proper

- instructions, training and supervision;
- (i) Use gas detector to detect any hazardous or inflammable gas in confined areas like sewers/manholes prior to maintenance process;
 - (j) Provide suitable personal protective equipment that may include waterproof/abrasion-resistant gloves, footwear, eye and respiratory protection. Face visors are particularly effective against splashes. Equipment selection and a proper system for inspection and maintenance are important;
 - (k) Provide adequate welfare facilities, including clean water, soap, nail brushes, disposable paper towels, and where heavy contamination is foreseeable, showers;
 - (l) For remote locations portable welfare facilities should be provided;
 - (m) Areas for storage of clean and contaminated equipment should be segregated and separate from eating facilities;
 - (n) Provide adequate first-aid equipment, including clean water or sterile wipes for cleansing wounds, and a supply of sterile, waterproof, adhesive dressings;
 - (o) Make effective arrangements for monitoring the health of staff; and
 - (p) Keep emergency preparedness plan ready before starting the work of sewage system cleaning.

104. Biological hazards are among the environmental risks that may adversely impact the health and wellness of the workers and the community. Breakouts of diseases such as diarrhea, flu or pandemics such as the COVID19 shall be avoided. Designs and implementation of treatment systems shall ensure that disease-causing pathogens or viruses are disinfected and will not cause any health issues.

105. **Operation of FSSM.** Households of 13 Wards will be covered with FSSM system wherein which septage from individual septic tanks at houses will be collected via mobile/vehicle mount tankers with suction equipment, transport and discharged into STP for safe treatment and disposal. Although system will be completely mechanized, given the very harmful nature of septage, following precautionary measures shall be implemented:

- Create awareness program on the FSSM in general public;
- Implement health and safety plan for FSSM;
- Provide proper training to the workers, and staff in safe handling of FSSM tasks, provide all necessary personal protection equipment and ensure their usage;
- Ensure that the system is operated completely mechanically, with least involvement of workers; there shall be no direct contact of septage to any worker or staff;
- Ensure proper facilities for workers including showers, wash areas, toilets, drinking water, eating and resting places;
- Conduct regular health checks; and
- Ensure that tankers cleaning is done mechanically, and in the demarcate area at STP, and the wastewater generated in the process shall be discharged into STP.

Cumulative Impacts

106. Cumulative impacts are those that result from the successive, incremental, and/or combined effects of a project or activity when added to other existing, planned, and/or reasonably anticipated future ones. The subproject aims to improve urban water supply and sewerage in Dungarpur Town, by rehabilitating, augmenting, and creating required new infrastructure.

107. Both water supply and sewerage works are proposed to be taken up simultaneously in Dungarpur Town, which is a small town congested with people, traffic and activities. There are

sensitive places like hospitals, schools, and religious places. Works will be spread over entire town, covering all the roads and streets. Although no other notable public works are anticipated during the project implementation on public roads, there will be usual construction activities, such as building construction, as Dungarpur is a developing town. Given dry and windy weather conditions, dust generation from cumulative construction activities may be significant, and this may increase the particulate matter concentration in ambient air. Dust control measures suggested in the EMP aim to minimize the dust generation from the subproject construction activities. Suggested trenchless method, by avoiding excavation, will also help in reducing the overall dust generation from the subproject activities. If there are any road improvement works proposed to be implemented in Dungarpur, scheduling of works needs to be coordinated with the respective road agency (ULB or Public Works Department [PWD]) so that improved roads are not subjected for excavation. There is also a need to streamline water and sewer line works to avoid repeated excavations in the same road/street. The increase in road traffic, disturbance to traffic, public safety and worker safety issues, damage to existing utilities, influx of outstation workers, etc., due to various simultaneous construction works will be notable. However, the measures suggested in the EMP will minimize these impacts greatly, and therefore effective implementation of EMP must be ensured. Thus, the net impacts are unlikely to be significant.

108. Project Benefits. The citizens of the Dungarpur will be the major beneficiaries of the improved water supply and sewerage systems, as (i) they will be provided with a constant supply of better quality water, piped into their homes at an appropriate pressure; and (ii) the human waste from the homes will be removed rapidly, which otherwise would flow in open drains. This should improve the environment, should deliver major improvements in individual and community health and well-being. The project will improve the over-all health condition of the town as water borne diseases will be reduced. Diseases of poor sanitation, such as diarrhea and dysentery, should be reduced, so people should spend less on healthcare and lose fewer working days due to illness, so their economic status should also improve, as well as their overall health.

VII. PUBLIC CONSULTATION AND INFORMATION DISCLOSURE

A. Overview

109. The active participation of stakeholders including local community, NGOs/CBOs, and the media in all stages of project preparation and implementation is essential for successful implementation as well as operation of the project. It will ensure that the subprojects are designed, constructed, and operated with utmost consideration to local needs, ensures community acceptance, and will bring maximum benefits to the people. Public consultation and information disclosure is a must as per the ADB policy.

110. A three tier consultation process has been adopted for RSTDSP project: focus group discussions, primary household sample surveys and a town-level public consultation workshop. Most of the main stakeholders have already been identified and consulted during preparation of preliminary design and IEE, and any others that are identified during project implementation will be brought into the process in the future. Primary stakeholders of the subproject are: residents, shopkeepers and businesspeople who live and work alongside the roads in which network improvements will be provided, and government and utility agencies responsible for provision of services, Dungarpur Municipal Council, Public Health Engineering Department, and Rajasthan Pollution Control Board. Secondary stakeholder are: NGOs and CBOs working in the area, community representatives, beneficiary community in general, government agencies, the executing and implementing agencies (LSGD and RUDSICO-EAP), Government of India and the ADB.

B. Public Consultation

36. Informal and formal consultation are conducted with local population of the area, about at 8 places along with proposed alignment with about 54 persons in month of March and April 2022. Discussions were held about proposed project components, EMP measures, grievance redressal, ownership of land, tree cutting, wastewater, reuses of treated effluent of proposed STP, and general people perception for proposed project. **(Appendix 6).**

1. Consultation during Project Preparation

111. Institutional consultations were conducted with the Governmental Departments such as Local Self Government Department, Pollution Control Board, Public Health Engineering Department, Dungarpur Municipal Council, etc. The project proposals are formulated in consultation with Dungarpur Municipal Council and the proposals have been finalized only after certification of Municipal Council that the proposals suit the requirements of the ULB.

112. Focus-group discussions with residents and other stakeholders were conducted to learn their views and concerns. A social and environmental impact assessment has been conducted in the town, covering sample households and nearby vendors to understand the basic characteristics of town, health status, and the infrastructure service levels, and also the demand for infrastructure services.

113. It was observed that people are willing to extend their cooperation as the proposed activities are supposed to enhance the infrastructure service levels and the living standard of the public. The public expressed their concern regarding the nuisance and disturbance (dust, road closure and traffic management activities) during the construction stage which can have impact on their day to day activities. Public demanded for advance notice before construction and proper warning signs along the construction area to avoid accidents and inconvenience. Public opined that an appropriate operation and maintenance system should be in place, especially for sewerage system, for its best functioning and to have the maximum health and aesthetic benefits. Regarding water supply people were ready to bear cost of water through modern meters but demanded continuous supply of water in day. Regarding sewerage works people were demanding sewage house connections in whole town because they are suffering a lot due to unsafe sewage disposal in drains.

114. A town-level City Level Committee (CLC) has been formed in Dungarpur district by Government orders. City Level Committee meeting was organized during the initial design stage in which representatives of primary and secondary stakeholders were invited. Consultation were also conducted with the Khandeshwar Mahadev Mandir temple priest, the temple is located about 200 m upstream of STP location on Do river, he informed that a tube well is present in the temple premises which fulfil all water requirement in the temple. Temple is not using Do river water. CLC meeting was conducted on 30.06.2022 to discuss various issues like demand and supply gap in water supply, land availability, scope of works etc. under the chairmanship of District Collector in which representatives of primary and secondary stakeholders were invited. The feedback and concerns of the stakeholders have taken into consideration in detail designs of the project. Proposed works were approved by CLC members in this meeting. Minutes of Meeting of CLC vide dated 30.06.2022 and photographs are attached in **Appendix 6.**

2. Consultation During Construction

115. Prior to start of construction, Dungarpur Municipal Council and PIU with the assistance of Consultants conducting information dissemination sessions at major intersections and solicit the help of the local community leaders/prominent citizens to encourage the participation of the people to discuss various social and environmental issues. At each ward/neighborhood level, focus group meetings were conducted to discuss and plan construction work with local communities to reduce disturbance and other impacts, and provide a mechanism through which stakeholders can participate in project monitoring and evaluation.

116. A constant communication is being established with the affected communities to redress the environmental issues likely to surface during construction and operational phases and also regarding the grievance redress mechanism. Municipal Council /PIU with the help of Community Awareness and Participation Consultant (CAPC) will organize public meetings and will appraise the communities about the progress on the implementation of EMP. Meeting will also be organized at the potential hotspots/sensitive locations before and during the construction.

117. A stakeholder consultation was conducted by RUIDP-PIU Dungarpur at Collectorate EPD-Meeting Hall, Dungarpur on dated 05.04.2023 in which ADM Dungarpur, Chairaman Nagar Parishad, Executive Engineer PHED & PWD Dungarpur, and elected Parshad participated I the meeting. Details of this Stakeholder Consultation are provided in the **Appendix 6**.

118. Mr. Hemendra Nagar (ADM-Dungarpur) and Mr. Amrit Lal Kalasua Chairman (Nagar Parishad Dungarpur) discussed about need of this proposed project for Dungarpur City. Elected Ward Member's suggested that contractor and project implementation unit need to engage with councillors of wards, prior to commencement of works and suggestion of councillors need to be incorporated during implementation of the project.

C. Information Disclosure

119. Executive summary of the IEE will be translated in the local language and made available at the offices of Municipal Council, RUDSICO-EAP- PMU and PIU. Copies of summary was provided to participants of city level workshop to be organized in Dungarpur. Hard copies of the IEE will be accessible to citizens as a means to disclose the document and at the same time creating wider public awareness. Electronic version of the IEE in English and Executive Summary in Hindi will be placed in the official website of the Municipal Council /RUDSICO-EAP after approval of the IEE by Government and ADB. Stakeholders will also be made aware of grievance register and redress mechanism.

120. Public information campaigns via newspaper/radio/TV, to explain the project details to a wider population were conducted primary by circulating pamphlets. Public disclosure meetings will be conducted at key project stages to inform the public about the progress and future plans. Prior to start of construction, the PIU will issue Notification on the start date of implementation in local newspapers A board showing the details of the project will be displayed at the construction site for the information of general public.

121. Local communities are continuously consulted regarding location of construction camps, access and hauling routes and other likely disturbances during construction. The road closure together with the proposed detours will be communicated via advertising, pamphlets, radio broadcasts, road signage, etc.

122. Project related information shall be disclosed through public consultation and making relevant documents available in public locations. PMU and PIUs shall provide relevant safeguards information in a timely manner, in an accessible place and in a form and languages understandable to affected person and other stakeholders. For illiterate people, other suitable communication methods will be used. Before start of construction works, social outreach team (SOT) of contractor and CAPP team are providing advance public notice/ public information by distributing pamphlets showing works details, toll free complaint registration number, also by individual consultation with each and every household and shop owner of the area/section.

123. The following documents shall be made available at the offices of project agencies - PMU, PIU and Block level offices for public reference, and shall also be uploaded on respective websites.

- (i) Summary of project and draft IEE (in Hindi and English);
- (ii) Draft IEE Report (in English);
- (iii) Final IEE Report (in English);
- (iv) Updated/amended IEE (in English);
- (v) Corrective action plan prepared during project implementation (English); and
- (vi) Semi-annual Environmental Monitoring Reports (English).

124. A concise summary of project and draft IEE report (in Hindi), providing all necessary details of designs, implementation arrangements, subproject locations, likely issues and mitigation and monitoring measures and grievance redress mechanism, shall be made available to the stakeholders at consultation meetings. This should also provide contact information of project agency. This summary shall also be displayed at the notice boards of PMU, PIU and other public places. During project implementation, relevant information about any major changes to project scope will be shared with beneficiaries, affected persons, vulnerable groups, and other stakeholders. Draft IEE has already been posted on ADB and RUDSICO website. Further, the following will be again posted on ADB website.. PMU will send written endorsement to ADB for disclosing these documents:

- (i) final IEE;
- (ii) a new or updated IEE and corrective action plan prepared during project implementation, if any; and
- (iii) environmental monitoring reports.

VIII. GRIEVANCE REDRESS MECHANISM

A. Project Specific Grievance Redress Mechanism

125. A project-specific, three-tier grievance redress mechanism (GRM) covers both environment and social issues. The GRM was established on 20 January 2023 in Dugarpur to receive, evaluate, and facilitate the resolution of affected persons' concerns, complaints, and grievances about the social and environmental performance at project level. The GRM will aim to provide a time-bound and transparent mechanism to voice and resolve social and environmental concerns related to the project. Assessment of the GRM designed and implemented for Rajasthan Urban Sector Development Program (RUSDP)¹⁷ the system was effective in timely resolution of

¹⁷ The procedures followed for grievance redress during implementation of RUSDP Phase III included the project GRM and the pilot GRM software application (smart check) in Pali, the Sampark portal of Government of Rajasthan, and the Chief Minister's helpline. Complaints received through various channels were mostly minor and pertained to

grievances in a transparent manner.¹⁸ The multichannel, project-specific, three-tier GRM is functional at RUSDP, hence the design of GRM for RSTDSP takes into account the proposed institutional structure for RSTDSP and the positive features and learnings from the previous GRM.¹⁹

126. Common Grievance Redress Mechanism. A common GRM is in place for social, environmental, or any other grievances related to the project. Implementation of the resettlement plans/RIPPs/DDR/IEEs will follow the GRM described below. The GRM will provide an accessible and trusted platform for receiving and facilitating resolution of affected persons' grievances related to the project.

127. Public awareness campaigns within entire ULB/Municipal area will ensure that awareness on grievance redress procedures is generated. The nodal officer- social/environment at field level through community awareness and public participation consultant (CAPPC) will conduct ULB/Municipal area-based awareness campaigns to ensure that poor and vulnerable households are made aware of grievance redress procedures and entitlements. Contractors will provide pamphlets to communities prior to start of works and billboards during construction. The pamphlets and billboards will include relevant environmental and social safeguards, GRM information, and contact details of key personnel from PIU and contractors.

B. Grievance Redress Process

128. Affected persons will have the flexibility of conveying grievances/suggestions by dropping grievance redress/suggestion forms in complaint/suggestion boxes that will be installed by project PIUs or by e-mail, by post, or by writing in a complaints register in ULB offices/complaints register at contractor's work site²⁰ or by sending a WhatsApp message to the PIU²¹ or by dialling the phone number of town level PIU/CAPPC or by dialling a toll-free number.²² Any aggrieved person can also avail the facilities of online grievance monitoring system 'Rajasthan Sampark' portal to

damage to existing water supply pipelines and disruption of water supply during construction, delays in road restoration, and pending new connections. Complaints related to damage to private property (compound walls/steps, etc.) were less in number. The grievances were mostly possible to resolve in coordination with the contractors. Complaints received were immediately referred by the CAPC/PMDSC supervision staff to the PIU Nodal officer (safeguards) and concerned engineer at PIU, who advised them on further action. Follow up with the contractor on complaint resolution was undertaken by PIU Nodal officer CAPC and PMDSC and final feedback sought from complainant upon resolution. Complaints requiring inter-departmental coordination were referred to the PMU for resolution, and feedback provided to complainant. The PMU kept regular track of grievances through WhatsApp and email alerts, ensuring registration and follow-up until resolution.

¹⁸ Town-level grievance registration data indicates that a large number of grievances were registered, pointing to the effectiveness of the multi-channel GRM. No major grievance was received for RUSDP Phase III. The GRM helped smoothen the process of project implementation, hence the proposed architecture for the RSTDSP GRM remains similar, with some refinement, taking into account the changes in institutional setup proposed for project implementation.

¹⁹ Continued logistics support at field level will be key to successful management of grievance redress under RSTDSP. The target date for establishment of the first level (PIU level) and second level (Zonal level) of GRM is before loan negotiation.

²⁰ RUSDP piloted an online application based live GRM counter for resolution of public grievances over and above the usual process of grievance registration and redressal. This app based GRM - "RUIDP Smart Check" is available at Google play store (free of cost) and is operational. The RUIDP Smart Check "app" was launched in Pali town in July 2017 and is proposed to be scaled up in RSTDSP project towns. For persons without access to the application, the traditional channels will continue to be available.

²¹ It is suggested for each PIU to have a dedicated WhatsApp group for registration of grievances and receipt of quick feedback, to be followed by more formal communication.

²² Project contractors in all project towns will have a toll-free number with specific working hours for registration of grievances related to RSTDSP.

register their grievances which is a parallel mechanism of grievance registration, in addition to the project GRM.²³ Careful documentation of the name of the complainant, date of receipt of the complaint, address/contact details of the person, location of the problem area, and how the problem was resolved will be undertaken and feedback provided to the complainant on action/decision taken. The Safeguard and safety officer of town/city level PIU will have the overall responsibility for timely grievance redressal on environmental and social safeguards issues and for registration of grievances, related disclosure, with the assistance of project consultants. In case of grievances that are immediate and urgent in the perception of the complainant, the contractor, and officials of PIU with assistance from CMSC and CAPPCC on-site will provide the most easily accessible or first level of contact for quick resolution of grievances. Contact numbers and names of the concerned PIU safeguard and safety officer, contractors, CAPPCC and CMSC personal will be posted at all construction sites at visible locations.

(iv) **1st level grievance.** The contractors, PIU executive engineer/assistant engineer designated as safeguard and safety officer (social and environment), CMSC (safeguard staff) and CAPPCC can immediately resolve issues on-site, in consultation with each other and will be required to do so within 7 days of receipt of a complaint/grievance. If required, city level monitoring committee (CLMC)²⁴ will be involved in resolution of grievances at the 1st level;

(v) **2nd level grievance.** All grievances that cannot be redressed within 7 days at field/PIU level will be brought to the notice of Zonal PIU headed by Additional Chief Engineer (ACE). The ACE at zonal PIU will resolve the grievance within 7 days of receipt of complaint/grievance in discussion with the ASO, field level PIU, CMSC, CAPPCC and the contractor; and

(vi) **3rd level grievance.** All the grievances that are not addressed by Zonal PIU within 7 days of receipt will be brought to the notice of the PMU. Depending on the nature of grievance, the project officer (social/environment) at PMU will resolve the grievance within 15 days of receipt of grievance with necessary coordination of Zonal PIU and CMSC and guidance/instruction of additional project director (APD-PMU)..

(vii) Grievances not redressed through this process within/at the project level within stipulated time period will be referred to the CLC/GRC, which has been set up.²⁵ In its role as a GRC, the CLC will meet whenever there is an urgent, pending grievance. Other grievances can be discussed during its regular meetings. Zonal PIU will inform the CLC regarding any grievances required to be resolved urgently. The GRC will resolve the grievance within 15 days of receiving the complaint. In case of any indigenous peoples impacts in subprojects, the CLC/GRC must have representation of the affected indigenous people community, the chief of the tribe or a member of the tribal council as traditional arbitrator (to ensure that traditional grievance redress systems are integrated) and an NGO working with indigenous people groups.

(viii) The multi-tier GRM for the project is outlined below (**Figure 25**), each tier having time-


²³ <http://www.sampark.rajasthan.gov.in/RajSamWelcome.aspx>

²⁴ The CLMC has been formed at the town/city level for planning and monitoring of work, resolve issues related to departmental coordination etc. It is headed by Commissioner/Executive Officer ULB (Chairman) and city engineer of public health engineering department (PHED), public works department (PWD) and head of PIU acting as Member Secretary.

²⁵ City Level Committee (CLC)/grievance redress committees (GRCs) has been constituted for each town/city under the Chairmanship of District Collector to provide overall subproject guidance and "to sort out issues and remove hindrances, if any". CLC formed at city-level/district level with members composed of: District Collector as Chairperson, and following as members: ULB Commissioner/Mayor/Chairman; Deputy Mayor/Vice Chairman ULB; Chairman/Secretary Urban Improvement Trust (UIT); Head of Zonal/field level PIU as Member Secretary; one representative each from relevant government departments as appropriate (PWD/PHED/Town Planning Department etc.). All CLCs in their role as GRCs will have at least one-woman member/chairperson. In addition, for project-related grievances, representatives of affected persons, community-based organizations (CBOs), and eminent citizens will be invited as observers in GRC meetings. The concerned Member of Parliament (MP) and Member of Legislative Assembly are also part of the CLC.

bound schedules and with responsible persons identified to address grievances and seek appropriate persons' advice at each stage, as required. The GRC will continue to function throughout the project duration.

Figure 25: Grievance Redress Process

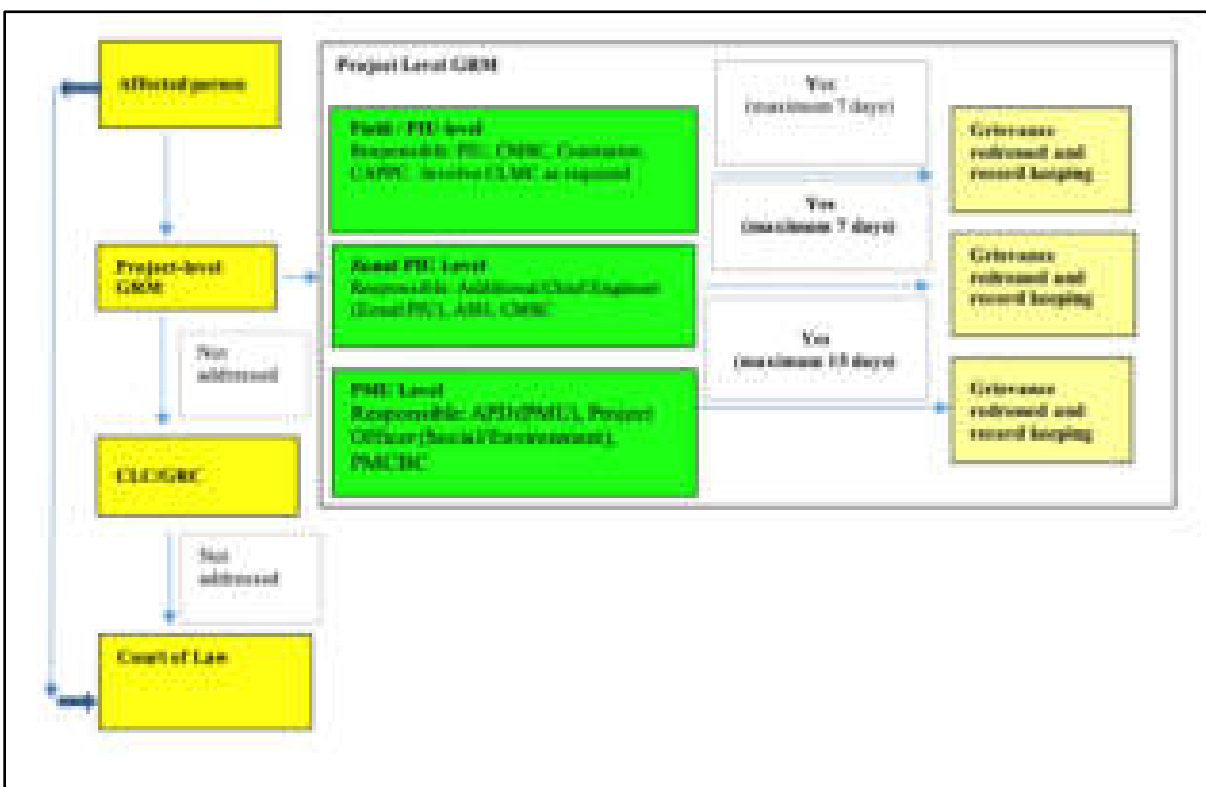

APD = Additional Project Director, ASO = Assistant Safeguards Officer, CAPPC = community awareness and public participation consultant, CMSC = construction management and supervision consultants, CLC = city level committee, CLMC = city level monitoring committee, GRC = grievance redress committee, PIU = project implementation unit, PMU = program management unit, PMCBC = project management and capacity building consultant.

129. The project GRM notwithstanding, an aggrieved person shall have access to the country's legal system at any stage and accessing the country's legal system can run parallel to accessing the GRM and is not dependent on the negative outcome of the GRM. In case of grievance related to land acquisition, resettlement and rehabilitation, the affected persons will have to approach a legal body/court specially proposed under the Right to Fair Compensation and Transparency in Land Acquisition, Rehabilitation and Resettlement Act (RFCTLARRA), 2013.²⁶

130. People who are, or may in the future be, adversely affected by the project may submit complaints to ADB's Accountability Mechanism. The Accountability Mechanism provides an independent forum and process whereby people adversely affected by ADB-assisted projects can voice, and seek a resolution of their problems, as well as report alleged violations of ADB's operational policies and procedures. Before submitting a complaint to the Accountability Mechanism, affected people should make an effort in good faith to solve their problems by working

²⁶The Authority admits grievance only with reference to the Land Acquisition and R&R issues under the RFCTLARRA, 2013.

with the concerned ADB operations department. Only after doing that, and if they are still dissatisfied, should they approach the Accountability Mechanism²⁷.

131. **Record-keeping.** The PIU of each town and PMU will both keep records of grievances received, including contact details of complainant, date the complaint was received, nature of grievance, agreed corrective actions and the date these were affected and final outcome. The number of grievances recorded and resolved and the outcomes will be displayed/disclosed in the PMU office, PIU offices, and on the web, as well as reported in monitoring reports submitted to ADB on a semi-annual basis.

132. **Periodic review and documentation of lessons learned.** The PMU Project Officer (Environment) will periodically review the functioning of the GRM in each town and record information on the effectiveness of the mechanism, especially on the project's ability to prevent and address grievances.

133. **Costs.** Contractors are required to allocated budget for pamphlets and billboards as part of the EMP. Costs involved in resolving the complaints (meetings, consultations, communication and reporting/information dissemination) will be borne by the concerned PIU at town level while costs related to escalated grievances will be met by the PMU. Cost estimates for grievance redress are included in resettlement cost estimates.

134. Presently GRC in 14 ongoing project towns are functional as per RSTDSP's Grievance Redress Mechanism (GRM). Therefore 2nd and 3rd level GRC are already functional at Zonal PIUs (at Jaipur and Jodhpur) and PMU levels. PIU level GRC shall be formed in upcoming project towns after PIUs in new towns are established through office order from PMU for the same.

IX. ENVIRONMENTAL MANAGEMENT PLAN

A. Environmental Management Plan

135. The purpose of the environmental management plan (EMP) is to ensure that the activities are undertaken in a responsible, non-detrimental manner with the objectives of: (i) providing a proactive, feasible, and practical working tool to enable the measurement and monitoring of environmental performance on-site; (ii) guiding and controlling the implementation of findings and recommendations of the environmental assessment conducted for the project; (iii) detailing specific actions deemed necessary to assist in mitigating the environmental impact of the project; and (iv) ensuring that safety recommendations are complied with.

136. A copy of the EMP must be kept at work sites at all times. The EMP was included in the bid documents and will be further reviewed and updated during implementation. The EMP will be made binding on all contractors operating on the site and was included in the contractual clauses. Non-compliance with, or any deviation from, the conditions set out in this document constitutes a failure in compliance.

137. For civil works, the contractor will be required to (i) establish an operational system for managing environmental impacts (ii) carry out all of the monitoring and mitigation measures set forth in the EMP; and (iii) implement any corrective or preventative actions set out in safeguards monitoring reports that the employer will prepare from time to time to monitor implementation of this IEE and EMP. The contractor shall allocate budget for compliance with these EMP measures, requirements and actions. EMP for various stages is given in **Tables below**.

²⁷ Accountability Mechanism. <http://www.adb.org/Accountability-Mechanism/default.asp>

Table 30: Design Stage Environmental Management Plan

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
Water Treatment Plant (WTP)	Inefficient treatment, treated water characteristics not satisfying the standards	i) Design treatment process that is suitable for raw water source characteristics duly considering the seasonal variation in quality if any (ii) Duly consider quality of groundwater that will be supplemented for surface water supply variations (iii) Treated water and supplied water at consumer end should meet the drinking water standards all times	DBO Contractor/PIU	Design consultants' cost
Water Treatment Plant (WTP)	Design to prevent pollution due to wastewater and sludge	Ensure that the following are included in the WTP design: (i) Backwash water reuse system and sludge recovery and disposal system (ii) Backwash recycling components: Filter backwash holding tank, recovered water storage tank and pumping for recycling (iii) Sludge management system components: Gravity thickeners for sludge from clarifiers, mechanical sludge dewatering system, storage facility for dewatered sludge (iv) Disposal of sludge at a landfill or the disposal site provided by the ULB	DBO Contractor/PIU	Project costs
WTP, CWRs and STP	Hazardous / harmful chemicals	(i) Reduce the use of chemicals in the treatment process to the extent possible (water treatment); provide non-chemical alternatives or easily recoverable and/or reusable chemicals or biocompatible alternatives. (ii) Establish proper handling / storage / application system according to the relevant standards, safety precautions and prevent accidental release / spill (iii) Provide leak/spill detection, collection / capture and safe disposal facilities such as chlorine absorption and neutralization facility (iv) Provide ventilation, lighting, entry and exit facilities; visible & audible alarm facilities to alert chemical/chlorine leak (v) Facility for isolation in the event of major leakages (vi) Eye wash & shower facility (vii) Personal protection and safety equipment for the operators (masks, oxygen cylinders, gloves, etc.,)	DBO Contractor/PIU	Project costs

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
		(viii) Provide training to the staff in safe handling and application of chemicals, material safety, and standard operating procedures and emergency responses (ix) Develop emergency response procedures		
Design of Sewage Treatment Plant	Treated effluent not meeting the disposal standards and associated impacts on receiving environment	STP design to meet latest norms for wastewater disposal into inland water bodies (ref Appendix C-8 for detailed parameters) including: BOD < 10 mg/l Total Suspended Solids < 20 mg/l Fecal coliform < 100/100 ml	Consultants / PMU	Project Costs
	Impairment of STP treatment efficiency	Ensure continuous uninterrupted power supply (i) Provide back-up facility (such as generator) and make sure that adequate fuel supplies during operation for running of generator when required; (ii) Provide operation and maintenance manual with all standard operating procedures (SOPs) for operation and maintenance of the facility; this should include guidance on the follow up actions in case of process disruptions, inferior quality of treated water; etc. Necessary training (hands-on and classroom / exposure visits) shall be provided to the ULB staff dealing with STP. (iii) The scope of work of facility contractor should include extended operation period (at least five years) to ensure smooth operation, training to the ULB staff and transfer of facility to Dungarpur Municipal Council (iv) Design should include online monitoring for the minimum BOD, pH and Ammonia at the inlet and outlet of the plant	Consultants / PMU	Project Costs
	Mixing of industrial effluent with sewage	No industrial wastewater shall be allowed to dispose into municipal sewers No domestic wastewater from industrial units shall be allowed into municipal sewers (i) Ensure that there is no illegal discharge through manholes or inspection chambers (ii) Conduct public awareness programs; in coordination with RSPCB, issue notice to all industries for compliance	PIU / ULB	Project Costs

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
		(iii) Conduct regular wastewater quality monitoring (at inlet and at outlet of STP) to ensure that the treated effluent quality complies with the standards		
STP	Treated effluent discharge into West Do River, and associated impacts on river water and downstream users	(i) Obtain of consent of RPCB for discharge of treated wastewater into West Banas River (ii) Conduct a baseline water quality assessment of receiving water body – Do River at the discharge location (iii) Regularly monitor the treated wastewater quality at STP and ensure that it meets the discharge standards (iv) Monitor water quality periodically during operation phase as per the Environmental Monitoring Plan	DBO Contractor/ PIU	Project Costs
STP	Sludge management and reuse	(i) Prepare a sludge management plan (ii) Prepare a dried Sludge utilization plan for Dungarpur within the help of Agriculture Department / CLC; plan should also include if any additional processing is required for sludge to use as soil conditioner (iii) Plan should clearly various potential uses and demand in Dungarpur and surroundings (iv) Establish usage limits, where required, (geographical / crops / type of application / type of soils etc.); adopt international good practice suggested by agencies like World Health Organization (WHO), Food and Agricultural Organization (FAO) of the United Nations. (v) Identify a landfill / suitable site for disposal of surplus dried sludge (vi) Monitor sludge quality during operation phase as per the Environmental Monitoring Plan, ensure that it meets the quality parameters established by FCO In case of sludge not meeting the quality parameters, it shall not be used as soil condition, and shall be disposed at appropriate disposal site (if it falls under hazardous category, it shall be disposed as per the Hazardous Waste Management Rules, 2016)	DBO Contractor/ PIU	Project costs
Sewer network – collection & conveyance	Poor design leading to overflows, blockages, and creating nuisance, pollution	(i) Limit the sewer depth where possible (ii) Sewers shall be laid away from water supply lines and drains (at least 1 m, wherever possible);	DBO Contractor / PIU	Project costs

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
		(iii) In all cases, the sewer line should be laid deeper than the water pipeline (the difference between top of the sewer and bottom of water pipeline should be at least 300 mm) (iv) In unavoidable, where sewers are to be laid close to storm water drains, appropriate pipe material shall be selected (stoneware pipes shall be avoided) (v) For shallower sewers and especially in narrow roads, use small inspection chambers in lieu of manholes; (vi) Design manhole covers to withstand anticipated loads & ensure that the covers can be readily replaced if broken to minimize silt/garbage entry (vii) Ensure sufficient hydraulic capacity to accommodate peak flows and adequate slope and gas vents in gravity mains to prevent buildup of solids and hydrogen sulfide generation (viii) Take necessary precautionary measures to protect sewer network, and to avoid disposal of solid wastes, debris, wastewater into newly laid sewers from the time it is constructed to the start of operation phase		
FSSM	Occupational health and safety issues, and impact on STP process	(i) Conduct detailed survey of the households to be covered with FSSM to design the system to suit the local conditions, such as type of septic tanks and their location in the houses (ii) Create awareness program on the FSSM from collection to treatment system that will be adopted (iii) Design the sewage treatment process duly considering mixing of septage (iv) Ensure that the FSSM system is completely mechanized no human touch, even accidentally, from collection at household to discharge into STP, and in periodic cleaning of tankers (v) Demarcate a proper area for cleaning of mobile tankers in STP premises, and ensure that the wastewater shall be discharged into STP	DBO Contractor / PIU	Project costs

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
		(vi) Provide proper training to the workers, and staff in safe handling of FSSM tasks, provide all necessary personal protection equipment (vii) Ensure proper facilities for workers including showers, wash areas, toilets, drinking water, eating and resting places (viii) Conduct regular health checks (ix) Prepare Health and Safety Plan for FSSM		
Asbestos cement (AC) pipes in existing water supply system: clearing, transfer and disposal; work in narrow streets, and interventions in existing AC pipelines	Health impacts due to air borne asbestos if handled unsafely, cut, drilled or broken into pieces	(i) Develop ACM Management Plan (AMP) that includes identification of hazards, the use of proper safety gear and disposal methods. Sample AMP is provided in Appendix C-20. Adhere to the workflow process suggested in IEE (ii) Conduct awareness program on safety during the construction work (iii) Undertake the construction work stretch-wise; excavation, pipe laying and trench refilling should be completed on the same day (iv) Provide barricades, and deploy security personnel to ensure safe movement of people and also to prevent unnecessary entry and to avoid accidental fall into open trenches (v) Identify risk of intervention with existing AC pipes. If there is significant risk, implement the AMP strictly that includes identification of hazards, the use of proper safety gear and disposal methods. (vii) Maintain records of AC pipes as per the AMP (viii) Refer to the instructions of the Asbestos Expert	DBO Contractor/PMU	Project costs
Asbestos materials in existing PHED campus	Health impacts due to air borne asbestos if handled unsafely, cut, drilled or broken into pieces	(i) Conduct survey and inventory of existing asbestos materials on site (ii) Conduct risk assessment to determine extent of asbestos materials currently on-site (ii) Coordinate and provide support to the asbestos management service provider on the requirement of sampling, testing and disposing existing asbestos materials (iii) Ensure the selected area for temporary storage is suitable for safe storage of asbestos materials	DBO Contractor/PMU	Project costs

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Cost and Source of Funds
		(iv) Incorporate international and national standards considered in designing the temporary storage (v) Ensure that handling and disposal of asbestos materials are carried out by specially trained service provider/s following Government of India requirements, or in their absence, internationally recognized procedures Refer to the requirements of the Asbestos Management Plan and instructions of the Asbestos Expert		
Location impacts of proposed components	Nearby community may be affected due to increased pollution during construction and operation	(i) sites should be selected so that nearby community may have no or minimum impact due to proposed works (ii) Mitigation measures are prepared and included in design and EMP is attached with contract documents	Consultants/PMU	No cost required
Requirement of tree cutting	Tree cutting may result loss of aesthetics and increase in air pollution	(i) sites should be selected so that minimum tree cutting is required (ii) project documents should include the minimum tree cutting provisions (iii) Provision for Compensatory plantations should be included in contract documents	Consultants/PIU/PMU	No cost required
Energy Efficiency	Loss of natural resources	(i) Use energy efficient electrical equipment (ii) Provision of use of energy efficient equipment in contract agreements and BOQ	Consultants/PMU	No cost required
Incorporating EMP and Health and Safety requirements into Contractor Bid Document	Implementation of the EMP	The EMP should be included in the Bid Document so that the selected Contractor understands the issues and makes necessary plans to prepare and implement the EMP	PMU	Project Costs
	Implementation of the Health and Safety measures by contractor	Health and safety requirements should be incorporated as part of the contract bid document so that the selected Contractor understands the issues and makes necessary plans to prepare and implement the health and safety requirements.	PMU	Project Costs
Preparation of plans and protocols	Various impacts	(i) Preparation of ACM Management Plan (ii) Prepare traffic management plan (iii) Prepare occupational health and safety plan (iv) Prepare spoils management plan	DBO Contractor and CMSC with the assistance of PMCBC (for ACM plan)	Project costs

Table 31: Environmental Management Plan of Anticipated Impacts during Pre-Construction

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
Compliance with environmental subproject selection criteria	Environmental impacts due to subproject	Compliance with environmental subproject selection criteria A compliance checklist is appended to this report (Appendix 2)	Consents, permits, clearance, NOCs, etc. A compliance checklist is appended to this report (Appendix 2)	PIU and Dungarpur Municipal Council	PMU	No costs required
Legal compliance	Environmental legal noncompliance may attract legal actions Failure to obtain necessary consents, permits, NOCs etc. can result to design revisions and/or stoppage of works	(i) Obtain all consents, clearances (CTE/CTO from RSPCB), permits NOCs etc. before start of construction works Ensure that all necessary approvals for construction to be obtained by contractor are in place before start of construction	Consents, permits, clearance, NOCs, etc.	PIU/Consultants in coordination of Dungarpur Municipal Council	PMU	Cost of obtaining all consents, permits, clearance, NOCs etc. prior to start of civil works responsibility of PIU.
Environmental monitoring of baseline conditions of air, noise, <u>water</u> and soil	To establish base line environmental conditions	Environmental monitoring through NABL approved laboratory	Environmental Monitoring Report of Air, noise, <u>soil</u> and water quality	Construction contractor	Consultants/PIU	Contractor
Utilities	Telephone lines, electric poles and wires, water lines and gas pipelines within proposed project area	Identify and include locations and operators of these utilities in the detailed design documents to prevent unnecessary	-List and maps showing utilities to be shifted -Contingency plan for services disruption	Contractor in collaboration with PIU and with approval of PMU	CMSC/ PIU	No cost required. Mitigation measures are part of TOR of PMU, <u>PIU</u> and Consultants

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
		disruption of services during construction phase; and (ii) Require construction contractors to prepare a contingency plan to include actions to be taken in case of unintentional interruption of services. (iii) Require contractors to prepare spoils management plan (Appendix C-13) and traffic management plan (Appendix C-14)				
Construction work camps, hot mix plants, stockpile areas, storage areas, and disposal areas.	Disruption to traffic flow and sensitive receptors	Prioritize areas within or nearest possible vacant space in the project location. If it is deemed necessary to locate elsewhere, consider sites that will not promote instability and result in destruction of property, vegetation, irrigation, and drinking water supply systems.	-List of pre-approved sites for construction work camps, areas for stockpile, <u>storage</u> and disposal -Waste management plan	Contractor to finalize locations in consultation and approval of PIU	CMSC/ PIU	No cost required. Mitigation measures are part of TOR of PIU and Consultants and also part of contractual terms

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
		Do not consider residential areas. Written consent of landowners/ (not lessee/s) for reuse of excess spoils to agricultural land Take extreme care in selecting sites to avoid direct disposal to water body which will inconvenience the community. (v) For excess spoil disposal, ensure (a) site shall be selected preferably from barren, infertile lands. In case agricultural land needs to be selected, written consent from landowners (not lessees) will be obtained; (b) debris disposal site shall be at least 200 m away from surface water bodies; (c) no residential areas shall be located within 50 m downwind side of the site; and (d) site is minimum 250 m away from sensitive				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
		locations like settlements, ponds/lakes or other water bodies.				
Sources of Materials	Extraction of materials can disrupt natural land contours and vegetation resulting in accelerated erosion, disturbance in natural drainage patterns, ponding and water logging, and water pollution.	Prioritize sites already permitted by the Department of Mines and Geology. If other sites are necessary, inform construction contractor that it is their responsibility to verify the suitability of all material sources and to obtain the approval of PMU and If additional quarries will be required after construction is started, inform construction contractor to obtain a written approval from PIU. Bid document to include requirement for verification of suitability of sources and permit for additional quarry sites if necessary.	Permits issued to quarries/sources of materials	Contractor to prepare list of approved quarry sites and sources of materials with the approval of PIU	CMSC/ PIU	No cost required. Mitigation measures are part of TOR of PIU and Consultants and, also part of contractual terms
Consents, permits,	Failure to obtain necessary consents, permits, NOCs, etc.	Obtain all necessary consents (including CTE for STP from	Consents, permits, clearance, NOCs, etc.	PIU and Consultants	CMSC/ PIU	No cost required. Cost of obtaining all consents,

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
clearances, NOCs, etc.	can result to design revisions and/or stoppage of works	RSPCB). permits, clearance, NOCs, etc. prior to award of civil works. (following consents are required- Tree cutting- local authority Storage, handling and transport of hazardous materials- RSPCB Sand mining, quarries, borrow areas- Department of mines and Geology Traffic diversion/road cutting- local authority, traffic police Ensure that all necessary approvals for construction to be obtained by contractor are in place before start of construction. Acknowledge in writing and provide report on compliance all obtained consents, permits, clearance, NOCs, etc.				permits, clearance, NOCs, etc. prior to start of civil works responsibility of PIU. Mitigation measures are part of TOR of PIU and Consultants

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Implementation	Monitoring of Mitigation	Cost Source and of Funds
		include in detailed design drawings and documents all conditions and provisions if necessary				

Table 32: Environmental Management Plan of Anticipated Impacts during Construction

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
EHP Implementation Training	Irreversible impact to the environment, workers, and community	(i) Project manager and all key workers will be required to undergo EHP implementation including spoils management, Standard operating procedures (SOP) for construction works, occupational health and safety (OH&S), core labor laws, applicable environmental laws, etc. (ii) Contractor has to depute a qualified EHS personnel in the start of the project to conduct training to all the personnel and effective monitoring of mitigation measures during construction.	Training Plan and its implementation Achievement of the environmental performance targets by the Contractor.	Construction Contractor	CMSC/ PIU	Cost of EHP Implementation Orientation Training to contractor is responsibility of PMU. Other costs responsibility of contractor.
Air Quality	Emissions from construction vehicles, equipment, and machinery used for installation of pipelines resulting to dusts and	(i) Consult with PIU on the designated areas for stockpiling of clay, soils, gravel, and other construction materials. (ii) Damp down exposed soil and any stockpiled material on site by water sprinkling necessary during dry weather. (iv) Use tarpaulins to cover sand and other loose material when transported by trucks; and	-Visual inspection -No complaints from sensitive receptors -Records -PUC certificates - CTE and CTO. -Periodic Air Quality Monitoring.	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
	Increase in concentration of vehicle-related pollutants such as carbon monoxide, sulphur oxides, particulate matter, nitrous oxides, and hydrocarbons	(v) Fit all heavy equipment and machinery with air pollution control devices which are operating correctly. (vi) Quarterly environmental monitoring for ambient air as per EMP				
Water quality	Mobilization of settled silt materials, and chemical contamination from fuels and lubricants during installation of pipelines can contaminate nearby surface water quality.	(i) Prepare and implement a silt management plan. (ii) Avoid stockpiling of earth fill especially during the monsoon season unless covered by tarpaulins or plastic sheets. (iii) Install temporary silt traps or sedimentation basins along the drainage leading to the water bodies. (iv) Place storage areas for fuels and lubricants away from any drainage leading to water bodies. (v) Dispose any wastes generated by work in designated sites, and (vi) Conduct surface quality Monitoring according to the Environmental Management Plan (EMP).	Areas for stockpiles, storage of fuels and lubricants and waste materials. -Number of silt traps installed along trenches leading to water bodies. -Records of surface water quality monitoring. -Effectiveness of water management measures. -No visible degradation to nearby drainages, nullahs or waterbodies due to civil works	Construction Contractor	CMSC/ PAU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
Noise Levels	Increase in noise level due to earth-moving and excavation equipment, and the transportation of equipment, materials, and people	(i) Plan activities in consultation with PIU/Consultants so that activities with the greatest potential to generate noise are conducted during periods of the day which will result in least disturbance; (ii) Horns should not be used unless it is necessary to warn other road users or animals of the vehicle's approach; (iii) Minimize noise from construction equipment by using vehicle silencers, fitting jackhammers with noise-reducing mufflers, and portable street barriers the sound impact to surrounding sensitive receptor; and (iv) Maintain maximum sound levels not exceeding 80 decibels (dba) when measured at 10 m or more from the vehicle/s. (v) Quarterly environmental monitoring for ambient noise as per EMP	-Complaints from sensitive receptors; -Use of silencers in noise-producing equipment and sound barriers; -Equivalent day and nighttime noise levels (see Appendix C-6)	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.
Ground Water Quality	Contamination of ground water quality due to spillage of oil and lubricants	Prepare and implement a spills management plan; Provide impermeable liner on the ground and place layer of mortar or concrete over it in the oil and lubricants storage areas, provide spillage trap in oil and lubricant store, use dip tray and pump to pour oil from oil and lubricant drums; Dispose any oil contaminated wastes generated by construction activities in scientific manner; and Conduct ground water quality monitoring according to the EMP	-CTO and CTE compliance; -Periodic G/W Quality Monitoring Reports; -Areas for storage of fuels and lubricants and waste materials; - Number of oil traps installed in oil and lubricant storage areas;	Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
Landscape and aesthetics	Impacts due to excess excavated earth, excess construction materials, and solid waste such as removed concrete, wood, packaging materials, empty containers, spoils, oils, lubricants, and other similar items.	(i) Prepare and implement spoils management plan; (ii) Avoid stockpiling of excess excavated soils; (iii) Coordinate with ULB/PIU for beneficial uses of excess excavated soils or immediately dispose to designated areas; (iv) Recover used oil and lubricants and reuse or remove from the sites; (v) Manage solid waste according to the following preference hierarchy: reuse, recycling and disposal to designated areas; (vi) Remove all wreckage, rubbish, or temporary structures which are no longer required; and (vii) Request PIU to report in writing that the necessary environmental restoration work has been adequately performed before acceptance of work.	(i) Complaints from sensitive receptors; (ii) Worksite clear of hazardous wastes such as oil/fuel (iii) Worksite clear of any excess excavated earth, excess construction materials, and solid waste such as removed concrete, wood, packaging materials, empty containers	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.
Existing Infrastructure and Facilities	Disruption of service and damage to existing infrastructure at specified project location	(i) Obtain from PIU the list of affected utilities and operators if any; (ii) Prepare a contingency plan to include actions to be done in case of unintentional interruption of service (iii) Inform nearby community in advance about the nature and timings of disturbance	As per contingency plan	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.
Ecological Resources – Terrestrial	Loss of vegetation and tree cover	(i) Minimize removal of vegetation and disallow cutting of trees; (ii) If tree-removal will be required, obtain tree-cutting permit from the Revenue Department; and (iii) Plant three native trees for every one that is removed.	-Records -Plant native tree species as per RUDSICO-EAP Policy	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsibility for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
Construction near <u>Dimiya</u> dam	Habitat Disruption Disturbance during Nesting Season: Increased Human-Crocodile Conflict	- All project related site staff, construction workers and supervisors, shall be made aware of the sensitive sites, and prevent any harm or damage or disturbance to trees, vegetation, wildlife, birds etc., - Schedule works during dry season to avoid contaminated runoff from the work sites entering lake; clear the sites of materials, debris, and consolidated the refilled trenches prior to onset of monsoon. - No construction camps (workers accommodation, material / waste / soil storage) should be established within 200 m from the boundary of dam; camps should not be located close to drainage lines/streams that flow into dam. - Movement of workers and staff should be confined to work site, and not be allowed in dam area which may disturb the sensitive area; ensure via strict supervision no poaching, fishing, cutting / damaging trees/vegetation or wildlife, birds etc., - Proper accommodation and facilities shall be provided within the camps, and workers shall not use the lake or surroundings for open defecation, bathing, or fishing / hunting, collecting firewood etc. Contractor should put in place, a proper system to monitor the staff and workers to prevent damage/ disturbance.	Monitoring as Environment management plan	Construction Contractor	CM/SC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		- Implement sediment and erosion control measures to prevent soil erosion and sedimentation in the dam. Prevent entry of silt-laden / contaminated runoff into dam or drains leading to dam from the construction sites or construction camps. Appropriate measures such as silt traps, sedimentation ponds, and filtration systems should be installed to prevent sediment and other pollutants from entering the water supply. Soil stabilization measures should also be taken to prevent soil erosion during construction. Construction near dam to be planned in dry seasons only. - Place storage areas for fuels and lubricants away from any drainage leading to water bodies. - Store fuel, construction chemicals etc., on an impervious floor, also avoid spillage by careful handling. - Do not use equipment that generate heavy noise, ground vibration, dust etc., (such as pneumatic drills, dozers etc.), within 100 m of Dam. Adapt manual excavation as far as possible - Construction sites often generate significant amounts of dust that can impact nearby habitats. Dust suppression measures, such as watering down exposed soil, can help to reduce dust levels.				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		• Dispose any wastes generated by construction activities in designated sites; and • Monitor the project closely throughout construction to ensure that all mitigation measures are being implemented effectively and that any issues are identified and addressed promptly. • Conduct surface quality inspection according to the environmental management plan (EMP). • Conduct continuous consultations with the local people during the works • Install inlet of intake pipe in the dam with appropriate screen to avoid entry of aquatic organisms into inlet • Select a construction methodology that is least disturbing, and appropriate for the in-situ soil condition, and able to complete the construction work prior to onset of monsoon. • Erect temporary barriers to form enclosed construction area with least disturbance • Implement work site safety at works in water body				
Land use	Environmental issues due to land use change	The impact due to change in land use will be negligible due to this project.	-Latest land use records	Not applicable	PMU/ ULB	Not applicable

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
Accessibility	Traffic problems and conflicts near project locations and haul road	- Plan transportation routes so that heavy vehicles do not use narrow local roads, except in the immediate vicinity of delivery sites. (i) Schedule transport and hauling activities during non-peak hours. - Locate entry and exit points in areas where there is low potential for traffic congestion. (iv) Keep the site free from all unnecessary obstructions. - Drive vehicles in a considerate manner. (vi) Coordinate with Traffic Police for temporary road diversions and with for provision of traffic aids if transportation activities cannot be avoided during peak hours. - Notify affected sensitive receptors 1-week in advance by providing sign boards informing nature and duration of construction works and contact numbers for concerns/complaints. - Plan and execute the work in such a way that the period of disturbance/ loss of access are minimum. (ix) Provide pedestrian access in all the locations until normalcy is restored.	- Traffic route during construction works including number of permanent signages, barricades and flagmen on worksite (Appendix C-14). (i) Complaints from sensitive receptors. (ii) Number of signages placed at project location.	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.
Socio-Economic – Income	Impede the access of residents and	Prepare and implement spoils management plan Contractor to implement RP and to follow mitigation measures prescribed such as-	Complaints from sensitive receptors.	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures

Field	Anticipated Impact	Mitigation Measures		Indicator of Compliance	Responsibility for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
	customers to nearby shops	• (ii) Leave spaces for access between mounds of <u>soil</u>. • Provide walkways and metal sheets where required for people. • Increase workforce in front of critical areas such as institutions, place of worship, business establishment, hospitals, and <u>schools</u>. • (iv) Consult businesses and institutions regarding operating hours and factoring this in work schedules, and • Provide sign boards for pedestrians to inform nature and duration of construction works and contact numbers for concerns/complaints.		• (i) Spills management plan • (iii) Number of walkways, signages, and metal sheets placed at project location.			responsibility of contractor.
Socio-Economic – Employment	Generation of temporary employment and increase in local revenue	• Employ at least 50% of the labour force, or to the maximum extent, local persons within the 2-km immediate area if manpower is <u>available</u>. • (ii) Secure construction materials from local market. • (iii) Comply with <u>labor laws</u>.		• Employment <u>records</u>. • (ii) Records of sources of materials • (iii) Compliance to <u>labor laws</u>.	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures, responsibility of contractor.
Occupational Health and Safety	Occupational hazards which can arise during work	• (A) Comply with all national, state and local <u>labor laws</u> (see Appendix C-12) • (B) Ensure that qualified EHS personnel is	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures, responsibility of contractor.		

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		deputed to look the H&S matter - Develop and implement site-specific occupational health and safety (OH&S) Plan which will include measures such as: (a) excluding public from the site; (b) ensuring all workers are provided with and use personal protective equipment like helmet, gumboot, safety belt, gloves, nose mask and ear plugs; (c) OH&S Training for all site personnel; (d) documented procedures to be followed for all site activities; and (e) documentation of work-related accidents; - Ensure that qualified first-aid can be provided at all times. Equipped				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		first-aid stations shall be easily accessible throughout the site. <u>Provide medical insurance coverage for workers.</u> • (iv) Secure all installations from unauthorized intrusion and accident risks. • The project area experiences extreme temperature during summer months of April and May, which may affect the health of workers engaged in construction work. Contractor should take necessary measures during summers including the following: • (a) work schedule should be adjusted to avoid peak temperature				

Field	Anticipated Impact	Mitigation Measures		Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		including the following: • (a) work schedule should be adjusted to avoid peak temperature hours (12 – 3 PM); (b) provide appropriate shade near the workplace; allow periodic resting and provide adequate water, and (c) provide necessary medicine and facilities to take care of dehydration related health issues • Provide supplies of potable drinking <u>water</u>; • Provide clean eating areas where workers are not exposed to hazardous or noxious substances Provide H&S orientation					

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		training to all new workers to ensure that they are apprised of the basic site rules of work at the site, personal protective protection, and preventing injuring to fellow workers. Provide visitor orientation if visitors to the site can gain access to areas where hazardous conditions or substances may be present. Ensure also that visitor/s do not enter hazard areas <u>unescorted</u>; • Ensure the visibility of workers through their use of high visibility vests when working in or walking through heavy equipment operating areas. Ensure moving equipment is				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		outfitted with audible back-up alarms; Mark and provide sign boards for hazardous areas such as energized electrical devices and lines, service rooms housing high voltage equipment, and areas for storage and disposal. Signage shall be in accordance with international standards and be well known to, and easily understood by workers, visitors, and the general public; as appropriate, a) Disallow worker exposure to noise level greater than 85 dBA for a duration of more than 8 hours per day without hearing protection. The				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		than 8 hours per day without hearing protection. The use of hearing protection shall be enforced actively. • (xii) Provide proper solid and liquid waste management program in workers' campsite, separate from spoils and debris disposal, as their presence can add to existing waste volume at the project sites. Site-specific CH&S Plan: • Equippe d first-aid stations, medical insurance coverage for <u>workers</u>. • Number of accidents. - Supplies of potable drinking <u>water</u>.				

Field	Anticipated Impact	Mitigation Measures		Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		- Clean eating areas where workers are not exposed to hazardous or noxious substances - record of H&S orientation trainings - personal protective equipment% of moving equipment - equipped with audible back-up alarms - permanent sign boards for hazardous areas such as energized electrical devices and lines, service rooms housing high voltage equipment, and areas for storage and disposal. (xi) - Compliance to core labor laws (see Appendix C-12)					

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
Community Health and Safety	- Traffic accidents and vehicle collision with pedestrians during material and waste ~~transportation~~ routes to avoid times of peak-pedestrian activities. - Laise with PIUULB in identifying high-risk areas on route cards/<del>map</del>~~Maintain~~ regularly the vehicles and use of manufacturer-approved parts to minimize potentially serious accidents caused by equipment malfunction or premature failure. - Provide road signs and flag persons to warn of on-going trenching activities.	As per Traffic Management Plan given in Appendix C-14	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.	
Safety of sensitive groups (children, elders etc.) and ~~others~~ pedestrians in narrow streets	- Trench excavation in narrow streets will pose high risk to children and elders in the <del>locality</del>~~Provide~~ prior information to the local people about the nature and duration of ~~work~~ - Conduct awareness program on safety during the construction <del>work</del>~~Undertake~~ the construction work stretch-wise; excavation, pipe ~~laying~~ and trench refilling should be completed on the same day - Provide barricades, and deploy security personnel to ensure safe movement of people and ~~also~~ to prevent unnecessary entry and to avoid accidental fall into open trenches	-H&S plan including appropriate signs for each hazard present -Construction vehicles condition in H&S plan. Complaints from neighbourhood and monitoring of accidents	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.	
Work Camps and work sites	Temporary air and noise pollution from machine operation, water	-Condition in list of preapproved	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.	

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsibility for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
	pollution from storage and use of fuels, oils, solvents, and lubricants • Unsanitary and poor living conditions for <u>workers</u><u>Consult</u> with PIU before locating project offices, sheds, and construction <u>plants</u>; • Minimize removal of vegetation and disallow cutting of <u>trees</u><u>Provide</u> drinking water, water for other uses, and sanitation facilities for <u>employees</u>; • Ensure conditions of <u>livability</u> at work camps are maintained at the highest standards possible at all <u>times</u><u>Train</u> employees in the storage and handling of materials which can potentially cause soil <u>contamination</u>; • Recover used oil and lubricants and reuse or remove from the <u>site</u><u>Manage</u> solid waste according to the preference hierarchy: reuse, recycling and disposal to designated <u>areas</u>; • (viii) Ensure unauthorized persons especially children are not allowed in any worksite at any given time.	sites for construction work camps, areas for stockpile, storage and disposal prepared by the Contractor. Drinking water and sanitation facilities for employees				
Impacts due to night works (if required as per nature of works and feasibility at site)	Occupational hazards which can arise during work at night in extreme and unavoidable cases	(i) Contractors should have <u>hand-held</u> noise level meter for measurement of noise during night hours (ii) Contractors should have <u>hand-held</u> lux meter for the measurement of illumination during night hours (iii) Preferably <u>electrical</u> connections <u>is</u> available for running	As per Management Plan for night works (Appendix 21).	Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		~~equipments~~, otherwise sound proof/super silent Diesel Generator set should be available (iv) Sound level should not increase as per FMP (v) Illumination should be adequate as required according to nature of <u>works</u> (vi) As far as possible ready-mix concrete from batching plant to be used, otherwise the concrete should be prepared away from residential areas and brought to the <u>site</u> (vii) All the noise activity like hammering, cutting, crushing, running of heavy ~~equipments~~, should be done in <u>day time</u> and avoided in night time (viii) Workers engaged in night works should have adequate rest/sleep in <u>day time</u> before start of night works (ix) Worker engaged for night works should have previous experience of night works and should be physically fit for such works including clear vision in <u>night</u> (x) All the necessary provisions of traffic aids such as traffic signals, road signage, barricades, cautions boards, traffic diversion boards etc. should be available with fluorescent/retro-reflective <u>arrangements</u> (xi) Workers should be trained before start of night works about				

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		risks and hazards of night works and their mitigation measures and should be provided all the protective aids (PPEs) including fluorescent/retro-reflective vests (xii) Horns should not be permitted by equipments and vehicles (xiii) Workers should not shout and create noise (xiv) First aid and emergency vehicles should be available at site. (xv) Emergency preparedness plan should be operative during night works (xvi) Old persons and pregnant women and women having small kids should not work in nighttime. (xvii) All the vehicles and equipments, being used at night works should have adequate type of silencers/enclosures/mufflers to reduce noise (xviii) All the vehicles should be checked for working head lamps, tail lamps, inner lights etc. before start of night works				
Social and Cultural Resources	Risk of archaeological chance finds	(i) Consult with concerned religious authorities, nearby people and devotees in pre-construction phase and explain the work method and duration of proposed works, take their suggestions and comments and incorporate in design the mitigation measures required (ii) Adjacent to religious/social sites, undertake excavation and	Chance protocol find	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		construction work in such a way that no structural damage is caused to the religious building. (ii) Observe the local rituals and important dates of festivals, weekly/monthly/annual religious occasions in the religious places and do not make any disturbance/hindrance/obstacles during such time to the religious places. (iv) provide proper signage, barricades etc. to protect public and devotees from dangers of construction works.				
Monsoon preparedness	Disruption of utilities and water logging in trenches	(i) As for a possible avoid trench works and excavation works (pipe laying) during monsoon season to avoid any water logging and accident due to it (ii) if open trenches are not avoidable during monsoon, keep ready all the mitigations measures to avoid water logging such as dewatering pumps and sufficient pipes, traffic assistance, barricades etc. (iii) Guidelines for safety during monsoon is attached as Appendix C-18	As per monsoon preparedness plan & as per Appendix C-19 "Guidelines for Safety during Monsoon/Heavy Rainfall"	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.
Submission of EMP implementation report	Unsatisfactory compliance to EMP	(i) Appointment of supervisor to ensure EMP implementation (ii) Timely submission of monitoring reports including pictures	Availability and competency of appointed supervisor Monthly report	Construction contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
COVID-19 prevention and control during construction works	Health risk to workers due to COVID-19 virus	(i) provide face mask, hand gloves and sanitizers to workers during works (ii) Keep social distancing (iii) Educate workers about risks of COVID-19 (iv) Health check-up of workers suffering with symptoms of COVID-19 and test for same (v) isolation of workers suspected/suffering with COVID-19 and due medical care (vi) follow guidelines of WHO/Central/State/Local government and RUDSICG-EAP regarding COVID-19 (refer Appendix C-23)	Compliance of COVID-19 protocol and guidelines	Construction contractor	PIU/Consultants	Contractor
Post-construction clean-up	Damage due to debris, spoils, excess construction materials	(i) Remove all spoils wreckage, rubbish, or temporary structures (such as buildings, shelters, and latrines) which are no longer required and (ii) All excavated roads shall be reinstated to original condition. (iii) All disrupted utilities restored (iv) All affected structures rehabilitated/compensated (v) The area that previously housed the construction camp is to be checked for spills of substances such as oil, paint, etc. and these shall be cleaned up. (vi) All hardened surfaces within the construction camp area shall be ripped, all imported materials removed, and the area shall be top soiled and regressed using the	PIU/Consultant report in writing that (i) worksite is restored to original conditions ; (ii) camp has been vacated and restored to pre-project conditions ; (iii) All construction related structures not relevant to O&M are removed, and (iv) worksite clean-up is satisfactory.	Construction Contractor	CMSC/ PIU	Cost for implementation of mitigation measures responsibility of contractor.

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost and Source of Funds
		guidelines set out in the revegetation specification that forms part of this document. (vi) The contractor must arrange the cancellation of all temporary services. (vii) Request PIU to report in writing that work sites and camps have been vacated and restored to pre-project conditions before acceptance of work.				

Table 33: Environmental Management Plan of Anticipated Impacts during Operation

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost Source and of Funds
Construction disturbances, nuisances, public & worker safety	All work sites	Implementation of dust control, noise control, traffic management, & safety measures. Site inspection checklist to review implementation is appended at Appendix C-16	All the dust control will be done by water sprinkling measures at site, noise will be kept well within prescribed limits of standards, Follow Traffic management Plan as given in Appendix C-14 and all the safety measures such as PPE's etc. Site inspection will be done as per checklist is given in Appendix C-16.	Weekly during construction	Supervising staff and safeguards specialists	No costs required

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost Source and of Funds
Check the leakages, blockages, overflow problem in sewers	It may affect the sewer system, contaminate land, water and create public health issues	Effective operation to avoid and/or immediate clearance of such leaks, blockages Implementation of regular O&M schedules	Follows regular O & M schedule	Dungarpur Municipal Council/O&M contractor	Dungarpur Municipal Council	DBO contractor cost O&M Cost
Check the leakages, blockages, overflow problem in sewers	Occupational health & safety: for personnel cleaning underground sewers there is a risk due to oxygen deficiency and harmful gaseous emissions (hydrogen sulphide, carbon monoxide, methane, etc.);	(i) Provide necessary health & safety training to the staff engaged sewer cleaning & maintenance (ii) provide appropriate personal protection equipment (including oxygen masks)	-Training and Awareness campaign for Occupational, Health & Safety to ensure the use of PPE's.	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council	O&M Cost
Consent to Operate	Periodical renewal of consent to operate, if not done, may attract penal action from State Pollution Control Board	Renew the consent to operate (CTO) of STP before expiry date and follow all the conditions set forth in CTO	RSPCB	Dungarpur Municipal Council/PHED /O&M Contractor	Dungarpur Municipal Council/PHED /O&M Contractor	Dungarpur Municipal Council/PHED /O&M Contractor
Treated effluent quality	Water pollution of the receiving body if treated effluent does not meet the standards set by CPCB/RSPCB	Regular monitoring (parameters tests) of treated effluent quality Follow all the parameters given in CTE/CTO	Test results records	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor
Reuse of Treated effluent/safe disposal	Adverse impact on water hydrology and crops	Prepare a plan of reuse of treated effluent in agriculture or other gainful purposes	Records on treated water reuse	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor
Achieving targeted sludge reuse	Violation of ULB commitment under the project. Moreover, a land has been identified for safe sludge disposal. Hence, it is imperative to achieve the targeted sludge reuse under the project.	Ensure that the targeted sludge reuse is achieved throughout the project period	Records	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor	Dungarpur Municipal Council/O&M Contractor

Field	Anticipated Impact	Mitigation Measures	Indicator of Compliance	Responsible for Mitigation	Monitoring of Mitigation	Cost Source and of Funds
Safety precautions during sewage manhole cleaning	Health and safety risk to workers engaged in sewage manhole cleaning	Ensure all the safety equipment are available during manual cleaning As far as possible, use CCTV and mechanical cleaning (sewage jetting machine) for cleaning of manhole	-Training and Awareness campaign for Occupational, Health & Safety to ensure the use of PPE's.	O&M contractor for 10 years and then Dungarpur Municipal Council	Dungarpur Municipal Council	Dungarpur Municipal Council
Routine maintenance of CWR and other facilities to ensure delivery of safe drinking water	Health impact due to supply of unsafe drinking water in the system	Ensure periodical maintenance and cleaning of OHSRs, CWRs to ensure delivery of safe drinking water Periodical testing of treated water to ensure treated water quality meets the required standards	Maintenance Records	O&M contractor for 10 years and then PHED, Dungarpur.	PHED, Dungarpur	O&M cost of contractor
Leakages in water supply pipe lines	Entry of waste water into water supply pipes and health risk to public due to poor quality water	Ensure to identify and repair leakage immediately Strengthen grievance mechanism and attend the grievance of any leakage	Maintenance Records; Periodic Leakage Report;	O&M contractor for 10 years and then PHED, Dungarpur.	PHED, Dungarpur	O&M cost of contractor
Asset management	Reduction in NRW Increased efficiency of the system	Preparation and implementation of O&M Manual	O&M Manual; Implementation Records;	O&M contractor for 10 years and then PHED, Dungarpur	PHED, Dungarpur	O&M cost of contractor

Table 34: Environmental Monitoring Plan of ambient air, noise, water and soil quality and other during Construction

Monitoring field	Monitoring location	Monitoring parameters	Frequency	Responsibility	Cost Source & of Funds
Construction disturbances, nuisances, public & worker safety	All work sites	Implementation of dust control, noise control, traffic management, & safety measures. Site inspection checklist to review implementation is appended at Appendix C-16	Weekly during construction	Supervising staff, EHS officer and safeguards specialists	No costs required
Impacts on wildlife species (crocodiles, birds)	Dimiya Dam Intake site	Implementation of recommended mitigation measures based on biodiversity study	Continuous	Supervising staff, EHS officer and safeguards specialists	Contractor
		Biodiversity monitoring	Once during construction	Supervising staff, EHS officer and safeguards specialists	Contractor
Tree cutting	STP, SPS, Pipe laying, RWR and CWR sites	Tree cutting permit taken, Tree cutting done	Continuous	Supervising staff, EHS officer and safeguards specialists	Contractor
Construction, Labour Camp, storage yard Management	Construction, Labour Camp, storage yard Management	As per SEMP	Weekly	EHS officer, Environment Specialist of consultant	contractor
Solid waste management	Construction, Labour Camp, storage yard Management	As per SEMP	Weekly	EHS officer, Environment Specialist of consultant	contractor
Construction and demolition waste management	All construction site	As per SEMP and applicable rules and regulations	Weekly	EHS officer, Environment Specialist of consultant	contractor
Consent to establish of STP, WTP, batching plants, crusher, hot mix plant. DG sets etc.	STP, WTP batching plants, crusher, hot mix plants etc	Copies of Consents	Periodically	EHS officer, Environment Specialist of consultant	No cost required for monitoring cost for obtaining CTE/CTO from PMU and for others from Contractor
Ambient air quality	9 locations (STPs-1, SPS-3, CWRs-2, RWR-1, Pipe	PM ₁₀ , PM _{2.5} , NO ₂ , SO ₂ , CO	Quarterly except Monsoon period	Contractor	Contractor Contractor

Monitoring field	Monitoring location	Monitoring parameters	Frequency	Responsibility	Cost Source & of Funds
	laying-1), Intake-1 during construction)				
Ambient noise	9 locations (STPs-1, SPS-3, CWRs-2, RWR-1, Pipe laying-1), Intake-1 during construction)	Day time and night time noise levels	Quarterly	Contractor	Contractor
Ground Water quality	8 locations (STPs-1, SPS-3, CWRs-3, RWR-1) during construction	pH, TDS, Total Hardness, Zn, Chloride, Iron, Copper, DO, Manganese, Sulphate, Nitrate, Fluoride, Hg, Cadmium, Cr ⁺⁶ , Arsenic, Lead, Total Alkalinity, Phosphate, Phenolic compound	Quarterly except Monsoon period	Contractor	Contractor
Soil quality	8 locations (STPs-1, SPS-3, CWRs-3, RWR-1) during construction	pH, Elect. Conductivity (at 25°C), Moisture (at 105°C), Texture (silt, clay, sand), Calcium (as CaO), Magnesium (as Mg), Permeability, Nitrogen (as N), Sodium (as Na), Phosphate (as PO ₄), Potassium (as K), Organic Matter, oil and grease	Quarterly except Monsoon period	Contractor	Contractor
Surface Water	2 locations- Vijay Chakra Sagar Dam and other water body	pH, TDS, Total Hardness, Zn, Chloride, Iron, Copper, DO, Manganese, Sulphate, Nitrate, Fluoride, Hg, Cadmium, Cr ⁺⁶ , Arsenic, Lead, Total Alkalinity, Phosphate, Phenolic compound	Quarterly except Monsoon period	Contractor	Contractor

Table 35: Environmental Monitoring Plan of Anticipated Impacts during Operation

Monitoring field	Monitoring location	Monitoring parameters	Frequency	Responsibility	Cost & Source of Funds
Monitoring of raw sewage quality	Inlet of the STP	Suspended solids, pH, Temperature Oil and grease, Total residual chlorine, Ammonical nitrogen (as N), BOD, COD, Nitrate Nitrogen The values should be within the limit specified by CPCB to discharge into municipal sewers	As per O&M Plan	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Monitoring of treated effluent quality	Outlet of STP	pH, BOD, COD, TSS, NH ₄ -N, N-total, Fecal Coliform (as per Appendix C-8)	As per O&M Plan	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Monitoring of plantations	Plantations locations	Nos. of tree survived	monthly	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Biodiversity monitoring (crocodiles, avifauna)	Dimiya Dam	Population of crocodiles, avifauna	Bi-annually (covering different seasons per year)	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Sewer network to sustain operational efficiency and avoid clogging and early occurrence of leakages	Sewer network	to be included in the O&M plan prepared under the project	as per O&M plan	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Consent to operate (CTO) from RSPCB	STP/WTPs	CTO should be renewed before expired	5 yearly	Dungarpur Municipal Council /PHED	Dungarpur Nagar Palika, PHED
Reuse of treated effluent and safe disposal	STP outlet	Treated effluent is being used in agriculture or other gainful purposes	Continuously	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Sludge Reuse and safe disposal	Sludge Management	Sludge is being gainfully used	Continuously	O&M Contractor/Municipal Council	O&M Contractor/Municipal Council
Monitoring of quality of water supplied to consumers	Consumer end-random sampling in all zones	As per CPHEEO norms (refer Appendix - C-1)	Daily	O&M Contractor	DBO contractor Cost
Pipeline network to sustain	Pipeline network	to be included in O&M plan prepared under the project	Daily/when required	O&M Contractor	DBO contractor Cost

Monitoring field	Monitoring location	Monitoring parameters	Frequency	Responsibility	Cost & Source of Funds
operational efficiency and avoid early occurrence of leakages					
Reduction of NRW	Pipe line networks	As per RUDSICO-EAP norms	Daily/when required	O&M Contractor	DBO contractor Cost

B. Institutional Requirements

138. The Local Self Government Department (LGSD) is the executing agency which is responsible for the overall strategic guidance and ensure the compliance with ADB loan covenants. RUDSICO is the implementing agency responsible for the technical supervision and project implementation. The RUDSICO Board (under the chairmanship of the Honorable Minister), the LGSD and the City Level Monitoring Committees (CLMCs, under the chairmanship of their respective commissioner/executive officer) is proposed to monitor the project implementation. The PMU is already established at state-level (Jaipur) and headed by a dedicated Project Director. The PIUs have two zonal offices (1 in Jaipur and 1 in Jodhpur). Each zonal office is headed by an additional chief engineer. Urban Local Bodies (ULBs) will be the final custodian and user of the created infrastructure. As primary stakeholders, the ULBs will be involved and engaged in the day-to-day monitoring and implementation.

139. At the PMU level, the Project Director is being supported by Additional Project Director (Chief Engineer-level) and a Chief Engineer, who are being supported by Dy Project Directors (Technical and Administration) and a financial advisor. There is one project officer for Social and another project officer for Environmental aspects within PMU.

140. The PMU is being supported by the Project Management and Capacity Building Consultants (PMCBC). The PMCBC shall manage preparation/vetting design documents, tendering of contracts, implementation of resettlement, environmental management and gender action plans; setting and managing project performance monitoring systems, planning and managing implementation of training and capacity building as well as institutional strengthening activities besides preparing reports as per ADB requirements. PMCBC has engaged a social safeguard specialist and environmental safeguard specialist at the PMU level for managing all social and environmental safeguard related support services as envisaged in its scope of work. They will be assisted by concerned field level safeguard support staffs of CMSCs and PIU.

141. There are two zonal PIUs already established in Jaipur and Jodhpur. One PIU shall be established at every town before award of new projects. PIUs at the town-level shall be headed by a Superintending Engineer / Executive Engineer, who shall work as Project Manager and shall sign the contract documents, manage the contract and disburse payments as Drawing and Disbursing Officer.


142. **Construction management and supervision consultants (CMSCs)** - 2 nos. of CMSCs catering to Jaipur and Jodhpur units are already established. They shall directly support PIUs in day to day contract management, construction supervision including quality management of ongoing works etc. This shall include work measurement, quantities, verification of bills of contractors etc. In compliance with the EMP, the CMSCs shall develop a strategy to overcome

the difficulties of construction/traffic management in narrow streets and also prepare detailed plans for detour of traffic during excavation for pipe laying. The CMSC will propose and implement mechanism for coordination among all stakeholders such as traffic police, roads department, user committees, etc., for smooth construction execution. Adequate measures shall be taken for working near physical cultural resources involving close coordination with the Department of Archaeology. The CMSC will lead design of surveys and investigations required for the protection of archaeological sites/heritage areas and prepare Archaeological Impact Assessments, or other agreed upon document to be approved by the Department of Archaeology for the archaeologically sensitive locations.

143. **Community awareness and public participation consultants (CAPPC)**- CAPC core unit is already established at PMU, Jaipur and at fields in ongoing 14 project towns. CAPC field team and PIU is already established Dungarpur town. CAPC is closely work in the field (with PIUs) to facilitate creation of project awareness and ensuring public participation for all project works at the community level. This mainly involve house connections for water supply, sewerage and metering. CAPPC shall also undertake various IEC activities to promote and pursue health and hygiene among the communities.

144. **Figure 26** shows Environmental Safeguards Implementation Arrangements within RUDSICO-EAP and **Table 36** summarize the institutional responsibility of environmental safeguards implementation at all stages of the project.

Figure 26: Environmental Safeguards Implementation Arrangement

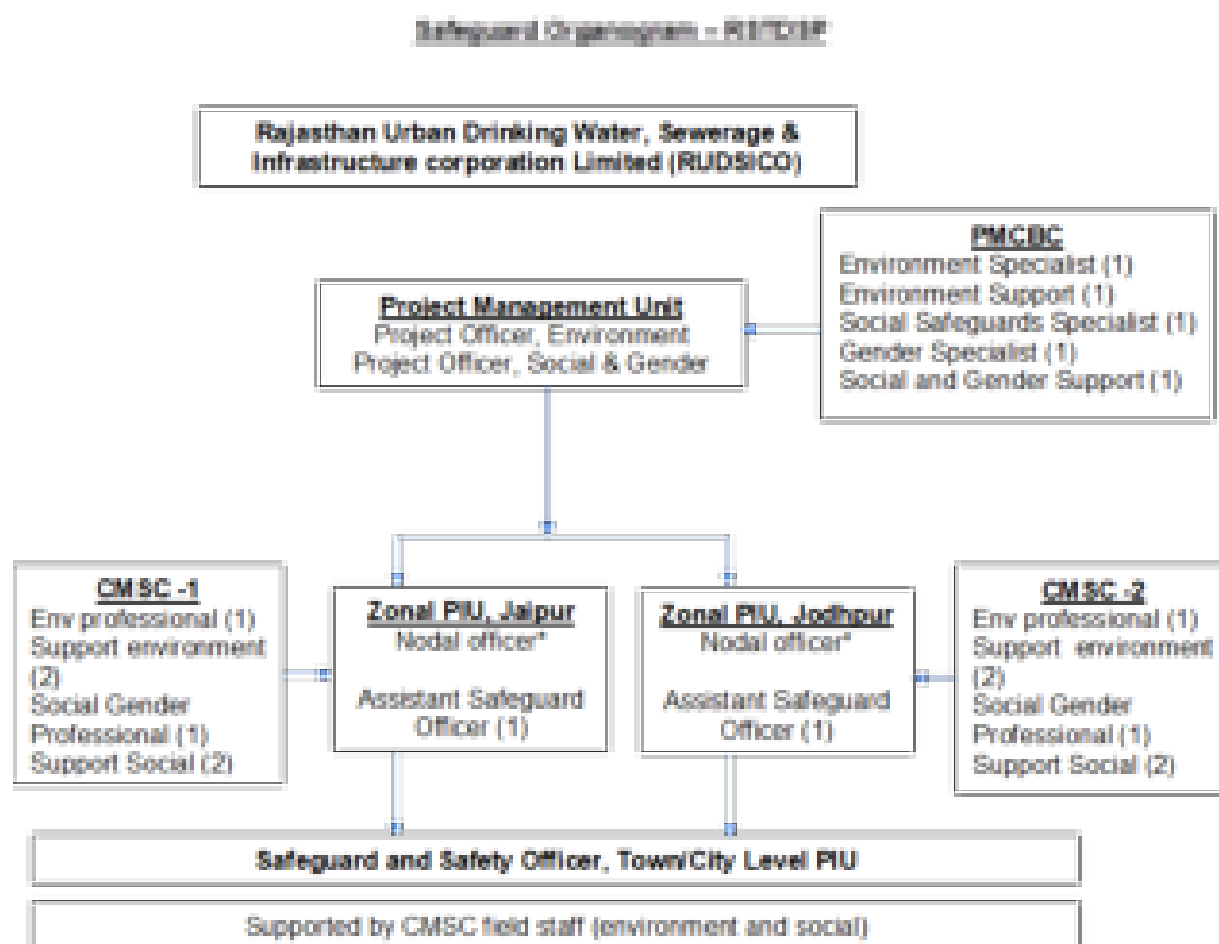

(Zonal PIU) will be led by a nodal officer of the rank of assistant chief engineer who will also be the nodal person for safeguards and gender compliances in project implementation by town level PIUs. This will be supported by CMSC in execution of these responsibilities.

145. Project Management Unit. RUDSICO will establish a state-level PMU, headed by dedicated project director, and housed in EAP division of RUDSICO. For the purpose of project implementation, 2 Zonal project implementation units (Zonal PIUs), at Jaipur and Jodhpur, headed by additional chief engineers (ACE) are established. At PMU, there are two dedicated project officers (i) project officer (Environment) and (ii) project officer (Social and Gender), who will be responsible for compliance with the environmental, social safeguards and gender in program implementation. Key responsibilities of the project officer (Environment) are enumerated in **Table 36**.

146. The PMU will be supported by 3 institutional consultants under the supervision and control of PD, PMU: (i) the project management and capacity building consultants (PMCBC) will support the PMU; (ii) 2 CMSC will support the 2 zonal PIUs and town-level PIUs; and (iii) CAPPC, will support the zonal PIUs and town-level PIUs.

147. Zonal Project implementation units (Zonal PIUs). There are 2 zonal level PIUs at Jaipur and Jodhpur. Under each zonal PIU, there will be city/town level PIUs, for ease of day-to-day

monitoring and management at local level. The additional chief engineer at each Zonal PIU will serve as the Nodal Officer, Safeguards and Gender. Each Zonal PIU will be staffed with an assistant safeguards officer (ASO Environmental and Social Safeguards) who will assist PMU project officer (environment/social) in implementation of the environmental/social safeguards and GESI action plan in PIUs under its jurisdiction. Zonal PIUs will undertake internal monitoring and supervision and record observations throughout the project period to ensure that the safeguards and mitigation measures are provided as intended.

148. The zonal level ASO will oversee safeguards implementation by the city/town level PIUs, coordinate public consultations, information disclosure, regulatory clearances and approvals, implementation of resettlement plans, EMP implementation, and grievance redressal.

149. **Town/City Level Project Implementation Unit.** The town-level PIUs shall be responsible for the quality of works executed under the project and will be guided by the zonal PIUs. The city/town PIUs will be responsible for implementation of the IEE. The town-level PIUs will be headed by a project manager (executive engineer or assistant engineer) and supported by CMSC field staff. Environment Safeguard Professional of CMSCs will assist PIUs in implementation of environmental safeguard. At each PIU, the Assistant Project Manager will be given additional responsibilities of safeguard tasks and will be designated as safeguard and safety officer (SSO). The SSO will be assisted by the social and gender specialist and environment specialist of CMSC in reviewing updated/revised IEEs, etc. They will also be responsible for coordination of field level activities related to safeguards conducted by the DBO contractor and CMSC.

150. **Contractors.** The contractor will be required to update the IEE and will be responsible for providing final design (including pipe alignments) to the supervision consultant for finalization/updating of resettlement plan. The contractor shall appoint an environment, health and safety (EHS) engineer who will be responsible on a day-to-day basis for (i) ensuring implementation of EMP, (ii) coordinating with the town-level PIUs and environment specialists of project consultant teams; (iii) community liaison,²⁸ consultations with interested/affected people, (iv) field-level grievance redress; and (iv) reporting.

151. The Contractor has required to submitted to RUDSICO-EAP, for review and approval, a SEMP including (i) proposed sites or locations for construction work camps, storage areas, hauling roads, lay down areas, disposal areas for solid and hazardous wastes; (ii) specific mitigation measures following the approved EMP; (iii) monitoring program per SEMP; (iv) budget for SEMP implementation. No works can commence prior to approval of SEMP.

152. A copy of the EMP or approved SEMP will be kept on-site during the construction period at all times. Non-compliance with, or any deviation from, the conditions set out in the EMP or SEMP constitutes a failure in compliance and will require corrective actions. The EARF and the IEEs specify responsibilities in EMP implementation during design, construction and O&M phases.

153. **RUDSICO-EAP** will ensure that bidding and contract documents include specific provision requiring Contractors to comply with: (i) all applicable labor laws and core labor standards on (a) prohibition of child labor as defined in national legislation for construction and maintenance activities; (b) equal pay for equal work of equal value regardless of gender, ethnicity, or caste and (c) elimination of forced labor; and (ii) the requirement to disseminate information on sexually

²⁸ Reasonable size social outreach team (SOT) to be appointed by contractor to facilitate community liaison, consultations and R&R implementation (including resolution of grievances). Requirement of SOT was included in bid document.

transmitted diseases including HIV/AIDS, to employees and local communities surrounding the project sites.

Table 36: Institutional Roles and Responsibilities for Environmental Safeguards Implementation

Responsible Agency	Responsibility		
	Pre-Construction Stage	Construction Stage	Post-Construction
PMU (Project Officer; Environment),	(i) Review REA checklists and assign categorization based on ADB SPS 2009 (ii) Review and approve EIA/IEE (iii) Submit EIA/IEE to ADB for approval and disclosure in ADB website (iv) Ensure approved IEEs are disclosed in RSTDSP/PMU websites and summary posted in public areas accessible and understandable by local people. (v) Ensure environmental management plans (EMPs) are included in the bid documents and contracts (vi) Organize an orientation workshop for PMU, PIU, ULB and all staff involved in the project implementation on (a) ADB SPS, (b) Government of India national, state, and local environmental laws and regulations, (c) core labor standards, (d) OH&S, (e) EMP implementation especially spoil management, working in congested areas, public relations and ongoing consultations, grievance redress, etc. (vii) Assist in addressing any grievances brought about through the Grievance Redress Mechanism in a timely manner as per the IEEs (viii) Organize an induction course for the training of contractors preparing them on EMP implementation, environmental monitoring requirements related to mitigation measures; and taking immediate actions to remedy unexpected adverse	(i) Over-all environmental safeguards compliance of the project (iii) Monitor and ensure compliance of EMPs as well as any other environmental provisions and conditions. (i) Review monthly monitoring report (ii) Prepare and submit to ADB semi-annual monitoring reports (iv) If necessary, prepare Corrective Action Plan and ensure implementation of corrective actions to ensure no environmental impacts; (iii) Review and submit Corrective Action Plans to ADB (iv) Organize capacity building programs on environmental safeguards (iv) Coordinate with national and state level government agencies (vi) Assist in addressing any grievances brought about through the Grievance Redress Mechanism in a timely manner as per the IEEs (ix) Coordinate PIUs, consultants and contractors on mitigation measures involving the community and affected persons and ensure that environmental concerns and suggestions are incorporated and implemented	Compliance monitoring to review the environmental performance of project component, if required and as specified in EMP

Responsible Agency	Responsibility		
	Pre-Construction Stage	Construction Stage	Post-Construction
	impacts or ineffective mitigation measures found during the course of implementation. (ix) Ensure compliance with all government rules and regulations regarding site and environmental clearances as well as any other environmental requirements (x) Assist PMU, PIUs, and project NGOs to document and develop good practice construction guidelines to assist the contractors in implementing the provisions of IEE. (xi) Assist in the review of the contractors' implementation plans to ensure compliance with the IEE.		
PIU, Safeguard and Safety Officer (SSO)	(i) Ensure IEE is included in bid documents and contract agreements. Ensure cost of EMP implementation is provided. (iv) Disclose of approved EIAs/IEEs. (v) Obtain all necessary clearances, permits, consents, NOCs, etc. Ensure compliance to the provisions and conditions. (vi) EMP implementation regarding sites for disposal of wastes, camps, storage areas, quarry sites, etc. (vii) Organize an induction course for the training of contractors, preparing them on EMP implementation, environmental monitoring requirements related to mitigation measures, and on taking immediate action to remedy unexpected adverse impacts or ineffective mitigation measures found during the course of implementation.	(i) Oversee day-to-day implementation of EMPs by contractors, including compliance with all government rules and regulations. (ii) take necessary action for obtaining rights of way; (iii) oversee implementation of EMPs, including environmental monitoring by contractors; (iv) take corrective actions when necessary to ensure no environmental impacts; (v) submit monthly environmental monitoring reports to PMU, (vi) conduct continuous public consultation and awareness; (vii) address any grievances brought about through the grievance redress mechanism in a timely manner as per the IEEs; and	(i) Conducting environmental monitoring, as specified in the EMP. (ii) Issuance of clearance for contractor's post-construction activities as specified in the EMP.
Consultant – 1.PMCBC-Environmental	(i) Review IEE/EMP submitted by CMSC and revise report to submit to PMU	(i) Monitor EMP implementation (ii) Assist in addressing any grievances brought about	

Responsible Agency	Responsibility		
	Pre-Construction Stage	Construction Stage	Post-Construction
Safeguard Specialist – 1 no. Asbestos Expert – 1no. Heritage Expert – 1no. Biodiversity Expert – 1no.	(ii) Assist PMU and PIU in obtaining all necessary clearances, permits, consents, NOCs, etc. Ensure provisions and conditions are incorporated in the IEE and detailed design documents. (iii) Assist in ensuring IEE is included in bid documents and contract agreements. (iv) Assist in determining adequacy of cost for EMP implementation. (v) Assist in addressing any concern related to IEE and EMP. (vi). Conduct specific assessment requirements	through the Grievance Redress Mechanism in a timely manner as per the IEEs.	
Consultant- 2. CMSC- 2 nos. Environmental safeguards professional	(i) Update initial environmental assessment for proposed project using REA checklists and submit to PIU/PMCBC (ii) Assist in summarizing IEE and translating to language understood by local people.	Monitoring of Implementation of EMP at site by contractor Recommend corrective action measures for non-compliance by contractors Assist in the review of monitoring reports submitted by contractors (iv) Assist in the preparation of monthly monitoring reports conduct continuous public consultation and awareness;	(i) Assist in the inspection and verification of contractor's post-construction activities.
Contractors (EHS Engineer)	(i) Review the IEE and provide information about changes needed as per revised design and scope of works to ESS of PMCBC for final revision of IEE (ii) Prepare EHS plan and take approval from CMSC/PIU and Ensure EMP implementation cost is included in the methodology. (iii) Undergo EMP implementation orientation by ESS of supervision consultant prior to start of works (iv) Provide EMP implementation orientation to all workers prior to deployment to worksites (v) Seek approval for camp sites and sources of materials.	(i) Implement EMP. (ii) Implement corrective actions if necessary. (iii) Prepare and submit monitoring reports including pictures to PIU (iv) Comply with all applicable legislation, is conversant with the requirements of the EMP; (v) Brief his staff, employees, and laborer about the requirements of the EMP and provide environmental awareness training to staff, employees, and laborers; (vi) Ensure any sub-contractors/ suppliers who are utilized within the context of the contract comply with all requirements of the EMP. The Contractor will be held	(i) Ensure EMP post-construction requirements are satisfactorily complied (ii) Request certification from PIU

Responsible Agency	Responsibility		
	Pre-Construction Stage	Construction Stage	Post-Construction
	(vi) Ensure copy of IEE is available at worksites. Summary of IEE is translated to language understood by workers and posted at visible places at all times.	responsible for non-compliance on their behalf; (vii) Bear the costs of any damages/compensation resulting from non-adherence to the EMP or written site instructions; (viii) Ensure that PIU and ACM/SO are timely informed of any foreseeable activities related to EMP implementation.	

Capacity Building and Development

219. Executing and implementing agencies need to have a sustained capacity to manage and monitor environmental safeguards. Although specialist consultants support will be available to PMU and PIUs, it is necessary to mainstream safeguards in day-to-day working. Therefore, PMU and PIUs require capacity building measures for (i) a better understanding of the project-related environmental issues; and (ii) to strengthen their role in preparation of IEE, implementation of mitigation measures, and subsequent monitoring. Trainings and awareness workshops are included in the project with the primary focus of enabling the PMU and PIU staff to understand impact assessments and carry out environmental monitoring and implement EMPs. After participating in such activities, the participants will be able to review environmental assessments, conduct monitoring of EMPs, understand government and ADB requirements for environmental assessment, management, and monitoring (short- and long-term), and incorporate environmental features into future project designs, specifications, and tender documents and carry out necessary checks and balances during project implementation.

220. PMCBC's ESS shall assess the capabilities of the target participants, customize the training modules accordingly and provide the detailed cost.

221. Typical modules would be as follows: (i) sensitization; (ii) introduction to environment and environmental considerations in water supply and wastewater projects; (iii) review of IEEs and integration into the project detailed design; (iv) improved coordination within nodal departments; and (v) monitoring and reporting system. Specific modules customized for the available skill set will be devised after assessing the capabilities of the target participants and the requirements of the project. The contractors will be required to conduct environmental awareness and orientation of workers prior to deployment to work sites. The proposed training project, along with the frequency of sessions, is presented in **Table 37**.

Table 37: Capacity Building Program on EMP Implementation

Sl. No.	Description	Target Participants and Venue	Cost and Source of Funds
1	Introduction and Sensitization to Environmental Issues (1 day) - ADB Safeguards Policy Statement -EARF of RSTDSP -Government of India and Rajasthan applicable safeguard laws, regulations and policies	All staff, ULBs and consultants involved in the project At PMU, Jaipur	PMU cost

	including but not limited to core labor standards, OH&S, etc. -Incorporation of EMP into the project design and contracts -Monitoring, reporting and corrective action planning		
2	Treated Effluent Reuse Concepts, Design and Management	All staff at PMU and ULBs	PMU cost
3	Sludge Reuse Concept, Design and Management	All staff at PMU and ULBs	PMU cost
4	EMP implementation (2 days) -Roles and responsibilities -OH&S planning and implementation -Wastes management (water, hazardous, solid, excess construction materials, spoils, etc.) -Working in congested areas, - Public relations - Consultations - Grievance redress -Monitoring and corrective action planning -Reporting and disclosure -Post-construction planning	All staff and consultants involved in the subproject All contractors before start of construction works At PIU	PMU cost
5	Plans and Protocols (1 day) -Construction site standard operating procedures (SOP) - Asbestos Management Plan -Heritage Impact Assessment -Biodiversity and Critical Habitat Assessment - Site-specific EMP -Traffic management plan -Spoils management plan -Waste management plan - Chance find protocol - O&M plans - Post-construction plan	All staff and consultants involved in the project All contractors before start of construction works or during mobilization stage. At PIU	PMU cost Contractors cost as compliance to contract provisions on EMP implementation
6	Experiences and best practices sharing - Experiences on EMP implementation - Issues and challenges - Best practices followed	All staff and consultants involved in the project All contractors All NGOs At PMU Jaipur	PMU Cost
7	Contractors Orientation to Workers on EMP implementation (OH&S, core labor laws, spoils management, etc.)	All workers (including manual laborers) of the contractor prior to dispatch to worksite	Contractors cost as compliance to contract provisions on EMP implementation

Monitoring and Reporting

222. Prior to commencement of the work, the DBO contractor will submit a compliance report to PIU ensuring that all identified pre-construction environmental impact mitigation measures as detailed in the EMP will be undertaken. PIU with the assistance of the SO and ESS of PMCBC, consultant will review the report and thereafter PMU will allow commencement of works.

223. During construction, results from internal monitoring by the DBO contractor will be reflected in their monthly EMP implementation reports to the PIU and ACM, CMSC. Project officer

	Particulars	Stages	Unit	Total Number	Rate (INR)	Cost (INR)	Costs Covered By
1	Air quality monitoring**	Pre-construction and Construction (quarterly)	per sample	81	4920	3,98,520	Civil works cost
2	Noise levels monitoring**	Pre-construction and Construction (quarterly)	Per sample	81	1980	1,60,380	Civil works cost
3	Groundwater quality**	Pre-construction and Construction (quarterly)	per sample	72	6720	4,83,840	Civil works cost
4.	Soil quality**	Pre-construction and Construction (quarterly)	per sample	72	5880	4,23,360	Civil works cost
5	Surface Water	Pre-construction and Construction (quarterly)	per sample	18	6720	1,20,960	Civil works cost
	Subtotal (B)					15,87,060	
C.	Capacity Building						
1.	Introduction and sensitization to environment issues	Pre-construction	lump sum			100,000	PMU
2.	EMP implementation	Construction	lump sum			50,000	PMU
3.	Plans and Protocols	Construction	lump sum			25,000	PMU
			lump sum			25,000	Civil works cost
4.	Experiences and best practices sharing	Construction/Post-Construction	lump sum			100,000	PMU
5.	Contractors Orientation to Workers on EMP implementation	Prior to dispatch to worksite	Lump sum			25,000	Civil works cost
	Subtotal (C)					325,000	
D	Civil Works						
1	Water Sprinkling for dust suppression	Construction	KL	5000	111	555,000	Civil works cost
2	Rainwater Harvesting for water conservation	Construction at proposed STP sites	Nos.	1	438819	438819	Civil works cost
3	Implementation of Asbestos Management Plan	Construction-Inventory Testing Overall Supervision for Asbestos Removal Storage Transportation Disposal / Treatment	Lumpsum		-	7,000,000	Civil works cost

	Particulars	Stages	Unit	Total Number	Rate (INR)	Cost (INR)	Costs Covered By
		Documentation and Reporting					
4	Barricading						
	Providing and fixing Barricading using 40 mm dia M.S. pipe vertical and horizontal posts	Construction	m	162637	50	8131850	Civil works cost
	Providing and fixing using 40 mm dia M.S. pipe ("B" class) as vertical post and PVC tape	Construction	m	159277	38.50	6132164	Civil works cost
	MS Pipe with nut and bolt and GI corrugated sheets	Construction	Sq.m.	775	101	78275	Civil works cost
	Sub Total (D)					22,774,927	
E	Grievance Redressal Mechanism				Lump sum	350,000	Civil works cost
	Sub Total (F)					350,000	
	Total (A+B+C+D+E+F)				INR	2,50,97,737	

* After the confirmatory survey by DBO contractor cutting of 2 trees (One *Mangifera indica* and one *Azadirachta indica* will be required at CWR construction site and RWR site. No . tree cutting is required for pipe line works. AT draft IEE stage higher side of tree cutting numbers were taken as 5 trees. As per RUDSICO-EAP policy; compensatory plantation in the ratio of 1:3 is to be followed during construction works. Therefore 15 numbers of trees are taken as compensatory plantation.

Summary of EMP Cost incurred by Institution :

Contractor Cost - INR 250,97,737/-
 PMU Cost - INR 275,000/-
Total - INR 25372737/-

(In Words: Rupees Two Crores Fifty Three Lacs Seventy Two Thousand Seven Hundred and Eighty Seven only)

Table 39: Details of environment monitoring locations

Project components where environmental monitoring is required	Total numbers of environmental monitoring required in one quarter	Total numbers of environmental monitoring required in one year (three quarters leaving quarter of monsoon)	Project duration	Total number of environmental monitoring required during project duration
STP-1 SPS-3 CWR-2 RWR-1 Intake Well-1	Air- 9 Noise- 9 Ground Water- 8 Surface Water-2 Soil- 8	Air- 27 Noise- 27 Ground Water- 24 Surface Water-6 Soil- 24	3 years	Air-81 Noise- 81 Ground Water- 72 Surface Water-18 Soil- 72

WS/WW networks- 1				
Total-6 Locations				

X. CONCLUSION AND RECOMMENDATION

229. The process described in this document has assessed the environmental impacts of all elements of the Dungarpur water supply and sewerage subproject. All potential impacts were identified in relation to pre-construction, construction, and operation phases. Planning principles and design considerations have been reviewed and incorporated into the site planning and design process wherever possible; thus, environmental impacts as being due to the project design or location were not significant. During the construction phase, impacts mainly arise from the construction dust and noise, the need to dispose of large quantities of waste soil and import a similar amount of sand to support the sewer in the trenches; and from the disturbance of residents, businesses, traffic and important buildings by the construction work. The social impacts (access disruptions) due to construction activities are unavoidable, as the residential and commercial establishments exist along the roads where sewers will be laid. A resettlement plan has been developed in accordance with ADB SPS 2009 and Government of India laws and regulations.

230. Presently water is supplied to consumers daily but the frequency of supply is once in a day for the average duration of 1-1.5 hours and supply is only ~70 LPCD against the desired service of 135 LPCD.

231. In present source of water at Dungarpur are (I) surface water sources: Edward Samand and Vijay Chakra Sagar Dimiya dam (II) underground water: tube wells/ bore wells and open wells/dug wells. Due to rocky terrain the yield of these ground water sources is very less and as the water table is regularly depleting fast therefore these would not sustain for longer.

Proposed sources for water supply for Dungarpur are-

232. Existing Edward Samand Dam and Vijay Chakra Sagar Dam is a drinking water reservoir already connected with the existing system are sustainable sources with respect to quantity & quality; The Edward Samand dam has the total storage of 137 McFt excluding the dead storage of the dam. For proposed water supply project only 4.54 MLD i.e. about 61 McFt water is proposed to be drawn from the source. PHED has provided past 12 year water level Details of both the dams and dam was full in all the 12 years

233. New proposed Som Kamala Amba (SKA) Dam on Som River: To meet out the shortfall demand of the town Dungarpur, the state Government has sanctioned a public importance project namely Drinking Water Supply Project for 151 Villages and 1 town of District Dungarpur (Dungarpur town itself) based on Som Kamla Amba Dam on Som River, (called source project) which is a sustainable source for the project proposed by PHED. Som Kamla Amba dam is located on Som river basin amidst in Dungarpur district of Rajasthan state. This dam is situated about 45 KM distant from Dungarpur town. Presently the project is under execution, transmission main from the Som Kamla Amba Dam to Dungarpur town has been laid and construction work of intake well and water treatment plant is under progress. As per PHED officials project will be commissioned up to December 2022. Source sustainability report of Somkamla Amba dam and other surface and ground water sources is given in Appendix 4. The construction of Som Kamla Amba Dam was completed in the year 2000. This dam is located in Ashpur Tehsil of Dungarpur District, Rajasthan to provide the Irrigation cum drinking water facilities. Capacity of dam at FTL

of 213.5 m is 172.75 MCM and live storage capacity 160 MCF there is 93.75 % dependability of required 47.33 MCF quantity for Dungarpur town on the basis of past 15-year record of storage of Sam Kamla Amba dam. PHED has provided past 23 year water level Details of dam and out of 23 year 19 years dam was 100 % full.

234. A survey/study on flora and fauna in Vijay Chakra Dam was conducted by a biodiversity expert in reference to the sighting of mugger crocodile (*Crocodylus palustris*) in the area. Based on the results of the study, the final location of intake has been decided. From the original proposal of constructing a new intake, it has been changed to refurbishing of existing intake to minimize impacts on wildlife, particularly, *Crocodylus palustris*, which is a vulnerable species per IUCN and is protected under wildlife conservation act. Recommendations during the design, construction and operation are discussed in this IEE.

235. Development of Ground Water sources. At present there are 7 Nos Tube wells and 15 Nos Dug Wells / Open wells, out of these existing TW/ OW, 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desilting, with re commissioning work. The ground water will be used in Lean Season or during repair maintenance works in infrastructures supplying surface water

236. Dungarpur Municipal Council does not have any organized sewerage system. Presently the wastewater from kitchens & bathrooms is discharged into storm water drains culminating finally to the Nallah or on ground, which pollutes the environment and contaminates the ground water. Most of the residential, commercial buildings and educational institutions have on-site septic tanks and soak pits. The effluents from the septic tanks directly drain into the open drains. In the absence of safe disposal system of sewage, the people of town are exposed to unhealthy and unhygienic environment.

237. The subproject is formulated to address gaps in water and sewerage infrastructure in a holistic and integrated manner. The Project Components include improvements in water supply and sewerage infrastructure to improve the service level of water supply as per PHED recommended norms of 135 LPCD. Whole the sewage generated from municipal limits shall also be treated at STP as per latest effluent norms.

238. Proposed sites of STP and SPSs are located away from habitation areas. However, there are only shrubs and 2-3 trees at these locations which may need to be cut during construction. Adequate compensatory afforestation measures are being proposed under the project to counter the tree-cutting activity. Also, It is proposed to reuse the treated effluent for use in agriculture, horticulture, development of urban forestry etc. and remaining treated effluent is proposed to be discharged in to a nearby drains or vacant govt. lands. In order to achieve recommended standards it is proposed to achieve very low BOD (BOD 10) and suspended solids in the treated effluent from proposed STPs.

239. At the STP, sewage sludge will be removed continuously from reactors, and solidified using decanter, and stored in sludge drying beds for a period of 7-15 days. The treatment and drying processes kill enteric bacteria and pathogens. Because of its high content of nitrates, phosphates and other plant nutrients the sludge can be used as organic fertilizer.

240. Contractor will propose the plan with best methods for reuse of treated effluent and sludge as per guidelines of CPHEEO and best international practices in consultation with RUDSICO-EAP and Municipal Council and submit it in RUDSICO-EAP for approval. In order to aid preparation of a viable treated wastewater reuse and sludge reuse plan, an institutional and

capacity building component shall be incorporated in the Project to enable the ULB staff to develop an understanding of the relevant issues.

241. Certain new initiatives have been taken in the project viz., promoting wastewater reuse, sludge reuse and contractor to work on private properties to provide sewerage connections. Hence, appropriate guidelines for these measures should be provided for these new initiatives. These could include viz., Guidelines for the ULBs for promoting wastewater reuse; Guidelines for the ULBs for sludge reuse; and Guidelines for the Contractors to work within the private properties.

242. Anticipated impacts of sewerage system during operation and maintenance will be related to repair of blocks, overflows and leakages in sewers. Sewers are not 100% watertight and leaks can occur at joints. Faulty section will be exposed and repaired following the same basic procedure as when the sewer was built. Also, sewer pipes require regular maintenance as silt inevitably collects in areas of low flow over time. Necessary equipment for cleaning and removal of blockages in the sewers are included in the project.

243. Anticipated impacts of water supply during operation and maintenance will be related to detection and repair of leaks, pipe bursts. These are, however, likely to be minimal, as proper design and selection of good quality pipe material shall mean that leaks are minimal. Leak repair work will be similar to the pipe-laying work.

244. The public participation processes undertaken during project design ensured stakeholders are engaged during the preparation of the IEE. The planned information disclosure measures and process for carrying out consultation with affected people will facilitate their participation during implementation. The project's grievance redress mechanism will provide the citizens with a platform for redressing grievances, and describes the channels, timeframe, and mechanisms for resolving complaints about environmental performance.

245. The Environmental Management Plan proposed in the project includes mitigation measures for identified impacts, training and capacity building activities, a monitoring plan to ensure that the environmental standards are maintained throughout the project construction period and a reporting plan to ensure that the project is implemented as per environmentally sound engineering and construction practices. The budgetary provision for mitigating the anticipated impacts by proposed subproject component is made in the project for effective implementation of the EMP Plan. the EMP Plan. Total estimated cost for EMP implementation is approx. INR 25372737/- (In Words: Rupees Two Crores Fifty Three Lacs Seventy Two Thousand Seven Hundred and Eighty Seven only

246. The EMP will assist the PMU, PIU, Consultants and contractors in mitigating the environmental impacts, and guide them in the environmentally sound execution of the proposed project. The EMP will also ensure efficient lines of communication between PIU/ULB, PMU, consultants and contractor. A copy of the EMP shall be kept on-site during the construction period at all times. The EMP shall be made binding on all contractors operating on the site, and will be included in the contractual clauses. Non-compliance with, or any deviation from, the conditions set out in this document shall constitute a failure in compliance.

247. The project will benefit the general public by contributing to the long-term improvement of water supply and sewerage system and community liveability in Dungarpur. The potential adverse environmental impacts are mainly related to the construction period, which can be minimized by the mitigation measures and environmentally sound engineering and construction practices.

248. Therefore, as per ADB SPS, the project is classified as environmental category B and does not require further environmental impact assessment.

249. Recommendations. Based on the findings of the draft IEE, several recommendations have been made for this subproject. The compliance status of these recommendations is as follows:

- Include this IEE in bid and contract documents - Complied:
- Conduct safeguards induction to the contractor upon award of contract - Complied:
- Ensure contractor appointed qualified environment, health and safety (EHS) officers prior to start of works - Complied
- Timely disclosure of information and establishment of GRM - Complied
- Involvement of contractors, including subcontractors, in first-level GRM - Complied

250. Recommendations to be complied in final IEE

- Obtain all statutory clearances at the earliest possible time and ensure that the conditions/provisions are incorporated into the detailed design. - being complied
- Ensure commitment from PMU (Project Management Unit), PIUs (Project Implementation Units), project consultants, and contractors to protect the environment and people from any impact during project implementation. - being complied
- Update/revise this IEE based on the detailed design and/or if there are unanticipated impacts, changes in scope, alignment, or location. - being complied
- Update and implement the asbestos management plan according to site-specific conditions.- being complied
- Ensure that sludge management protocols are compliant with environmental regulations (Solid Waste Management Rules 2000 and its amendments) and solid waste disposal should have a designated site (dumping on vacant lot is not allowed) - being complied.
- Strictly supervise EMP implementation - being complied
- Continuous consultations with stakeholders; being complied.
- Documentation and reporting on a regular basis as indicated in the IEE. – being complied

Appendix 1: REA Check list

Instructions:

The project team completes this checklist to support the environmental classification of a project. It is to be attached to the environmental categorization form and submitted to the Environment and Safeguards Division (RSES) for endorsement by the Director, RSES and for approval by the Chief Compliance Officer. This checklist focuses on environmental issues and concerns. To ensure that social dimensions are adequately considered, refer also to ADB checklists and handbooks on (i) involuntary resettlement, (ii) indigenous peoples planning, (iii) poverty reduction, (iv) participation, and (v) gender and development. Answer the questions assuming the “without mitigation” case. The purpose is to identify potential impacts. Use the “remarks” section to discuss any anticipated mitigation measures.

Country/Project Title: India/Rajasthan Secondary Towns Development Investment Program (RSTDP)/Dungarpur Water Supply and Waste Water Project, Distt. Dungarpur, Rajasthan
Sector Division: *Urban Development*

REA Checklist- Sewerage

SCREENING QUESTIONS	Yes	No	REMARKS
A. Project Siting Is the project area...			
Densely populated?	√		Subproject activities are scattered to entire town including the low, medium and densely populated areas.
Heavy with development activities?	√		Dungarpur Town is a developing town with continuous urban expansion, there are no major industries and mostly agriculture, business and service are the common occupations
Adjacent to or within any environmentally sensitive areas?		√	There are no environmental sensitive areas near the proposed sites.
Cultural heritage site		√	There are no any cultural heritage site in Dungarpur Municipal areas or near to any proposed site. Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments
Protected Area		√	
Wetland		√	
Mangrove		√	
Estuarine		√	
Buffer zone of protected area		√	
Special area for protecting biodiversity		√	
Bay		√	
Potential Environmental Impacts Will the Project cause...			

SCREENING QUESTIONS	Yes	No	REMARKS
Impairment of historical/cultural monuments/areas and loss/damage to these sites?		√	There are no any cultural heritage site in Dungarpur Municipal areas or near to any proposed site. Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments
Interference with other utilities and blocking of access to buildings; nuisance to neighboring areas due to noise, smell, and influx of insects, rodents, etc.?	√		Construction work may interfere with the water supply, power and communication lines. Access to houses and business may be affected during pipe laying works. Construction works may cause nuisance to public in form of traffic disturbance, utility disruption, increased noise and air pollution. Proposed STP sites are located away from inhabited areas. Adequate green buffer around the site will be provided to minimize the nuisance due to bad odour, if any.
dislocation or involuntary resettlement of people		√	Project does not involve land acquisition / involuntary resettlement /displacement. During the sewer construction, particularly in narrow streets there may be temporary disruption to household and there will also be temporary loss of livelihood to roadside vendors, the same is addressed in the Resettlement Plan.
Disproportionate impacts on the poor, women and children, Indigenous Peoples or other vulnerable groups?		√	
Impairment of downstream water quality due to inadequate sewage treatment or release of untreated sewage?		√	There are three major surface water bodies namely Do River, Sabela Lake and Gap Sagar Lake. Spoil leakage from construction sites of SPS and STP may be possibly into the water bodies. There is proposal of reuse of treated effluent from STP and unused treated effluent shall be discharged in to nearby land or drains, therefore treated effluent needs to meet prescribed standards set by the Central Pollution Control Board (CPCB).
Overflows and flooding of neighboring properties with raw sewage?		√	Raw sewage shall not cause any flooding and overflowing and will be ensured through regular operation and maintenance.

SCREENING QUESTIONS	Yes	No	REMARKS
Environmental pollution due to inadequate sludge disposal or industrial waste discharges illegally disposed in sewers?	√		Inadequate sludge disposal may cause environmental pollution (soil and Water) This sewerage system will cater only domestic wastewater, no industrial wastewater discharge is allowed into the sewerage system. As a precaution, ULB should take responsibilities that wastewater from industrial units should not be allowed into sewers.
Noise and vibration due to blasting and other civil works?		√	Blasting for underground works is prohibited in RUDSICO-EAP works
risks and vulnerabilities related to occupational health and safety due to physical, chemical, and biological hazards during project construction and operation?	√		Occupational health and safety risks are negligible due to chemical and biological hazards during construction in sewerage works, physical hazards may arise due to safety risks during construction works. During operation of sewerage system physical and biological hazards may cause health and safety risks to workers for which mitigation measures will be required
Discharge of hazardous materials into sewers, resulting in damage to sewer system and danger to workers?		√	This sewerage system will cater only domestic wastewater, no industrial wastewater discharge is allowed into the sewerage system.
Inadequate buffer zone around pumping and treatment plants to alleviate noise and other possible nuisances, and protect facilities?		√	STP is located in remote areas away from habitation. ULB will make provision of buffer zone of 200 mts for STP.
Road blocking and temporary flooding due to land excavation during the rainy season?	√		Road blocking/diversion will be done during pipe laying with prior permission from concerned authorities. Contractor has to prepare proper traffic management plan before excavation on roads. Underground construction works (sewer laying, foundations) will be carried out in non-monsoon period. In Dungarpur Town, rainfall is scanty and confined only to a limited period. No impacts envisaged
Noise and dust from construction activities?	√		Road cutting (cement and bituminous roads) for sewer laying works is likely to generate noise and dust. Scheduling of works appropriately and prior information to the affected people will minimize the impact. Dust generation will be controlled through water sprinkling, immediate transportation of excess soil, covered transport etc.

SCREENING QUESTIONS	Yes	No	REMARKS
traffic disturbances due to construction material transport and wastes?	√		Linear activities like sewer laying along the roads is likely to disrupt traffic. Vehicle movement for construction purpose will increase the traffic. Identification of alternate routes, allowing limited - at least one-way traffic, prior information about the works and alternative arrangements, providing information/sign boards etc will reduce the impact.
temporary silt runoff due to construction?	√		Mitigation measures will be required to protect silt runoff from construction activities during rains
hazards to public health due to overflow flooding, and groundwater pollution due to failure of sewerage system?	√		Sewerage system will be designed with applicable standards. Adequately trained staff and necessary equipment will be in place for regular operation and maintenance of the system. Proposed treatment system will be efficient and appropriate repair and maintenance procedure will be developed. Sufficient funds for operation will be ensured. Backup power supply system is part of project.
deterioration of water quality due to inadequate sludge disposal or direct discharge of untreated sewage water?		√	No untreated/partially treated sewage will be disposed. STP is designed to meet the peak demand. Regular monitoring of treated water will be conducted to check the treatment efficiency.
contamination of surface and ground waters due to sludge disposal on land?		√	Digested Sludge from reactors will be disinfected to be contamination free and will be collected and stabilized / dried before disposal/reuse. This process will ensure the dried sludge is harmless.
Health and safety hazards to workers from toxic gases and hazardous materials which may be contained in sewage flow and exposure to pathogens in sewage and sludge?		√	It is unlikely that sewage contain hazardous substances. Necessary apparatus and personal protection equipment will be provided. Staff will be trained in safe handling of sewage and sludge, and in cleaning of sewers.
large population increase during project construction and operation that causes increased burden on social infrastructure (such as sanitation system)?		√	Most of the unskilled workers will be hired locally, some of skilled workers will be brought from outside but numbers will not so large to have impacts on social infrastructure and services.
Social conflicts between construction workers from other areas and community workers?		√	The contractor will be utilizing the local labour force as far as possible; in case if it is necessary, labour camps and facilities will be provided appropriately. No conflicts envisaged

SCREENING QUESTIONS	Yes	No	REMARKS
risks to community health and safety due to the transport, storage, and use and/or disposal of materials such as explosives, fuel and other chemicals during construction and operation?		√	No explosives shall be used in project. Fuel and other chemicals will be used in very less quantities which will not have significant impact on community health and safety. Safe handling of fuels and chemicals will be ensured by contractor.
community safety risks due to both accidental and natural hazards, especially where the structural elements or components of the project are accessible to members of the affected community or where their failure could result in injury to the community throughout project construction, operation and decommissioning?	√		Community safety risk may be there during construction during excavation for pipe laying, equipment and vehicle operation, construction of STP etc. for which mitigation measures will be required by contractor

Checklist for Preliminary Climate Risk Screening

Country/Project Title: India/Rajasthan Secondary Towns Development Investment Program (RSTDP), Dungarpur Town Water Supply and Waste Water Project, District Dungarpur, Rajasthan

Sector : Urban Development

Subsector: Water Supply and Waste Water

Division/Department: SARD/SAUW

Screening Questions		Score	Remarks ²⁹
Location and Design of project	Is siting and/or routing of the project (or its components) likely to be affected by climate conditions including extreme weather related events such as floods, droughts, storms, landslides?	0	No such issue may affect the project
	Would the project design (e.g. the clearance for bridges) need to consider any hydro-meteorological parameters (e.g., sea-level, peak river flow, reliable water level, peak wind speed etc)?	0	No such issue may affect the project
Materials and Maintenance	Would weather, current and likely future climate conditions (e.g. prevailing humidity level, temperature contrast between hot summer days and cold winter days, exposure to wind and humidity hydro-meteorological parameters likely affect the selection of project inputs over the life of project outputs (e.g. construction material)?	0	No such issues may affect the project
	Would weather, current and likely future climate conditions, and related extreme events likely affect the maintenance (scheduling and cost) of project output(s) ?	0	No such issue may affect the project
Performance of project outputs	Would weather/climate conditions, and related extreme events likely affect the performance (e.g. annual power production) of project output(s) (e.g. hydro-power generation facilities) throughout their design life time?	0	No problem will envisaged in future which likely affect the performance of project output

²⁹ If possible, provide details on the sensitivity of project components to climate conditions, such as how climate parameters are considered in design standards for infrastructure components, how changes in key climate parameters and sea level might affect the siting/routing of project, the selection of construction material and/or scheduling, performances and/or the maintenance cost/scheduling of project outputs.

Options for answers and corresponding score are provided below:

Response	Score
Not Likely	0
Likely	1
Very Likely	2

Responses when added that provide a score of 0 will be considered low risk project. If adding all responses will result to a score of 1-4 and that no score of 2 was given to any single response, the project will be assigned a medium risk category. A total score of 5 or more (which include providing a score of 1 in all responses) or a 2 in any single response will be categorized as high risk project.

Result of Initial Screening (Low, Medium, High): Low

Other Comments: The proposed subproject activity involves construction of One new STP, CWRs and pump houses along with water supply and sewerage networks and the anticipated environmental impacts are very marginal and the construction activity does not impose any threat to the existing climatic conditions.

REA Checklist- Water Supply

SCREENING QUESTIONS	Yes	No	REMARKS
Water Supply			
Project Siting Is the project area-			
Densely populated?	√		Some part of the city is densely populated, whereas outer area is less dense. Water supply is proposed in all town including densely populated areas of town
Heavy with development activities?	√		Dungarpur is a developing town; urban expansion is considerable
Adjacent to or within, any environmentally sensitive areas?		√	There could be no or temporary and limited impact on biodiversity especially to <i>Crocodylus palustris</i> in the dam as the construction of new intake well is dropped from the scope of work. Refurbishment works are limited to existing intake well which is at the shore of the dam. Further, the mitigation measures are provided in EMP, which will take care of any temporary impacts which are reversible.
Cultural heritage site	√		There are no any cultural heritage sites in Dungarpur Municipal areas or near to any proposed site. Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments
Protected Area		√	
Wetland		√	
Mangrove		√	
Estuarine		√	
Buffer zone of protected area		√	
Special area for protecting biodiversity		√	
Bay		√	
Potential Environmental Impacts Will the Project cause...			
Pollution of raw water supply from upstream wastewater discharge from communities, industries, agriculture, and soil erosion runoff?		√	There are three major surface water bodies namely Do River, Sabela Lake and Gap Sagar Lake. No water supply components are proposed at adjoining to these water bodies.
Impairment of historical/cultural monuments/areas and loss/damage to these sites?		√	There are no any cultural heritage sites in Dungarpur Municipal areas or near to any proposed site. Jain Temple, Baroda (approx. 16 km) and Dev Somnath Temple (approx. 37 km) in Dungarpur district are ASI Monuments, these temples are far away from municipal boundary and therefore project activities will not have impact on both the protected monuments
Hazard of land subsidence caused by excessive ground water pumping?		√	No new ground water source will be used for proposed water supply

Social conflicts arising from displacement of communities?		√	Project does not involve land acquisition /displacement. No social conflicts envisaged
Conflicts in abstraction of raw water for water supply with other beneficial water uses for surface and ground waters?		√	Water allocation is done for Dungarpur from Surface Water (Dams) and Under Ground Water Sources as per Government norms.
Unsatisfactory raw water supply (e.g. excessive pathogens or mineral constituents)?		√	Raw water shall be taken from Som Kamla Amba Dam and Edward Samand, which may contain pathogens or mineral constituents, for which sufficient treatment of raw water will be done at WTPs at At Udai vilas H/W and At Bori H/W, from where treated water shall be supplied for Dungarpur Town Water Supply project.
Delivery of unsafe water to distribution system?	√		Adequate treatment of water will be done at WTPs by DBO contractor to ensure delivery of safe water.
Inadequate protection of intake works or wells, leading to pollution of water supply?		√	Adequate safety measures will be required during operation of intake in Dungarpur
Over pumping of ground water, leading to salinization and ground subsidence?	√		No any new Ground water pumping will be done for water supply
Excessive algal growth in storage reservoir?		√	Periodical maintenance regime should be followed during O&M period to check algal growth in the system
Increase in production of sewage beyond capabilities of community facilities?		√	Construction of One new STP is proposed under RSTDSP works. Sewerage system has been designed keeping in mind for future waste water discharge from residences
Inadequate disposal of sludge from water treatment plants?	√		Rehabilitation of 2 WTPs is proposed in RSTDSP works. Sludge handling and disposal will be considered DBO contractor
Inadequate buffer zone around pumping and treatment plants to alleviate noise and other possible nuisances and protect facilities?		√	Proposed sites for pumping stations are demarcated with boundary wall and away from habitations
Impairments associated with transmission lines and access roads?		√	Old transmission lines will be replaced with new transmission line on existing ROWs therefore no such problem will emerge
Health hazards arising from inadequate design of facilities for receiving, storing, and handling of chlorine and other hazardous chemicals.	√		Chlorination is proposed in WTPs where mitigation measures for safety in chlorine handling will be required
health and safety hazards to workers from handling and management of chlorine used for disinfection, other contaminants, and biological and physical hazards during project construction and operation?	√		Chlorination is proposed in WTPs where mitigation measures for safety in chlorine handling will be required
Dislocation or involuntary resettlement of people		√	There is no resettlement of people for project implementation. Only temporary livelihood impacts are anticipated for which Resettlement Plan is also prepared for temporary impacts on vendors
disproportionate impacts on the poor, women and children, Indigenous Peoples or other vulnerable groups?		√	No such impact is envisaged

Noise and dust from construction activities?	√		All the construction machineries employed should comply with noise emission standards of Central Pollution Control Board. Dust suppression measures such as water sprinkling will be employed
Increased road traffic due to interference of construction activities?	√		Excavation and laying pipelines along public roads will interfere with the traffic. Construction material transport will increase traffic within city. Proper traffic management and construction planning will be ensured to minimize the interference
Continuing soil erosion/silt runoff from construction operations?	√		Construction work during monsoon shall be carried out with due care so that silt run off due to construction operation is prevented. No construction will be allowed during rains.
Delivery of unsafe water due to poor O&M treatment processes (especially mud accumulations in filters) and inadequate chlorination due to lack of adequate monitoring of chlorine residuals in distribution systems?	√		There is possibility of delivery of unsafe water due to poor O&M of storage and distribution facilities. O&M contractor has to ensure the quality of water to be supplied. Penalty provisions should be made in O&M contract for delivery of unsafe drinking water
Delivery of water to distribution system, which is corrosive due to inadequate attention to feeding of corrective chemicals?		√	Not envisaged, pipes of corrosion free materials (PVC pipes) shall be used in the project and provision should be made in designs
Accidental leakage of chlorine gas?	√		Chlorination is proposed in WTPs where mitigation measures for safety in chlorine handling will be required
Excessive abstraction of water affecting downstream water users?		√	Only water allocated for the water supply from PHED/WRD shall be used for proposed project.
Competing uses of water?		√	Only water allocated for the water supply from PHED/WRD shall be used for proposed project.
Increased sewage flow due to increased water supply		√	Sewerage system is already considered under RSTDSP works considering proposed water supply development works in Dungarpur
large population influx during project construction and operation that causes increased burden on social infrastructure and services (such as water supply and sanitation systems)?		√	Most of the unskilled workers will be hired locally, some of skilled workers will be brought from outside but numbers will not so large to have impacts on social infrastructure and services
Social conflicts if workers from other regions or countries are hired?		√	The contractor will be utilizing the local labour force as far as possible; in case if it is unavoidable, labour camps and facilities will be provided appropriately. No conflicts envisaged
risks to community health and safety due to the transport, storage, and use and/or disposal of materials such as explosives, fuel and other chemicals during operation and construction?		√	No explosives shall be used in project. Fuel and other chemicals will be used in very less quantities which will not have significant impact on community health and safety. Safe handling of fuels and chemicals will be ensured by contractor.

community safety risks due to both accidental and natural hazards, especially where the structural elements or components of the project are accessible to members of the affected community or where their failure could result in injury to the community throughout project construction, operation and decommissioning?	√		Community safety risk may be there during construction during excavation for pipe laying, equipment and vehicle operation, construction of CWRs, OHSRs, pump houses etc. for which mitigation measures will be required by contractor

Appendix 2: Compliance with Environmental Criteria for Subproject Selection

Components	Criteria	Compliance
All subprojects		
	Subproject will avoid potentially significant adverse impacts that are diverse, irreversible or unprecedented (ADB SPS Category A for environment).	Complied- Sub project is not having significant adverse impacts, anticipated impacts are temporary and reversible and can be mitigated through mitigation plans suggested in IEE
	Comply with all requirements of ADB SPS 2009 and follow procedures set in this EARF.	Complied- Sub project complies all the requirements of ADB SPS 2009
	Comply with relevant national, and local laws, rules and regulations regarding EIA, environmental protection, pollution prevention (water, air, noise, solid waste, etc.), wildlife protection, core labor standards, physical cultural resources, health and safety, and other laws in specific sectors as indicated below	Complied- Sub project complies all relevant national and local laws, rules and regulations applicable to this type of sub projects
	Reflect inputs from public consultations	Complied- Stakeholder's consultations are conducted in the project planning phase and suggestions are incorporated in project designs
Location	Avoid involuntary resettlement by prioritizing rehabilitation over new construction using vacant government land where possible, and taking all possible measures in design and selection of site or alignment to avoid resettlement impacts	Complied- All components of sub project are planned on government land only. No land acquisition is done to avoid any involuntary resettlement.
	Avoid or minimize the cutting of trees	Complied- Tree cutting is avoided as far as possible and if tree cutting is unavoidable, it has been minimized to lowest level and If any tree cutting is required for construction works, prior permission from local administration for tree cutting will be required and compensatory plantation as per RUDSICO-EAP policy will also be required
Biodiversity	Avoid locating subprojects in critical habitats, such as, but not limited to, wildlife/bird sanctuaries, national parks, tiger reserves, elephant reserves, conservation reserves or core zone of biosphere reserves. Appendix 1 provides preliminary analysis using the International Biodiversity Assessment Tool (IBAT) key biodiversity areas, protected areas, IUCN red list species and likelihood of critical habitats per town.	There are no environmentally protected areas, core zones of biosphere reserves and highly valued habitat in the town. However, presence of vulnerable wildlife species (crocodile) has been noted in Dimiya Dam. However, there could be no or temporary and limited impact on biodiversity especially to <i>Crocodylus palustris</i> in the dam as the construction of new intake well is dropped from the scope of

	Should not directly affect environmentally protected areas, core zones of biosphere reserves and highly valued habitat	work. Refurbishment works are limited to existing intake well which is at the shore of the dam. Further, the mitigation measures are provided in EMP, which will take care of any temporary impacts which are reversible.
	If work is proposed with the aim of improving the conservation or management of designated subproject sites (e.g. improved drainage), this must only be undertaken: (i) after a comprehensive study and development of management plans and criteria; and (ii) with the direct involvement and approval of national and local bodies responsible for the subproject site.	Not applicable to this sub project
Physical Cultural Resources	Should not result in the destruction/damage of or encroachment onto physical cultural resources (PCR) ³⁰ such as archaeological monuments; heritage sites and movable or immovable objects, sites, structures, group of structures, and natural features and landscapes that have archaeological, paleontological, historical, architectural, religious, aesthetic or other cultural significance.	Complied- There are no any prohibited or protected areas or any archaeological or historical or protected monuments in the town. Project components will not impact any religious structures.
Existing Facilities to be rehabilitated or expanded	Conduct environmental audit of existing facilities ³¹ per ADB SPS	Complied- only refurbishment of existing Intake well, OHSRs, CWRs, and pump houses and Rehabilitation of existing Tube Wells are proposed and no environmental issues are anticipated in proposed refurbishment/ rehabilitation works
Associated Facilities ³²	Analyze environmental impacts and risks to be included in the IEE	Not applicable to this sub project
Asbestos-containing materials (ACM) including, but not limited to, pipes, roofing, ceilings, insulation materials, excess pipes stored in	Avoid handling or removing any ACM. Ensure asbestos concrete (AC) pipes facilities containing asbestos will not be disturbed and left in-situ. Appendix 4 (of EARF) provides asbestos management plan. RUDSICO shall include AMP in all contracts.	Being complied- No use of new ACM is proposed in sub project. There are existing asbestos cement pipes underground in the existing water supply networks, the alignment will be fine-tuned during the detailed design, to avoid existing AC pipe alignments as far as possible.

³⁰ Physical cultural resources as defined as “movable or immovable objects, sites, structures, groups of structures, and natural features and landscapes that have archaeological, paleontological, historical, architectural, religious, aesthetic, or other cultural significance. Physical cultural resources may be located in urban or rural settings and may be above or below ground or under water. Their cultural interest may be at the local, provincial, national, or international level.”

³¹ ADB SPS Appendix 4 para 12 on Existing Facilities

³² ADB SPS Appendix 1 para 6 defines associated facilities as “not funded as part of the project (funding may be provided separately by the borrower/client or by third parties), and whose viability and existence depend exclusively on the project and whose goods or services are essential for successful operation of the project”

PHED campuses, walls, etc.		Outline of ACM management plan is included in IEE and shall be updated before start of construction works by DBO contractor
	When designing subproject infrastructure that involves excavation in urban areas the relevant authorities must be consulted to ascertain the location of any ACM prior to any subproject activity. Locations of new infrastructure must then be designed to avoid excavating or disturbing any ACM.	Will be complied- DBO contractor shall provide details (location and quantity) of ACMs in the updated ACM management plan
Right-of-way	Locate water supply pipelines within the right of way (ROW) of other linear structures (roads, irrigation canals) as far as possible, to reduce new land acquisition.	Complied- Water supply pipes will be laid with ROW of roads
	Ensure that pipelines ROW do not require land acquisition from individual farmers that is a significant proportion of their total land holding (>10%).	Complied- no land acquisition is required for pipe laying works
Water Supply		
Sustainability	Utilize water sources at sustainable levels of abstraction only (i.e. without significant reductions in the quantity or quality of the source overall)	Being Complied- Presently source of water at Dungarpur Town is ground water whereas surface water Som Kamla Amba Dam and Edward Samand Dam will be used in proposed water supply system under RSTDSP.
Quality (raw water, treated water)	Ensure that water supply to consumers comply with the national drinking water standards at all times and confirm this by regular monitoring at WTPs and in domestic premises.	Will be complied- Regular water quality monitoring shall be done and before supply of the water to consumers, it shall be ensured that water quality meet the national drinking water standards at all times
	Avoid using water sources that may be polluted by upstream users	Being Complied- there are no source of pollution in Som Kamla Amba Dam and Edward Samand Dam.
	Avoid water-use conflicts by not abstracting water that is used for other purposes (e.g. irrigation)	Being Complied- Only allocated water from source will be utilized for proposed water supply
Location	As far as possible locate all new facilities – Water Treatment Plants (WTP), Tube Wells (TW), etc. away from houses, shops or any other premises used by people, thus establishing a buffer to reduce the effects of noise, dust and the visual appearance of the site.	Will be complied
	Locate WTPs at sites where there is no risk of flooding or other hazards that might impair functioning of the WTP or present a risk of damage to the WTP or the surrounding area	Not applicable to this sub project- no WTP is proposed under the sub project

Design	Ensure that the water supply system improvements are combined with improvements in sewerage to deal with the increased discharge of domestic wastewater.	Complied- Water supply and sewerage system in town are designed considering the water supply to consumers at standard of 135 lpcd therefore increased discharge due to increased water supply will not affected sewerage system of town
Sewerage		
Location	Previous projects considered 500m as distance consideration from nearest habitation. This has been reduced to 100m considering facilities will be located in developed areas and technology to be used. RSTDSP considered using Sequencing Batch Reactor (SBR) technology in STPs, which is proven to cause minimal odor as compared to other treatment technologies such as Waste Stabilization Pond or Activated Sludge Process. As far as possible, new Sewage Treatment Plants (STP) should be preferably 100m away from any inhabited areas, in locations where no urban expansion is expected in the next 20 years, thus establishing a buffer to reduce effects of odor, visual appearance or other nuisance of the site (this may be reviewed depending on the technology adopted for the treatment of effluent).	Complied- No dense habitations are found within 100 mts from both STP site. STP site has sufficient area for future expansion of STP
	As far as possible Sewage Pumping Stations (SPS) and wet wells should be located preferably 50m from any inhabited areas and from sites such as hospitals, schools, temples, etc. to minimize nuisance impacts from odor, rodents, etc.	Complied- No habitations exist within 50 mts from SPS sites.
	Locate STP at sites where there is no risk of flooding or other hazards that might impair function of the STP or present a risk of damage to the STP or the surrounding area	Complied- There is no risk of flooding or other hazards at both STP sites that might impair function of the STP or present a risk of damage to the STPs or the surrounding area.
Quality	Ensure that sewage is treated at all times to national waste water discharge standards and confirm this by regular monitoring of effluent from the STP.	Will be complied- Regular monitoring of Treated waste water shall be done and after meeting all national waste water discharge standards
Treated water	Ensure that no wastewater is discharged into a water course in which it could be a hazard to downstream users (e.g. a waterway that is used as a source of water for domestic or municipal supply)	Will be complied- treated water STP shall be discharged in Treated water Storage ponds located within the proposed STP site campus from where it shall be reuse by nearby farmers.
Sludge	Include measures to ensure the safe disposal of sewage sludge and if possible, to promote	It is proposed that safe and beneficial use of sewage sludge

	its safe and beneficial use as an agricultural fertilizer	as an agricultural manure shall be promoted
Right-of-way for sewer network	Locate sewage pipelines within the right of way (ROW) of other linear structures (e.g. roads) wherever feasible, to reduce new land acquisition.	Complied- Sewers pipes will be laid along the roads/streets in the City within the road right of way (ROW) therefore there is no need of land acquisition.
	Ensure that routes of sewage mains do not require land acquisition from individual farmers that is a significant proportion of their total land holding (10%)	

Appendix 3: Audit report of existing water supply system in Dungarpur

1 Introduction

Based on 2011 census the population of town is 47706 people, accordingly the present population for the year 2021 is about 53540. At present an intermittent water system is running in the town. The water supply of the town is depending on two local surface water Reservoirs viz Edward Samand and Vijay Chakra Sagar dam constructed exclusively for water supply needs, in addition to these, some sub surface sources (T/Ws and O/Ws) are also connected with the system, but due to rocky terrain the yield of these ground water sources is very less and the water table is regularly depleting fast therefore these would not sustain for longer. Owing to short fall in demand, the residents of town are facing acute scarcity of drinking water. To provide the relief from problem mentioned above, this project report is being framed, for this an over view of the existing system & infrastructure along with its utility for this project is being discussed in this chapter as follows:

2 Present water production and supply

At present an intermittent water supply system is running in the town. The present production of clear water is 6.4 MLD, but in fact due to system losses only 3840 KL of treated water is being reached to the consumers giving a service level of supply is only ~70 LPCD against the desired service of 135 LPCD. Thus, there is 35- 40% NRW in the system. The frequency of supply is once in a day for the average duration of 1.00-1.5 hours.

3 Quality of water

The raw water drawn from surface Reservoirs undergoes through the water treatment plant and is filtered and well-treated before supply to the beneficiaries. After that, treated water is distributed among the consumers. The quality of water drawn from underground water sources is also potable and fit for domestic use.

4 Present sources and production

As mentioned above at present the main sources of water are Edward Samand and Vijay Chakra Sagar dam. Beside these earlier some small quantity of water was also being obtained from nearby small Mandawa Khapeda anicut near to Taraghati, but now it has been closed as there is no sufficient water in this anicut. In addition to these, some sub surface sources (2 T/Ws and 2 O/Ws) are also at present running with the system. The details of surface sources together with the running tube wells & open wells and production details of water from these are given below in the table:

Table C-1 : Details of sources and production

S. No.	Source	Net Capacity of Reservoir (mcft)	Present production MLD	Anticipated production in MLD for the year			Utility for this project
				2025	2040	2055	
1	Edward Samand	134	2.4	4.54	4.54	4.54	Proposed to keep continue for this project
2	Vijay Chakra Sagar	40	1.0	3.1	3.1	3.1	Proposed to keep continue for this project.
3	Tube wells	-	1.0	1.0	1.0	1.0	Proposed to keep continue for this project, after augmentation and will be used in case of lean Season and repair
4	Open Wells	-	2.0	2.0	2.0	2.0	

S. No.	Source	Net Capacity of Reservoir (mcft)	Present production MLD	Anticipated production in MLD for the year			Utility for this project
				2025	2040	2055	
							maintenance of surface water infrastructure
5	SKA	172.75	-	0.59	2.46	4.36	New Source for Dungarpur town
		Total	6.4	11.23	13.1	15	

5 Location of ground water sources

Table C-2 : Details of ground water sources

S.No.	Location	Type	No.	Production MLD
Tube wells				
1	Patrakar colony TW	Tube well	1	0.5
2	Darji wada TW	Tube well	1	0.5
	Total		2	1.0
Open wells				
1	Rani Bao OW	Open well	1	1.0
2	Kela bao OW	Open well	1	1.0
	Total		2	2.0 MLD

6 Site Visuals





Figure 1 : Edward Dam



Figure 2 : Vijay Chakr Sagar (Dimiya) Dam

Raw water conveyance system

- 7 The raw water from Edward Samand is carried out to raw water Sump at Bori H/Ws

(WTP) by means of DI pipe line (by gravity flow) from there raw water is being pumped to WTP (3.25 MLD) at the same H/Ws for treatment. Balance 1.29 MLD me raw water is also carried out to Udaivilas H/Ws where another WTP (4.54 MLD) exists. Similarly, 3.25 raw water from Vijay Chakra Sagar (Dimiya) is carried out to Udaivilas H/Ws (WTP-3.25+1.29= 4.54 MLD) by means of DI pipe line through inter mediate pumping at Taraghati pumping station. The details of these raw water conveyance pipe lines are given below in Table Below:

Table C-3 : Details of ground water sources

S.N.	From	To	Details of raw water pipe line			Utility for this project
			Material	Dia in mm	Length In Mtr.	
1	Edward Samand	RW Sump at Bori H/Ws (WTP)	DI K-7	(a) 400 (b) 350	1490 7510	Useful, shall be utilised for this project
2	RW Sump at Bori H/Ws	Udaivilas H/Ws (WTP)	DI K-9	200	5950	Useful, shall be utilised for this project
3	Vijay Chakra Sagar (Dimiya)	Udaivilas H/Ws (WTP) Via Intermediate pumping station at Taraghati	DI K-9	200	10000	Replacement by 250 mm dia to accommodate flow and change of alignment along road.
		Total				

8 Raw water storage

There is at present only 4 raw water reservoirs with the system the details of the same are given below:

Table C-4 : Details of RWRs

S. No.	Location	Nos.	Capacity of RWRs in KL	Year of construction	Utility for this project
1	At Bori (Masonry)	1	350	1980	Heavy leakages in bottom hence new RCC RWR proposed.
2	At Bori (RCC)	1	235	2000	Useful, shall be utilised for this project
3	At Tara ghati (RCC)	1	175	1996	Not useful for this project, as it is being proposed to carry the raw water directly to the WTP at Udaivilas H/Ws
4	At Tara ghati (RCC)	1	175	2007	
	Total	4			



Figure 3 : Bori R.W.R. (235 KL)



Figure 4 : Bori R.W.R. (350 KL)



Figure 5 : Taraghati R.W.R. (175 KL)

9 Existing clear water reservoirs

Details of head works and CWRs

There was Five Head works in the system with the six CWRs & pump houses but at present only four Head works are in use in the system, as one Head Works has now been closed due to ruined & unusable condition of CWR and pump house. The details of H/Ws and CWRs are given below.

Table C-5 : Details of CWRs

S.no	Location of Head Works	Location of Existing CWR	Capacity of existing CWR (kl)	Year of construction	Condition (Based on Preliminary Inspection) and feasibility for reuse in this project.
1	Udaivilas	1. RCC CWR -1	113	1990	No need of this CWR as a new CWR of sufficient capacity (325 KL) has been constructed adjoining to existing Pump house.
		2. RCC CWR-2	325	2007	Useful, recommended to be kept continue for this project.
2	Bori	RCC CWR	325	2007	Useful, recommended to be kept continue for this project.
3	Chandpole	Masonry CWR-	500	1960	Ruined & unusable condition at present not in use.
4	Aen Office	Masonry CWR	263	1985	Useful, recommended to be kept continue for this project.
5	New colony / Nai Abadi	RCC CWR	272	1980	Useful, recommended to be kept continue for this project.



Figure 6 : CWR at Udaivilas (113 KL)



Figure 7 : CWR at Udaivilas (113 KL)



Figure 8 : CWR at Udaivilas (325 KL)



Figure C-9 : CWR at Bori head works (325 KL)



Figure 10 : Masonry CWR at AEN office (263 KL)

10 Existing service reservoirs

At present from water supply distribution point of view, the entire town has been divided into 20 zones. In these zones 23 Service Reservoirs (13 ESRs and 10 GLSRs) of various capacities are available in the respective zone areas; from these clear water is being supplied to the consumers. The details of Service Reservoirs are as follows:

Table C-6 : Details of existing SRs

Sl. No.	Location	Type of service Reservoir	Capacity of OHRs in KL	Staging in m	Year of construction	Condition (Based on Preliminary Inspection) & utility for this project.
1	Rajpura/New ESR (existing zone-1)	RCC ESR	150	18	2015	OK, may be kept continue for this project.
2	Navadera(existing zone-2A)	RCC ESR	325	15	2007	OK, may be kept continue for this project

Sl. No.	Location	Type of service Reservoir	Capacity of OHRs in KL	Staging in m	Year of construction	Condition (Based on Preliminary Inspection) & utility for this project.
3	Chand pole (existing zone-3)	Masonry GLSR	200	On hill	1968	Heavy leakages and new RCC OHSR proposed.
4	Meera Dungari (existing zone-4)	RCC GLSR	225	On hill	2007	OK, may be kept continue for this project
5	Khantwara (existing zone-5)	(a) GLSR 1	250	On hill	1979	Damaged therefore Replaced by new CWR given at 5 (b)
		(b). RCC GLSR-2	225	On hill.	2016	OK, may be kept continue for this project
6	Ghati-I (existing zone-7)	Masonry GLSR At Aen office campus.	200	On hill	1968	Require roof repairing, and may be used after that.
8	Ghati-II (existing zone-8)	GLSR	454	On hill	1988	Damaged, not proposed to keep continue.
9	City (existing zone-9) H/Ws at Aen office campus.	(a). RCC CWR (act as GLSR)	100	At bottom of hill	1985	Cannot work as SR, it is situated at the lower level and cannot serve the terminal head as required.
		(b) Masonry. GLSR	168	On hill	1968	OK, at present in use may be used under this project after some refurbishment.
10	New Abadi +Shastri Nagar (existing zone-10)	(a) RCC GLSR at AEN office campus hill.	450	On hill	1988	OK, may be kept continue for this project
		(b)RCC ESR	100	15	2007	OK, may be kept continue for this project
11	Sindhi Colony existing zone-11	RCC ESR	325	18	2007	OK, may be kept continue for this project
12	Pratap Nagar (existing zone-12)	RCC ESR	75	15	2007	OK, may be kept continue for this project
13	Indira Colony +Laxmi nagar (existing zone-13)	RCC ESR	227	15	1996	Top dome leakage, bracings, columns damaged, and not repairable, required replacement.
14	Old RHB (existing zone-14)	RCC ESR	272	15	1986	Top dome leakage, bracings, columns damaged, and not repairable, required replacement.
15	New RHB (existing zone-15) Shivaji Nagar	RCC ESR	100	15	2001	OK, may be kept continue for this project if required.

Sl. No.	Location	Type of service Reservoir	Capacity of OHRs in KL	Staging in m	Year of construction	Condition (Based on Preliminary Inspection) & utility for this project.
16	Patrakar Colony (existing zone-16)	RCC ESR	140	18	2007	OK, may be kept continue for this project
17	Hospital (existing zone-17)	RCC ESR	50	12	2001	Not feasible for this project as capacity & staging of the ESR is very less
18	Sabela (existing zone-18)	RCC ESR	50	12	2001	Not feasible for this project as capacity & staging of the ESR is very less
19	Modern School	RCC ESR	210	18	2013	OK, may be kept continue for this project
20	Ashok Nagar	RCC ESR	113	18	2013	OK, may be kept continue for this project
	TOTAL		4484			



Figure 11 : Existing ESR at Navadera (325 KL)



Figure 12 : Masonry GLSR for Ghati-I at hill near AEN office (200 KL)



Figure 13 : RCC CWR (Act as GLSR at AEN office capus)



Figure 14 : Masonry GLSR on hill at AEN office for city zone



Figure 15 : RCC GLSR on hill near AEN office for new abadi zone



Figure C-16 : Indra colony ESR- 227 KL



Figure 17 : Old RHB ESR- 272 KL

11 Existing pump houses

Table C-7 : Details of existing pump houses

S. No	Location	Size of PH (m x m)	Construction year	Utility for this project
1	Vijay Chakra Sagar (Dimiya) PH-2 for Raw water	5 X 4	2007	The replacement of pumps is recently taken up by PHED, GoR and will be used under present project. OK, may be keep continue for this project.
2	Mandwa Anicut PH- for Raw water	3 X 3	2007	No utility of these pumps for this project, as the duty conditions of these pumps do not suit for this project as per present design requirement.
3	Taraghati PH-1	3 X 5	1996	Not required as this intermediate pumping station has been proposed to be curtailed. Raw water from Dimiya shall directly be carried out to WTP at Udaivilas.
4	Taraghati PH-2	3 X 5	2007	
5	Udaivilas RGF PH-(I)	7 X 8	1990	Not proposed to keep continue, as this is not able to create a positive suction, therefore a new pump house of required dimensions is being proposed. This may be used to store the material.
6	Udaivilas RGF PH-(II)	3 X 3	2002	Not required to keep continue, as of very small size, may be used as a store room.

S. No	Location	Size of PH (m x m)	Construction year	Utility for this project
7	Main pump house	5 X 7	1960	The PH at present in ruined & unusable condition therefore proposed to be demolished and to construct new PH against this.
8	Chandpole pump house	5 X 7	1960	Not proposed to keep continue, as this is not able to create a positive suction, therefore a new pump house of required dimensions is being proposed. This may be used to store the material.
9	Bori RGF (I)	4 X 5	2002	Require repair and may be used after that
10	Bori RGF (II)	4 X 5	2007	Require some minor repair and may be used after that.
11	Nai Abadi GLR-1	5X10	1960	Require repair and may be used after that.
12	Nai Abadi GLR-1	3 X 3	2007	Not required to keep continue for this project as P/H-1 is of adequate size.



Figure -18 : PH at vijay chakra sagar dam



Figure 19 : PH at Udaivilas



Figure 20 : PH at Bori



Figure -21 : Clear water PH at Bori



Figure 22 : AEN Office PH



Figure -23 : Nai Abadi PH

12 Existing pumping machinery

The details of pumping sets installed at various pumping stations / HWs and tube wells / open wells are as follows:

Table C-8 : Details of existing P&M

S. No	Location	Type	Nos	Discharging Capacity in LPS	Head IN M	Utility for this project
1	For tube wells/OWs	Submersible	13	2.5 to 7.00 lps	90 to 140	No utility of these pumps for this project, as these sources are not being proposed to be continue for this project.
2	Vijay Chakra Sagar (Dimiya) PH for Raw water to Taraghati	centrifugal pump sets	2	39.45	55	No utility of these pumps for this project, as it is proposed to curtail this intermediate PH at Taraghati pump house. Raw water is proposed to be carried out directly to the WTP at Udaivilas.

S. No	Location	Type	Nos	Discharging Capacity in LPS	Head IN M	Utility for this project
3	Taraghati PH-1	centrifugal pump sets	2	24.72	40	No utility of these pumps for this project, as the raw water is proposed to be carried out directly to the WTP at Udaivilas from Vijay chakra Sagar Dam.
4	Udaivilas H/Ws (I)	Submersible				no utility of these pumps for this project as duty conditions do not match with the project requirement
5	Udaivilas H/Ws (II)	centrifugal pump sets	2	60	20	
		centrifugal pump sets	2	4.72	85	
		centrifugal pump sets	2	38.74	85	
		centrifugal pump sets	2	22.15	30	
6	Main pump house	centrifugal pump sets	2	15.33	65	no utility of these pumps for this project as duty conditions do not match with the project requirement
7	Bori RGF (I) for RWR	centrifugal pump sets	2	23.62	50	no utility of these pumps for this project as duty conditions do not match with the project requirement
8	Bori RGF (II) for CWR	centrifugal pump sets	2	23.08	60	no utility of these pumps for this project as duty conditions do not match with the project requirement
		centrifugal pump sets	2	13.92	95	
		centrifugal pump sets	2	23.71	105	
9	Nai Abadi GLR (CWR)	centrifugal pump sets	2	19.4	55	no utility of these pumps for this project as duty conditions do not match with the project requirement
		centrifugal pump sets	2	16.5	50	
		centrifugal pump sets	4	10.12	45	

13 Existing rising main

Table C-9 : Details of existing rising main

Size in mm	Type of pipe and length in Meter					Remark
	GI	DI	CI	AC	Total	

50	30				30	
65	60				60	
80			30	700	730	
100		1010	90	90	12550	
150		860	2250	18500	25900	
200		10500	1500	5500	26800	
350		7510			7510	
400		1490			1490	
TOTAL	90	21370	3870	24790	50120	

14 Existing distribution system

The distribution system has been laid of CI-LA / DI K-7 / AC-10 and AC-15 pipes. The size & material wise length of pipe lines are given in the table below.

Table C-10 : Details of existing distribution system

Size in mm	Type of pipe and length in M				Total	Remark
	CI -LA	DI	AC-10	AC-15		
50	50				50	
80	8375		34410		42785	
100	6090	12400	18465	26500	63455	
125			2200		2200	
150	4010	4800	6100	6030	20940	
200	1450	1420		300	3170	
250		700			700	
300		0			0	
TOTAL	19975	19320	61175	32830	133300	

As the existing AC pipes and CI pipes are so old and in damaged condition so to reduce the NRW existing AC and CI pipelines are not proposed to use only existing DI pipeline is proposed to be use.

15 Existing house connections

Table C-11 : Details of present house connections

S.No.	Category	Metered	Flat Rate	Total
1	Domestic	8352	287	8639
2	Commercial	122	0	122
3	Industrial	0	0	0
4	Govt.	89	0	89
5	ULB	188	0	188
	Total	8751	287	9038

REFURBISHMENT OF EXISTING INFRASTRUCTURE

16 Existing pump house and CWRs

At present, 12 pump houses (details mentioned in chapter-4, Section- 4.9) in 8 HWs are available with the system out of these 6 pump houses are using to carry the raw water obtained from sources to respective RGF and other PHs are used to transfer the clear water to service reservoirs Pump houses available in these H/Ws are at present in working condition. The pumps already installed in these pump houses would not be useful for this project as the duty conditions of the pump shall not be matched with the design parameters of the proposed pumps. Out of these, the details of pump houses require refurbishment are given below:

Table 0–1 : Details of existing PHs

S. No	Location	Size of PH MxM	Year of construction	Condition (Based on Preliminary Inspection) and feasibility for reuse in this project.
1	Vijay Chakra Sagar (Dimiya) PH-1 for Raw water	4 x 5	1996	The replacement of pumps is recently taken up by PHED, GoR and will be used under present project.
2	Udaivilas RGF (I)	7 X 8	1990	Require repair and may be used after that.
3	Bori RGF (I)	4 X 5	2002	Require repair and may be used after that.
4	Bori RGF (II)	4 X 5	2007	Require some minor repair and may be used after that.
5	Nai Abadi CWR-PH-1	5 X 10	2007	Require repair and may be used after that.
6	Main pump house at AEn PHED office	5 x 7	1960	Proposed to be demolished, as in ruined condition.
7	Chandpole pump house	5 x 7	1960	Proposed to be demolished as in ruined condition.

17 Existing raw water storage

There are 4 raw water Reservoirs (details mentioned in chapter-3) to collect the raw water 2 at Bori and 2 at Taraghati. Out of these, the details of reservoirs require refurbishment are given below:

Table 0–2 : Status of existing raw water storage

S. No.	Location	Nos	Capacity of RWRs in ML	Year of construction	Utility for this project
1	At Bori (Masonry)	1	350	1980	Not Useful, heavy leakages at bottom & walls, there for Proposed to be demolished,

18 Status of existing clear water storage reservoirs

There are 6 CWRs (details mentioned in chapter-4) to collect the clear water. Out of these, the details of reservoirs require refurbishment are given below:

Table 0–3 : Status of existing CWRs

S.no	Location of Head Works	Type of CWR	Capacity of existing CWR (kl)	Year of construction	Condition (Based on Preliminary Inspection) and feasibility for reuse in this project.
1	Udaivilas	2. RCC CWR-2	325	2007	Useful, recommended to be kept continue for this project after some minor repairing & painting work.
2	Bori	RCC CWR	325	2007	Useful, recommended to be kept continue for this project after some minor repairing & painting work.

S.no	Location of Head Works	Type of CWR	Capacity of existing CWR (kl)	Year of construction	Condition (Based on Preliminary Inspection) and feasibility for reuse in this project.
3	Chandpole	Masonry CWR-	500	1960	Ruined & unusable condition therefore proposed to be demolished.
4	Aen Office	Masonry CWR	263	1985	Useful, recommended to be kept continue for this project.
5	New colony / Nai Abadi	RCC CWR	272	1980	Useful, recommended to be kept continue for this project after some minor repairing & painting work.

19 Status of existing SRs (ESRs & GLSRs)

At present there are 23 Service Reservoirs (13 ESRs and 10 GLSRs) of various capacities are available in the various locations (details mentioned in chapter-4). Out of these, the details of reservoirs require refurbishment are given below:

Table 0-4 : Status of existing CWRs

Sl. No.	Location	Type of service Reservoir	Capacity of OHRs in KL	Staging in m	Year of construction as informed by local official PHED	Condition (Based on Preliminary Inspection) & utility for this project.
1	Navadera (existing zone-2)	RCC ESR	325	15	2009	Full capacity could not be utilized due to new population residing on higher sides of hill, hence addition OHSR proposed.
2	Chand pole (existing zone-3)	Masonry GLSR	200	On hill	1968	Not Useful, heavy leakages at bottom & walls, hence new RCC OHSR proposed.
3	Meera Dungari (existing zone-4)	RCC GLSR	225	On hill	2009	OK, may be kept continue after painting work.
4	Mahakaleshwar (existing zone-6)	RCC GLSR	75	On hill	2009	Very less capacity and not suitable as SR due to new locality residing on higher sides of hills, hence new OHSR proposed
5	Ghati-I (existing zone-7)	Masonry GLSR at AEn office campus.	200	On hill	1970	Require roof repairing, and may be used after that.
6	AEN office campus hill.	RCC GLSR at AEn office campus hill.	450	On hill	1990	OK, may be kept continue after some minor repairing work & painting work
7	AEN office campus hill.	Masonry GLSR at AEn office campus hill.	168	On hill	1968	OK, at present in use & may be kept continue after some minor repairing work & painting work

Sl. No.	Location	Type of service Reservoir	Capacity of OHRs in KL	Staging in m	Year of construction as informed by local official	Condition (Based on Preliminary Inspection) & utility for this project.
8	Shastri colony	RCC ESR	100	15	2009	OK, may be kept continue after painting work.
9	Sindhi Colony) existing zone-11	RCC ESR	325	18	2009	OK, may be kept continue after painting work.
10	Pratap Nagar (existing zone-12)	RCC ESR	75	15	2009	OK, may be kept continue after painting work.
11	Indira Colony +Laxmi nagar (existing zone-13)	RCC ESR	227	15	1996	Top dome leakage, require and not usable require replacement.
12	Old RHB (existing zone-14)	RCC ESR	272	15	1990	Top dome leakage, bracings, columns damaged, and not repairable, required replacement.
13	Patrakar Colony (existing zone-16)	RCC ESR	140	18	2009	OK, may be kept continue after painting work.
14	Modern School	RCC ESR	210	18	2013	OK, may be kept continue after painting work.
15	Ashok Nagar	RCC ESR	113	18	2013	OK, may be kept continue after painting work.

20 Status of existing Distribution system

Present distribution system is very old of AC/PVC pipes of undersize. There often happen leakages in the lines increasing quantity of NRW in the system. The whole system is required to be replaced by HDPE pipelines. After laying the lines, the provision of road repairs has also been proposed in the project.

21 Status of existing rising mains

All the AC / old CI pipe lines laid for rising mains are to be replaced by DI K-7 pipes as per policy of the RUIDP, therefore the provision of new DI K-7 pipelines have been taken wherever required as per design.

22 Existing water treatment plant

There are two rapid gravity water treatment plants of capacity of 4.54 MLD and 3.25 MLD with the existing system. Thus, there is a total capacity of WTP is 7.79 MLD. The details are as follows:

Table 0-5 : Details of RWRs

S.No.	Location	Type of WTP	Capacity MLD	Year of construction	Remark/ Utility for this project
1	RGF at Udaivilas	RGF	4.50	1987-88	Useful, recommended to be kept continue for this project after some minor repairing
2	Bori RGF	RGF	3.25	2007-08	Useful, recommended to be kept continue for this project after some minor repairing.

S.No.	Location	Type of WTP	Capacity MLD	Year of construction	Remark/ Utility for this project
	Total	-	7.79	-	-



Figure 1 : Udai vilas RGF



Figure 2 : Udai vilas clarifloculator



Figure 3 : Bori clarifloculator



Figure 4 : Bori RGF

Environment Audit of Existing WTP at Bori

Introduction

Under the ADB funded Rajasthan Secondary Towns Development Sector Project (RSTDSP), it is proposed to water supply and sewerage project in Dungarpur Town. Since adequate capacity treatment facility is already in Bori WTP 3.25 MLD and Uday Vilash WTP 4.45 MLD, no new WTPs is proposed for this Project. Sustainability of new water supply infrastructure and realisation of intended purpose. The existing WTP at Bori is an associated facility as per the ADB Safeguard Policy Statement 2009. Compliance with the environmental safeguards will ensure the subproject sustainability.


The objectives of this study is to (i) assess the compliance of the water treatment plant (WTP) with country's environmental regulatory framework; (ii) improve environmental performance, as required, through monitoring the effectiveness of the management system; and (iii) increase the RSTDSP's knowledge of its activities, thus increasing its ability to continually improve and minimize future potential liabilities. The details of existing plant, process and used technology are given below:

Name	WTP at Bori Head Works				
1. Location of Plant:	In the Campus of Bori Head Works				
2. Capacity (MLD):	3.25 MLD				
3. Technology:	Rapid Gravity Filter				
4. Executing agency:	PHED				
5. Implementing agency:	PHED				
6. Asset Owner:	PHED				
7. Date of completion of construction works of WTP:	A. RGF-1: 2002 B. RGF-2: 2007				
8. Status of work progress of WTP: (completed/uncompleted components with %)	completed/				
9. Nos., locations and capacities of Pumping Stations:	S. N	Location	Size of PH (m x m)	Const. year	
	3	Bori RGF (I)	4 X 5	2002	
	4	Bori RGF (II)	4 X 5	2007	
10. Land ownership details	PHED				
11. Status of Consent to Establish (CTE) from Pollution Control Board: obtained/not obtained	To till date not taken				
12. Status of Consent to Operate (CTO) from Pollution Control Board: obtained/not obtained	To till date not taken				
13. Details of water supplied areas with WTP: (ward nos./localities)	Rajpura, Navadera, Chanpole, Meeradungari, Khantwara, (Zone 1 to 5)				
14. Total Population covered (number and %):					
15. What are the parameters of treated water:	Parameters				Value
	PH				7.9
	Turbidity (NTU)				0.2
	Temperature (°C)				None
	Odour Colour (Hazen Units)				None
	Residual Chloride (mg/l)				-
	Chloride (mg/l)				100
	Fluoride (mg/l)				0.24
	Nitrate (mg/l)				5
	Total Alkalinity (mg/l)				210
	Total Hardness (mg/l)				230

	<table> <tr> <td>Calcium Hardness (mg/l)</td><td>130</td></tr> <tr> <td>Magnesium Hardness(mg/l)</td><td>100</td></tr> <tr> <td>TDS (mg/l)</td><td>330</td></tr> </table>	Calcium Hardness (mg/l)	130	Magnesium Hardness(mg/l)	100	TDS (mg/l)	330												
Calcium Hardness (mg/l)	130																		
Magnesium Hardness(mg/l)	100																		
TDS (mg/l)	330																		
16. Is there facility of laboratory for testing these parameters, if yes, give details	Yes in PHED Campus																		
17. Filter media replacement done if any:	No																		
18. How many times filter media replaced and last replacement detail:	NA																		
19. What are the proposals/methods for reuse/disposal of back wash water from WTP:	Nil																		
20. Quantity of Sludge generated from WTP:	400 kg/month																		
21. Sludge Dewatering and drying system:	By evaporation																		
22. What are the proposals/methods for reuse/disposal of generated sludge from WTP:	For the plantation in nurseries																		
23. Is this plant anywhere related/dependent on proposed WTP under RUIDP Phase- project:	Yes, This WTP will be used for proposed scheme																		
24. Status and type of electricity connection: (connection number and approved load, KW)	180 KW																		
25. Whether DG set installed, if yes give capacity and type of DG set:	100 KVA																		
26. Numbers of employees for operation of plant (designation wise numbers of employees):	11																		
27. WTP Process	Rapid gravity filters employing graded sand are washed by separate use of air and water through the bed by reverse flow and the used washwater is removed by a washwater collection channel. Combined air-water wash would intermix the media and result in loss of media. The first operation is to allow the filter to drain down until the water lies a few centimetres above the top of the bed. Air is then introduced through the collector system at a rate of about 6.5–7.5 mm/s. The air breaks up the surface scum and dirt is loosened from the surface of the sand grains. This is followed by an upward flow of water at a carefully selected velocity to expand and fluidise the bed. Under this condition the voids between grains of sands are increased and resulting rotation of grains and consequent attrition between grains produces a scouring action to remove attached deposits. The wash rate should be just sufficient to achieve fluidisation velocity (incipient fluidisation) with little bed expansion. Increasing the backwash rate beyond this state would be counter productive because as the distance between sand grains increases, the scouring action is reduced. High backwash rates may result in loss of sand and wastage of water and energy. The washwater collection channel cill is usually placed about 100–150 mm above the sand. Component of WTP <table> <tr> <th>Component</th><th>Bori</th></tr> <tr> <td>Aeration Fountain</td><td>1</td></tr> <tr> <td>Flash Mixer</td><td>1</td></tr> <tr> <td>Flocculator</td><td>1</td></tr> <tr> <td>Clarifier -</td><td>1</td></tr> <tr> <td>Rapid Sand Filters and Filter House</td><td></td></tr> <tr> <td>Filter Sand</td><td>2</td></tr> <tr> <td>Wash Water Tank</td><td>1</td></tr> <tr> <td>Wash Water Pumps</td><td>2</td></tr> </table>	Component	Bori	Aeration Fountain	1	Flash Mixer	1	Flocculator	1	Clarifier -	1	Rapid Sand Filters and Filter House		Filter Sand	2	Wash Water Tank	1	Wash Water Pumps	2
Component	Bori																		
Aeration Fountain	1																		
Flash Mixer	1																		
Flocculator	1																		
Clarifier -	1																		
Rapid Sand Filters and Filter House																			
Filter Sand	2																		
Wash Water Tank	1																		
Wash Water Pumps	2																		

	Air Blower	2
	Chemical House	1
	Solution tanks	3
	Pure Water Sump and Sump House	
	Capacity of sump – (CWR)	1
	Pump House	1
	Store House	1
	Vacuum feed type Chlorinators	2

Process Flow Diagram of WTP at Bori

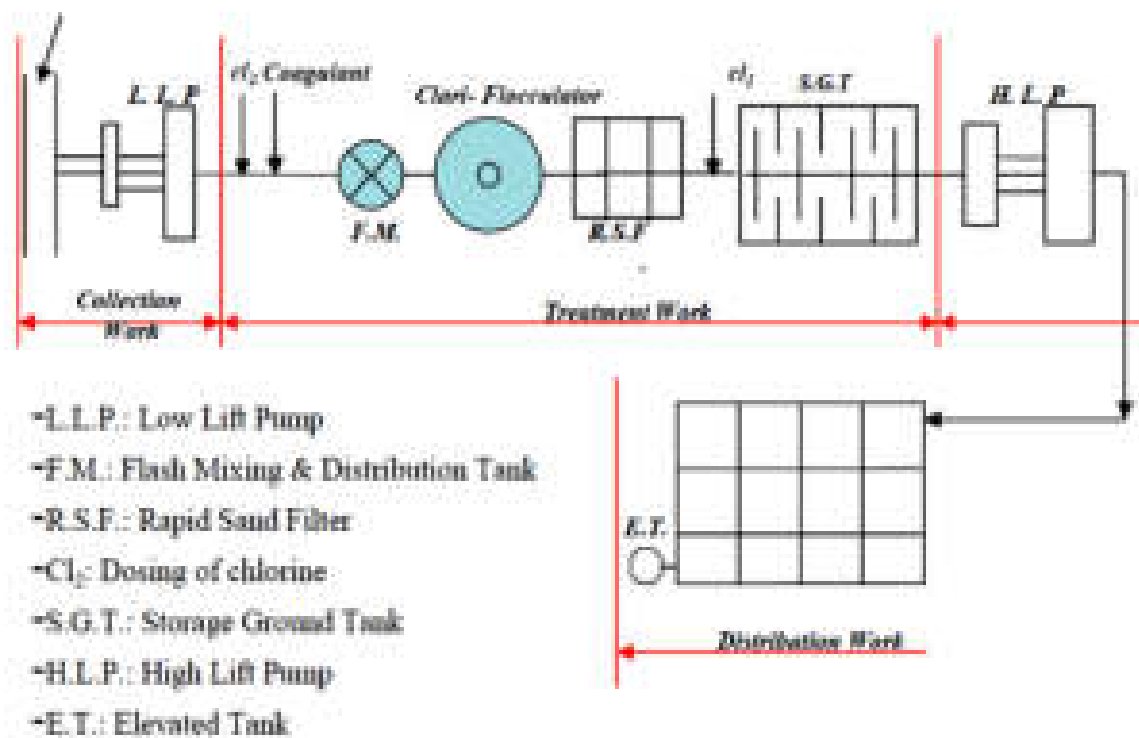

View of Bori WTP

Exiting WTP Plant Component Layout Diagram



Compliance with Applicable National and State Laws, Rules, and Regulations

Law, Rules, and Regulations	Description and Requirement	WTP at Bori PHED Headworks
		Y = compliant (if applicable, specify expiration date of permit/clearance) N = non-compliant ³³ N/A = not applicable (state justification)
EIA Notification	The EIA Notification of 2006 states that environmental clearance is required for certain defined activities/projects.	N/A Environmental clearance is not required as WTPs are not listed in the EIA Notification's "Schedule of Projects Requiring Prior Environmental Clearance"
Manufacture, Storage, and Import of Hazardous Chemical Rules, 1989	Storage of chlorine (threshold quantity greater than 10 tons but less than 25 tons) in WTPs will require clearance from PESO	N/A Storage of is always less 10 tons
Water (Prevention and Control of Pollution) Act of 1974, Rules of 1975, and amendments	Consents (CTE and CTO) from RSPCB	N Currently no CTE and CTO are applied for WTP, CTE will be applied and taken before start of construction works and CTO before start of operation with new components
Air (Prevention and Control of Pollution) Act of 1981, Rules of 1982 and amendments.	Consents (CTE and CTO) from RSPCB	N For DG set Consent will be applied and taken before start of works
Environment (Protection) Act, 1986 and CPCB Environmental Standards	Emissions and discharges from the facilities to be created, refurbished, or augmented shall comply with the notified standards.	Y No source of waste except very quantity silt and clay.
Noise Pollution (Regulation and Control) Rules, 2002 amended up to 2010	Applicable ambient noise standards with respect to noise for different areas/zones	Y No source of noise
National Institute of Occupational Safety and Health (NIOSH) Publication No. 2002-149	Compliance with NIOSH Guidance for Controlling Potential Risks to Workers Exposed to Class B Biosolids	N Training and proper PPEs are required
Forest (Conservation) Act,	As per Rule 6, every user agency, who wants to use any	N/A

³³Compliant = There is sufficient and appropriate evidence to demonstrate that the particular regulatory requirement has been complied with; non-compliant = clear evidence has been collected to demonstrate the particular regulatory requirement has not been complied with.

Law, Rules, and Regulations	Description and Requirement	WTP at Bori PHED Headworks
		Y = compliant (if applicable, specify expiration date of permit/clearance) N = non-compliant ³³ N/A = not applicable (state justification)
1980 and Forest Conservation Rules, 2003 as amended	forest land for non-forest purposes shall seek approval of the central government.	
Ancient Monuments and Archaeological Sites and Remains Rules of 1959	No development activity is permitted in the “protected area,” and all development activities likely to damage the protected property are not permitted in the “controlled area” without prior permission of the Archaeological Survey of India (ASI). Protected property includes the site, remains, and monuments protected by ASI or the State Department of Archaeology.	N/A
The Child Labor (Prohibition and Regulation) Act, 1986	No child below 14 years of age will be employed or permitted to work in any of the occupations set forth in the Act's Part A of the Schedule or in any workshop wherein any of the processes set forth in Part B of the Schedule are present.	Y WTP is operated by PHED staff. No children are engaged.

Corrective Action Plan

In the existing 3.25 MLD WTP unit at Bori PHED Headworks no CTE and CTO were taken for both WTP plant and DG set under Air and Water Act therefore consent to establish and consent to operate will be taken from RSPCB.

Repair works and improvement of electromechanical works will improve the treatment capacity of WTP.

Environment Audit of Existing WTP at Uday Vilas Headworks

Introduction

Under the ADB funded Rajasthan Secondary Towns Development Sector Project (RSTDSP), it is proposed to water supply and sewerage project in Dungarpur Town. Since adequate capacity treatment facility is already in Bori WTP 3.25 MLD and Uday Vilas WTP 4.45 MLD, no new WTPs is proposed for this Project. Sustainability of new water supply infrastructure and realisation of intended purpose. The existing WTP at Uday Vilas PHED Campus is an associated facility as per the ADB Safeguard Policy Statement 2009. Compliance with the environmental safeguards will ensure the subproject sustainability.

The objectives of this study is to (i) assess the compliance of the water treatment plant (WTP) with country's environmental regulatory framework; (ii) improve environmental performance, as required, through monitoring the effectiveness of the management system; and (iii)

increase the RSTDSP's knowledge of its activities, thus increasing its ability to continually improve and minimize future potential liabilities. The details of existing plant, process and used technology are given below:


WTP neat Uday Vilas				
1. Location of Plant:	Near Uday Vilas Head Works near Uday Vilas Hotel			
2. Capacity (MLD):	4.54 MLD			
3. Technology:	Rapid Gravity Filter			
4. Executing agency:	PHED			
5. Implementing agency:	PHED			
6. Asset Owner:	PHED			
7. Date of completion of construction works of WTP:	1990			
8. Status of work progress of WTP: (completed/uncompleted components with %)	completed/ Repair works are proposed in this subproject.			
9. Nos., locations and capacities of Pumping Stations:	S. N	Location	Size of PH (m x m)	Const. year
	1	Udayvilas RGF PH-(I)	7 X 8	1990
	2	Udayvilas RGF PH-(II)	3 X 3	2002
10. Total Area of land used for WTP (sq.m.):	2800			
11. Land ownership details: (khasra nos. and title)	PHED			
12. Details of water supplied areas with WTP: (ward nos./localities)	Mahakaleshwar, Gati, Shastri Colony, Sindhi Colony, Pratap Nagar, Indira Colony, Morden School, Old RHP, Pratakar Colony and Ashok Nagar (Zone-6 to 16)			
13. What are the parameters of treated water:	Parameters		Values	
	pH		7.5	
	Turbidity (NTU)		7.0	
	Temperature (°C)		None	
	Odour Colour (Hazen Units)		None	
	Total Alkalinity (as CaCO ₃)		N.O	
	Total Hardness (as CaCO ₃)		110	
	Calcium Hardness (mg/l)		80	
	Magnesium Hardness (mg/l)		60	
	Chloride (as Cl ⁻) (mg/l)		60	
	Nitrates (as NO ₃) (mg/l)		5	
	Fluoride (as F ⁻) (mg/l)		0.15	
	Total Dissolved Solids (mg/l)		340	
14. Is there facility of laboratory for testing these parameters, if yes, give details	Yes in PHED Campus			
15. Quantity of Sludge generated from WTP:	300 kg/month			
16. Sludge Dewatering and drying system:	By evaporation			
17. What are the proposals/methods for reuse/disposal of generated sludge from WTP:	For the plantation in nurseries			
18. Status and type of electricity connection: (connection number and approved load, KW)	115 KW			
19. Whether DG set installed, if yes give capacity and type of DG set:	62.5 KVA			
20. Numbers of employees for operation of plant (designation wise numbers of employees):	10			
21. WTP Process	Rapid gravity filters employing graded sand are washed by separate use of air and water through the bed by reverse flow and the used wash water is removed by a wash water collection channel. Combined air-water wash would intermix the media and result in loss of media. The first			

operation is to allow the filter to drain down until the water lies a few centimetres above the top of the bed. Air is then introduced through the collector system at a rate of about 6.5–7.5 mm/s. The air breaks up the surface scum and dirt is loosened from the surface of the sand grains. This is followed by an upward flow of water at a carefully selected velocity to expand and fluidise the bed. Under this condition the voids between grains of sands are increased and resulting rotation of grains and consequent attrition between grains produces a scouring action to remove attached deposits. The wash rate should be just sufficient to achieve fluidisation velocity (incipient fluidisation) with little bed expansion. Increasing the backwash rate beyond this state would be counter productive because as the distance between sand grains increases, the scouring action is reduced. High backwash rates may result in loss of sand and wastage of water and energy. The wash water collection channel cell is usually placed about 100–150 mm above the sand.

Component of WTP

Component	Uday Vilash
Aeration Fountain	1
Flash Mixer	1
Flocculator	1
Clarifier -	1
Rapid Sand Filters and Filter House	
Filter Sand	2
Wash Water Tank	1
Wash Water Pumps	2
Air Blower	2
Chemical House	1
Solution tanks	3
Pure Water Sump and Sump House	
Capacity of sump – (CWR)	1
Pump House	1
Store House	1
Vacuum feed type Chlorinators	2

Process Flow Diagram of WTP at Uday Vilas PHED Headworks

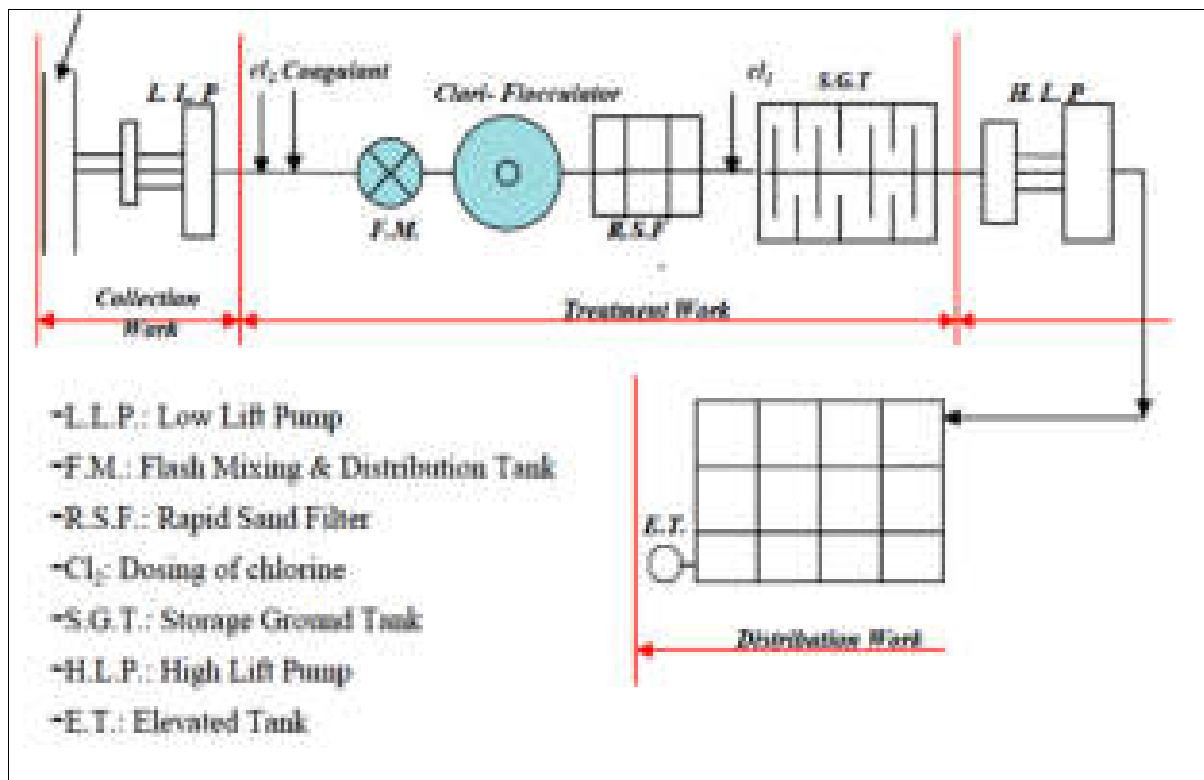

View of Uday Vilas WTP



Exiting WTP Plant Component Layout Diagram



Compliance with Applicable National and State Laws, Rules, and Regulations

Law, Rules, and Regulations	Description and Requirement	WTP at Uday Vilash PHED Headworks
		Y = compliant (if applicable, specify expiration date of permit/clearance) N = non-compliant ³⁴ N/A = not applicable (state justification)
EIA Notification	The EIA Notification of 2006 states that environmental clearance is required for certain defined activities/projects.	N/A Environmental clearance is not required as WTPs are not listed in the EIA Notification's "Schedule of Projects Requiring Prior Environmental Clearance"
Manufacture, Storage, and Import of Hazardous Chemical Rules, 1989	Storage of chlorine (threshold quantity greater than 10 tons but less than 25 tons) in WTPs will require clearance from PESO	N/A Storage of is always less 10 tons
Water (Prevention and Control of Pollution) Act of 1974, Rules of 1975, and amendments	Consent to operate from RSPCB	N Currently no CTE and CTO are applied for WTP, CTE will be applied and taken before start of construction works and CTO before start of operation with new components
Air (Prevention and Control of Pollution) Act of 1981, Rules of 1982 and amendments.	Consent to operate from RSPCB	N For DG set Consent will be applied and taken before start of works
Environment (Protection) Act, 1986 and CPCB Environmental Standards	Emissions and discharges from the facilities to be created, refurbished, or augmented shall comply with the notified standards.	No No source of waste except very quantity silt and clay.
Noise Pollution (Regulation and Control) Rules, 2002 amended up to 2010	Applicable ambient noise standards with respect to noise for different areas/zones	Y No source of noise
National Institute of Occupational Safety and Health (NIOSH)	Compliance with NIOSH Guidance for Controlling Potential Risks to Workers Exposed to Class B Biosolids	N Training and proper PPEs are required

³⁴Compliant = There is sufficient and appropriate evidence to demonstrate that the particular regulatory requirement has been complied with; non-compliant = clear evidence has been collected to demonstrate the particular regulatory requirement has not been complied with.

Law, Rules, and Regulations	Description and Requirement	WTP at Uday Vilash PHED Headworks
		Y = compliant (if applicable, specify expiration date of permit/clearance) N = non-compliant ³⁴ N/A = not applicable (state justification)
Publication No. 2002-149		
Forest (Conservation) Act, 1980 and Forest Conservation Rules, 2003 as amended	As per Rule 6, every user agency, who wants to use any forest land for non-forest purposes shall seek approval of the central government.	N/A
Ancient Monuments and Archaeological Sites and Remains Rules of 1959	No development activity is permitted in the “protected area,” and all development activities likely to damage the protected property are not permitted in the “controlled area” without prior permission of the Archaeological Survey of India (ASI). Protected property includes the site, remains, and monuments protected by ASI or the State Department of Archaeology.	N/A
The Child Labor (Prohibition and Regulation) Act, 1986	No child below 14 years of age will be employed or permitted to work in any of the occupations set forth in the Act’s Part A of the Schedule or in any workshop wherein any of the processes set forth in Part B of the Schedule are present.	Y WTP is operated by PHED staff. No children are engaged.

Corrective Action Plan

In the existing 4.53 MLD WTP unit at Uday Vilash PHED Headworks no CTE and CTO were taken for both WTP plant and DG set under Air and Water Act, Therefore consent to establish and consent to operate will be taken from RSPCB.

Repair works and improvement of electromechanical works will also improve the treatment capacity of WTP.

Appendix 4: Source Sustainability Report of Dhungarpur Water Supply Scheme

Selection of water source. An alternative source analysis has been conducted to select a feasible and sustainable source of water supply to meet the ultimate design demand of Dungarpur town. Four alternatives which were studied are: (i) SKA (Som Kamla Amba Project) (ii) Vijay Chakra Sagar (Dimiya) Dam and (iii) Edward Sagar and (iv) Ground Water. A proposal of drawing a collective supply from all four is finalized based on the techno-economic and environment considerations as elucidated below, letter of allocation of the four dams is at Figure 1,2 and 3.

OFFICE OF EXECUTIVE ENGINEER PHED DIVISION DUNGARPUR

S. NO. /EE/DPH/2021-22/ 1596 Date: 12-03-2021

Commissioner
Nagar Palikhaat
Dungarpur

Subject: Regarding Implementation of reorganisation of UWSS Dungarpur to be implemented through RUWDP

Reference: EE PHED Project Division B Udaipur dated 12.08.2021

In continuation of above referred letter provision of transfer of water from Somkamla Amba dam to UWSS Dungarpur has been modified in resubmitting proposal of 151 Villages of Blocks Aspur, Dobra and Dungarpur of District Dungarpur, in view of utilization of existing WTP's and already laid pipelines so that increased demand of rural sector may be met out without change in transmission system. Details of provision are as under:

S.No	Name of surface source	Transfer of water		Quantity in MLD	Remarks
		From	To		
1	Edward Sarnand Dam	Edward Sarnand Dam	Bori WTP RWR	4.54	Capacity of Edward Sarnand Dam is 127 Mch and annual raw water requirement is only 61 Mch. Existing gravity line connects Bori WTP and Bori WTP to Udaivilas WTP will be sufficient to carry water.
2		Bori WTP RWR	Bori WTP	3.25	
3		Bori WTP RWR	Udaivilas WTP	1.29	
4	Dimiya Dam	Dimiya Dam	Udaivilas WTP	3.1	Capacity of Dimiya Dam is 44.87 Mch and annual raw water requirement is 18 Mch. Provision of 1 raising of dimiya dam by 1 mtr will enhance 14 Mch Raw water. Existing pipeline of 200 mm DI & B will be sufficient to carry water.
5	Ground water			1.5	During summer if any deficient due to reduction in ground water may be supplemented by SBA system.
	Total			9.14	

Fig. 1 Letter of Allocation

Particulars	Year 2021	Year 2027	Year 2052
Design Demand at UWSI Dungarpur@ ELIS UPCD/10% institutional demand and 10% transmission and distribution losses	9.73	11.6	13.50
Less	9.14	9.14	9.14
Transfer from S.A system	0.59	2.46	4.36

Looking to above modifications following provisions to be taken in DPR being prepared by RUDP:

- Provision of suitable Pump Machinery and Electric equipments needs to be taken up at Borl head Works.
- Construction of 450 EL capacity RCC RWE at Borl head Works under the provisions to be taken.
- Renovation/Upgradation of both WTP's.
- To increase the water supply production from Vijay Chakra Sagar (Deerniya) Dam by 1.0 meter has been proposed as per discussions held with WRD Department and an Estimate for Raising the height of Vijay Chakra Sagar Dam by 1.0 meter has been framed by WRD Dungarpur for an Approx. cost of Rs 9.50 Crores. This work may be proposed to be got Executed by WRD under the budget head available with project PRID.
- Presently the intake Pump House for Pumping Raw Water from Deerniya Dam is in the back water of dam and as the water recedes in the dam during summer season, water is to be brought near the existing Pump House to be Pumped by the Centrifugal Submersible Pumps/sets installed there in an approach channel which usually got silted up every year after monsoon season, proposed to extend as per design the existing 100mm Diameter DI & S Rising Pipe line near Pump House for the length of 2.0 KM above HFL on the bank of surface water Source along the nearby hilly alignment and provision for construction of a suitable RCC Intake near the spillway section is proposed to get the maximum benefit in pumping the raw water during severe drought conditions.
- CWT at pump/pole in UIR campus along with pumping machinery.
- Existing Ground Water Resources may also be got drilled and deepened as per requirement to increase the ground water source production on this scheme upto 1.50 MLD and this work maybe got included in the DPR.

Fig. 2 Letter of Allocation




Fig. 3 Letter of Allocation

- i. **Som Kamla Amba Scheme:** This is a scheme under PHED which proposes to take water from Som Kamla Amba Dam and supplies water to 151 villages and Dungarpur town itself. This project is under construction and the tentative date of completion is in December 2022.
 - a) **Location:** The rising main of this scheme has already been laid and will supply water proposed for Dungarpur town at Bhogilal Pandya Circle.
 - b) **Details of Dam:** - As per the report published by World Bank for Dam Rehabilitation and Improvement Project (Drip II). The construction of Som Kamla Amba Project across Som river, a tributary of Mahi river was completed in the year 2000. The dam is located in Ashpur Tehsil of Dungarpur District, Rajasthan to provide the Irrigation cum drinking water facilities. This dam supplies drinking water to the town with the capacity of 8.1 MCM., besides irrigation supply to 26998.6 ha of Gross Command Area (GCA) and 19155.42 ha of Culturable Command Area (CCA). **Fig. 4**
 - c) **Location:** The dam is located at the coordinate 23°58'11.05"N and 73°58'56.77"E on Moran River.
 - d) **Sustainability and environmental considerations of Som Kamla Amba Project:** -It is proposed to fulfil 4.36 MLD in the year 2055 and as this project is designed to fulfil the requirement of Dungarpur hence is it sustainable. Water Quality of the Dam has been evaluated from reports in **Fig 5** published by World Bank for Dam Rehabilitation and Improvement Project (**Drip II**). **DPR report summary provided by Chief Engineer (SP) PHED (Jaipur) is given below**


OFFICE OF THE CHIEF ENGINEER (SPECIAL PROJECTS)
PUBLIC HEALTH ENGINEERING DEPARTMENT RAJASTHAN
 F-28, New Building, 1 Floor, 2, CIVIL LINES - JAIPUR - 302008
 ☎0140-2220551 Fax-0140-2222585 e-mail-cj.ceap@nic.in


No. CE (SP)/PHED/Dungarpur/ DPR /2018-EN 2630-2631 Dated 26-07-2018

✓ Chief Engineer,
 RUJDP
 Jaipur

Sub: Regarding preparation of DPR of water supply based on Som Kamla Amba Dam for Dungarpur Town.


Ref: Your letter no. 4371 dated 02.02.2018

In reference to above matter and your referred letter, Please find enclosed a copy of DPR of water supply project of 151 villages of Aspur Dobra and Dungarpur block and Dungarpur town District Dungarpur form Som Kamla Amba Dam estimated cost Rs. 365 Crore. Cost distribution in rural area and urban area (Dungarpur town) under the project is enclosed in the DPR.


 (B. Krishnan)
 Chief Engineer (SP)
 PHED, Jaipur
 Dated: 26-07-2018

No. CE (SP)/PHED/tender/ Jaipur /2018-EN/ 2630-2631
 Copy to following for information :

1. P.S. to Principal Secretary, Government of Rajasthan, PHED, Jaipur


 Chief Engineer (SP)
 PHED, Jaipur

5.2.1 Water Demand Assessment

There are urban and rural areas in the project area, therefore parameters applicable for urban and rural sector are considered. According to the guidelines issued by the Chief Engineer (HQ) PHED, water supply of 135 litres per capita per day (lpcd) for Durgapur town and 15 litres per capita per day (lpcd) for rural habitations are adopted. In addition 10% Provision for institutional & other demand is also taken for rural area.

The following parameters are used, as agreed by the department, to work out design water demand of the project:

For Rural area:

- Water loss through Water Treatment Plant : 3.0 %
- Water loss through transmission and cluster Pumping mains : 5.0%
- Water loss through distribution system : 10.0%

For Urban area:

- Unaccounted for water : 15.0%
- Transmission loss : 5.0%

Water available from Edward Samand Dam and Vijay Chakra Sagar dam for Durgapur town is 3400 KLD. Water demand for 151 villages and 1 town (Durgapur) to be benefited under Project is worked out for urban and rural areas and tabulated below:

Table 5-5: Projected Water Demand for Urban & Rural areas of Project

S. N.	Sector	Type of water	Water Demand in KLD for the year		
			2021	2036	2051
1	Urban	Clear Water	5357.04	6675.10	8191.76
		Raw Water	5522.72	6881.55	8445.11
2	Rural	Clear Water	10564	14620.8	17826.3
		Raw Water	10580.45	15071.5	18468.5
3	Total requirement from Son Kandi Dam	Clear Water	15621.02	21295.91	26018.04
		Raw Water	16103.17	21953.06	26913.57

Clear water demand shown above includes institutional and distribution & transmission losses. Raw water demand includes filtration losses over the clear water demand. Urban and Rural population projection and water demand for 151 villages with their other habitations and Durgapur town to be benefited in the project is given in Volume-II: Annexures.

CHAPTER 4.0 PROJECT COMPONENTS

4.1 Water Source

As discussed earlier Son Kania Amba Dam located in Aspur Block of Durgapur district is adopted source of water for this project. Capacity of dam at F.T.L. of 213.50 m is 172.75 MCM (6102 MCF) and live capacity is 160.30 MCM (5661 MCF). There is 93.75% dependability for 47.22 MCM quantities on the basis of past 15 years record of storage of Son Kania Amba Dam.

Total raw water requirement for 151 villages & 1 town covering Aspur, Dobra, and enroute Durgapur Blocks shall be as given below:

Table 4-1: Project Phase wise coverage of villages & Town

Project Source	Coverage	Population for year		Raw Water Requirement for year 2051	
		2011	2051	ML/day	MCM/yr
SKAD	1 town	41106	69337	8.19	2.99
	151 villages	180238	462482	20.82	7.60
	TOTAL	227744	531819	29.01	10.59

- ✓ For Durgapur town, availability of 3400 KLD clear water is ensured from Edward Samard Dam & Vijai Chakra Sagar dam. Raw water requirement corresponding to 3400 KLD shall be about 1.24 MCM per year which is deducted from the total requirement to arrive at net requirement from Son Kania Amba Dam. Against the net raw water requirement of about 10.32 MCM per year for the above mentioned blocks, with 93.75% dependability, 47.22 MCM quantities in the dam is available. Therefore Department decided to use Son Kania Amba dam as sustainable surface water source for water supply projects for 151 villages & 1 town (Durgapur) of above mentioned blocks of Durgapur district.

4.2 Design periods for various Components of Project

Design period etc. for various component of project, given in Table below, are adopted as per CPHEED manual and PHED guide lines.

Table 4-2: Design Period for Project Components

S. No.	Particulars	Design Period
1	Pumping Station- Civil Works	30 years
2	Pumping Machinery and allied equipment	15 years
3	Raw water & clear water pumping main	30 years
4	Village Cluster Distribution Pipe lines	30 years
5	Clear water reservoir	2 hour storage capacity for the demand of design year 2051
6	Over Head Service Reservoir	Half day demand of design year 2051
7	Pumping Hours	20 hours

CHAPTER 4.0 PROJECT COMPONENTS

6.1 Water Source

As discussed earlier Son Kamla Amba Dam located in Aspur Block of Durgapur district is adopted source of water for this project. Capacity of dam at F.T.L. of 213.50 m is 172.75 MCM (6102 MCF) and live capacity is 160.30 MCM (5661 MCF). There is 93.75% dependability for 47.22 MCM quantities on the basis of past 15 years record of storage of Son Kamla Amba Dam.

Total raw water requirement for 151 villages & 1 town covering Aspur, Dobra, and enroute Durgapur Blocks shall be as given below:

Table 6-1: Project Phase wise coverage of villages & Town

Project Source	Coverage	Population for year		Raw Water Requirement for year 2051	
		2011	2051	ML/day	MCM/yr
SKAD	1 town	41106	69337	8.19	2.99
	151 villages	180238	462482	20.82	7.60
	TOTAL	227744	531819	29.01	10.59

- ✓ For Durgapur town, availability of 3400 KLD clear water is ensured from Edward Samard Dam & Vijai Chakra Sagar dam. Raw water requirement corresponding to 3400 KLD shall be about 1.24 MCM per year which is deducted from the total requirement to arrive at net requirement from Son Kamla Amba Dam. Against the net raw water requirement of about 10.32 MCM per year for the above mentioned blocks, with 93.75% dependability, 47.22 MCM quantities in the dam is available. Therefore Department decided to use Son Kamla Amba dam as sustainable surface water source for water supply projects for 151 villages & 1 town (Durgapur) of above mentioned blocks of Durgapur district.

6.2 Design periods for various Components of Project

Design period etc. for various component of project, given in Table below, are adopted as per CPHEED manual and PHED guide lines.

Table 6-2: Design Period for Project Components

S. No.	Particulars	Design Period
1	Pumping Station- Civil Works	30 years
2	Pumping Machinery and allied equipment	15 years
3	Raw water & clear water pumping main	30 years
4	Village Cluster Distribution Pipe lines	30 years
5	Clear water reservoir	2 hour storage capacity for the demand of design year 2051
6	Over Head Service Reservoir	Half day demand of design year 2051
7	Pumping Hours	20 hours

6.3 Proposed Components under the Project

On the basis of Draft Report of the project submitted earlier, the following components are included in the project:

- Intake structure at Som Kamla Amba Dam
- Raw Water Pumping Main
- Water Treatment plant
- Transfer Pumping Stations & Transfer Pumping Mains
- Cluster Pumping Stations & Cluster Pumping Mains
- Over Head Service Reservoirs & Cluster Distribution System
- Village Distribution System
- SCADA
- IEC activity

Under this project 151 villages with their 344 other habitations of three blocks and one town namely Durgapur of Durgapur district shall be benefitted. Block wise breakup is as given below:

Table 6-1: Block wise coverage of Main & Other Habitations

S.N.	Block	Main Habitations	Other Habitations
1	Aspur	47	44
2	Davra	88	163
3	Durgapur	16	37
	Total	151	244

6.3.1 Intake Structure

Intake structure shall be constructed on upstream of dam at a location so to draw water from dam from the lowest available level. On right side of dam, there exists sluice gate arrangement to take water in a canal constructed for irrigation purpose. As per data provided by WRD, sill level of sluice arrangement is 200.50 m and top bank level (TBL) of dam is 217.50 m. However, as per contour plan of the upstream side of the dam provided by the department vide letter no. 607 dated 26.12.14, the lowest level is 193 m. Therefore as desired by the department lowest level of 193 m has been adopted for the purpose of design of pumps etc.

Looking to total water demand of project, it is considered appropriate to provide Jetty type intake structure in the reservoir of dam with suspended pump set. Drawing showing general arrangement of intake structure and raw water pump set is enclosed. Following are the levels proposed for different stages of intake structure.

Table 6-4: Levels proposed for different stages of intake structure

1	Top Bank Level of Dam	217.50 m
2	F.T.L. of Dam	211.50 m
3	SL level of Dam	200.50 m
4	Lowest level on upstream side of dam	191.00 m
5	Maximum Water Depth	20.50 m
6	Top level of Intake structure	217.50 m

6.3.2 Raw Water Pumps

Raw water pumps shall be installed at intake structure for water demand for 131 villages and one town. In this project, pumps are proposed for the demand of design year 2036 whereas electrical and instrumentation components are proposed for water demand for the year 2051. A transmission loss @ 5%, distribution losses @ 10%, institutional demand @ 10% has been added for working out clear water demand. For working out raw water requirement, filtration loss @ 3% has been included in clear water requirement and accordingly capacities of pumps for raw water pumping station are finalized. Clear & raw water demand for the year 2036 and 2051 are as given below:

Table 6-5: Clear & Raw Water Demand

Clear water demand (KLD)		Raw water Demand (KLD)	
2036	2051	2036	2051
21295.91	29018.04	21953.06	29913.57

There can be choice of three types of pumps for lifting raw water from dam i.e. HSC centrifugal (HSC) pump, Vertical turbine (VT) pumps and Submerged Centrifugal (SubCF) pumps. For installation of HSC pumps, large and heavy structure below ground due to positive head requirement and to lift water from the lowest level shall be required therefore use of HSC pumps is ruled out. Comparison between VT and Submerged CF pumps is made below on the basis of available details:

Table 6-6: Comparison of VT and Sub CF pumps

S.N.	Particulars	VT Pump	Sub CF Pump
1	App. Cost of M/C with allied ancillaries	Rs.25000 - 27000 per HP	Rs.24500 - 27500 per HP
2	Required civil structure	Large & heavy structure	Relatively light structure
3	Reduction in efficiency	10 to 20% reduction in efficiency after 5 to 10 years of operation	5 to 10% reduction in efficiency in 5 to 10 years of operation
4	Ease of repair within pump house	Possible but very time taking & cumbersome	Possible & less time taking
5	% reliability in operation	Moderate (85 to 90%)	High (95 to 99%)
6	Maintenance	Re-lubrication after 500-1000 running hrs, gland tightening & re-alignment is required	Only re-lubrication after 4000-75000 running hrs required

Looking to above comparison, it is proposed to install submerged centrifugal pumps. Two working pump sets and one standby pump set are proposed to be installed looking to quantity of water to be pumped. With 20 hrs of pumping in a day, sub-CF pump sets each of 152.45 lps or 548.82 cum per hour at 33 m head for the design year 2036 are proposed.

6.3.3 Raw Water Pumping Main

The WTP shall be constructed at main Head Works, proposed to be developed behind existing treatment plant. Clear Water Reservoir and clear water pump station etc shall also be housed along with WTP at this Head Works. Raw water pipe line of 600 mm Ø K-7 about 850 m in length from intake structure to WTP to meet the water demand for the design year 2051 is proposed to be laid.

6.3.4 Water Treatment Plant

Conventional type rapid gravity water treatment plant is proposed at main Head Works where land identified by PHED. The plant shall have modular design for future expansion. In this project, it is proposed to construct a treatment plant for the intermediate water demand of year 2036, which will be upgraded to the demand for the year 2051 with addition of clariflocculator and filter beds. However, inlet channel and other civil works shall be constructed to meet water demand of year 2051. Clear water demand for the year 2036 & 2051 is given in table - 6.4

The filtration process will involve Pre-chlorination, Rapid mixing of Chemicals, Clariflocculation, Filtration and Post Chlorination. The power driven valves and the inlet gates are proposed to be operated from individual control consoles positioned adjacent to each filter house in the operation gallery with visibility to respective filter bed. There will be mimic & LED display system on the water treatment plant control panel indicating status of various motors, pumps, and compressors. The various system parameters e.g. levels, pressures, flow are also proposed to be displayed digitally on control panel.

For instrumentation, Ultrasonic Channel type flow meters are proposed in inlet channel & at outlet of each filter bed. Level switches for alarm for high head loss across filter & overflow conditions are proposed. Flow control system for chlorine is proposed as vacuum feed type, with vacuum chlorinator, Chlorine detection system and alarms are also proposed in chlorination chamber and chlorine-pail.

Also, the provision for suitable water testing laboratory with adequate manpower is proposed to carry out daily testing for various parameters of treated water.

The plant will operate for 20 hours per day and will deliver required quality and quantity of treated water. Recirculation of back wash water has been proposed to reduce filtration losses. It is envisaged that treatment plant losses will be about 2%. Sludge disposal has been proposed either through sludge drying beds or sludge lagoons. The location of treatment plant shall be in the rural area; therefore disposal of sludge shall not be a problem and may be done in environment friendly manner.

In beginning WTP of 21.29 MLD is proposed to meet the water demand of year 2036. It shall be upgraded to 29.01 MLD in future. Since WTP shall run for 24 hours in a day therefore WTP shall be of 887.07 cum per hour capacity in the beginning and shall be upgraded to 1208.73 cum per hour capacity in future.

6.5.5 Transmission System

Under this project 151 villages of Aspur, Dorra and enroute Durgam block and Durgam town are envisaged to be benefitted from surface water of Sain Karla Amba Dam. Land required for construction of water treatment plant, pump station etc. has been identified by PHED near existing headwork's which is about 850 m from the dam. After treatment of raw water, clear water shall be stored in clear water reservoir and then it shall be pumped to TPSs and CPSs through transfer mains.

Water from main Head Works shall be pumped from TPS-1 in two directions. Supply of water from TPS-1 shall be towards East side for 21 Mhs and 18 Ohs of Aspur Block (Zone-A) and towards West side for remaining villages of 90 clusters i.e. 120 Mhs and 216 Ohs (Zone-B). Area towards East is low lying area with respect to location of Main Head Works, housing WTP and TPS-1.

ZONE-A:

Looking to topography of Zone-A, two following alternatives of transmission system is considered:

Alternative-1:

In this alternative, water shall be transferred from TPS-1 to cluster pump stations namely CPS-1 (near Dhandal) and CPS-2 (near Puripari). From CPS-1, water shall be pumped in to six OHSRs of clusters A/CL-02; A/CL-07; A/CL-08; A/CL-10; A/CL-13 & A/CL-15 to feed water to 17 Mhs and 21 Ohs of Aspur Block. From CPS-2, water shall be pumped to six OHSRs of clusters A/CL-01; A/CL-03; A/CL-11; A/CL-12; A/CL-16 & A/CL-18 to feed water to 14 Mhs and 07 Ohs of Aspur Block. Design of transfer and cluster pumping mains are given in Volume-II: Annexures. Schematic diagram for Alternative-1 is attached.

Alternative-2:

Looking to low lying area in this direction, it is proposed to pump water in to elevated balancing reservoir to be constructed on a nearby hillock adjacent to already existing balancing reservoir of a project benefitting 61 villages. From the balancing reservoir, OHSRs of all the 12 clusters as mentioned in Alternative-1, shall be fed under gravity. Design of transfer pumping main from TPS-1 to cluster balancing reservoir and design of gravity system are given in Volume-II: Annexures. Capacity of balancing reservoir is adopted as 4 hrs pumping for the total water demand for the year 2011. Schematic diagram for Alternative-2 is attached.


Cost Comparison of Alternative-1 & 2:

Cost of both alternatives is compared as per details given below on the basis of Volume II: Annexures.

S.N.	Description	Cost in Rs. Crore for	
		Alternative-1	Alternative-2
1	Total length of Pipe Line (KM)	63.186 KM	58.838 KM
2	Cost of Pipes	8.79	9.07
3	Earthwork for laying of pipe lines	1.68	1.65


S.N.	Description	Cost in Rs. Crore for	
		Alternative-1	Alternative-2
4	Cost of civil works, EMI etc for TPS-1, CPS-1 & CPS-2	4.74	0.52
5	Cost of CWRs of 175 KL & 125 KL capacity for CPS-1 & CPS-2 resp.	8.15	0.00
6	Cost of elevated balancing reservoir of 600 KL with 18 m staging	0.00	1.08
7	Cost of 11 KV power feeder line for CPS-1 & CPS-2	0.52	0.00
8	Capitalized Energy Charges	1.83	1.63
TOTAL		18.01	14.24

It is evident from the total cost of alternatives that Alternative-2 i.e. feeding OHSRs for 12 clusters of Zone-A through a balancing reservoir, is economical in comparison to Alternative-1 i.e. feeding 12 OHSRs through pumping from CPS-1 & CPS-2. It is therefore proposed to adopt Alternative-2 for Zone-A.

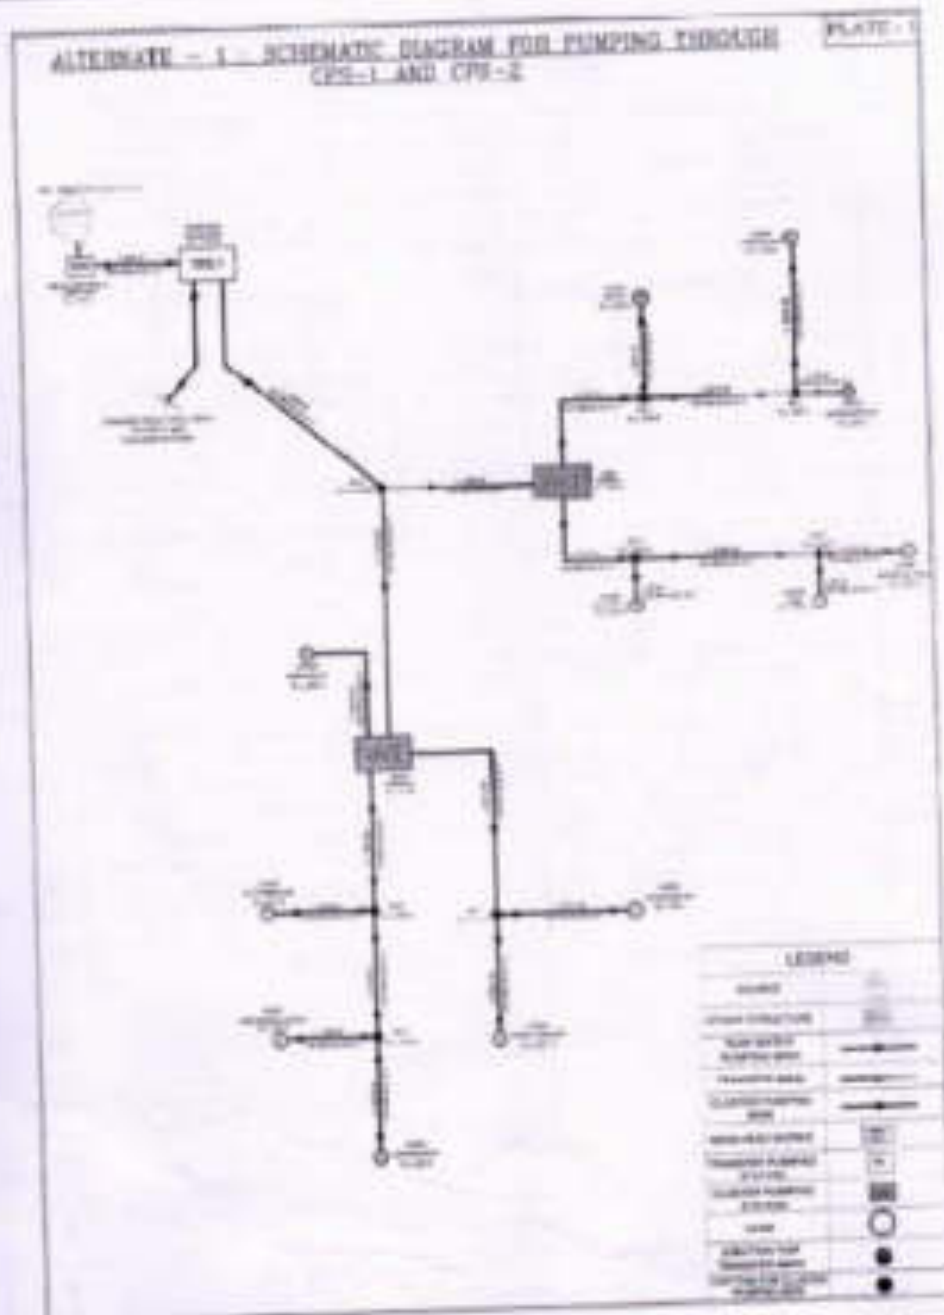

ALTERNATE - 2 - SCHEMATIC DIAGRAM FOR GRAVITY SYSTEM IN PLACE OF CFS-1 & CFS-2

PLATE - 2

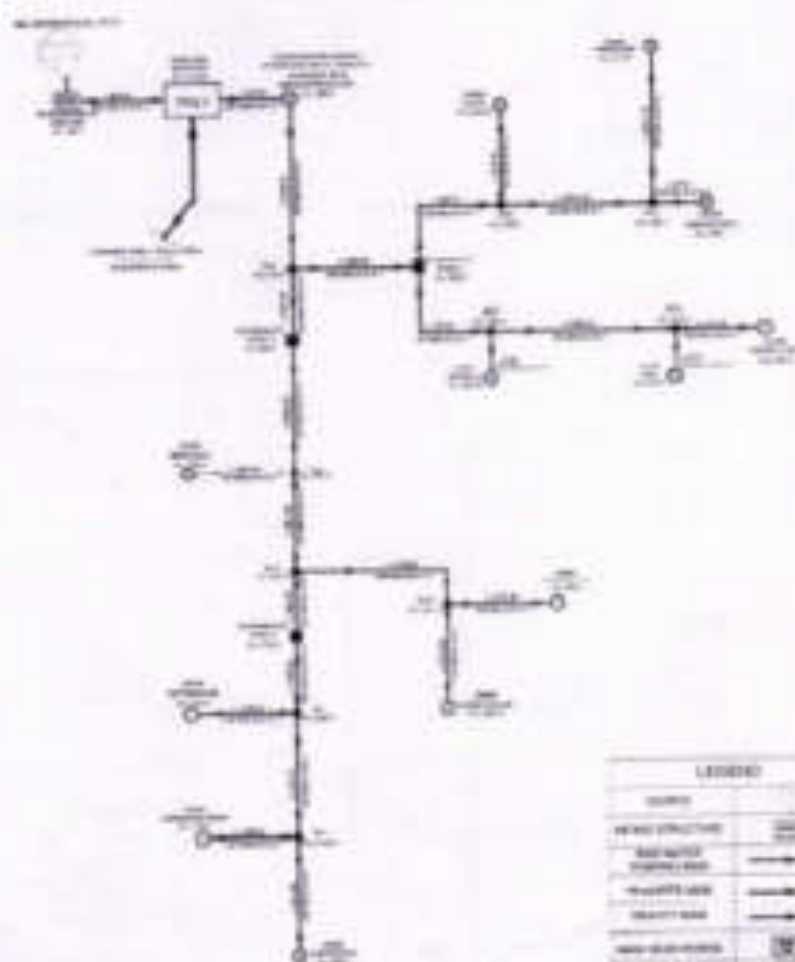

LEDGER	
ACCOUNT	DATE
PAID BY CHECK	
BANK OF AMERICA	11/11/11
WELLS FARGO	11/12/11
CHASE	11/13/11
PAID BY CREDIT	
CREDIT CARD	11/14/11
CREDIT CARD	11/15/11
CREDIT CARD	11/16/11
CREDIT CARD	11/17/11
CREDIT CARD	11/18/11
CREDIT CARD	11/19/11
CREDIT CARD	11/20/11
CREDIT CARD	11/21/11
CREDIT CARD	11/22/11
CREDIT CARD	11/23/11
CREDIT CARD	11/24/11
CREDIT CARD	11/25/11
CREDIT CARD	11/26/11
CREDIT CARD	11/27/11
CREDIT CARD	11/28/11
CREDIT CARD	11/29/11
CREDIT CARD	11/30/11
CREDIT CARD	12/01/11
CREDIT CARD	12/02/11
CREDIT CARD	12/03/11
CREDIT CARD	12/04/11
CREDIT CARD	12/05/11
CREDIT CARD	12/06/11
CREDIT CARD	12/07/11
CREDIT CARD	12/08/11
CREDIT CARD	12/09/11
CREDIT CARD	12/10/11
CREDIT CARD	12/11/11
CREDIT CARD	12/12/11
CREDIT CARD	12/13/11
CREDIT CARD	12/14/11
CREDIT CARD	12/15/11
CREDIT CARD	12/16/11
CREDIT CARD	12/17/11
CREDIT CARD	12/18/11
CREDIT CARD	12/19/11
CREDIT CARD	12/20/11
CREDIT CARD	12/21/11
CREDIT CARD	12/22/11
CREDIT CARD	12/23/11
CREDIT CARD	12/24/11
CREDIT CARD	12/25/11
CREDIT CARD	12/26/11
CREDIT CARD	12/27/11
CREDIT CARD	12/28/11
CREDIT CARD	12/29/11
CREDIT CARD	12/30/11
CREDIT CARD	12/31/11

ZONE-B:

From TPS-1, water shall be transferred for remaining part of project area and Durgapur Town on west side under Zone-B. Water shall be pumped to TPS-2 near Bachariya village towards Durgapur town with intermediate tapping near Dhatana village for CPS-3. The campus for TPS-2 is clubbed with CPS-4 and the water from TPS-2 is pumped to TPS-3 near Kherakhos with intermediate tapings for CPS-5, CPS-6, CPS-7 and CPS-8. Pump station CPS-9 is also located in the campus of TPS-3. From TPS-3 water shall be transferred to CPS-10 & CPS-11 and to CWRs of Chandpole P.S., New Colony P.S. & Main P.S. for Durgapur town.

6.3.6 Clear Water Reservoirs

Clear water reservoirs shall be constructed at each transfer & cluster pump stations to facilitate pumping. Capacity of each reservoir is provided equal to two hours pumping as per norms of the department. Under this project there are in all 12 pump stations which includes 9 cluster pumping stations and 3 transfer pump stations. Out of these, TPS-2 and CPS-4 shall be combined pump stations and shall be located near village Bachariya. Similarly TPS-3 and CPS-9 shall be combined pump stations and shall be located near village Kherakhos. Normally two units of CWRs are provided to facilitate its cleaning without disturbing water supply. Therefore rectangular with partition / two circular (separate or concentric) CWRs are proposed at each transfer / cluster pump station. However site and shape etc may change as per availability of land for pump stations. At TPS-2 and TPS-3 where CPS-4 and CPS-9 shall also be housed, one unit of CWR for cluster pump stations shall be provided and piping arrangement shall be made in such a way so as to draw water from CWR of TPS during cleaning operation of CWR for CPS.

In general, separate CWRs for TPS and CPS shall be constructed for each pump station. Objective to propose separate CWR for CPS is to do chlorination if required before pumping into OHSRs whereas it is not needed in CWR for TPS. It is envisaged that before pumping water into OHSRs quantity of chlorination should be made good in water to required level if it is consumed while travelling from TPS. At first stage adequate chlorination shall be done at WTP located in Main Head Works. A detail of CWRs is given in Volume-II: Annexures. However capacities of CWRs is given below:

Table 6-7: Details of clear water reservoirs

S. No.	P.S.	Location	Type	Total Capacity (ML)
1	TPS-1	Main Head Works	Rectangular	3000
4	CPS-3	Near Dhatana	Circular	125
5	TPS-2	Near Bachariya	Rectangular	2500
6	CPS-4		Circular	150
7	CPS-5	Near Odwadyn	Circular	125
8	CPS-6	Near Phoon Talai	Circular concentric	300
9	CPS-7	Near Vada Punali	Circular	250
10	CPS-8	Near Itadi Fala	Circular concentric	300
11	TPS-3	Near Kherakhos	Circular	1300
12	CPS-9		Circular	125
13	CPS-10	Near Teeswar	Circular	250
14	CPS-11	Near Toraniya	Circular	300
			TOTAL	8675

6.3.7 Pump Stations

Civil works and E&I except pump sets of pump stations will be constructed/ provided for the requirement of design year of 2031. Pump sets shall be installed for the demand of the year 2036 with 10 hours of pumping in a day. There are 3 transfer pump stations and 9 cluster pump stations proposed in this project. Pump details are given in Volume-II: Annexures; however brief details are given below:

Table 6-8: Pump Station wise Kilowatt requirement

S. N.	Pumping Station	No. of Pump Sets		Kilowatt Requirement	
		Working	Standby	Total Working	Total including Standby
1	Intake	1	2	166.0	332.0
2	TPS-1	1	2	301.0	601.0
3	TPS-2	1	2	164.0	328.0
4	TPS-3	1	2	180.00	360.00
5	CPS-1	1	2	14.5	33.0
6	CPS-4	1	1	18.5	37.0
7	CPS-5	1	2	22.5	45.0
8	CPS-6	1	2	33.5	67.0
9	CPS-7	1	2	26.5	53.0
10	CPS-8	1	2	21.5	43.0
11	CPS-9	1	2	27.3	55.0
12	CPS-10	2	2	30.5	41.0
13	CPS-11	2	2	24.0	48.0
	Total	28	38	1199	2238

6.3.8 Transfer Pumping Mains

Economical analysis of transfer pumping mains has been carried out with modified Hazen-Williams formula for 20 hour pumping based on consideration of annual energy charges and investment on capital charges with 10% interest rate on capital investment. MS/DI pipes have been adopted as per department policy of pipes for water supply projects.

Where sufficient ground slopes are available, pipe line has been designed as gravity transfer mains. A detail of transfer pumping / gravity mains is given below:

Table 6-9: Details of Transfer Pumping Mains

S. No.	Size (mm)	Length of pipeline (KM)		Total Length KM
		MS	DI K-7	
1	400	0	15.596	15.596
2	400	0	15.84	15.84
3	300	0	17.999	17.999
4	200	0	17.089	17.089
5	300	0	5.885	5.885
6	400	0	1.889	1.889
7	400	0	4.023	4.023
8	300	0	5.862	5.862
9	600	6.83	0	6.83
10	400	18.204	0	18.204

6.3.9 Cluster Pumping Mains

Economical analysis of cluster pumping mains has been carried out with modified Hazen-Williams formula for 20 hour pumping based on consideration of annual energy charges and investment on capital charges with 10% interest rate on capital investment. DI pipes have been adopted as per department policy of pipes for water supply projects.

where sufficient ground slopes are available, pipe line has been designed as gravity transmission mains. A detail of Cluster pumping / gravity mains is given below:

Table 6-10: Details of Cluster Pumping Mains

S. No.	Size (mm)	Type of pipe	Length of DI pipe of class		Total Length in KM
			K-7	K-9	
1	100	DI	78.349	2.222	80.621
2	150	DI	67.857	1.036	68.893
3	200	DI	3.489	0	3.489
TOTAL			149.745	3.258	153.003

6.3.10 Village Clusters

151 villages along with their 244 other habitations of Aspar, Doms and Dangarpur Blocks of Dangarpur district are envisaged to be benefitted under this project. On the basis of topography of the area, available route between villages, ground level etc., number of main & other habitations are clubbed into a group to form a cluster. It is proposed to construct one centrally located "Over Head Service Reservoir" (OHSR) in a cluster as far as possible and to connect habitations of that cluster with OHSR through pipe lines. Efforts are made to keep all habitations of a Gram Panchayat in one cluster; however deviation is made where it is not techno-economically feasible to do so. A "Village Transfer Chamber" (VTC) shall be constructed outside the habitation where a control valve and meter shall be installed. Efforts are made to provide one VTC for main & other habitations of a village however if it is not possible to do so due to layout of habitations, two or more VTCs are provided for one village & its other habitations. OHSRs of clusters shall be filled through cluster pumping mains from cluster pumping stations. Details of clusters are given in Volume-II: Annexures. There are 62 clusters covering 151 main habitations and 244 other habitations.

6.3.11 Cluster Distribution Mains

As per policy for selection of pipes for water supply Schemes / projects of PHED Rajasthan issued vide circular: RWSMB/2015-16/2 by Technical Member, RWSMB, Jaipur, MS/DI pipes are recommended in rocky/rain rocky strata for distribution mains of diameter more than 200 mm and for diameter up to 200 mm. DI pipes are recommended in rocky strata and HDPE/DI pipes in non rocky strata. Pratappgarh, Arind and Peepalkhoont Blocks of Pratappgarh district is a hilly area and strata in general are rocky. Selection of pipe for distribution mains in this area was discussed with project authorities of the department and they were of the view to adopt DI pipes looking to strata conditions in ongoing projects. Therefore DI pipes are adopted for distribution mains as per pipe policy of the department to connect

VTCs of habitations with respective OHSRs. Minimum size of DI pipe line is kept as 100 mm as per guide lines of the department. Pressure reducing valves/Orifice plates shall be installed at suitable locations to reduce pressure whenever residual pressures are more than 22 m. Cluster distribution pipe lines have been designed for the water demand of year 2031 including 10% distribution water loss. Total cluster distribution pipe lines proposed under this project are:

Table 6-11: Details of Cluster Distribution

S.No.	Nominal Dia of pipe(mm)	Cluster distribution DI K-7 pipe line (KM) for Total
1	100	263.565
2	150	62.894
3	200	0.957
4	250	1.835
Total		329.351

6.3.12 Over Head Service Reservoir

BCC OHSR for each cluster has been proposed at a location from where water can be supplied to all the habitations of that cluster up to VTC through cluster distribution pipe lines. Capacity of a service reservoir is proposed 50% of design water demand i.e. total design water demand for the year 2031 of all the villages of that cluster. Staging of OHSR is proposed to be kept minimum 18 m to obtain at least 7 m residual head at highest level of habitations. In all 62 clusters are proposed in the project area of this project. Generally one OHSR is proposed in one cluster but more than one may also be proposed looking to topography of area.

There shall be total 62 New OHSRs of the following capacity in this project.

Table-6-13: Details of Proposed Overhead Service Reservoirs

S.No.	Capacity (KL)	No. of OHSR of Staging		
		18 m	20 m	22 m
1	100 KL	22	0	0
2	150 KL	9	1	1
3	200 KL	11	2	1
4	250 KL	8	0	2
5	300 KL	1	0	0
6	350 KL	0	0	0
7	400 KL	0	1	0
8	Balancing Reservoir of 600 KL	1	0	0
Total		55	4	4

6.3.13 Village Distribution

Habitations having population upto 4000 as per 2011 census shall be fed through Public Stand posts as per policy of the department. However as per scope of consultancy assignment, village distribution design is required to be done for villages having population 3000 or more as per 2011 census. There are 8 villages having population of 3000 or more namely Vajdari, Falorj, Mandawa, Vallota, Pagara, Vassi Pal, Dandi & Pal Kakhanda. Village distribution design has been done for these villages and appended with project.

For the purpose of quantity estimation for village distribution for the villages having population less than 3000, three habitations in each of two categories of population i.e. 0 to 1000 & 1001 to 3000 and only one available habitation in the category of population 3001 to 3000 were selected from 151 main habitations of Durgapur district and village distribution designs are done to work out average quantity of pipes required in each category of population. According to these sample calculations, total quantity of pipes required for all habitations of this project has been assessed. In general in villages HDPE Grade 80 PN 6 pipes are proposed to be laid. Along the main road of other habitations DI pipes are being provided. PSPs and cattle water troughs (CWT) shall be placed at locations in consultation with the water health committees of the village. At each PSP a platform and a soak pit shall be constructed.

Durgapur district being tribal area, provision of one public stand post for 100 persons and cattle water trough for 250 persons as per design population for the year 2036 has been taken for estimation purpose. Provision of pipelines made for village distribution is as given below:

Table 6-12: Details of Village distribution

S.No.	Dia. of HDPE Grade 80 PN 6 pipe (mm)	Pipe Length (KM) for		
		W.H.	C.W.T.	Total
1	90	142.959	212.030	354.989
	TOTAL	142.959	212.030	354.989
S.No.	Dia. of DI K-7	Pipe Length (KM) for		
		W.H.	C.W.T.	Total
1	100	52.117	67.851	119.968
2	150	0.315	0.315	0.630
		52.432	68.166	120.598

There are 8 villages having population of 3000 or more namely Vagdari, Faloni, Mandawa, Valota, Pagara, Vassi Pal, Dandi & Pal Kolihanda. It is estimated that about 40% of design population (for year 2036) may not afford to take house connections and may like to take water from PSPs for domestic purpose and use CWTs for their cattle and remaining 60% of design population may take house connections. Break-up of population and household connections for these eight villages is as given below:

Table 6-13: Details of PSPs & Connections in Habitations having 3000 plus Population

Habitation	Pop. As per census 2011			Design population of MH for yr. 2036 served with		No. of Household in Main Habitations for yr. 2011 as per Census		No. of Household in Main Habitations for design yr. 2036 served with	
	MH	CH	Total	PSPs	Connections	Total	MH	PSPs	Connections
DANDI	1790	3476	5266	1264	1935	3200	303	12	290
FALONI	1419	1960	3379	1034	1555	2589	289	11	313
VAGDARI	2887	276	3163	1710	2532	4242	506	22	612
MANDAWA	1504	1967	3471	1088	1633	2721	254	11	307
KOHANDA	1837	2914	4751	1347	2020	3367	345	14	375
VALOTA	960	1230	2190	690	1035	1725	196	7	212
VASSI PAL	644	1483	2127	464	697	1161	123	5	132
PAGARA	1486	1671	3157	1072	1608	2680	290	11	317

Provision in the estimates of these eight villages has been taken for PSPs & CWTs and house connections. Provision for water meter for individual house is not taken in the estimate. YTC shall be provided at the entry point of habitations and VWSIC shall be responsible to make payment of water charges as meter installed in YTC.

VWSG shall make suitable arrangement for collection of water charges from habitant using PSPs and house connections.

Provision of one public stand post for 100 persons and cattle water trough for 250 persons as per design population for the year 2026 has been taken for estimation purpose. Total number of PSPs and CWTs co-worked out for the project are as given below:

Table 6-14: Details of PSPs & CWTs

S.N.	Description	PSP	CWT
1	Main habitations	1932	813
2	Other habitations	1368	626
Total		3300	1439

6.4 Soil Investigation

Soil investigation work was awarded to M/s Hydrominivron Consultancy (P) Ltd, Jaipur by the consultant as per provision in the agreement. 50 points were selected for bore log & soil resistivity upto a depth of 3-8 m along the alignment of main transmission pipe lines at an interval of about 5 Km.

On the basis of soil investigation report submitted by M/s Hydrominivron Consultancy (P) Ltd, Jaipur, soil resistivity for 33 locations points is found more than 100 Ohm, and for 9 locations points soil resistivity is found in the range of 50-100 Ohm and remaining 8 locations points, soil resistivity is found in the range of 20-50 Ohm which is safe. On the basis of bore logs of different locations, selection of type of pipe for rocky & non rocky strata is made as per policy of the department.

Detailed soil investigation report is provided as Appendix 1.

6.5 Dedicated Power Feeder

To ensure regular and uninterrupted power supply, it is proposed to connect each pumping station with 11 KV dedicated power feeder from the nearest available 33/11 KV GSS. Direct Power Feeders of 11 KV are proposed from nearest 33/11 KV GSS or extension from existing 11 KV power lines for respective cluster pumping stations. The power availability has been taken as 20 hours for design of all the Operating Units.

Brief details are given below in a table.

Table 6-13: Details for Power Feeder

S. N.	PS Number	Location of PS	Nearest GSS	Approx. Distance	Type of Sub Station
1	TPS1	Main Headworks/Aspur	Aspur	2.5 km	33/11 KV
2	CPS2	Dhams/Aspur	Indira	3 km	33/11 KV
3	TPS1/TPS2	Kachharia/Doms	Mahul	2 km	33/11 KV
4	CPS5	Dhams/Doms	Vadi Pal	6.5 Km	33/11 KV
5	CPS6	Poonatara/Doms	Mahul	3 km	33/11 KV
6	CPS7	Vada Punak/Doms	Punak GSS	2 km	33/11 KV
7	CPS8	Maddala/Doms	Darai	5 km	33/11 KV

e) **Distance from STP**

STP of 4 MLD is proposed at Do River, Udaipur Road which is 28 km away from Som kamla Amba Dam. MSL of Proposed STP site and Somkamla Amba Dam are 267m and 213 respectively.

Project	Som Kamla Amba Project
River	Som river, a tributary of Mahi
Lat/Long	23° 58' 00" / 74° 02' 00"
GCA	26998.60 ha
CCA	19155.42 ha
Annual water supply	8.01 MCM
Catchment Area	5376 sq km
Main Dam	
Type	Earthen Dam
Length	620 m
Top elevation	217.50 m
Height of dam above lowest river bed level	27 m
Lowest river bed level	190.5 m
Spillway	
Type	Ogee spillway
Length	244 m
Location of spillway	Central spillway
Crest level	335.40 m
Number of bays	13
Discharge capacity at MWL	20045 cumec
Size of spillway gate	15 m wide and 12.885 m high
Reservoir	
Maximum water level	215.50 m
Full Reservoir Level	33.50 m
MDOL	200.50 m
Live storage	160.30 MCM
Gross storage	172.80 MCM
Reservoir spread area	36.18 sq km
Year of start of construction	1977
Date of completion	1992
Year of first impoundment	2004

Fig. 4 Details of Som Kamla Amba Dam

Ambient Air Quality and Noise

Site-specific data of ambient air quality and sound levels at project site is not available. However, general observation is made during site visit that area is free from air and noise pollution. This is substantiated by the fact that the dam is away from habitation, traffic and industries and that there are no anthropogenic sources of air/noise pollution in the vicinity. Therefore, ambient air is clean and sound levels are observed low. They are expected to be well within the prescribed limits.

Water Quality

Water quality data of Som Kamla Amba reservoir was taken from "Ecology and Fisheries of selected Reservoirs of Southern Rajasthan", a study by Sharma, V. K. and Kushal, D. K. of Central Inland Fisheries Research Institute (ICAR) Kolkata. Bull No. 138. Water in Som Kamla Amba reservoir remains clear imparting a greenish tinge. The water temperature varied from 17 in winter to 28°C in post-monsoon. The alkaline water (PH 7.4) is favorable for fish growth. Dissolved oxygen varied from 6.0 to 8.4 mg/l. Assessment of the productivity based on total alkalinity (122 mg/l) reflected the water body fairly productive. Calcium content of water ranged between 27 and 30 mg/l. Magnesium concentration was of high range (8.4-21.6 mg/l). Chloride values fluctuated from 10.0 to 18.0 mg/l. Higher values of specific conductance (601 µMho/cm) supported the eutrophic character of the reservoir. Table 3.1 give water quality data.

Table 3.1: Water Quality of Som Kamla Amba Reservoir

Depth (in m)		Surface	2	4	6	8
Water Temperature (deg C)	Summer	25.5	-	-	-	-
	Post Monsoon	28	27.5	27	26.3	26
	Winter	17	16.5	16.4	16	-
pH	Summer	8.12	-	-	-	-
	Post Monsoon	7.65	8.30	7.35	7.94	7.95
	Winter	6.45	6.52	6.59	6.61	-
DO (ppm)	Summer	8	-	-	-	-
	Post Monsoon	8.4	8	6	5.6	5.2
	Winter	6	5.6	5.6	5.2	-
Total alkalinity (ppm)	Summer	205.8	-	-	-	-
	Post Monsoon	86	90	90	92	96
	Winter	95	1032	117.6	131.8	-
Conductivity (micro-mhos/cm)	Summer	881	-	-	-	-
	Post Monsoon	429	414	412	411	402
	Winter	494	495	502	505	-

Natural Hazards

Potential of natural hazards such as flooding and earthquake is not significant. Project is designed for a design flood value of 20500 cumec, revised design flood has been worked as 21767 cumec by CWC i.e. a nominal 6.18% increase. Project falls in earthquake zone II, there is no revision and dam design has taken care of this aspect as well. Bureau of Indian Standards [IS 1893 (Part I):2002], has grouped the country into four seismic zones, viz. Zone II, III, IV and V. Zone II is the least active and Zone V is the most active.

Source: World Bank for Dam Rehabilitation and Improvement Project (Drip II)

Fig 5: - Water Quality Report of Som Kamla Amba Reservoir

- ii. **Vijay Chakra Sagar Dam:** Situated near Dimiya village, Dungarpur and this dam comes under control of WRD. This dam is used for raw water source for urban water supply in Dungarpur. The dam is not used of irrigation purposes at all.
 - d) **Location:** The dam is located at the coordinate 23°46'44.82"N and 73°46'5.69"E on Moran River.
 - e) **Selection of Site:** Presently the existing intake well for pumping raw water from Dimiya dam is in back water of dam, during the summer season water is to be brought near

existing pump house by the centrifugal submersible pumps. So in order to get the maximum benefit in pumping the raw water during severe drought conditions a new intake well is proposed near the spillway section of the Vijay Chakra Sagar dam (Dimiya dam).

f) **Gauge level of Dam**

Since the construction of the Dimiya dam PHED has continuously maintained the daily water level and storage capacity details of the same are as follows: -

Table-1 Gauge Details of VIJAY CHAKRA SAGAR (DIMIYA) DAM					
S.no.	Year	Gauge of Dam	Filling of Dam	Vol. of Dam	Remark
1	2010	29 Feet	29 Feet	40 McFt	Full
2	2011	29 Feet	29 Feet	40 McFt	Full
3	2012	29 Feet	29 Feet	40 McFt	Full
4	2013	29 Feet	29 Feet	40 McFt	Full
5	2014	29 Feet	29 Feet	40 McFt	Full
6	2015	29 Feet	29 Feet	40 McFt	Full
7	2016	29 Feet	29 Feet	40 McFt	Full
8	2017	29 Feet	29 Feet	40 McFt	Full
9	2018	29 Feet	29 Feet	40 McFt	Full
10	2019	29 Feet	29 Feet	40 McFt	Full
11	2020	29 Feet	29 Feet	40 McFt	Full
12	2021	29 Feet	29 Feet	40 McFt	Full

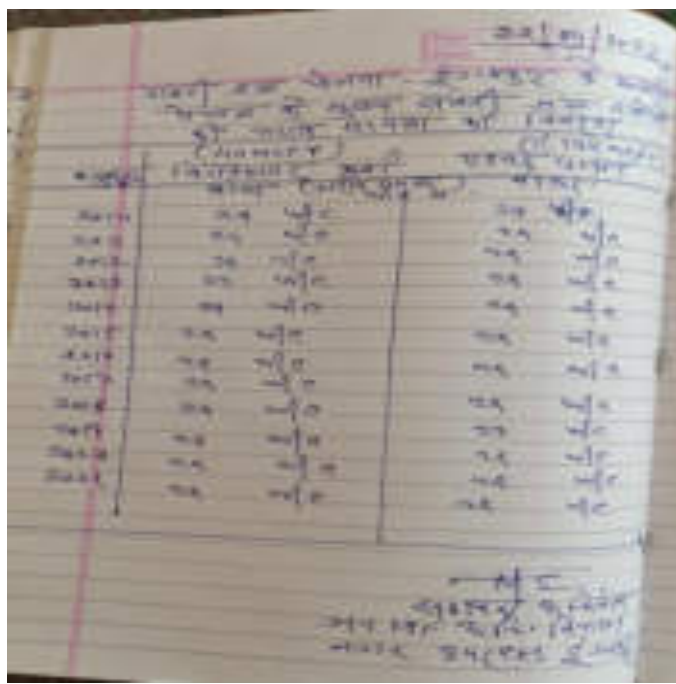


Fig. 6 Gauge Details of Vijay Chakra Sagar (Dimiya) Dam

g) **Distance from STP**

4 MLD STP is proposed at DO River, Udaipur Road (Dungarpur) which is 18.4 km away from Vijay Chakra Sagar Dam. The MSL of proposed STP site and Vijay Chara Sagar Dam are 267m and 251m respectively. No direct drain from STP site is connected with Vijay Chara Sagar Dam.



Fig. 7 Distance of STP from Dimiya Dam



Fig. 8 Existing Intake at Dimiya Dam



Fig. 9 Catchment of Vijay Chakra Sagar Dam

Sustainability and environmental considerations of Vijay Chakra Sagar Dam. The Vijay Chakra Sagar (Dimiya) dam has the capacity of 44.87 Mcft storage. For proposed water supply project only 3.1 MLD i.e. about 40 McFt water is allocated and proposed to be drawn from the source. Therefore, source is sustainable. Water Quality of the Dam has been evaluated from reports in Fig 10.

OFFICE OF THE JUNIOR CHEMIST
PUBLIC HEALTH ENGINEERING DEPARTMENT, Lab. Durgapur(Raj.)
REPORT OF THE CHEMICAL EXAMINATION OF WATER

No. Lab/Tests/Chem/2021-2022: **26-29**
 To :
 Assistant Engineer
 PHED City Sub.Dn. Durgapur

Date: **9/04/2021**
 District: **Durgapur**
 Tahsil: **Durgapur**

Name of Sample Taker: **Lab. Staff**

(Chemical Test Report kept in PPH)

S.N.	Dist.	Area	Sub Area	Location	Sample No.	Date of Collection	Date of Examination	pH	Specific Gravity	Residual Chlorine	Hardness	Total Solids	Calcium	Magnesium	Iron	Copper	Lead	Mercury	Fluoride	Chloride	SO ₄
1	Durgapur	City	UNICEF City	UNICEF City	Raw Water ROP	1	08.04.2021	08.04.2021	8	1.0	-	70	0.25	7	180	200	120	60	400		
2	Durgapur	City	UNICEF City	UNICEF City	Filter Water ROP	2	08.04.2021	08.04.2021	7.5	0.9	1	100	0.24	6	210	230	130	100	390		
3	Durgapur	City	UNICEF City	UNICEF City	OPR Near ROP	3	08.04.2021	08.04.2021	7.6	0.2	1	100	0.24	5	210	230	130	100	390		
4	Durgapur	City	UNICEF City	UNICEF City	OPR Near ROP	4	08.04.2021	08.04.2021	7.8	0.2	1	100	0.24	5	210	230	130	100	390		


 Junior Chemist
 PHED Lab Durgapur

Date: **04/05/21**

No. Lab/Tests/Chem/2021-2022:
 Copy to:
 1 The Supt. Engineer, PHED, Circle Durgapur.
 2 The Supt. Chemist, P.H.E.D. Laboratory, Udatpur.
 3 The Executive Engineer, PHED, Dn. Durgapur


 Junior Chemist
 PHED Lab Durgapur

Fig. 10 Water Quality report of Vijay Chakra Sagar Dam

- iii. **Edward Sagar Dam:** Since the construction of dam PHED has continuously maintained the daily water level and storage capacity of the Edward Sagar Dam. The Edward Sagar Dam has the total storage of 137 McFt excluding the dead storage of the dam. It is not used for irrigation purpose.
- a. Location:-It is located at $23^{\circ}47'19.78''\text{N}$ and $73^{\circ}40'16.78''\text{E}$.



Fig. 11 Intake as Edward Sagar Dam



Fig. 12 Catchment of Edward Sagar Dam

OFFICE OF THE JUNIOR CHEMIST
PUBLIC HEALTH ENGINEERING DEPARTMENT, LABORATORY DUNGARPUR
EXAMINATION REPORT FOR ALUM DOSE

No. Lab/Tech/Chem/2021-2022: 356-331 Dated: 21.06/2021

To: Assistant Engineer, P.H.E.D. City Sub. Div. District - Dungarpur
Dungarpur (Raj) Tehsil - Dungarpur

Ref No. (N. SP-1) : 21.06.2021 Name of Sample Taken: Jim PHED City

Source	Raw Water			
Source Location	Beel Head Works			
Collection Point	Filter House			
Collection Time	Dungarpur			
Station				
Station Code No.	Urban			
Date of Collection	21.06.2021			
Date of Examination	22.06.2021			
Lab Sample No.	274			

Note - Results of Alum Dose, Chlorine Demand & TDS are

1	pH of Raw Water	8.1		
2	Turbidity (NTU)	8.3		
3	Temperature (°C)	30.0		
4	Colour	N.O		
5	Odour	N.O		
6	Alum Dose (mg/L)	20 mg/L		
7	Chlorine Demand (mg/L)	3 mg/L		
8	Total Dissolved Solids (mg/L)	270		
9	pH of Treated Water	7.8		

No. Lab/Tech/Chem/2021-2022/ Dated: 20/06/2021

Copy to:

- 1 The Supdt. Engineer, P.H.E.D. Circle, Dungarpur
- 2 The Supdt. Chemist, P.H.E.D. Circle, Dungarpur
- 3 The Executive Engineer, P.H.E.D., Div. Dungarpur.

Junior Chemist
PHED Lab Dungarpur

Junior Chemist
PHED Lab Dungarpur

Fig 13 Water Quality Report of Edward Sagar Dam

Date: 22/05/2022

शिवरी जल योजना - डूंगरपुर के अन्तर्गत
पंचजन के मुख्य सतही जल स्मॉल
की गराव क्षमता का विवरण

वर्ष	(40 MLD) विजयपुर डूंगरी क्षेत्र (नगरपालिका)	(125 MLD) एडवर्ड सगर क्षेत्र
2010	29 मीटर	29 मीटर
2011	29 मीटर	29 मीटर
2012	29 मीटर	29 मीटर
2013	29 मीटर	29 मीटर
2014	29 मीटर	29 मीटर
2015	29 मीटर	29 मीटर
2016	29 मीटर	29 मीटर
2017	29 मीटर	29 मीटर
2018	29 मीटर	29 मीटर
2019	29 मीटर	29 मीटर
2020	29 मीटर	29 मीटर
2021	29 मीटर	29 मीटर

सहस्र जल निगम
अनल. आ. वि. विभाग
नगर उपाययोजना

Fig 14 Gauge Details on Edward Sagar Dam

b. Distance from STP

STP of 4 MLD is proposed at Do River, Udaipur Road which is 13 km away from Edward Sagar Dam. MSL of Proposed STP site and Edward Sagar Dam are 267m and 312 respectively. Proposed STP site and Edward Sagar Dam are connected through a drain but runoff discharge is from Edward Sagar Dam to STP site therefore no adverse impact of STP to Dam.

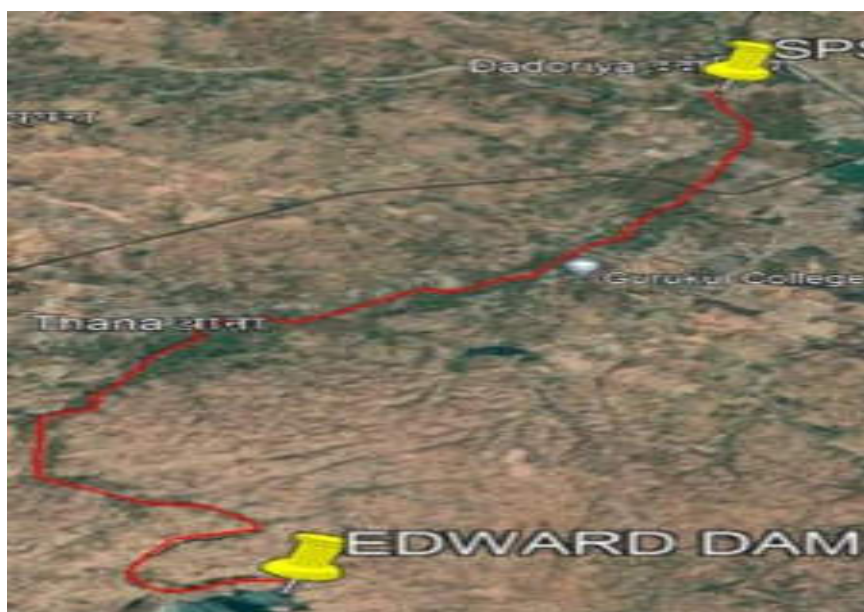


Fig 15 Distance between Dungarpur STP and Water supply source at Edward Sagar Dam

77. Sustainability and environmental considerations of Edward Sagar Dam. The Edward Samand dam has the total storage of 137 McFt excluding the dead storage of the dam. For proposed water supply project only 4.54 MLD i.e. about 61 McFt water is proposed to be drawn from the source. Therefore, source is sustainable.

78. Edward Sagar Dam Water quality. Water Quality of the Dam has been evaluated from reports given in Fig 13.

- iv. **Ground Water Source:** Presently Dungarpur town is partially dependent on ground water. Location and details of existing tube wells & open wells are as follows. -

S. No.	Location	Type	No.	Production Per Day (In KL)
Tube Wells				
3.	Patrakar colony TW	Tube well	1	500
4.	Darjiwada TW	Tube well	1	500
	Total		2	1000
Open Wells				
3.	Rani Bao OW	Open well	1	1000
4.	Kelabao OW	Open well	1	1000
	Total		2	2000

Based on the reports, it was finalized that out of the complete water requirement for the project only 1.5 MLD water will be taken from the ground water source. **Water quality of the underground water has been analyzed based on the reports in fig. 16 and 17.**

Sustainability and environmental considerations of Ground water sources. 1.5 MLD of the total requirement of the proposed project is planned to be taken from ground water sources. As per the data available, a total of 3 MLD water is available in the ground water sources. 2 Nos Tube wells and 2 Nos Open wells are proposed to be deepening and desalting, with re commissioning work.

Production and other details of existing Open Wells in summer season 2021																
Open well Location	DW No	Total depth in Mtr	Water table in Mtr.	Yield or discharge per hour in liters	Draw down in Mtr.	Open Well / R.C.C. / Masonry	Bore dia in mm	Installed Pump set details				Chemical parameter in ppm				Reasons of failure if any
								Discharge in lps	Head in Mtr.	KW	Discharge in KLH	CL	Fluoride	TDS	Nitrate	
Near Mahadev Mandir 1	1	12	8	50000	5.0	RCC	8	-	-	-	-	330	0.55	570	8	Not used in present time
Near Mahadev Mandir 2	2	12	8	10000	5.0	RCC	8	-	-	-	-	310	0.33	570	8	Not used in present time
Kamdev	3	12	8	10000	5.0	RCC	8	3.75	90-120	7.5	13500	330	0.55	800	8	-
Poland	4	10	8	10000	5.0	RCC	8	-	-	-	-	290	0.55	600	8	Not used in present time
Near Well	5	12	8	10000	5.0	RCC	8	-	-	-	-	310	0.55	615	8	Not used in present time
Ram Das	6	10	8	50000	5.0	Masonry	8	3.75	90-120	9.3	13000	330	0.55	875	8	-
Kita Das	7	10	8	50000	5.0	Masonry	8	2.5	90-120	5.5	9000	330	0.55	680	8	-
Bur open well 1	8	10	8	10000	5.0	Masonry	8	1.75	90-120	8.3	13500	330	0.55	580	8	-
Bur open well 2	9	10	8	10000	5.0	Masonry	8	-	-	-	-	300	0.35	488	8	Not used in present time
Bur open well 3	10	10	8	10000	5.0	Masonry	8	-	-	-	-	300	0.35	475	8	Not used in present time
Ashok Nagar	11	12	8	30000	7.0	RCC	8	3.75	90-120	8.3	13500	300	0.55	1130	40	-
Pat ki Sakhi	12	18	8	10000	7.0	Masonry	8	2.5	90-120	5.5	9000	300	0.55	1130	15	-
Chat Das	13	15	8	10000	7.0	Masonry	8	2.5	90-120	5.5	9000	300	0.55	920	15	-
Near S.P. Garden	14	18	8	10000	7.0	RCC	8	3.75	90-120	8.3	13500	300	0.55	1022	40	-
D.T. Dandi	15	18	8	30000	7.0	Masonry	8	2.5	90-120	5.5	9000	300	0.55	1030	30	-

Fig. 16 Details of Ground Water Source

Production and other details of existing Tube Wells in summer season 2021																		
Tube Well Location	TWT No	Total depth in Mtr	Water Table in mtr	Yield or discharge per hour in liter	Draw down in mtr	Total length of M.S. casing pipe in mtr	Total length of M.S. strainer pipe in mtr	Total bore drilling in Alluvium strata (mtr)	Total bore drilling in rock (mtr)	Installed Pump set details			Discharge in MLD	Chemical parameter in ppm				Reasons of failure if any
										Discharge in lps	Head in mtr	NW		Ca	Fluoride	TDS	nitrate	
Pattayat Colony	1	125	5	30000	7.0	4	-	5	115	2.5	90-120	2	11500	110	0.50	773	35	-
Chirpawla	2	90	5	30000	8.0	3	-	5	85	3.75	90-120	2.5	11500	130	0.5	660	30	-
Falbhager	3	128	2	50000	8.0	6	-	5	145	-	-	-	-	199	0.46	752	32	Not used in present time
Near Railway Jaffar	4	130	4	30000	6.0	3	-	2	142	-	-	-	-	112	0.34	545	32	Not used in present time
Nr. Nara Colony Pump house	5	90	5	20000	10.0	5	-	5	85	-	-	-	-	100	0.4	230	19	Not used in present time
Nr. Karamda	6	90	2	20000	10.0	5	-	5	82	-	-	-	-	130	0.20	347	17	Not used in present time
Jahan Patti	7	150	5	20000	10.0	6	-	5	145	-	-	-	-	120	0.54	550	19	Not used in present time



 Ach

Fig. 17 Details of Ground Water Source

Table 2. Rainfall Data of Dungarpur

year	Jsn	Feb	March	April	May	june	july	aug	sep	oct	nov	dec
1980	0	0	0	0	0	372.8	214.8	137.2	86.5	0	0	0
1981	1.6	0	0	0	0	39.8	254.1	349.7	66.9	0	57.2	0
1982	6	0	0	50.6	87.8	51.5	408.7	139.8	21.7	4.5	182.2	10
1983	0	0	0	6.8	0	118	254.7	238.1	104.2	79.1	0	0
1984	0	0	0	0	0	19.2	303..0	489.2	66.6	0	0	0
1985	0	0	0	0	0	9.6	112	147.5	5.8	126.5	0	0
1986	0	0	0	0	0	61.2	278.4	112.1	14.4	40.8	0	0
1987	0	0	0	0	0	51.8	38.8	412	0	0	0	20
1988	0	0	0	0	0	30.3	232.4	379.5	65.6	0	0	0
1989	0	0	0	0	0	187.2	211.1	186.2	72.8	0	0	0
1990	0	0	0	0	14.2	24.2	262.8	215.7	123.8	9.1	5	0
1991	0	0	0	0	0	10	450	70.2	19.6	0	0	0
1992	0	0	0	0	14.2	24.2	262.8	215.7	123.8	9.1	5	0
1993	0	4	0	0	0	93.5	472.5	32	76	3	11	0
1994	7	0	0	0	0	220.5	329.7	366	311.9	0	4.8	0
1995	27	0	0	0	0	37.9	236.1	107.5	86.2	0	0	1
1996	3	0	0	0	3	99	282	265	128	14	0	0
1997	0	0	0	2	8	129	160	354	92	6	2	0
1998	0	0	0	0	0	78.8	167.2	121.5	303.5	43.5	0	0
1999	0	8	0	0	0	103	131	49	31	66	0	0
2000	0	0	0	0	0	39.7	247.3	162	36	0	0	0
2001	0	0	0	0	0	242	422	124	1	2	0	0
2002	0	2	0	0	0	126	3	129	103	6	0	0
2003	0	50	0	0	0	64	401	157	36	0	0	0
2004	0	0	0	0	9	108	129	373	56	0	0	0
2005	0	0	0	0	0	92	163	107	210	0	0	0

2006	0	0	0	0	0	199	237	917	258	0	0	0
2007	0	7	3	5	20	47	174	266	58	0	0	0
2008	0	0	0	4	7	8	95	108	85	0	9	3
2009	0	0	1	0	0	46	499	315	12	40	1	0
2010	0	0	0	0	0	35	227	262	154	0	81	1
2011	0	0	0	0	0	6	291	495	185	0	0	0
2012	0	0	0	0	0	19	359	458	342	0	0	0
2013	0	26	0	15	0	158	614	258	286	79	0	0
2014	40	15	0	1	25	4	358	126	306	0	0	0
2015	8	0	35	0	0	245	413	92	56	0	0	0
2016	0	0	0	0	0	34	482	433	24	28	0	0
2017	0	0	0	0	0	48	482	328	156	0	0	5
2018	0	0	0	0	0	284	263	165	98	0	0	0
2019	0	0	0	0	1	129	107	383	294	70	0	0
2020	0	0	2	0	0	3	146	308	64	0	0	0

Source: Annual Rainfall Data reports by Water Resource Department, Government of Rajasthan.

Particulars	Year 2025	Year 2040	Year 2055
Design Demand of clear water (In MLD)	9.28	10.28	10.99
Availability of clear water (In MLD)	9.73	11.60	11.00
Edward Samand Dam	4.54	4.54	4.54
Vijay Chak Sagar Dimiya Dam	3.1	3.1	3.1
Ground water	1.5	1.5	-
Transfer from SKA (Som Kamla Amba) system	0.59	2.46	4.36
Remark	Water availability is sufficient.	Water availability is sufficient.	Water availability is sufficient.

Fig 18 Demand V/S Availability analysis

Conclusion: On the basis of above techno-economic and environment considerations it is find out that all four source are sustainable.

Appendix 5: Letter for Allotment of Water for Dungarpur Town Water Supply Project of Dungarpur

OFFICE OF EXECUTIVE ENGINEER PHED DIVISION DUNGARPUR

S. NO. /EE/DWA/2021-22/ 1596

Date: 12-03-2021

Commissioner
Nagar Palikahad
Dungarpur

Subject: Regarding Implementation of reorganization of UWSS Dungarpur to be implemented through RLIDP

Reference: EE PHED Project Division II Udaipur dated 12.08.2021

In continuation of above referred letter provision of transfer of water from Somkunda Arbis dam to UWSS Dungarpur has been modified in retrofitting proposal of (i) Villages of Blocks Aspur, Dawa and Dungarpur of District Dungarpur, in view of utilization of existing WTP's and already laid pipelines so that increased demand of rural sector may be met out without change in transmission system. Details of provision are as under:

S.No	Name of surface source	Transfer of water		Quantity in MLD	Remarks
		From	To		
1	Edward Samand Dam	Edward Samand Dam	—	4.54	Capacity of Edward Samand Dam is 127 Mch and annual raw water requirement is only 61 Mch. Existing gravity line upto Bori WTP and from WTP to Udaipur WTP will be sufficient to carry water.
2		Bori WTP RWR	Bori WTP	3.25	
3		Bori WTP RWR	Udaipur WTP	1.29	
4	Dimiya Dam	Dimiya Dam	Udaipur WTP	3.1	Capacity of Dimiya Dam is 44.87 Mch and annual raw water requirement is 18 Mch. Provision of raising of Dimiya dam by 1 mtr will enhance 14 Mch water. Existing pipeline of 200 mm DI K-8 will be sufficient to carry water.
5	Ground water	—	—	1.5	During summer if any deficient due to reduction in ground water may be supplemented by SKA system.
	Total			9.14	

Particulars	Year 2022	Year 2033	Year 2052
Design Demand of UWSS Dungarpur@115 LPCD/10N institutional demand and 15% transmission and distribution losses	9.73	11.6	13.50
Less	9.14	9.14	9.14
Transfer from SKA system	0.59	2.46	4.36

Looking to above modifications following provisions to be taken in DPR being prepared by RUIDP:

- Provision of suitable Pump Machinery and Electric equipments needs to be taken up at Bori Head Works.
- Construction of 450 KL capacity RCC RWR at Bori Head Works under the provisions to be taken.
- Renovation/Upgradation of both WTP's.
- To increase the water supply production from Vijay Chakra Sagar (Deemiya) Dam by 1.0 meter has been proposed as per discussions held with WRD Department and an Estimate for Raising the height of Vijay Chakra Sagar Dam by 1.0 meter has been framed by WRD Dungarpur for an Approx. cost of Rs 9.50 Crores. This work may be proposed to be got Executed by WRD under the budget head available with project PHED.
- Presently the intake Pump House for Pumping Raw Water from Deemiya Dam is in the back water of dam and as the water recedes in the dam during summer season, water is to be brought near the existing Pump House to be Pumped by the Centrifugal Submersible Pumpsets installed there in an approach channel which usually got silted up every year after monsoon season, proposed to extend as per design the existing 200mm Diameter Di K-9 Rising Pipe line near Pump House for the length of 2.0 KM above HFL on the bank of Surface water Source along the nearby hilly alignment and provision for construction of a suitable RCC intake near the spillway section is proposed to get the maximum benefit in pumping the raw water during severe drought conditions.
- CWR at chandpole in GLR campus along with pumping machinery.
- Existing Ground Water Resources may also be got disilted and deepened as per requirement to increase the ground water source production on this scheme upto 1.50 MLD and this work maybe got included in the DPR.

Therefore you are requested to take necessary provisions in reorganization schemes to be implemented through RUIDP, if any query consultant may be asked to this office and project officers.


Executive Engineer
PHED Division Dungarpur (Ra)

S.NO. 1596 - 1600

Date: 11-08-2021

Copy forwarded to

- (1.) The Additional C.E. Project PHED Udaipur/Region Udaipur
- (2.) The Superintending Engineer project PHED Circle Banswara/Circle Dungarpur.
- (3.) Executive Engineer, PHED, Project Division II Udaipur
- (4.) Executive Engineer, RUIDP, Jaipur


Executive Engineer
PHED Division Dungarpur (Ra)

Details of water supply scheme from Som Kamla Amba Dam

दुंगरपुर जिले में वृहद प्रसारित एवं प्रस्तावित पेयजल परियोजनाओं का सविनय विवरण

प्रसारित पेयजल परियोजना—

1. सोम कमला अम्बा दम सतही स्रोत से जिला दुंगरपुर के पंचायत समिति आसपुर, बीरवा एवं दुंगरपुर के 151 ग्राम एवं 244 वार्डों में दुंगरपुर शहर की पेयजल परियोजना—

दुंगरपुर जिले के किसानसभा क्षेत्र आसपुर के 136 ग्राम (पंचायत समिति आसपुर 47 ग्राम एवं बीरवा के 89 ग्राम) एवं किसानसभा क्षेत्र दुंगरपुर के 16 ग्राम (दुंगरपुर पंचायत समिति के 16 ग्राम) कुल 151 ग्राम एवं 244 वार्डों तथा शहर दुंगरपुर की सतही स्रोत सोम कमला दम से अस्थाित पेयजल परियोजना की योजना की अनुमानना में परियोजना की प्रस्ताविका एवं वित्तीय स्वीकृति विभागीय विभागों की बैठक संख्या 745 में दिनांक 18-10-2018 की तारीख 285.00 करोड़ एवं विभागीय तकनीकी समिति की 686 वी बैठक दिनांक 18-07-2018 तकनीकी समिति द्वारा तारीख 286.85 करोड़ की तकनीकी स्वीकृति उपरान्त 20-09-2018 को समर्थ 253.15 करोड़ का कार्यादेश मेलने एल.एम्.टी लिमिटेड कंपनी को जारी कर दिया गया।

परियोजना में आसपुर,बीरवा एवं दुंगरपुर पंचायत समिति के ग्राम क्रमशः 47.88 एवं 16 व वार्डों की क्रमशः 44,183 एवं 37 (कुल 151 ग्राम एवं 244 वार्डों) व शहर दुंगरपुर सम्मिलित है।

योजना का निम्न कार्य का प्रावधान लिख गया है:-

प्रस्तावित परियोजना के अन्तर्गत प्रस्तावित कार्य का विवरण निम्नानुसार है:-

• इन्टेकवेज एवं इन्टेक स्टेशन	क	1 वरत
• पाईप लाइन	क	100 कि०मी० से 850 कि०मी० मात्र, तथा 80एनएम एचसीपी पाईप लाइन कुल लम्बाई 1888 कि०मी०
• जल संचयन संयंत्र	क	21.25 एनएमएससी० क्षमता, वर्ष 2035 की संघ अनुमान
• खनिज स्टेशन	क	11(सम्मिलित 1 इन्टेक खनिज स्टेशन)
• प्रकाश जलाशयों की संख्या	क	63(सम्मिलित 01 नं. 800 के एल जल जलाशय)

भौतिक एवं वित्तीय प्रगति :-वर्तमान में योजना का 70 प्रतिशत भौतिक प्रगति प्राप्त कर ली गई है एवं 1001.48 किलोमीटर के पाईप प्राप्त हो चुके हैं, जिसमें से 850 किलोमीटर पाईपलाइन जाती जो चुकी है एवं 475 किलोमीटर की टेन्डींग कर दी गई है, योजना का जल संचयन संयंत्र एवं इन्टेक वेज का कार्य प्रगति पर है। योजना के अन्तर्गत 81 जल जलाशयों में से 36 जल जलाशयों का कार्य पूर्ण हो चुका है तथा 20 का कार्य प्रगतिरत है एवं 5 पर निर्माण कार्य शुरू किया जाना बाक है। परियोजना में अब तक कुल तारीख समर्थ 135.18 करोड़ व्यय किये जा चुके हैं। प्रस्तावित परियोजना का कार्य मई सितम्बर 2022 तक पूर्ण किया जाना सम्मिलित है।

Approval of Water supply scheme under Jal Jivan Mission for Dungarpur town

 **OFFICE OF THE CHIEF ENGINEER (RURAL), PHED, RAJASTHAN**
JAL BHAWAN, 2 CIVIL LINES, JACOB ROAD, JAIPUR
Phone: 0141-2222183, e-mail: ce_r@phed.in

No. F.2(11)PHED/CE(R)/JJM/SLSSC-25th/2021-22/14/11 - 83 Date: 14.07.2021

MINUTES OF 25th MEETING OF STATE LEVEL SCHEME SANCTIONING COMMITTEE (SLSSC) DATED 02.07.2021

The 25th meeting of State Level Scheme Sanctioning Committee (SLSSC) of PHED, Rajasthan (7th meeting under Jal Jeevan Mission) was held on 2nd July, 2021 under the Chairmanship of Additional Chief Secretary, PHED through Video Conferencing. The List of Participants is enclosed.

At the onset of the meeting, Chief Engineer (Rural) briefed about sanctions and progress so far under JJM as under:-

No. of FHTCs	Sanctions	TS issued	Tender invited	Work order issued / Work started
OTMP	28,97,912	23,31,358	20,70,743	5,38,471
MP	36,16,368	7,08,078	5,19,593	16,206
Total	65,14,278	30,39,436	25,90,336	5,54,737

It was also submitted that

- > The work order for all small OTMP schemes will be issued by September, 2021 and for Major Projects by December, 2021.
- > It is expected that good progress for FHTCs will start in October, 2021.
- > ISAs finalized in 27 districts (ISAs for 6 districts are in advance stage of finalization).
- > SPMU started functioning from June, 2021.
- > Tenders invited for DPMU & will be finalized in July, 2021.
- > NABL Accreditation of 6 Districts Lab in 21-22 (Now 12 NABL out of 33. Applied for remaining). Tenders invited for the establishment of 102 BL.

Chairman SLSSC & ACS, PHED desired that in next meeting of SLSSC the gap between sanctions & work started should be much lesser than present position.

The following were considered:-

Agenda- 1 Confirmation of minutes of 24th SLSSC meeting held on 26.05.21 (Minutes issued vide no. 1453-1529 dated 14.06.21)

Chief Engineer (Rural) submitted that the minutes of 24th SLSSC meeting held on 26.05.21 was issued vide no. 1453-1529 dated 14.06.21. Minutes were issued incorporating the suggested modification conveyed from NJJM vide their letter dated 14.06.2021 on draft minutes send to them by email dated 28.05.21.

SLSSC was requested to confirm the same with amendment that in Additional Agenda-1, Name of Scheme at Proposal No.2 of Table 10 of Dist- Dholpur may be read as WSS Kasol Khers & Kherpura in place of WSS Kasol Khers & Kherpur.

Under Secretary to Govt, NJJM, New Delhi vide letter no. W-11011/5/2021-JJM/II-DGWS Dated 14.07.21 Conveyed comments on Agenda- 1 as under:

1
14/7/21

SLSSC 25th, Minutes dated 16/07/2021

Agenda- 20 Proposals for Revised A&F Sanction of "WSP for 151 villages of Aspur, Donda and Durgapur blocks and Durgapur town from Bom Kamala Dam, Dist Durgapur " by SLSSC (Major Project)

Following Project was proposed for Revised A&F Sanction by SLSSC detailed as under:-

Sanctioned & Revised Proposal	Estimated Cost (Rs. in Crore)			No. of villages Planned			No. of FHTCs Planned	Average Per FHTC Cost (in Rupees)
	Total	Central Share	State Share	Total	PWS	Non PWS		
Sanctioned in 20 th SLSSC held on 11.02.21	401.93	167.40	234.53	151	143	8	32000	
Revised Proposed	159.79	73.90	85.89 (Include Urban Port- Rs. 10.90 Cr)	151	143	8	28299	52627/-
Net Increase /Decrease	-242.14	-93.50	-148.64	0	0	0	-3701	

The scheme / proposal wise details are available in prescribed Table-10. Chief Engineer (SP) submitted as under:-

1. In the original A&F Sanction estimated cost of original ongoing project having NWQSM share was also included along with retrofitting works for providing FHTCs in the project villages. The NWQSM share on this ongoing project has been fully utilized.
2. Now only retrofitting works for providing FHTCs in the project villages are proposed in JJM.
3. The Scrutiny of the projects has been made as per guidelines of JJM. The Project's DPR has been scrutinized as per general Comments regarding design & estimates of GoI conveyed vide letter dated 12.03.2021. This is final DPR based on actual survey.

Therefore, Revised A&F of above project was sought by CE (SP). SLSSC was requested to accord revised A&F sanction of above project with decreased cost Rs. 242.14 Cr.

It was decided to accord revised approval (revised A&F sanction) of the above project with revised cost Rs. 159.79 Cr as per funding pattern proposed. (Annexure of Agenda- 20).

[Action by CE(SP)]

Agenda- 21 Proposals for Approval (A&F Sanction) of "Strengthening & Rehabilitation of water supply system of Bhim Constituency of Dist Rajasamand from Chambal River & Retrofitting of Chambal Bhiwara Project" which was provisionally approved in 23rd SLSSC (Major Project)

Water Supply Project namely "Strengthening & Rehabilitation of water supply system of Bhim Constituency of Dist Rajasamand from Chambal River & Retrofitting of Chambal Bhiwara Project" was proposed for Approval (A&F Sanction) which was provisionally approved in 23rd SLSSC held on 25.03.21 at Additional Agenda-4 detailed as under:-

16/7/21

Revised A/R 151 Village is sent to SCSCC 13th

Date - 16/06/2021

Work of Retreating of 151 villages of Aspur, Dewa & Durgapur Blocks and Durgapur Town of Durgapur District from Sam Kalia Archa Dam Under Jal Jeevan Mission

Detailed Project Report

Chapter-7 General Abstract of Cost

S.No	Particulars	Amount (Lacs)
Part-A (Rural Works): Work Proposed for Rural Areas Under JRM		
1	Class Water Pump Machinery for Cluster USB	1.00
2	Cluster Distribution	1771.42
3	Village Distribution	13208.17
4	Solar Borehole Tube Well with 100 supporting structure for 10000 PE Tank	147.17
	Sub Total	14227.76
	Add 5% physical contingencies	711.39
	G.M. cost for Ten years as per 10% T & B	112.11
	TOTAL Part-A	15051.26
PART B: HOUSEHOLD TAP CONNECTIONS		
5	Functional Household Tap Connections	778.56
	Total Part-B	778.56
Part-C (Urban Works): Work Proposed for UWS Durgapur		
6	Pumping Machinery at Durgapur Town	30.00
7	Pumping Machinery at Adarsh Samudra Bore	15.72
8	Rain Water Harvesting Main Borehole & Samudra Bore	17.00
9	Electrical Connection	21.00
10	Meterstation Works	34.70
11	Provision for Raising of Durgapur Town	926.64
	Total Amount	1075.06
	Add 5% physical contingencies	53.75
	G.M. cost for Ten years as per 10% T & B	1006.30
	TOTAL Part-C	15974.16
	Grand Total (Part-A+B+C)	15974.16
	In Crs	159.79

(Pradeep Kothari)
Executive Engineer
PJED Project Dir. Udaipur-II

(K C Meena)
Superintending Engineer
PJED Project Circle Baramulla


(S L Saini)
Additional Chief Engineer
PJED Project Region Udaipur

Appendix 6: Stakeholders and Public Consultation Consultations Conducted During Project Preparation

A. Stakeholders Consultations in CLC:

City level Stakeholder Committee (CLC) Meeting (dtd. 09.06.2021)- A town-level stakeholder consultation meeting was conducted to discuss various issues like land availability, scope of works etc. under the chairmanship of District Collector in which representatives of primary and secondary stakeholders were invited. The feedback and concerns of the stakeholders have been taken into consideration in detail designs of the project. City level Committee meeting was held on under the Chairmanship of District Collector, Dungarpur for finalization of works of Water Supply and Sewerage in Dungarpur town. Proposed works were approved by CLC members in this meeting. Minutes of Meeting of CLC vide dated are given below:

Minutes of CLC meeting with Outcomes



Government of Rajasthan



Office of the Executive Engineer, PIU,

Rajasthan Urban Sector Development Investment Program (RUSODIP), Udaipur

No./RUSODIP/PIU/UDP/01/PH IV/Dungarpur/2020-21/37-45

Date: 03/07/2021

A city level committee was held under the chairmanship of District Collector, Dungarpur at Collectorate, Dungarpur on 30.06.2021 to discuss the Water Supply & Sewerage Project proposed under RUSODIP Phase IV for Dungarpur town. List of members/officials attended the meeting is at annexure-A.


1. It was appraised that the DPR of Water Supply & Sewerage Project is prepared by the Consultant M/S Exceltech Consultancy & Projects Pvt. Ltd., Jaipur engaged by Municipal Council, Dungarpur, which will be considered under RUSODIP Phase IV. The suggestions from stake holders of city level committee will be considered in the project.
2. The basic scope of works & provision in DRs were briefed to the committee by power point presentation. The estimated cost of DPR is about Rs. 137.33 Cr. (Capital Cost) for works proposed under Water Supply & Sewerage sector and Rs. 15.77 Cr. For 10 years O&M. Total Cost of Project is 153.10 Cr. The capital cost for execution of works will be borne by the State Government financed by ADB under RUSODIP Phase IV. The O&M cost for water supply works is to be borne by PHED and for sewerage works (STP, SPS & Sewer line) by Municipal Council. The O&M cost for payment will be performance based under the contract. After completion of project works the whole town will be benefitted with water supply and sewerage facilities.
3. The brief scope of works are as follows:
 Water Supply Works: - The main source of treated water is Somkamlia Amba Drinking Water Supply Project for 151 Villages and 1 town (Dungarpur) of District Dungarpur for which work order has been placed by PHED and work of this project has been started. Two existing surfaces namely Edward Samand and Vijay Chakra Sagar shall continue to provide water to the town. All these sources are capable to meet out the ultimate demand of the Dungarpur town. Under the project, 2 nos. new CWRs capacity (300 KL) and all the old distribution pipe lines of AC & PVC pipes proposed to be replaced by DI K-7 pipe lines and also in the uncovered area within the municipal boundary limit of about 15.7 Kms. The entire area has been divided into 16 zones and 17 District Metering Area (DMA's) basis for non-revenue water (NRW) reduction. Provision of about 11634 Nos. house service connections with domestic water meters for intermittent pressurized water supply is taken in the DPR. The entire system is proposed for automation on SCADA base for smooth O&M.

Sewerage Works: There is no existing sewerage system in the town. The scope under the project to provide sewer network of about 60 km length, one Sewage Treatment Plant (STP) of 4.0 MLD, three sewer pumping stations (SPS) of 2.35 MLD, 2.60 MLD & 0.60 MLD respectively to pump sewage of low lying area to main sewer. STP 4.0 MLD is proposed to be constructed on identified land near Do River on Udaipur road. It was informed that STP is proposed on latest Sequential Batch Reactor (SBR) technology to meet out the latest effluent parameters. To reduce inconvenience to public deeper depth (3.5 mtr above) & Railway crossing & circles where traffic is more, 5.2 Km trenchless technology for laying of the sewer is proposed. Area of town which is on the outskirts and having less habitation and population density is low has been proposed with Faecal Sludge & Septage Management (FSSM).

4. District Collector Dungarpur directed that it is the important project for Dungarpur and RUIDP should follow all norms for the work to be executed for Water Supply and Sewerage project. It is also directed consultant to visit the site along with the local representatives of Nagar Parishad and take provisions in the DPR for redressal of water supply related problems in their area so that inconvenience to public should be minimized.
5. Hon'ble MP, Dungarpur welcome the project for Dungarpur town and requested that all the old distribution pipeline should be replaced by new HDPE and DI pipe line so that the water will available with required pressure. Chairman Nagar Parishad Dungarpur suggested that the availability of land first confirmed before finalization of project. It was agreed that consultant shall get all relevant land documents from municipality & will provide to RUIDP along with DPR and suggested to explore the possibility of use of treated effluent in gardens and fountains etc.
6. Municipal Board agreed to allot the land for construction of STP near DO River on Udaipur road, SPS-1 near Padambhusan Shri Bhogi Lal Pandya Circle, SPS-2 near Ashram Vatika & SPS-3 between R/CCO & Gap Sagar.
7. EE, PHED also requested to take following provision vide letter number AA/vrat/Dungar/2021-22/691 dated 01.07.2021:-
 - Rising main pipeline from vijaysagar dam to udaivilas filter plant 200/250 mm DI K9
 - Pump machinery with pump house and J-2 type quarters at vijaysagar dam.
 - Replacement of rising main pipeline A.C. pressure to DI K9 150 mm dia New colony pumping station to new RHB OHSR.
 - New OHSR at Problematic Area
 - New Colony
 - Navadara
 - Vagadmagari
 - New GLR at Problematic Area

- Ghati
 - Dismantling and construction of new OHSR
 - Old RHB :- 272 KL
 - Indira Colony :- 227 KL
 - Dismantling of GLSR and construction of new OHSR at chandpole
 - Construction of new RWR at bori filter plant.
 - Construction of new CWR at :-
 - New Colony
 - Main pump house
 - Chandpole
 - Udaivilas filter plant campus
 - Repairing and rejuvation of 2 nos. filter plant
 - Udaivilas filter plant :- 4.50 MLD
 - Bori Filter Plant :- 3.25 MLD
 - Replacement and installation of existing pump machinerries on various pump houses and filter plant.
 - Construction of J-2 type quarters at :-
 - Main pump house
 - Bori filter plant
 - Udaivilas filter plant
 - Chandpole
 - New colony pump house campus
 - JEN quarter at new colony pump house.
 - Construction of circle office building and residence building of SE.
 - Dismantling of Old RGF at main pump house.
 - Repairing and rejuvenation of existing building and pump house.
 - Repairing of west weir at adwardsamand dam (2 nos.)
8. It was also deliberated that for public complaint redressal provision to toll-free number along with provision for customer service centers will be taken under the contract. The O&M payment will be performance based under the contract.
9. The representative of the Municipal council suggested to take up the excavation of trenches for sewer work in such a way, that the trench excavated for laying sewer lines should not be laying longer without restoration.
10. It was assured that suggestions and directions of the city level committee will be incorporated in the proposed detailed project report.

After deliberation, the project was agreed by the committee for further course of action at RUJDP level. Meeting ended with vote of thanks to chair.


Executive Engineer
RUJDP (PIU) Barnswara
(Member Secretary, CLE Dungarpur)

No./RUJDP/PIU/UDF/01/PH-IV/ Dungarpur/2020-21/ 93-45

Date: 09/07/2021

Copy to the following for information and necessary action please.

1. PA to Hon'ble MP, Dungarpur
2. PA to Hon'ble MLA, Dungarpur
3. PA to The Project Director, RUJDP, PMU, Jaipur
4. The District Collector, Dungarpur
5. The Chairman, Nagar Parishad, Dungarpur
6. The Commissioner, Nagar Parishad, Dungarpur
7. The Superintending Engineer, PWD/PHED/AVVNL/WRD, Dungarpur
8. The Superintending Engineer, RUJDP Phase IV/WW/WS, Jaipur
9. The Sr. Town Planner, Udaipur
10. Guard File


Executive Engineer
RUJDP (PIU) Barnswara

B. Consultations during Social and Environmental Impact Assessment

Various consultations were done during social and environmental impact assessment of the project with residents of the town at various locations to understand their level of satisfaction about the present water supply and sewerage conditions in town and also to understand their awareness about the proposed works and their willingness/acceptance of the proposed works under RUSTDIP. Details of these consultations are given below-

Details of Public Consultations in Durgapur
A. Pubic Consultation with locality

Date & Area	Participants			Issues Discussed	Outcome	Photos
	Male	Female	Total			
March 12 th , 2022 Near Bus Stand and Nagar Palika	08	04	12	Project components under RSTDSP and the benefits to the Community. Process of logging grievance and its mechanism under the project. Present status and access of Waste Water facilities in the town and other concerned issues and challenges. Presence of any forest, wild life or any sensitive/unique environmental components nearby the project, Presence of historical/ cultural/ religious sites nearby. Unfavourable climatic condition	Pipeline laying work for sewerage is proposed in the area and it was informed by nearby habitation that proper and structured sewerage facilities are not available in this part of the town and residenst have their own septic tanks and soak pits. Some people living in outskirts area are prone to practice open defecation. Process of grievance mechanism was also briefed with participants for lodging complaints. Participants are happy with proposed project in the town. There is not any forest, wildlife or any sensitive /unique environmental, component near the project area. Mt. Abu Wildlife sanctuary is quite remote from the project area. There are not any historical/cultural and religious sites in nearby the subproject area.	

March 13th, 2022 Old Bus Stand and Near Bus Stand	09	03	12	Project components under RSTDSP and the benefits to the Community. Process of logging grievance and its mechanism under the project. Present status and access of Waste Water facilities in the town and other concerned issues and challenges. Dust and noise pollution and disturbances during construction work. Perception of villagers on tree felling and afforestation Safety of residents during construction phase and applying of vehicle for construction activities.	Pipeline laying work for sewerage is proposed in the area and it was informed by nearby habitation that proper and structured sewerage facilities are not available in this part of the town and residents have their own septic tanks and soak pits. Some people living in outskirts area are prone to practice open defecation. Process of grievance mechanism was also briefed with participants for lodging complaints. Drinking water is providing by PHED, but the supply is intermittent on alternate days which is less than requirement of households. Participants are happy with proposed project in the town. Contractor should use modern machinery and water sprinkler to control dust and noise during construction phase. All the pollution control measures will be adopted at site to control the fugitive emission in the area and for control of noise, PPE's will be provided to workers such as ear muff etc. Plantation activities provide shade, shelter and enhance the local biodiversity in the area. The contractor should take care of the safety arrangement during construction phase and should provide traffic diversion routes to avoid the vehicle congestion People should be made aware before start of work in particular area.	

B. Public Consultations with ST Community

Date & Area	Participants			Issues Discussed	Outcome	Photos
	Male	Female	Total			
April 8 th , 2022 Ward no-3 & 4, ST Community,, Dungarpur	00	04	04	Present water supply and sewerage condition, access to water supply, quality of water supply, project components and the benefits to the community, Project components under RSTDSP and the benefits to the community and Grievance redressal mechanism under the project. Presence of any forest, wild life or any sensitive/ unique environmental components	The consultation/s was conducted specifically with the scheduled tribe community. Some households do have individual water supply connection. Entire community could not afford domestic water supply connections due to (i) lack of funds to get the connection installed (ii) some households have constructed houses on land parcels without having land titles and hence not willing to take connections, (iii) have easy access to public water supply source and are not willing take individual connections. Willing to take new connections if 24*7 water supply is available which is of good quality. There is not any forest, wildlife or any sensitive /unique environmental, component near the project area. Mt. Abu Wildlife sanctuary is	

				nearby the project. Presence of historical/cultural/religious sites nearby. Drainage and sewerage problem facing. Dust and noise pollution and disturbances during construction work. Public Health by proposed water supply & Sewerage subproject	quite remote from the project area. There are not any historical/cultural and religious sites in nearby the subproject area. Open defecation was/is practice due to lack of individual toilets. Many have constructed toilets in the recent past availing subsidised schemes from the Municipality.	
April 8th, 2022 Ward no-9 & 10, ST Community,, Dungarpur	00	09	09	Present water supply and sewerage condition, access to water supply, quality of water supply, project components and the benefits to the community, Setting up worker camp site within the village/ project locality Plantation measures in nearby the area.	Some households do have individual water supply connection. Entire community could not afford domestic water supply connections. Women excited about the prospect of getting individual water connections. They opined that their energy, time and hard labour will be saved especially during summer months. Enquired if their area has been included under the project. Willing to take new connections if 24*7 water supply is available which is of good quality. There is enough space available nearby the project	

				Safety of residents during construction phase and applying of vehicle for construction activities. Requirement of enhancement of other facilities. Project components under RSTDSP and the benefits to the community and Grievance redressal mechanism under the project.	area to establish labour camp. People suggested to establish the worker camp away from the habitation so there is no conflict and disturbances. People want to plantation programme in the town and ensure the aftercare measures such as watering and manuring etc. The contractor should take care of the safety arrangement during construction phase and should provide traffic diversion routes to avoid the vehicle congestion.	
April 8th, 2022 Ward no-6 and nearby location, ST Community,, Dungarpur	03	08	11	Present water supply and sewerage condition, access to water supply, quality of water supply, project components and the benefits to the community, Presence of any forest, wild life or any sensitive/ unique environmental	The consultation/s was conducted specifically with the scheduled tribe community. Willing to take new connections if 24*7 water supply is available which is of good quality. There is not any forest, wildlife or any sensitive /unique environmental, component near the project area. Mt. Abu Wildlife sanctuary is quite remote from the project area. There are not any historical/cultural and	

				components nearby the project. Presence of historical/cultural/religious sites nearby. Unfavorable climatic condition. Occurrence of flood, earthquake etc. Project components under RSTDSP and the benefits to the community and Grievance redressal mechanism under the project.	religious sites in nearby the subproject area. . Open defecation was/is practiced due to lack of individual toilets. Many have constructed toilets in the recent past availing subsidised schemes from the Municipality. There are no natural disasters such as flood and earthquake occurred in recent past. The area is not prone for such incidences	

C. Consultations with stakeholders

Date & Area	Participants			Issues Discussed	Outcome	Photos
	Male	Female	Total			
April 8 th , 2022 PHED,, Dungarpur	06	00	06	Proposed water supply works and availability of land, R&R issues etc.	Meeting with PHED and Nagar Palika officials and discussion were done about proposed project under phase-4. PHED and Nagar Palika officers assured of their full cooperation with RUIDP/RSTDSP during planning and implementation of the project.	
April 8 th , 2022 Chairman Office Municipal Council, Dungarpur	10	02	12	Environments issues related to surface water bodies and solid waste disposal facilities in Dungarpur City	Meeting with Chairman and elected member of Municipal Council Dungarpur. Treated effluent of STP can be used in agricultural fields in nearby location of Do river and proposed STP location and in a bird park which is located near the gap sagar SPS location. House Keeping facilities in Dungarpur is very good but there is no facilities of sewerage.	

April 8 th , 2022 Incharge municipal waste storage yard, Dungarpur	04	00	04	Environments issues related to solid waste disposal facilities in Dungarpur City	In the Dungarpur city domestic solid waste is disposed on open land existed on Uday Vilas road.	





Consultation Attendance sheet

Rajasthan Secondary Towns Development Sector Project (RSTDSP) RUIDP Phase-IV

Consultation Sheet

Place: Near Bus Stand and Nagar Palika Town: Dungarpur Date: 12/03/2022
Topic Discussed During Consultation:

1. Discussion with local public for water supply &
2. Sanitation facilities in the town.






S. No.	Name	Gender		Address	Contact No.	Signature
		Male	Female			
①	Hemlata		✓	Near Nagar Palika Area		
②	Vimla		✓	— " —		
③	Sauita		✓	— " —		
④	Rajiv	✓		— " —		
⑤	Suresh	✓		— " —		
⑥	Manohar	✓		Near Bus Stand Area		
⑦	Harner Singh	✓		— " —		
⑧	Kanti Lal	✓		— " —		
⑨	Dileep Singh	✓		— " —		
⑩	Mupesh	✓		— " —		
⑪	Laxman	✓		— " —		
⑫	Saroj Devi		✓	— " —		

**Rajasthan Secondary Towns Development Sector Project (RSTDSP)
RUIDP Phase-IV**

Consultation Sheet

Place: Near Bus Stand and Nagar Palika Town: Bungarpur Date: 12/03/2022
Topic Discussed During Consultation:

1. Discussion with local public for water supply &
2. Sanitation facilities in the town.

S. No.	Name	Gender		Address	Contact No.	Signature
		Male	Female			
①	Hemlata		✓	Near Nagar Palika Area		
②	Urmila		✓	— " —		
③	Savitri		✓	— " —		
④	Raju	✓		— " —		
⑤	Suresh	✓		— " —		
⑥	Manohar	✓		Near Bus Stand Area		
⑦	Harner Singh	✓		— " —		
⑧	Kanti Lal	✓		— " —		
⑨	Dileep Singh	✓		— " —		
⑩	Mufresh	✓		— " —		
⑪	Laxman	✓		— " —		
⑫	Saroj Devi		✓	— " —		

Rajasthan Secondary Towns Development Sector Project (RSTDSP)
RUDP Phase-IV

Consultation Sheet

Place: Bus Stand Area town, Durgam puri Date: 13/10/2022

Topic Discussed During Consultation:

1. Discussions with local public and nearby households
2. regarding water supply & sewerage facilities in town

Sl. No.	Name	Gender		Address	Contact No.	Signature
		Male	Female			
1	Sunil Lal	✓		near Bus Stand Area		Sunil Lal
2	Singh		✓	— + —		
3	Rajni Lal	✓		— + —		Rajni Lal
4	Jeetu Lal	✓		— + —		Jeetu Lal
5	Vencho		✓	— + —		
6	Ashwani	✓		Old Bus Stand		Ashwani
7	Mehra		✓	— + —		
8	Uday Singh	✓		— + —		
9	Chagan Lal	✓		— + —		Chagan Lal
10	Dilip Singh	✓		— + —		Dilip Singh
11	Satish Khan	✓		Bus Stand Road		Satish Khan
12	Jitencho Patel	✓		— + —		Jitencho Patel

Rajasthan Secondary Towns Development Sector Project (RSTDSP)

RUDP Phase-IV

Consultation Sheet

Place: Ward No 3 (old) / 4 (New) near 28/04/2022

Topic/Issue: WTPM Consultations with Scheduled Tribes for Sewerage and Water Supply Project in Durgam puri Town

Sl. No.	Name	Occupation	Mobile no.	Signature
1.	Ranjita Karmachand (Shil)	Student	—	
2.	Veli Ba Karmachand (Shil)	Housewife	9119315120	
3.	Shashila Devi Shil	Housewife	—	
4.	Sadifa Devi Shil	Housewife	—	
5.				

Rajasthan Secondary Towns Development Sector Project (RSTDSP)
RUIDP Phase-IV
Consultation Sheet

Place: Chairman Nagar Parishad, Dungarpur Date: 05/04/2023
 Topic/Issue: Meeting With Chairman Nagar Parishad, Dungarpur

S.No	Name	Occupation	Mobile no.	Signature
1.	Amritlal Kolasia	Chairman Nagar Parishad	9950268111	
2.	Bhupesh Sharma	Electric Ward Parishad	9950268111	
3.	Babulal Saini	"	9950268111	
4.	Naresh Yadav	"	9950268111	
5.	Pankaj Jain	"	9950268111	
6.	Mr. Bhawna Kaur	"	9950268111	
7.	Heerika Joshi	"	9950268111	
8.	Sunanda Singh	"	9950268111	
9.	Purnima Singh	"	9950268111	

Stakeholder consultation after award of work: A stakeholder consultation meeting was organised in Dungarpur on environmental and social safe guard on 05.04.2023. Meeting was attended by about 50 peoples and the detail of stakeholder meeting is given below;

Rajasthan Secondary Towns Development Sector Project

Minutes of Stakeholder Consultation

Location: Collectorate EPD- Meeting Hall, Dungarpur

Date: 05.04.2023

Title: Stakeholder Consultation on Environment and Social Safeguard

Location: Collectorate EPD- Meeting Hall, Dungarpur

Date: 05.04.2023

Total Participants: 48 (Male: 40, Female: 8)

Objectives of Training Workshop:

The primary objective of this consultation was to enhance the knowledge on development induced social and environmental issues related to the implementation of the projects and to introduce the concept of social and environmental safeguards to address those social and environmental issues during the implementing of the projects. The training contains an awareness on social and environmental safeguard policies, best practices and operational guidelines globally practiced.

Participants:

As the module was setting the foundation to understand the concept of social and environmental safeguards, local government bodies (Municipal Council, PHED, District Administration, Forest Department) staff involved in implementation of the project would be preferred.

- Superintending Engineer of RUOP-IV, Dungarpur
- Executive Engineer RUOP-IV, Dungarpur
- Representatives of CMSC-II, Dungarpur & Jodhpur
- Representatives of EAGLE (Contractor Firm)
- Representatives of CPPC

Activity Schedule of Orientation/Training:

Stakeholder and Public Consultation program with Additional District Magistrate (ADM- Dungarpur), Chairman & Vice Chairman of Nagar Parishad Dungarpur, Elected Members of Nagar Parishad, PTO, Officials of PHED Dept., Project Implementation Unit (PIU), were


ACM
CMSC-II, PIU
RUOP, DUNGARPUR


(आरमिह जोगिता)
अतिरिक्त जिलाधिकारी
आरपीआईडीपी, पीआईयू
फंडा - बभुन, दुर्गपुर

held on 05.04.2023 at Collectorate EPD- Meeting Hall, Dungarpur. The objectives of this consultation was as follows:

- ✓ Component of proposed sewer and water supply project.
- ✓ Proposed pipe line networking
- ✓ Familiarity with the requirement of social and environment international safeguards, policies and operational guidelines that is applicable for the Rajasthan Secondary Towns Development Sector Project.
- ✓ Raising awareness on social and environment risks and implications of the subproject.
- ✓ Role of Contractor for ensure safeguard compliances during implementation of the subprojects.
- ✓ Role of local agencies for effective implementation of the subprojects and coordination with others departments for provide no-objection and others approval.
- ✓ Role of Safeguard Agency for ensure safeguard compliances and effective monitoring and reporting.

A one-day Training Workshop/ Consultation on Environmental and Social Safeguards of the Subproject at Dungarpur was conducted on 05.04.2023 at Collectorate EPD-Meeting Hall, Dungarpur.



[Signature]
ACM
CMSCTE, PU
RUDP, DUNGARPUR

[Signature]
(आचार्यजीवित)
अध्यक्ष, अभियंता
जलसु, काईसीपी, सीआईपी
पंजाब - भारत, गुजरात

Mr. Ashok Jangid (SE RUDP-PIU, Dungarpur) welcomed the distinguished guests and participants into the consultation. An agenda of consultation was briefed. He deliberated that the today consultation programme is focused on proposed project components & requirement, environmental and social issues (E&S) related to ADB funded waste water and water supply project of Dungarpur Town. He explained the objectives of the Project.



Mr. Dinesh Parmar, ACM-CMSE-II (Dungarpur) briefed about the Project Development Objectives (PDO). He explained the proposed Waste Water and Water Supply scheme of Dungarpur town & its components viz. One STP, 3 no's SPS, Pumps houses, Main holes, Rising main line, Transmission main line, House sewer & Water service connections. The project is based on O&M contract and operation and maintenance of the project assets will also be under the jurisdiction of contractor for 10 years.


ACM
CMSE-II, PIU
RUDP, DUNGARPUR


(अशोक जंगिद)
अधीक्षक अभियन्ता
आयु. वार्ड/वीपी, टीआईयू
शेख - चणुई, डुंगरपुर



Mr. Hemendra Nagar (ADM-Dungarpur) and Mr. Anrit Lal Kalsua Chairman (Nagar Palishad Dungarpur) have discussed need of this proposed project for Dungarpur City. Elected Ward Member's suggested that contractor and project implementation unit need to touch with councilors of each wards, prior to commencement of works and suggestion of councilors need to be incorporated during implementation of the project.

A power point presentation was presented by CMSC-II and CAPP Jaipur. Mr. Sujit Sharan Prasad (SDE-CAPP) presented the importance of public relation with project, woman empowerment, layout of proposed public consultation programs with project impacted persons from this project. Rajiv Sharma, Social Safeguard & Gender Specialist, CMSC-II Jodhpur briefed them about the main features of ADB safeguard policy. He deliberated that works should be undertaken in such a way that impacts should be minimized. If any impacts will be envisaged, especially livelihood, compensation shall be paid as per ADB agreed framework. Grievances mechanism will be operative throughout the project to ensure timely resolve the grievances.


ADM
CMSCII, PU
RUDP, DUNGARPUR


(अनरित लाल कालुआ)
अधीक्षक अभियन्ता
आवास एवं ईंधन विभाग
पंच - अमृत, दुर्गापुर



Dr. Mahaveer Saini, Environmental Specialist, CMSC, briefed them about the project activities and requirement of environmental monitoring periodically. He briefed about environmental laws and statutory clearances required for the project, environmental issues and mitigation measures, role and responsibility contractor to ensure environmental compliances. He emphasized that it is the responsibility of contractor to ensure that hard barricading (for sewer line) with retro-reflective arrangements for all the open trenches with GI sheets should be provided so that no person or animal can enter/fall in trench. An information board should also be firmly fixed at every such locations giving information about the duration of closure of works and contractor contact details for grievance, if any.


ACM
 CMSC II, RU
 RUIDP, DUNGARPUR


 (अपरिष्कारित)
 अधीक्षण अभियन्ता
 जल नदी विकास, पीएमई
 भेद - नदी, दुर्गपुर



During the meeting ADM suggested that quality of work should be maintained along with appropriated safety measures during the construction and work should be completed within the time limit. Chairman and some elected Parishads of Nagar Parishad gave suggestion for restoration of roads and barricading around open trenches to avoid any possibility of accidents during construction. Superintending Engineer RUDP-PU, Durgapur assured for quality of work along with adequate safety measures during construction and timely restoration.

The workshop was concluded with vote of thanks to all participants and distinguished guests by Mr. Hemendra Nagar (ADM-Durgapur).


ADM
 CMSC-II, PU
 RUDP, DURGAPUR


 (अधीक्षक जलसिंचन)
 जलसिंचन अधिकारी
 जल संचयन विभाग, पुणे
 पत्रिका - पुणे, पुणे

Attendance Sheet

**Office of The Superintending Engineer,
Project Implementation Unit (RSTSP),
RSTSP, PU - Durgapur**

Address: RSTSP, PU - Durgapur
E-mail: RSTSP.PU@ncl.nic.in

Stakeholder and Public consultation

Venue: District Collector Office - STD Meeting Hall, Durgapur
Date: 17th April 2021

ATTENDANCE SHEET

S.N.	Name of the Participant	Designation	Male/ Female	Mobile Number	Signature
ক্র.সং.	অংশগ্রহীতার নাম	পদ	পুরুষ/মহিলা	মোবাইল নং.	স্বাক্ষর
1.	Mr. Saikat Karmakar Mandal	District Collector, Durgapur			
2.	Mr. Anuraj Lal Khatun	Chairman, Nagar Parishad, Durgapur	Male	9500249111	
3.	Mr. Subirban Jais	Vice Chairman, Nagar Parishad, Durgapur	Male	9419445104	
4.	Mr. Subirban Khatun	Commissioner, Nagar Parishad, Durgapur	Male	9157727324	
5.	Hemant Kumar Singh	AS-DO	Male	9180432940	
6.	Mr. Subirban Khatun	P.O.	Male	9180432940	
7.	Charanjit Singh	AS-DO	Male	9180432940	
8.					
9.					
10.					
11.					
12.					
13.					
14.					
15.					
16.					
17.					
18.					
19.					
20.					

RSTSP/PU/DO/DO/DO

(Signature)
ACM
CMSC II, PU
RSTSP, DURGAPUR

(Signature)
(অসহীত জমিদার)
অসহীত জমিদার
আবদুল আজিজের পিসার
খোজ - মজুর, দুরগাপুর

**Office of The Superintending Engineer,
Project Implementation Unit (PIU) RUPP,
RUPP, P.O. - DUNGARPUR**

अध्यक्ष, पीयू, डुंगरपुर
Chairman, PIU, DUNGARPUR

सदस्य, पीयू, डुंगरपुर
Member, PIU, DUNGARPUR

Sr. No.	Name of the Participant सदस्य का नाम	Designation पद	Male/ Female पुरुष/महिला	Mobile Number संख्या नं.	Signature हस्ताक्षर
1					
2					
3					
4					
5					
6	Uday Kumar	P.S.O.	M	9809444444	
7	Ashok Jaisid	SE RUPP	M	9600111111	
8	Madhusudan Gera	EE RUPP	M	9876543210	
9	P.C. Chandra	Team Leader, RUPP	M	9876543210	
10	Omash Verma	ACM, CMSC	M	9876543210	
11	P. K. Chandra	Team Leader, RUPP	M	9876543210	
12	Omash Verma	ACM, CMSC	M	9876543210	
13	P. K. Chandra	Team Leader, RUPP	M	9876543210	
14	Omash Verma	ACM, CMSC	M	9876543210	
15	P. K. Chandra	Team Leader, RUPP	M	9876543210	
16	Omash Verma	ACM, CMSC	M	9876543210	
17	P. K. Chandra	Team Leader, RUPP	M	9876543210	
18	Omash Verma	ACM, CMSC	M	9876543210	
19	P. K. Chandra	Team Leader, RUPP	M	9876543210	
20	Omash Verma	ACM, CMSC	M	9876543210	
21	P. K. Chandra	Team Leader, RUPP	M	9876543210	
22	Omash Verma	ACM, CMSC	M	9876543210	
23	P. K. Chandra	Team Leader, RUPP	M	9876543210	
24	Omash Verma	ACM, CMSC	M	9876543210	
25	P. K. Chandra	Team Leader, RUPP	M	9876543210	
26	Omash Verma	ACM, CMSC	M	9876543210	
27	P. K. Chandra	Team Leader, RUPP	M	9876543210	
28	Omash Verma	ACM, CMSC	M	9876543210	
29	P. K. Chandra	Team Leader, RUPP	M	9876543210	
30	Omash Verma	ACM, CMSC	M	9876543210	
31	P. K. Chandra	Team Leader, RUPP	M	9876543210	
32	Omash Verma	ACM, CMSC	M	9876543210	

KOTOP/CMSC/2020/01

ACM
CMSC/PIU
RUPP, DUNGARPUR

(अध्यक्ष पीयू)
अध्यक्ष, पीयू, डुंगरपुर
पता - बलुवा, डुंगरपुर

S.No.		Name of the Participant		Designation		Date/Time		Mobile Number		Signature	
Sl. No.		Name of the Participant		Designation		Date/Time		Mobile Number		Signature	
01		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
02		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
03		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
04		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
05		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
06		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
07		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
08		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
09		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
10		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
11		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
12		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
13		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
14		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
15		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
16		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
17		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
18		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
19		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
20		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
21		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
22		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
23		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
24		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
25		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
26		[Signature]		[Signature]		[Signature]		[Signature]		[Signature]	
27		[Signature]		[Signature]							

ACM
CNSC II, PU
RUDIP, DUNGARPUR

(असोज-२०७३)
अध्यक्ष, अभियान
आनन्द, काठमाडौं, पोखरा
फोन - ९७७९९, ९७७९९

[illegible]

ACM
OVSCEI, PU
RUDIP, DUNGARPUR

(अष्टादश पंक्तिः)
अष्टादश पंक्तिः
अष्टादश पंक्तिः
अष्टादश पंक्तिः
अष्टादश पंक्तिः

Meeting Notice



Office of The Superintending Engineer,
Project Implementation Unit (RSTSEPI),
RUIDP, PTU - Durgapur



Address: RUIDP, PTU-Durgapur

Tel: 8220432314, 8220432315, 8220432316, 8220432317, 8220432318

E-mail: se@ruidp.org, se@ptu.org

Date: 21.03.2023

INVITATION FOR STAKEHOLDERS & PUBLIC CONSULTATION

RUIDP-PTU, Durgapur has scheduled a Stakeholder Meeting to be held in the chairmanship of District Collector, Durgapur on about 05.04.2023 at Collectorate EFD Meeting Hall, Durgapur for Durgapur Water Supply and Sewerage Project Under RUIDP-IV(Trench-B) to create awareness about design aspects of Durgapur Water Supply, layout of water supply project and Sewerage Project, implementation of environment management plan, environment & social safeguards, and provisions for safety during construction and operation phases.

Organizer: RUIDP - PTU, Durgapur

Venue: Collectorate EFD Meeting Hall, Durgapur

Date & Time: 05.04.2023 Time 03:00 PM


Syed Khatun Jangir
Superintending Engineer,
RUIDP, PTU, Phase IV,
Durgapur
Date: 21.03.2023

Tel: 8220432314, 8220432315, 8220432316, 8220432317, 8220432318

Copy to following for information and kind request to attend meeting:-

1. The District Collector, Durgapur
2. The Addl. Project Director, RUIDP Jaipur
3. Chairman, Nagar Palika, Durgapur
4. Vice-Chairman, Nagar Palika, Durgapur
5. Commissioners, Nagar Palika, Durgapur are requested to inform all councillor to participate in program.
6. Superintending Engineer Executive Engineer, Durgapur
7. Superintending Engineer Executive Engineer, PHED, Durgapur
8. Superintending Engineer Executive Engineer, AYVNL, Durgapur
9. Superintending Engineer Executive Engineer, PWD, Durgapur
10. Executive Engineer, RUIDP, PTU, Durgapur Nagawa
11. Forest Range Officer, Rajasthan Forest Department, Durgapur
12. Team Leader, CMSC-II, Zone - Jaipur
13. Team Leader, CAPP, Jaipur
14. Team Leader, PMCB, Jaipur
15. Assistant Construction Manager, CMSC-II, Durgapur Nagawa
16. District Information Officer, Durgapur
17. Contractor M/s Eagle Infra India Ltd., Durgapur
18. NODs: _____


Superintending Engineer,
RUIDP, PTU, Phase IV,
Durgapur
RUIDP/PMU/IGW/02


ACM
CMSC-II, PMU
RUIDP, DURGAPUR


(अश्विनी खातिवाल)
अधीक्षक अभियंता
नगरपालिका, बीकानेर,
फोन - 3494, दुरगपुर



पत्रिका



Guard



Test

3 स्वच्छ जलाशय और 5 पम्प हाउस बनेंगे, 190 किमी पाइप लाइन होगी



पत्रिका
ग्राउंड
रिपोर्ट

इंदूरपुर शहर में
जलप्रदाय व सीवरेंज
परियोजना के लिए
210.81 करोड़ स्वीकृत
परिष्कार न्यून में

[illegible]

सोवियत में समाधान किया जाये।
सुधा काशी में सम्मेलन में था।
सह पीपुल्स सभाओं अमुन नए
कलामुआ में भी प्रवेश कर रहे।
आपुल्लोवों के अतिथि
संभागत अनेक लोग न
समाजिक औरकाल औरकाल
में प्रवेशक के लगे कि न
कलेकाली को प्रवेशक समाज में।
इसमें समाज कि दूसरे के लिए
सर्वोत्तम समाज में न सोवियत
सोवियत के लिए 1968 में
को भी प्रवेशक को था।

जनसुविधा से जुड़े ये काम होंगे

॥ श्रीगणेशाय नमः ॥

[illegible]

ACM
CNSEII, MU
RIJOP, DUNGARPUR

(असाध्य-जानिज)
असौख्य अनियन्ता
असौख्य असौख्य, असौख्य असौख्य
असौख्य - असौख्य असौख्य

Appendix 7: Integrated Biodiversity Assessment Tool World Bank Group Biodiversity Risk Screen DUNGARPUR_STP



Integrated Biodiversity Assessment Tool


World Bank Group Biodiversity Risk Screen

DUNGARPUR_STP

- Country: India
- Location: (23.9, 75.7)
- IUCN Red List Biomes: Freshwater Terrestrial
- Created by: Helena Walcott

Overlap with:

Protected Areas	1 km: 0	10 km: 0	50 km: 0	0
World Heritage (WH)	1 km: 0	10 km: 0	50 km: 0	0
Key Biodiversity Areas	1 km: 0	10 km: 0	50 km: 2	2
Adverse for Zero Extinction (AZE)	1 km: 0	10 km: 0	50 km: 0	0
IUCN Red List	14			
Critical Habitat	Likely			

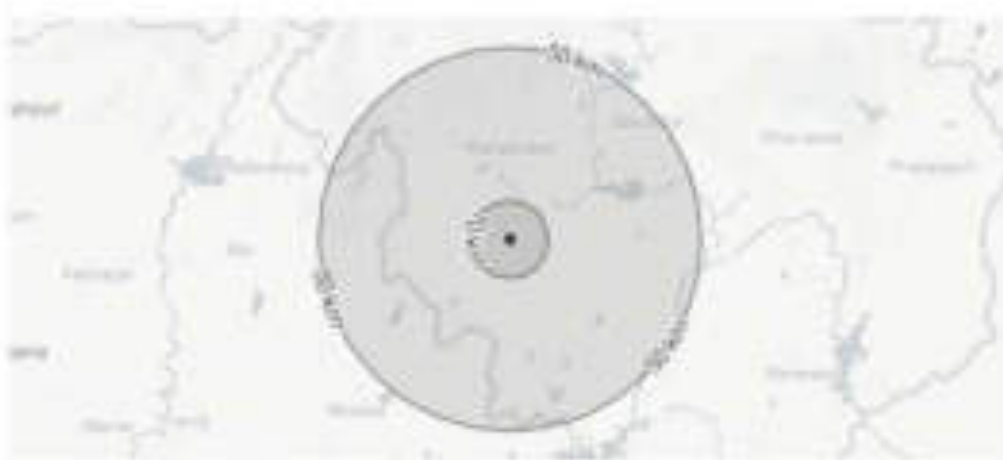

Displaying project location and buffers: 1 km, 10 km, 50 km



This report is based on IFC Performance Standard 6 (PS6) but applies to World Bank-financed projects of Social Obsolescence 2 (SO2).





About this report

The recommendations stated alongside any Protected Areas and Key Biodiversity Areas identified in this report are determined by the following:

Protected Areas:

- Highest risk, 'seek expert help' is stated if the report identifies a designation that includes either 'natural' or 'semi-natural' habitats.
- Assess for Critical Habitat is stated if the report identifies a Strict Nature Reserve, Wilderness Area or National Park associated by IUCN protected area categories Ia, Ib and Ic.
- Assess for biodiversity risk is stated if the report identifies any other type of protection area.

Key Biodiversity Areas:

- Highest risk, 'seek expert help' is stated if the report identifies an Alliance for Zero Extinction site.
- Assess for Critical Habitat is stated if the report identifies Critically Endangered or Endangered species. All species with restricted ranges OR congregatory species are coded in the IUCN Red List of Threatened Species.
- Assess for biodiversity risk is stated if the report identifies any other type of Key Biodiversity area.

IBAT provides initial screening for Critical Habitat values. Parliament (Standard 6) (PS6) defines these values for Critical Habitat (PS6, para. 19) and legally protected and internationally recognized areas (PS6, para. 20). PS6 will be triggered when FC client activities are located in modified habitats containing "significant biodiversity values," natural habitats, Critical Habitats, legally protected areas, or areas that are internationally recognized for biodiversity. References to PS6 and Guidance Notes (GN6) are provided to guide further assessment and detailed deliberations where necessary. Please see <https://www.ibat.org.au> for full details on PS6 and GN6.

The report screens for known risks within a standard three metre buffer of the coordinates used for analysis. This buffer is not intended to indicate the area of impact. The report can be used to:

- Scope risks to include within an assessment of risks and impacts
- Identify gaps within an existing assessment of risks and impacts
- Prioritize between sites as a portfolio for further assessment of risks and impacts
- Inform a preliminary determination of Critical Habitat
- Assess the need for engaging a biodiversity specialist
- Identify additional conservation experts or organizations to inform further assessment or planning

WARNING: IBAT aims to provide the most up-to-date and accurate information available at the time of analysis. There is however a possibility of incomplete, incorrect or out-of-date information. All findings in this report must be supported by further desktop review, consultation with experts and/or on the ground field assessment as described in PS6 and GN6. Please consult IBAT for any additional disclosures or recommendations applicable to the information used to generate this report.

Please note, sensitive species data are currently not included in IBAT reports in line with the [Conservation Data sharing Restrictions Policy for the IUCN Red List](https://www.ibat.org.au). This means in sensitive threatened species and areas flagged by sensitive species.



KNOW YOUR
ENVIRONMENT



IBAT
BIOLOGICAL
ASSESSMENT



Legal disclaimer

The Integrated Sustainability Assessment Tool (ISAT) and ISAT products, which include the ISAT Portal, reports, and data, are owned by ISAT Alliance and accessible by paid subscription.

The ISAT and ISAT products may contain references to or include content owned and provided by the International Bank for Reconstruction and Development ("IBRD"), the International Development Association ("IDA"), the International Finance Corporation ("IFC"), the Multilateral Investment Guarantee Agency ("MIGA"), and the International Center for Settlement of Investment Disputes ("ICSID"), collectively the "World Bank Group" or "WBG", individually the "WBG Member". The content owned and provided by the WBG Members (the "Member Content") is the respective property of the WBG Member and is protected under general principles of copyright.

The use of Member Content in ISAT and ISAT products is under license and intended for informational purposes only. Such use is not intended to constitute legal, accounting, or investment advice, an opinion regarding the appropriateness of any investment, or a solicitation of any type. Additionally, the information is provided on a strictly "as is" basis, without any assurance or representation of any kind.

The WBG Member does not guarantee the accuracy, reliability, or completeness of any Member Content included in ISAT or ISAT products or for the conclusions or judgments described therein. The WBG Member accepts no responsibility or liability for any omissions or errors (including, without limitation, typographical errors and technical errors) in any Member Content whatsoever or for reliance thereon. The trademarks, logos, service marks, and other information shown on any ISAT or ISAT do not imply any judgment on the part of WBG Member concerning the legal status of any facility or the endorsement or acceptance of such facilities. The findings, interpretations, and conclusions expressed in the ISAT and the ISAT products do not necessarily reflect the views of the WBG Member, its member countries, Executive Directors, or the governments it represents.

The WBG Members are international organizations established under their respective constituent agreement among their member countries. IBRD owns the WBG logo and trademark. The logo and other trademarks, service marks, graphics of a WBG Member are the trademarks, trademarks or registered trademarks of that WBG Member (the "WBG Member Mark"). The WBG logo and trademark and WBG Member Marks may not be copied, imitated, or used, in whole or in part, without the prior written permission of WBG or its Members, as appropriate. All other patents, copyrights, and licenses, including subsidiary rights, should be addressed as follows: I to IFC, to IFC Corporate Relations Department, 2701 Pennsylvania Avenue, N.W., Washington, D.C. 20003; I to MIGA, to MIGA Legal Affairs and Claims Group (aka Chief Counsel, Operations & Policy), 1015 H Street, N.W., 10th Floor, Washington, D.C. 20003; I to IDA and/or IIA, to the Office of the Publisher, The World Bank, 1818 H Street, N.W., Washington, D.C. 20433; Email: copyright@worldbank.org





Priority Species

Habitat of significant importance to priority species will trigger Critical Habitat status (see Table, page 16). IBAT provides a preliminary list of priority species that could occur within the Silesia buffer. This list is drawn from the IUCN Red List of Threatened Species (IUCN). This list should be used to guide any further assessment, with the aim of confirming known/likely occurrence of these species within the project area. It is also possible that further assessment may confirm occurrence of additional priority species not listed here. It is strongly encouraged that any new species information collected by the project be shared with species experts and/or IUCN whenever possible in order to improve IUCN datasets.

IUCN Red List of Threatened Species - CR & EN

The following species are sporadically found within portions of the area of interest. For the full IUCN Red List please refer to the associated data or report table.

Species Name	Common Name	Taxonomic Group	IUCN Category	Population Trend	Status
<i>Hydrophis stoliczkae</i>	Yellow Gorgon	Aves	EN	Decreasing	Threatened, Freshwater
<i>Colinus pectoratus</i>	Black-bellied Tern	Aves	EN	Decreasing	Threatened, Freshwater
<i>Helostoma temminckii</i>	Pollack Fish	Aves	EN	Decreasing	Threatened, Freshwater
<i>Neophila pinnatifida</i>	Egyptian Warbler	Aves	EN	Decreasing	Threatened, Freshwater
<i>Fulica chloei</i>	Gull Warbler	Aves	EN	Decreasing	Threatened, Marine, Freshwater
<i>Upupa epops</i>	Greater Auklet	Aves	EN	Decreasing	Threatened, Freshwater
<i>Synaldis yersini</i>	Least Tern	Aves	CR	Decreasing	Threatened
<i>Vireo gilvus</i>	Double Lining	Aves	CR	Decreasing	Threatened





Species Name	Common Name	Taxonomic Group	IUCN Category	Population Trend	Status
Giant Kingbird	White-capped Vulture	AVES	CR	Decreasing	Threatened
Common Kingbird	Red-headed Vulture	AVES	CR	Decreasing	Threatened
Giant Ibis	Ibis Vulture	AVES	CR	Decreasing	Threatened
Common Ibis		MACROPODIA	CR	Decreasing	Threatened
Marsh Macropod	Ibis Macropod	MAMMALIA	EN	Decreasing	Threatened
Apple Macropod	Green Eagle	AVES	EN	Decreasing	Threatened

Restricted Range Species

Species Name	Common Name	Taxonomic Group	IUCN Category	Population Trend	Status
White Ibis	Flamingo	POLYPODIPEDIA	LCR/LULC	Decreasing	Endangered
Common Ibis	Spotted Ibis	ACTINOPTERYGIA	LCR/LULC	Unknown	Marsh Endangered
Marsh Macropod	Great River Ibis	MALACOSTRACA	LCR/LULC	Unknown	Endangered





Biodiversity features which are likely to trigger Critical Habitat

Protected Areas

There are no protected areas to show for this report.

Key Biodiversity Areas

The following key biodiversity areas are found within 1 km and 10 km and 50 km of the site of interest.
For further details please refer to the associated csv file in the report folder.

Area Name	Distance	10k	50k	Recommendation
Jacksonville Lake and Wildlife Sanctuary	50 km	Yes	Yes	Assess for critical habitat.
Padonah Wildlife Sanctuary	50 km	Yes	No	Assess for critical habitat.

Species with potential to occur

Area Taxonomic group	Total assessed species	Total (CR, EN & VU)	CR	EN	VU	NT	LC	DD
AVES	319	25	5	7	8	12	39	0
REPTILIA	51	4	11	0	4	4	40	1
MAMMALIA	67	8	0	1	8	3	39	0
ACTINOPTERYGII	41	2	0	0	2	2	35	1
AMPHIBA	9	0	0	0	0	0	9	0
INSECTA	45	0	0	0	0	0	44	1
GASTROPODA	24	0	0	0	0	0	24	0



KNOW YOUR
ENVIRONMENT



LEARN HOW



Area Taxonomic group	Total assessed species	Total ICR, EN & VU	CR	EN	VU	NT	LC	DD
POLYPODIUM	2	0	0	0	0	0	2	0
GRAMINEAE	41	1	1	0	0	0	39	1
LEGUMINOSAE	49	1	11	0	1	0	46	2
ERICACEAE	10	0	0	0	0	0	10	0
MALACOSTRACA	8	0	0	0	0	0	8	0
NUCIFERAE	1	0	0	0	0	0	1	0
AGNATHOMYCTES	1	0	0	0	0	0	1	0



Recommended citation

IBAT. 2016. 2016 Report. Generated under license 6278-33484 from the Integrated Biodiversity Assessment Tool on 26 April 2017 (IBAT). www.ibat.biodiversity.gov.uk/

Recommended Experts and Organizations

For projects located in Critical Habitat clients must ensure that relevant experts with regional expertise are involved in further assessment (2040-1022). Clients are encouraged to develop partnerships with recognized and credible conservation organizations and/or academic institutes, especially with respect to potential developments in natural or Critical Habitat (2040-1023). Where Critical Habitat are triggered by priority species, species specialists must be involved. IBAT provides data originally collected by a large network of national partners, while species information is sourced via the IUCN Red List and affiliated species specialist groups. These experts and organizations are listed below. Please note that this is not intended as a comprehensive list of organizations and experts. These organizations and experts are under no obligation to support any further assessment and do so entirely at their discretion and under their terms. Any views expressed or recommendations made by these stakeholders should not be attributed to the IFC or IBAT for IFC partners.

BirdLife Partners

URL: <http://www.birdlife.org/worldwide/partners/taxa-life-partners>

Directory for Species Survival Commission (SSC) Specialist Groups and Red List Authorities

URL: <http://www.iucn.org/our-work/species-conservation/red-list>



KNOW YOUR
ENVIRONMENT



LEARN MORE

Appendix 8: Photographs of Proposed Component Locations and Existing components**Proposed Site-RWR-Bori HW****Proposed Site for CWR-Chand Pole HW****Proposed site for CWR-New Colony HW**

	
Proposed site of STP- Near Do River, Udaipur Road	
	
Proposed SPS site-Near Pandaya Circle	
	
Proposed SPS site-Ashram Vatika	
	
Proposed SPS site-Near Gap Sagar	

Appendix 9: Water Test Report of PHED lab Dungarpur

OFFICE OF THE JUNIOR CHEMIST
PUBLIC HEALTH ENGINEERING DEPARTMENT, Lab Dungarpur(Raj.)
REPORT ON THE ANALYTICAL EXAMINATION OF WATER

MLL Lab Test Charges 2018-2019: 54 - 53 Date: 20.08.2018
 To: (Initials): DFR
 To: (Initials): DFR

Asstt. Engineer
 PHED City Sub Div. Dungarpur
 P.O. No. 444/1812/18.08.2018

Name of Sample Taken: Govt. Staff


Source	Raw Water	Filter Water	Raw Water	Filter Water
Source Location	Raw Water Works	Raw Water Works	Filter Water Works	Filter Water Works
	R.T.	R.T.	R.T.	R.T.
Village Name & No.	Dungarpur	Dungarpur	Dungarpur	Dungarpur
Block name	Dungarpur	Dungarpur	Dungarpur	Dungarpur
Village Code No.	Dungarpur	Dungarpur	Dungarpur	Dungarpur
Date of Collection	14.08.2018	14.08.2018	14.08.2018	14.08.2018
Date of Examination	14.08.2018	14.08.2018	14.08.2018	14.08.2018
Lab Sample No.	100	101	102	103

Note: All reports to come pH are in mg/L

S. No.	Parameter	1	2	3	4
1	pH	7.4	7.2	7.4	7.4
2	Hardness (ppm)	140	140	140	140
3	Temporary Hardness (ppm)	None	None	None	None
4	Calcium Hardness (ppm)	None	None	None	None
5	Magnesium	0.01	0.01	0.01	0.01
6	Total Alkalinity (as CaCO ₃)	80	80	80	80
7	Total Hardness (as CaCO ₃)	140	140	140	140
8	Calcium Hardness	80	80	80	80
9	Magnesium Hardness	80	80	80	80
10	Chloride (as Cl ⁻)	80	80	80	80
11	Sulfate (as SO ₄ ²⁻)	4	4	4	4
12	Iron (as Fe)	0.15	0.12	0.07	0.10
13	Total Dissolving Solids	140	140	140	140

Appendix 10: Lab Test Report of Environment Monitoring

i. Soil Quality Test Report



SKS Test Labs Private Limited
 Multi-Element Analysis | ISO 9001:2015 | ISO 17025:2017



Test Report

Sample Number: 20230224

Name & Address of the Party

Shri. Rakesh Kumar Singh (Client)
 (Sample for Heavy Metals Analysis - Soil)
 Sample No. - 20230224 (Sample No. 20230224)
 123-45-67890 (Sample No. 123-45-67890)
 Sample No. 123-45-67890 (Sample No. 123-45-67890)

Sample Description

Soil

Location

123-45-67890 (Sample No. 123-45-67890)

Sample Collected by

SKS Test Labs (Sample No. 123-45-67890)

Parameter Requested

Heavy Metals Analysis

Sampling and Analysis

123-45-67890 (Sample No. 123-45-67890)

Method

Report No.

202302240000000000

Report No.

20230224

Party Reference No.

123

Report Date

12/02/2023

Period of Validity

12/02/2023 - 12/02/2024

Report Issue

12/02/2023

Sampling Date

12/02/2023

Sampling Quantity

1 kg

Sampling Type

12/02/2023

Sampling Method

12/02/2023

Sl. No.	Parameter	Test Method	Result	Unit
1	Lead (Pb)	GB 12345 (Pb) - 2023	1.21	mg/kg
2	Chromium (Cr)	GB 12345 (Cr) - 2023	0.05	mg/kg
3	Cadmium (Cd)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
4	Copper (Cu)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
5	Iron (Fe)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
6	Aluminum (Al)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
7	Fluorine (F)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
8	Chlorine (Cl)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
9	Sulfur (S)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg
10	Carbon (C)	Lead (Pb) No. 12345 (Pb) - 2023 (Sample No. 123-45-67890) Date: 12/02/2023	0.01	mg/kg




202302240000000000

Page No. 1/1

Plot No. 123, Block-12, New Delhi, India - 110001, New Delhi
 Tel: 123-456789, 9876543210
 Email: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
 ISO 9001:2015 Certified | ISO 17025:2017 Certified | ISO 14001:2015 Certified



Test Report

Sample Number: SKS/2023/012

Name & Address of the Party

M/S. Kapsala India Private Limited
 (Manufacturing Company) - Plot - 1, Sector - 1
 Postage No. - 401004, Chhatrapati Shivaji Maharaj
 117-01, Kapsala India Private Limited, India - 401004
 Pune Region, Maharashtra, India - 401004

Sample Description

SKS

Location

SKS - 1, Near Shree Kapsala India Private Limited

Sample Collected by

SKS Team (Mr. Anand)

Tester/Analyst

Mr. Anand

Sampling and Analysis
 Period

10/10/2023, 10/10/2023

Report No.

SKS/2023/012/001

Report No.

SKS/2023/012/001

Party Reference No.

SKS

Report Date

10/10/2023

Period of Analysis

10/10/2023 - 10/10/2023

Sample Size

10/10/2023

Sampling Date

10/10/2023

Sampling Quantity

1 kg

Sampling Type

Composite

Testing Method

Temp. Method

S. No.	Parameters	Test Method	Result	Units
1	pH (at 25°C)	IS - 3156 (P-20) 2015	7.21	-
2	Refractive Index	IS 14707: 2000	1.275	refractive
3	Moisture (as %)	Lab SOP No. SKS/2023/012/001 Issue No. 01, Date 10/10/2023	107.74	mg/kg
4	Moisture (as %)	ISO 15925:2005 Method 1A (Page 40) No. 2015	45.25	mg/kg
5	Protein (as %)	Lab SOP No. SKS/2023/012/001 Issue No. 01, Date 10/10/2023	115.20	mg/kg
6	Organic Matter	IS 3156 (P-20) 2015	0.80	%
7	Moisture (as %)	Lab SOP No. SKS/2023/012/001 Issue No. 01, Date 10/10/2023	107.74	mg/kg
8	Available Nitrogen (as %)	IS - 15925:2005 No. 2015	10.44	mg/kg
9	Soil Moisture	Lab SOP No. SKS/2023/012/001 Issue No. 01, Date 10/10/2023	0.81	%




SKS/2023/012/001

Page No. 1/1

Plot No. 25, Sector 1, Kapsala India Private Limited, Chhatrapati Shivaji Maharaj
 Postage No. 401004, Chhatrapati Shivaji Maharaj, 117-01, Kapsala India Private Limited, India - 401004
 E-mail: info@skstestlabs.com

www.skstestlabs.com


SKS Test Labs Private Limited

Road # 12, Newgate, 100 000 (100 000) (100 000) (100 000)


Test Report

Sample Number : 20200001

Name & Address of the Party :

 SKS Test Labs Private Limited
 (Overseeing Engineer - PWD - PWD - Government)
 Package No. - 20200001/20200001/20200001
 Lot No. - 20200001/20200001/20200001
 Project Master No. - 20200001/20200001/20200001

Report No : 20200001/20200001/20200001

Format No : 100001

Party Reference No : 100

Report Date : 20200001

Period of Analysis : 20200001/20200001/20200001

Report Date : 20200001

Sampling Date : 20200001

Sampling Quantity : 100g

Sampling Type : Composite

Packing Method : Tare, Sealed

Sample Description :

- 100g

Location :

- 100g

Sample Collected by :

- 100g

Forwarder Reported :

- 100g

Sampling and Analysis :

- 100g

S. No.	Parameter	Test Method	Result	Unit
1	Moisture (%)	IS 2710 (1970) 1997	1.01	%
2	Electrical Conductivity	IS 14707 (2001)	0.005	microhm
3	Chloride (mg/kg)	Lab 277 No. 20200001/20200001/20200001 Date 01.07.2020	00.15	mg/kg
4	Sulfate (mg/kg)	Lab 277 No. 20200001/20200001/20200001 Date 01.07.2020	00.01	mg/kg
5	Fluoride (mg/kg)	Lab 277 No. 20200001/20200001/20200001 Date 01.07.2020	00.01	mg/kg
6	Organic Matter	IS 2710 (1970) 1970	0.71	%
7	Magnesium (mg/kg)	Lab 277 No. 20200001/20200001/20200001 Date 01.07.2020	00.01	mg/kg
8	Available Nitrogen (mg/kg)	IS 10000 (1980) 1980	00.01	mg/kg
9	Iron (mg/kg)	Lab 277 No. 20200001/20200001/20200001 Date 01.07.2020	00.01	%




SKS Test Labs Private Limited

Page No. 01

 Plot No. 20, Block-B, Newgate, 100 000, Rajasthan
 Tel: 817-260440, 907020000, 90714720
 E-mail: info@skstestlabs.com

www.skstestlabs.com


SKS Test Labs Private Limited

Multi-Store Bangladesh | 100-1000 | 100-1000 | 100-1000


Test Report

Sample Number: 100-1000

Name & Address of the Party: SKS Test Labs Private Limited

 (Superintending Engineer, R.O.P., 1st Floor, Government
 Postage No. 100-1000, Dhaka-1000)
 100-1000, Dhaka-1000, Add: 1st Floor
 Police Hospital, No. 100-1000, 2nd Floor, Dhaka-1000

Sample Description:

Location:

Sample Collected by:

Parameter Requested:

 Sampling and Analysis
 Protocol:

100-1000, APHA & L1000

Report No.: 100-1000-1000-1000

Format No.: 100-1000

Party Reference No.:

Report Date: 100-1000

Period of Analysis: 100-1000-1000-1000

Receipt Date: 100-1000

Sampling Date: 100-1000

Sampling Quantity: 100-1000

Sampling Type: 100-1000

Packing Status: 100-1000

S. No.	Parameter	Test Method	Result	Unit
1	Ammonia Nitrogen	APHA 100-1000	0.11	mg/L
2	Electrical Conductivity	100-1000	0.11	mg/L
3	Dissolved Oxygen	Lab SOP No. 100-1000 Issue No. 01, Issue Date 01-01-2020	100-1000	mg/L
4	Dissolved Oxygen	100-1000 Method No. (Page 01) No. 100-1000	100-1000	mg/L
5	Dissolved Oxygen	Lab SOP No. 100-1000 Issue No. 01, Issue Date 01-01-2020	100-1000	mg/L
6	Dissolved Oxygen	100-1000 Method No. (Page 01) No. 100-1000	100-1000	mg/L
7	Dissolved Oxygen	Lab SOP No. 100-1000 Issue No. 01, Issue Date 01-01-2020	100-1000	mg/L
8	Dissolved Oxygen	100-1000 Method No. (Page 01) No. 100-1000	100-1000	mg/L
9	Dissolved Oxygen	Lab SOP No. 100-1000 Issue No. 01, Issue Date 01-01-2020	100-1000	mg/L




100-1000-1000-1000

Page No. 01

 Plot No. 25, Block D, Narayan Vihar, Jangal - 30000, Rajshahi
 Tel: 0141-290000, 0141-290000, 0141-290000
 E-mail: info@skstestlabs.com

www.skstestlabs.com

www.ashmoleanm.com



Test Report

Executive Summary [Download](#)

Source: http://www.bbc.co.uk/1/health/2005/05/050523_heart_disease.shtml

© 2004 Blackwell Publishing Ltd *Journal of Internal Medicine* 255: 103–110

Supervising Engineer RACGP, Pty, Queensland

Postage No. www.usps.gov

© 1997 by American Psychological Association or one of its allied publishers. This article is intended solely for the personal use of the individual user and is not to be disseminated broadly.

Group Accounts for Home Sales & Major Expenditures

Estimating the Weight

Strong female leadership

100

1976. / *Seag Street Pathways and Street Signs*

Stacy A. Greenwald, PhD

gung Thakur (1881–1890)

Agreement is required.

Conclusions and Perspectives

Sampling and methods

[illegible]

© 2004 Blackwell Publishing Ltd *Journal of Internal Medicine* 255: 103–110

[illegible]

Copyright © 2004 John Wiley & Sons, Ltd.

Source: *U.S. Census Bureau, Current Population Reports, 1990*

Source: *Author's calculations*.

Page 10 of 10

Prepared at Bangalore: 08/02/2007 11:45:00 AM

[illegible]

Sampling Date	8/20/2004

Sampling Quantity: 100 ml

Sampling Type	Count

Lengthwise

LEARNING OBJECTIVES

S. No.	Test Parameters	Test Method	Result	Unit	Limit as Per IS: 10500:2012	
					Acceptable Limit	Permissible Limit
1	pH	IS: 3025 (P-11): 2002	7.35	-	6.5 to 8.5	No Restriction
2	Chloride (as Cl ⁻)	IS: 3025 (P-22): 1999	264.17	mg/L	250	1000
3	Fluoride (as F ⁻)	APHA (22nd Edition): 800010: 2017	0.21	mg/L	0.2	1.0
4	Nitrate (as NO ₃ ⁻)	IS: 3025 (P-28): Chlorimetric Method: 1999	13.31	mg/L	45.0	No Restriction
5	Heavy Metals (as)	ISPH 230: 2000: 80001: 2017	16.27*100 < 0.1	mg/L	0.01	0.01
6	Sulfate (as SO ₄ ²⁻)	IS: 3025 (P-24)Sec 1: 2002	81.95	mg/L	300	400
7	Total Dissolved Solids (TDS)	IS: 3025 (P-25): 1999	426.29	mg/L	500	500
8	Total Dissolved Solids	IS: 3025 (P-25): 1999	1140.2	mg/L	500	500
9	Total Hardness (CaCO ₃)	IS: 3025 (P-25): 2000	320.3	mg/L	300	300
10	Copper (as Cu)	APHA (22nd Edition): 80001: 81100: 2017	16.22*100 < 0.005	mg/L	0.05	No Publication
11	Zinc (as Zn)	APHA (22nd Edition): Method No. 81100: 2017	16.22*100 < 0.01	mg/L	0.05	1.0
12	Iron (as Fe)	IS: 3025 (P-55): 2002	16.2*100 < 0.1	mg/L	1.0	No Publication
13	Lead (as Pb)	APHA (22nd Edition): 80001: 81100: 2017	16.2*100 < 0.1	mg/L	0.01	No Publication
14	Manganese (as Mn)	APHA (22nd Edition): 80001: 81100: 2017	16.2*100 < 0.05	mg/L	0.1	0.2
15	Mercury (as Hg)	APHA (22nd Edition): 81100: 2017	16.2*100 < 0.0001	mg/L	0.01	No Publication
16	Silica (as Si)	APHA (22nd Edition): 80001: 81100: 2017	16.2*100 < 0.5	mg/L	0.5	15.0
17	Alkalinity	APHA (22nd Edition): 81100: 2017	16.2*100 < 0.0001	mg/L	-	-




File No. 25, Sheet-3, Survey No. 10019, Page No. 10019

For more information, contact the author at joan@joanmiller.com.
Tel. 914-662-2122, ext. 1000; fax 914-662-2122.

© 2004 Blackwell Publishing Ltd, *Journal of Internal Medicine* 255: 105–112

www.vivestillborn.com



Test Report

Sample Number: 08060900

Name & Address of The Party We hope this letter finds you well.
Superintending Engineer R.S.P., P.O. - Gurgaon,
Haryana-60, RD-28/29/30, Sector-29
G.T.K. Road, Gurugram-122001, Haryana, India.
Phone Number: 96766 33333, 96766 33333.

Sample Description	Water Sample: Stream Water

Publication: 09/08-27 00:00:00

Images courtesy of: www.fox.com

© 2004 Blackwell Publishing Ltd

Schlagung und Weibere

700

11. ☐ **11.11.11**

Project fee: \$1000 (includes all materials and shipping)

Downloaded At: 11:53 11 September 2009

Page: 1/1

Author's address: Department of Psychology,
University of Illinois at Chicago, Chicago, IL
60607-7181, USA.
E-mail: jay@uic.edu

Report Date: 1/1/2000

Received 22 September 2005	Accepted 10 October 2005

Keywords: *depression, mood, anxiety, stress, coping, self-esteem, self-efficacy, self-compassion, self-kindness, self-compassion training, self-compassion meditation, self-compassion practice, self-compassion exercises, self-compassion techniques, self-compassion interventions, self-compassion programs, self-compassion apps, self-compassion books, self-compassion courses, self-compassion workshops, self-compassion retreats, self-compassion groups, self-compassion community, self-compassion support, self-compassion resources, self-compassion tools, self-compassion guides, self-compassion manuals, self-compassion worksheets, self-compassion handouts, self-compassion audio, self-compassion video, self-compassion podcast, self-compassion blog, self-compassion newsletter, self-compassion social media, self-compassion website, self-compassion app, self-compassion book, self-compassion course, self-compassion workshop, self-compassion retreat, self-compassion group, self-compassion community, self-compassion support, self-compassion resources, self-compassion tools, self-compassion guides, self-compassion manuals, self-compassion worksheets, self-compassion handouts, self-compassion audio, self-compassion video, self-compassion podcast, self-compassion blog, self-compassion newsletter, self-compassion social media, self-compassion website*

Keywords: *parenting stress, parenting self-efficacy, parenting practices, child adjustment, child maltreatment*


Sampling Quality: 100%

Sampling Type	Other

Longitude

S.No.	Test Parameters	Test Method	Result	Unit	Limit as Per IS: 10000:2013	
					Acceptable Limit	Permissible Limit
1	pH	IS 3020 (P-11): 2002	7.08	—	6.5 to 8.5	No Relaxation
2	Chloride (as Cl ⁻)	IS 3020 (P-32): 1999	245.49	mg/L	100	1000
3	Sulfate (as SO ₄ ²⁻)	APHA (2510 B) (Standard Method): 2017	0.10	mg/L	1.0	1.0
4	Hardness (as CaCO ₃)	IS 3020 (P-19): (Chemography Method): 1999	0.44	mg/L	450	No Relaxation
5	Phenols (as Phenol)	APHA (2540 B) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.001	0.002
6	Calcium (as Ca)	IS 3020 (P-24) (New): 2022	127.85	mg/L	300	400
7	Total Alkalinity (as CaCO ₃)	IS 3020 (P-31): 1999	913.94	mg/L	200	600
8	Total Dissolved Solids	IS 3020 (P-33): 1999	1149.4	mg/L	500	1000
9	Total Hardness (CaCO ₃)	IS 3020 (P-31): 1999	165.4	mg/L	200	500
10	Iron (as Fe)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.03	No Relaxation
11	Copper (as Cu)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.04	1.0
12	Lead (as Pb)	IS 3020 (P-34): 2002	16.32*10 ⁻³ (0.0001632)	mg/L	1.0	No Relaxation
13	Lead (as Pb)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.01	No Relaxation
14	Ammonia (as NH ₃)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.1	0.3
15	Nitrate (as NO ₃ ⁻)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.01	No Relaxation
16	Diss. (as Zn)	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	0.3	10.0
17	Arsenic	APHA (2214) (Standard Method): 2017	16.32*10 ⁻³ (0.0001632)	mg/L	—	—





SKS Test Labs Private Limited
WATER & WASTE ANALYSIS / CHEMISTRY / MICROBIOLOGY



Test Report

Sample Number: 1000000000

Name & Address of the Party:

M/s. Sagar Infra Pvt. Ltd.
Superintending Engineer (SE), (PW - Domestic)
Bhadrachalam, 507105 (P.O. - 507105)
C/O. M/s. Sagar Infra Pvt. Ltd., 2nd Floor,
Road No. 10, Sagar Infra Pvt. Ltd., Bhadrachalam.

Sample Description:

Water Sample (Drinking Water)

Location:

Drinking Water Supply Scheme

Sample Collected by:

M/s. Sagar Infra Pvt. Ltd.

Presentation:

Substrate Presentation

Sampling and Analysis

Method / Method

Lab No:

1000000000000000

Report No:

1000000000000000

Form No:

1000000000

Party Reference No:

1000000000000000

Report Date:

10/01/2020

Name of Analyst:

1000000000000000

Report Date:

10/01/2020

Sampling Date:

10/01/2020

Sampling Quantity:

100 ml

Sampling Type:

100 ml

Comments:


100 ml

S. No.	Test Parameters	Test Method	Result	Unit	Limit as Per IS: 10000:2012	
					Acceptable Limit	Permissible Limit
1	pH	IS: 3043 (P-11): 2002	8.01	—	6.5 to 8.5	No Relaxation
2	Chloride (as Cl ⁻)	IS: 3043 (P-22): 1999	10.00	mg/L	250	1000
3	Fluoride (as F ⁻)	APHA (2450) Bismuth Method, 2017	0.20	mg/L	1.5	1.5
4	Hardness (as CaCO ₃)	IS: 3043 (P-19) for Chlorimetric Method, 1999	0.00	mg/L	450	No Relaxation
5	Hardness (Temporary) (as CaCO ₃)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.10)	mg/L	0.001	0.002
6	Calcium (as Ca ²⁺)	IS: 3043 (P-23) for 1:1000	10.11	mg/L	200	400
7	Total Sulphate (as SO ₄ ²⁻)	IS: 3043 (P-23): 1999	100.12	mg/L	200	500
8	Total Dissolved Solids	IS: 3043 (P-23): 1999	400.0	mg/L	500	1000
9	Total Suspended Solids (TSS)	IS: 3043 (P-23): 2009	100.0	mg/L	200	500
10	Calcium (as Ca ²⁺)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.001	No Relaxation
11	Fluoride (as F ⁻)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.00	1.5
12	Iron (as Fe)	IS: 3043 (P-23): 2009	0.11	mg/L	1.0	No Relaxation
13	Copper (as Cu)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.01	No Relaxation
14	Manganese (as Mn)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.1	0.3
15	Barium (as Ba)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.01	No Relaxation
16	Strontium (as Sr)	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	0.1	10.0
17	Aluminum	APHA (2450) Bismuth Method, 2017	10.00 mg/L (0.00 - 0.00)	mg/L	—	—



Plot No. 25, Block B, Narayan Vihar, Jaipur - 302004, Rajasthan
Tel: 0141 2646442, 0141 2646443, 0141 2646444
E-mail: info@skstestlabs.com

www.skstestlabs.com


SKS Test Labs Private Limited

ISO 9001:2015 Certified | ISO 14001:2015 Certified



Test Report

Sample Number : 2407000005

Name & Address of the Party :

 M/s Eagle Ultra Industries
 (Superfining Engineer PWD, P.O. Bangalore)
 Package No. : 24070000050000000000
 LOT/ID : 24070000050000000000 / 24070000050000000000
 Place/Region for POC : Bldg. A, Eagle Complex

JAR No. : 11/2022/00000000000000000000

Report No. : 24070000050000000000

Format No. : 1.0.0.01

Party Reference No. : 24070000050000000000

Report Date : 11/08/2022

Period of Analysis : 08/08/2022 - 11/08/2022

Receipt Date : 08/08/2022

Sampling Date : 01/08/2022

Sampling Quantity : 2.5L

Sampling Type : 11.06

Longitude : -

Latitude : -

Sample Description :

Water Sample (Ground Water)

Location :

100ft & Pumping at PWD Office Complex

Sample Collected by :

SKS Test Lab, Bangalore

Preservation :

Cooling Preservation

Sampling and Analysis Method :

IS: 3155-1987

S. No. Test Parameters

Test Method

Result


Unit

Limit as Per IS: 3155-1987

S. No.	Test Parameters	Test Method	Result	Unit	Limit as Per IS: 3155-1987	
					Acceptable Limit	Permissible Limit
1	pH	IS: 3155 (P-1) 1987	8.21	-	6.5 to 8.5	No Restriction
2	Chloride (as Cl ⁻)	IS: 3155 (P-2) 1987	11.85	mg/L	100	1000
3	Fluoride (as F ⁻)	APHA (22nd Edition) 8000D-017	0.26	mg/L	1.0	1.0
4	Ammonia (as NH ₃)	IS: 3155 (P-3) 1987	0.05	mg/L	0.5	No Restriction
5	Phosphate (as PO ₄ -P)	APHA (22nd Edition) 8000D-017	0.02	mg/L	0.05	0.05
6	Sulfate (as SO ₄)	IS: 3155 (P-4) 1987	11.75	mg/L	100	400
7	Total Hardness (as CaCO ₃)	IS: 3155 (P-5) 1987	118.15	mg/L	100	500
8	Total Dissolved Solids	IS: 3155 (P-6) 1987	180.8	mg/L	500	2000
9	Total Suspended Solids	IS: 3155 (P-7) 1987	100.2	mg/L	100	500
10	Cadmium (as Cd)	APHA (22nd Edition) 8000D-017	0.001	mg/L	0.005	No Restriction
11	Copper (as Cu)	APHA (22nd Edition) 8000D-017	0.01	mg/L	0.05	1.0
12	Lead (as Pb)	IS: 3155 (P-8) 1987	0.01	mg/L	1.0	No Restriction
13	Iron (as Fe)	APHA (22nd Edition) 8000D-017	0.01	mg/L	0.01	No Restriction
14	Manganese (as Mn)	APHA (22nd Edition) 8000D-017	0.01	mg/L	0.1	0.5
15	Nitrate (as NO ₃)	APHA (22nd Edition) 8000D-017	0.01	mg/L	0.01	No Restriction
16	Chlorine (as Cl ₂)	APHA (22nd Edition) 8000D-017	0.2	mg/L	0.2	10.0
17	Ammonia	APHA (22nd Edition) 8000D-017	-	mg/L	-	-


 Plot No. 25, Block-B, Narayanpet Village, Jorpet - 560022, Bangalore
 Tel: 0141-2048882, 08-1111111111, 9902147298
 Email: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited

Unit 1, 2, 3, 4, 5, 6, 7, 8, 9, 10, 11, 12, 13, 14, 15, 16, 17, 18, 19, 20, 21, 22, 23, 24, 25, 26, 27, 28, 29, 30, 31, 32, 33, 34, 35, 36, 37, 38, 39, 40, 41, 42, 43, 44, 45, 46, 47, 48, 49, 50, 51, 52, 53, 54, 55, 56, 57, 58, 59, 60, 61, 62, 63, 64, 65, 66, 67, 68, 69, 70, 71, 72, 73, 74, 75, 76, 77, 78, 79, 80, 81, 82, 83, 84, 85, 86, 87, 88, 89, 90, 91, 92, 93, 94, 95, 96, 97, 98, 99, 100



Test Report

Sample Number: SKS/2023/001

Name & Address of the Party: M/s. ABC Pvt. Ltd., Plot No. 123, Sector 45, Gurgaon, Haryana - 122001

Sample Description: Drinking Water

Location: Plot No. 123, Sector 45, Gurgaon, Haryana

Sample Collected by: SKS Team (M. Sharma)

Preservation: 4°C Refrigeration

Sampling and Analysis Protocol: IS 4302:2013

SKS No.: SKS/2023/001

Report No.: SKS/2023/001

Project No.: 123456

Party Reference No.: ABC/2023/001

Report Date: 15/01/2023

Period of Analysis: 15/01/2023 - 16/01/2023

Report Date: 15/01/2023

Sampling Date: 15/01/2023

Sampling Quantity: 2 L

Sampling Type: Spot

Longitude: 76.6123

Latitude: 29.0123

S.No.	Test Parameters	Test Method	Result	Unit	Limit as Per IS: 4302:2013	
					Acceptable Limit	Permissible Limit
1	pH	IS 4302:2013 (11) 2013	7.50	-	6.5 to 8.5	No Rejection
2	Chlorine (as Cl ₂)	IS 4302:2013 (12) 1999	0.50	mg/L	0.50	1.00
3	Fluoride (as F ⁻)	APHA (2314) Chlorine Method No. 21105:2017	0.20	mg/L	1.5	1.5
4	Alkalinity (as CaCO ₃)	IS 4302:2013 (13) (Chemical) Method 2 1999	100	mg/L	400	No Rejection
5	Phosphate (as phosphate ion)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.001	0.010
6	Sulphate (as SO ₄)	IS 4302:2013 (14) (1) 2013	150	mg/L	200	200
7	Total Hardness (as CaCO ₃)	IS 4302:2013 (15) 1999	200	mg/L	200	200
8	Total Dissolved Solids	IS 4302:2013 (16) 1999	240	mg/L	200	200
9	Total Hardness (as CaCO ₃)	IS 4302:2013 (17) 2013	200	mg/L	200	200
10	Dissolved Solids	APHA (2314) Chlorine Method No. 21105:2017	10.00	mg/L	0.001	No Rejection
11	Copper (as Cu)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.01	1.0
12	Iron (as Fe)	IS 4302:2013 (18) 2013	0.10	mg/L	1.0	No Rejection
13	Lead (as Pb)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.01	No Rejection
14	Manganese (as Mn)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.1	0.2
15	Mercury (as Hg)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.01	No Rejection
16	Zinc (as Zn)	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	0.1	10.0
17	Arsenic	APHA (2314) Chlorine Method No. 21105:2017	0.010	mg/L	-	-






Plot No. 123, Sector 45, Gurgaon, Haryana - 122001, Rajasthan

Tel: 0122-2345678, 0122-2345679, 0122-2345680

E-mail: info@skstestlabs.com

www.skstestlabs.com


SKS Test Labs Private Limited


ISO 9001:2015 Certified | ISO 14001:2015 Certified | ISO 45001:2018 Certified



Test Report

Sample Number : 20230401
 Name & Address of the Party : M/s. Super Info Labs Limited
 (Manufacturing Engineer - HOD, P/O - Bangalore)
 Phone No. : 9876543210 (080) 12345678
 Email ID : info@superinfo.com
 Place : Hyderabad, India
 Report No. : SKS/20230401/001
 Format No. : T-01-01
 Party Reference No. : 2023
 Report Date : 11-04-2023
 Period of Analysis : 04/04/2023 - 11/04/2023
 Review Date : 04/04/2023

Sample Description : ABBQWT 2023
 General Information :
 Sampling Location : 2/F, 22/23/24/25/26/27/28/29/30/31/32/33/34/35/36/37/38/39/40/41/42/43/44/45/46/47/48/49/50/51/52/53/54/55/56/57/58/59/60/61/62/63/64/65/66/67/68/69/70/71/72/73/74/75/76/77/78/79/80/81/82/83/84/85/86/87/88/89/90/91/92/93/94/95/96/97/98/99/100/101/102/103/104/105/106/107/108/109/110/111/112/113/114/115/116/117/118/119/120/121/122/123/124/125/126/127/128/129/130/131/132/133/134/135/136/137/138/139/140/141/142/143/144/145/146/147/148/149/150/151/152/153/154/155/156/157/158/159/160/161/162/163/164/165/166/167/168/169/170/171/172/173/174/175/176/177/178/179/180/181/182/183/184/185/186/187/188/189/190/191/192/193/194/195/196/197/198/199/200/201/202/203/204/205/206/207/208/209/210/211/212/213/214/215/216/217/218/219/220/221/222/223/224/225/226/227/228/229/230/231/232/233/234/235/236/237/238/239/240/241/242/243/244/245/246/247/248/249/250/251/252/253/254/255/256/257/258/259/260/261/262/263/264/265/266/267/268/269/270/271/272/273/274/275/276/277/278/279/280/281/282/283/284/285/286/287/288/289/290/291/292/293/294/295/296/297/298/299/300/301/302/303/304/305/306/307/308/309/310/311/312/313/314/315/316/317/318/319/320/321/322/323/324/325/326/327/328/329/330/331/332/333/334/335/336/337/338/339/340/341/342/343/344/345/346/347/348/349/350/351/352/353/354/355/356/357/358/359/360/361/362/363/364/365/366/367/368/369/370/371/372/373/374/375/376/377/378/379/380/381/382/383/384/385/386/387/388/389/390/391/392/393/394/395/396/397/398/399/400/401/402/403/404/405/406/407/408/409/410/411/412/413/414/415/416/417/418/419/420/421/422/423/424/425/426/427/428/429/430/431/432/433/434/435/436/437/438/439/440/441/442/443/444/445/446/447/448/449/450/451/452/453/454/455/456/457/458/459/460/461/462/463/464/465/466/467/468/469/470/471/472/473/474/475/476/477/478/479/480/481/482/483/484/485/486/487/488/489/490/491/492/493/494/495/496/497/498/499/500/501/502/503/504/505/506/507/508/509/510/511/512/513/514/515/516/517/518/519/520/521/522/523/524/525/526/527/528/529/530/531/532/533/534/535/536/537/538/539/540/541/542/543/544/545/546/547/548/549/550/551/552/553/554/555/556/557/558/559/560/561/562/563/564/565/566/567/568/569/570/571/572/573/574/575/576/577/578/579/580/581/582/583/584/585/586/587/588/589/590/591/592/593/594/595/596/597/598/599/600/601/602/603/604/605/606/607/608/609/610/611/612/613/614/615/616/617/618/619/620/621/622/623/624/625/626/627/628/629/630/631/632/633/634/635/636/637/638/639/640/641/642/643/644/645/646/647/648/649/650/651/652/653/654/655/656/657/658/659/660/661/662/663/664/665/666/667/668/669/670/671/672/673/674/675/676/677/678/679/680/681/682/683/684/685/686/687/688/689/690/691/692/693/694/695/696/697/698/699/700/701/702/703/704/705/706/707/708/709/710/711/712/713/714/715/716/717/718/719/720/721/722/723/724/725/726/727/728/729/730/731/732/733/734/735/736/737/738/739/740/741/742/743/744/745/746/747/748/749/750/751/752/753/754/755/756/757/758/759/760/761/762/763/764/765/766/767/768/769/770/771/772/773/774/775/776/777/778/779/780/781/782/783/784/785/786/787/788/789/790/791/792/793/794/795/796/797/798/799/800/801/802/803/804/805/806/807/808/809/810/811/812/813/814/815/816/817/818/819/820/821/822/823/824/825/826/827/828/829/830/831/832/833/834/835/836/837/838/839/840/841/842/843/844/845/846/847/848/849/850/851/852/853/854/855/856/857/858/859/860/861/862/863/864/865/866/867/868/869/870/871/872/873/874/875/876/877/878/879/880/881/882/883/884/885/886/887/888/889/890/891/892/893/894/895/896/897/898/899/900/901/902/903/904/905/906/907/908/909/910/911/912/913/914/915/916/917/918/919/920/921/922/923/924/925/926/927/928/929/930/931/932/933/934/935/936/937/938/939/940/941/942/943/944/945/946/947/948/949/950/951/952/953/954/955/956/957/958/959/960/961/962/963/964/965/966/967/968/969/970/971/972/973/974/975/976/977/978/979/980/981/982/983/984/985/986/987/988/989/990/991/992/993/994/995/996/997/998/999/1000/1001/1002/1003/1004/1005/1006/1007/1008/1009/1010/1011/1012/1013/1014/1015/1016/1017/1018/1019/1020/1021/1022/1023/1024/1025/1026/1027/1028/1029/1030/1031/1032/1033/1034/1035/1036/1037/1038/1039/1040/1041/1042/1043/1044/1045/1046/1047/1048/1049/1050/1051/1052/1053/1054/1055/1056/1057/1058/1059/1060/1061/1062/1063/1064/1065/1066/1067/1068/1069/1070/1071/1072/1073/1074/1075/1076/1077/1078/1079/1080/1081/1082/1083/1084/1085/1086/1087/1088/1089/1090/1091/1092/1093/1094/1095/1096/1097/1098/1099/1100/1101/1102/1103/1104/1105/1106/1107/1108/1109/1110/1111/1112/1113/1114/1115/1116/1117/1118/1119/1120/1121/1122/1123/1124/1125/1126/1127/1128/1129/1130/1131/1132/1133/1134/1135/1136/1137/1138/1139/1140/1141/1142/1143/1144/1145/1146/1147/1148/1149/1150/1151/1152/1153/1154/1155/1156/1157/1158/1159/1160/1161/1162/1163/1164/1165/1166/1167/1168/1169/1170/1171/1172/1173/1174/1175/1176/1177/1178/1179/1180/1181/1182/1183/1184/1185/1186/1187/1188/1189/1190/1191/1192/1193/1194/1195/1196/1197/1198/1199/1200/1201/1202/1203/1204/1205/1206/1207/1208/1209/1210/1211/1212/1213/1214/1215/1216/1217/1218/1219/1220/1221/1222/1223/1224/1225/1226/1227/1228/1229/1230/1231/1232/1233/1234/1235/1236/1237/1238/1239/1240/1241/1242/1243/1244/1245/1246/1247/1248/1249/1250/1251/1252/1253/1254/1255/1256/1257/1258/1259/1260/1261/1262/1263/1264/1265/1266/1267/1268/1269/1270/1271/1272/1273/1274/1275/1276/1277/1278/1279/1280/1281/1282/1283/1284/1285/1286/1287/1288/1289/1290/1291/1292/1293/1294/1295/1296/1297/1298/1299/1300/1301/1302/1303/1304/1305/1306/1307/1308/1309/1310/1311/1312/1313/1314/1315/1316/1317/1318/1319/1320/1321/1322/1323/1324/1325/1326/1327/1328/1329/1330/1331/1332/1333/1334/1335/1336/1337/1338/1339/1340/1341/1342/1343/1344/1345/1346/1347/1348/1349/1350/1351/1352/1353/1354/1355/1356/1357/1358/1359/1360/1361/1362/1363/1364/1365/1366/1367/1368/1369/1370/1371/1372/1373/1374/1375/1376/1377/1378/1379/1380/1381/1382/1383/1384/1385/1386/1387/1388/1389/1390/1391/1392/1393/1394/1395/1396/1397/1398/1399/1400/1401/1402/1403/1404/1405/1406/1407/1408/1409/1410/1411/1412/1413/1414/1415/1416/1417/1418/1419/1420/1421/1422/1423/1424/1425/1426/1427/1428/1429/1430/1431/1432/1433/1434/1435/1436/1437/1438/1439/1440/1441/1442/1443/1444/1445/1446/1447/1448/1449/1450/1451/1452/1453/1454/1455/1456/1457/1458/1459/1460/1461/1462/1463/1464/1465/1466/1467/1468/1469/1470/1471/1472/1473/1474/1475/1476/1477/1478/1479/1480/1481/1482/1483/1484/1485/1486/1487/1488/1489/1490/1491/1492/1493/1494/1495/1496/1497/1498/1499/1500/1501/1502/1503/1504/1505/1506/1507/1508/1509/1510/1511/1512/1513/1514/1515/1516/1517/1518/1519/1520/1521/1522/1523/1524/1525/1526/1527/1528/1529/1530/1531/1532/1533/1534/1535/1536/1537/1538/1539/1540/1541/1542/1543/1544/1545/1546/1547/1548/1549/1550/1551/1552/1553/1554/1555/1556/1557/1558/1559/1560/1561/1562/1563/1564/1565/1566/1567/1568/1569/1570/1571/1572/1573/1574/1575/1576/1577/1578/1579/1580/1581/1582/1583/1584/1585/1586/1587/1588/1589/1590/1591/1592/1593/1594/1595/1596/1597/1598/1599/1600/1601/1602/1603/1604/1605/1606/1607/1608/1609/1610/1611/1612/1613/1614/1615/1616/1617/1618/1619/1620/1621/1622/1623/1624/1625/1626/1627/1628/1629/1630/1631/1632/1633/1634/1635/1636/1637/1638/1639/1640/1641/1642/1643/1644/1645/1646/1647/1648/1649/1650/1651/1652/1653/1654/1655/1656/1657/1658/1659/1660/1661/1662/1663/1664/1665/1666/1667/1668/1669/1670/1671/1672/1673/1674/1675/1676/1677/1678/1679/1680/1681/1682/1683/1684/1685/1686/1687/1688/1689/1690/1691/1692/1693/1694/1695/1696/1697/1698/1699/1700/1701/1702/1703/1704/1705/1706/1707/1708/1709/1710/1711/1712/1713/1714/1715/1716/1717/1718/1719/1720/1721/1722/1723/1724/1725/1726/1727/1728/1729/1730/1731/1732/1733/1734/1735/1736/1737/1738/1739/1740/1741/1742/1743/1744/1745/1746/1747/1748/1749/1750/1751/1752/1753/1754/1755/1756/1757/1758/1759/1760/1761/1762/1763/1764/1765/1766/1767/1768/1769/1770/1771/1772/1773/1774/1775/1776/1777/1778/1779/1780/1781/1782/1783/1784/1785/1786/1787/1788/1789/1790/1791/1792/1793/1794/1795/1796/1797/1798/1799/1800/1801/1802/1803/1804/1805/1806/1807/1808/1809/1810/1811/1812/1813/1814/1815/1816/1817/1818/1819/1820/1821/1822/1823/1824/1825/1826/1827/1828/1829/1830/1831/1832/1833/1834/1835/1836/1837/1838/1839/1840/1841/1842/1843/1844/1845/1846/1847/1848/1849/1850/1851/1852/1853/1854/1855/1856/1857/1858/1859/1860/1861/1862/1863/1864/1865/1866/1867/1868/1869/1870/1871/1872/1873/1874/1875/1876/1877/1878/1879/1880/1881/1882/1883/1884/1885/1886/1887/1888/1889/1890/1891/1892/1893/1894/1895/1896/1897/1898/1899/1900/1901/1902/1903/1904/1905/1906/1907/1908/1909/1910/1911/1912/1913/1914/1915/1916/1917/1918/1919/1920/1921/1922/1923/1924/1925/1926/1927/1928/1929/1930/1931/1932/1933/1934/1935/1936/1937/1938/1939/1940/1941/1942/1943/1944/1945/1946/1947/1948/1949/1950/1951/1952/1953/1954/1955/1956/1957/1958/1959/1960/1961/1962/1963/1964/1965/1966/1967/1968/1969/1970/1971/1972/1973/1974/1975/1976/1977/1978/1979/1980/1981/1982/1983/1984/1985/1986/1987/1988/1989/1990/1991/1992/1993/1994/1995/1996/1997/1998/1999/2000/2001/2002/2003/2004/2005/2006/2007/2008/2009/2010/2011/2012/2013/2014/2015/2016/2017/2018/2019/2020/2021/2022/2023/2024/2025/2026/2027/2028/2029/2030/2031/2032/2033/2034/2035/2036/2037/2038/2039/2040/2041/2042/2043/2044/2045/2046/2047/2048/2049/2050/2051/2052/2053/2054/2055/2056/2057/2058/2059/2060/2061/2062/2063/2064/2065/2066/2067/2068/2069/2070/2071/2072/2073/2074/2075/2076/2077/2078/2079/2080/2081/2082/2083/2084/2085/2086/2087/2088/2089/2090/2091/2092/2093/2094/2095/2096/2097/2098/2099/2100/2101/2102/2103/2104/2105/2106/2107/2108/2109/2110/2111/2112/2113/2114/2115/2116/2117/2118/2119/2120/2121/2122/2123/2124/2125/2126/2127/2128/2129/2130/2131/2132/2133/2134/2135/2136/2137/2138/2139/2140/2141/2142/2143/2144/2145/2146/2147/2148/2149/2150/2151/2152/2153/2154/2155/2156/2157/2158/2159/2160/2161/2162/2163/2164/2165/2166/2167/2168/2169/2170/2171/2172/2173/2174/2175/2176/2177/2178/2179/2180/2181/2182/2183/2184/2185/2186/2187/2188/2189/2190/2191/2192/2193/2194/2195/2196/2197/2198/2199/2200/2201/2202/2203/2204/2205/2206/2207/2208/2209/2210/2211/2212/2213/2214/2215/2216/2217/2218/2219/2220/2221/2222/2223/2224/2225/2226/2227/2228/2229/2230/2231/2232/2233/2234/2235/2236/2237/2238/2239/2240/2241/2242/2243/2244/2245/2246/2247/2248/2249/2250/2251/2252/2253/2254/2255/2256/2257/2258/2259/2260/2261/2262/2263/2264/2265/2266/2267/2268/2269/2270/2271/2272/2273/2274/2275/2276/2277/2278/2279/2280/2281/2282/2283/2284/2285/2286/2287/2288/2289/2290/2291/2292/2293/2294/2295/2296/2297/2298/2299/2300/2301/2302/2303/2304/2305/2306/2307/2308/2309/2310/2311/2312/2313/2314/2315/2316/2317/2318/2319/2320/2321/2322/2323/2324/2325/2326/2327/2328/2329/2330/2331/2332/2333/2334/2335/2336/2337/2338/2339/2340/2341/2342/2343/2344/2345/2346/2347/2348/2349/2350/2351/2352/2353/2354/2355/2356/2357/2358/2359/2360/2361/2362/2363/2364/2365/2366/2367/2368/2369/2370/2371/2372/2373/2374/2375/2376/2377/2378/2379/2380/2381/2382/2383/2384/2385/2386/2387/2388/2389/2390/2391/2392/2393/2394/2395/2396/2397/2398/2399/2400/2401/2402/2403/2404/2405/2406/2407/2408/2409/2410/2411/2412/2413/2414/2415/2416/2417/2418/2419/2420/2421/2422/2423/2424/2425/2426/2427/2428/2429/2430/2431/2432/2433/2434/2435/2436/2437/2438/2439/2440/2441/2442/2443/2444/2445/2446/2447/2448/2449/2450/2451/2452/2453/2454/2455/2456/2457/2458/2459/2460/2461/2462/2463/2464/2465/2466/2467/2468/2469/2470/2471/2472/2473/2474/2475/2476/2477/2478/2479/2480/2481/2482/2483/2484/2485/2486/2487/2488/2489/2490/2491/2492/2493/2494/2495/2496/2497/2498/2499/2500/2501/2502/2503/2504/2505/2506/2507/2508/2509/2510/2511/2512/2513/2514/2515/2516/2517/2518/2519/2520/2521/2522/2523/2524/2525/2526/2527/2528/2529/2530/2531/2532/2533/2534/2535/2536/2537/2538/2539/2540/2541/2542/2543/2544/2545/2546/2547/2548/2549/2550/2551/2552/2553/2554/2555/2556/2557/2558/2559/2560/2561/2562/2563/2564/2565/2566/2567/2568/2569/2570/2571/2572/2573/2574/2575/2576/2577/



SKS Test Labs Private Limited
 B-17 & 18, Narayana Nagar, Jaipur - 302016, Rajasthan



Test Report

Sample Number: 2020010101
 Name & Address of the Party: M/s. Shree Narayana Nagar, Jaipur - 302016, Rajasthan
 (Representing Engineer N/AEP, P.W.D. Department, Jaipur)
 (For the purpose of the test, the sample was collected from the site of the project)
 Report No.: SKS/2020/01010101
 Project No.: 2020/01010101
 Party Reference No.: 01
 Report Date: 11/01/2020
 Period of Analysis: 01/01/2020 to 11/01/2020
 Revised Date: 01/01/2020

Sample Description: 202001010101

General Information:
 Sampling Location: 01/01/2020 (New Street Narayana Nagar Jaipur City)
 Sample Collected At: 01/01/2020 (New Street Narayana Nagar Jaipur City)
 Sampling Equipment used: 01/01/2020
 Instrument Code: 01/01/2020
 Instrument Calibration Status: 01/01/2020
 Latitude: 27° 00' 00"
 Longitude: 75° 50' 00"
 Meteorological condition during monitoring: 01/01/2020
 Date of Monitoring: 01/01/2020 to 11/01/2020
 Time of Monitoring: 10:30 AM to 12:30 PM
 Ambient Temperature (°C): 30.00 (Max. 30.00)
 Surrounding Activity: Normal (Industrial & Residential)
 State of Monitoring: Regularly Monitored
 Sampling & Analysis Protocol: 01/01/2020
 Sampling Location: 01/01/2020
 Parameter Required: 01/01/2020

S. No.	Parameter	Test Method	Result	Unit	IS 4550:2002
1	Phosphate (as PO ₄ -P)	01/01/2020 (P-20.00)	04.21	µg/l	100
2	Phosphate (as PO ₄ -P)	01/01/2020 (P-20.00)	00.00	µg/l	00
3	Nitrogen (as NO ₃ -N)	01/01/2020 (N-20.00)	00.00	µg/l	00
4	Nitrogen (as NO ₃ -N)	01/01/2020 (N-20.00)	11.00	µg/l	00




01/01/2020

Page No. 1/1

Plot No. 25, Narayana Nagar, Jaipur - 302016, Rajasthan
 Tel: 0141-2600000, 0141-2600001, 0141-2600002
 E-mail: info@skstestlabs.com

www.skstestlabs.com


SKS Test Labs Private Limited

Unit 1 & 12, Annapurna 4 (201-0161) 11001 (011) 11001-0000


Test Report

Sample Number : 10000000000000000000
 Name & Address of the Party : M/s. Kapsa Infra India Limited
 (Representing Engineer: RUPAK SINGH, Designer)
 Package No.: JCT/0001/0000/00000000000000000000
 Location: JCT/0001/00000000000000000000, A-10, 1st Floor
 Project Name: JCT/0001/00000000000000000000
 Report No.: JCT/0001/00000000000000000000
 Project No.: JCT/0001/00000000000000000000
 Report Date: 11/01/2020
 Period of Analysis: 00/01/2020 to 11/01/2020
 Report Code: 00/01/2020

Sample Description : JCT/0001/00000000000000000000

Safety Information :
 Sampling Location : JCT/0001/00000000000000000000
 Sample Collected by : JCT/0001/00000000000000000000
 Sampling Equipment used : JCT/0001/00000000000000000000
 Instrument Code : JCT/0001/00000000000000000000
 Instrument Calibration Status : Calibrated
 Latitude : JCT/0001/00000000000000000000
 Longitude : JCT/0001/00000000000000000000
 Meteorological condition during monitoring : Clear Sky
 Date of Monitoring : JCT/0001/00000000000000000000
 Time of Monitoring : JCT/0001/00000000000000000000
 Ambient Temperature (°C) : Min. 15°C, Max. 25°C
 Surrounding Activity : JCT/0001/00000000000000000000
 Scope of Monitoring : JCT/0001/00000000000000000000
 Sampling & Analysis Protocol : JCT/0001/00000000000000000000
 Sampling Location : JCT/0001/00000000000000000000
 Parameter Required : JCT/0001/00000000000000000000

S. No.	Parameter	Test Method	Result	Unit	SAQS 2000
1	Particulate Matter (as PM - 10)	IS 3100 (P-10-2000)	61.27	µg/m³	100
2	Particulate Matter (as PM - 2.5)	IS 3100 (P-2.5-2010)	24.75	µg/m³	80
3	Sulphur Dioxide (as SO₂)	IS 3100 (P-10-2000)	24.80	µg/m³	80
4	Nitrogen Dioxide (as NO₂)	IS 3100 (P-10-2000)	15.28	µg/m³	80

Total of Result




00000000000000000000

Page No. 1/1

Plot No. 25, Block B, Naraina Vihar, Jodhpur - 326005, Rajasthan
 Tel: 0141-2049403, 0141-2049404, 0141-147208
 E-mail: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
ISO 9001:2015 Registered / (IN) 9001100010001 / ISO 9001



Test Report

Sample Number: 10100001
Name & Address of the Party: SKS Engineering India Limited
(Sundernagar Engineer Road, PO - Sundernagar)
Postage No. 741001 (Karnal District - 201301)
C/O SKS Test Labs Private Limited, A-10, Sector-10
Phase-III, Gurgaon, Haryana (India)
Sample Description: 10100001 A-10

Report No.: 10100001000000000000
Version No.: 1.0.0.0
Party Reference No.: SKS
Report Date: 11/01/2020
Method of Analysis: 10100001000000000000
Receipt Date: 10/01/2020

General Information
Sampling Location: 10100001 A-10
Sample Collected by: SKS Test Labs India Limited
Sampling Equipment used: 10100001
Reference Code: 10100001000000000000
Reference Certification Number: 10100001
Lab No.: 10100001
City/City: 10100001
Weatherological condition during monitoring: 10100001
Date of Monitoring: 10/01/2020 to 10/01/2020
Time of Monitoring: 10:00 hrs. to 12:30 hrs.
Ambient Temperature (°C): 10.0°C, Max. 10.0°C
Sampling Activity: 10100001 A-10
Scope of Monitoring: 10100001 A-10
Sampling & Analysis Protocol: 10100001 A-10
Sampling Duration: 10100001 A-10
Remarks/Remarks: 10100001 A-10

S.No.	Parameter	Test Method	Results	Unit	IS 4625:2003
1.	Particulate Matter (as PM ₁₀)	IS 4625 (P-1) 2003	10.10	µg/m ³	100
2.	Particulate Matter (as PM _{2.5})	IS 4625 (P-2) 2003	10.10	µg/m ³	50
3.	Water Vapor (as H ₂ O)	IS 4625 (P-3) 2003	10.10	µg/m ³	50
4.	Water Vapor (as H ₂ O)	IS 4625 (P-4) 2003	10.10	µg/m ³	50




10100001000000000000

Page No. 1/1

Plot No. 25, Block B, Narayan Nagar, Sector - 10, Gurgaon, Haryana
Tel: 9141 344433, 9612155566, 9612157790
E-mail: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
 40/2, S. S. Nagar Road, 401 001, 401 001, 401 001



Test Report

Sample Number : 10010000
 Name & Address of the Party : M/s. S. S. Nagar Road, 401 001, 401 001, 401 001
 Sample Description : 1. 10010000
 Report No. : 10010000000000
 Format No. : 1.0
 Party Reference No. : 10010000
 Report Date : 10/10/2020
 Period of Analysis : 10/10/2020
 Sample Date : 10/10/2020

General Information
 Sampling Location : 10010000
 Sample Collection by : 10010000
 Sampling Equipment used : 10010000
 Instrument used : 10010000
 Instrument Calibration Status : 10010000
 Latitude : 10010000
 Longitude : 10010000
 Meteorological condition during sampling : 10010000
 Date of Sampling : 10/10/2020
 Time of Sampling : 10:00 AM to 11:00 AM
 Ambient Temperature (°C) : 30, 32, 34, 36
 Recording Activity : 10010000
 Scope of Monitoring : 10010000
 Sampling & Analysis Protocol : 10010000
 Sampling Duration : 10010000
 Preservative Required : 10010000

S. No.	Parameter	Test Method	Result	Unit	NAAC 2019
1	Perchlorate Water (as Pb - 10)	10010000	10010000	ppm	100
2	Perchlorate Water (as Pb - 20)	10010000	10010000	ppm	100
3	Perchlorate Water (as Pb - 30)	10010000	10010000	ppm	100
4	Perchlorate Water (as Pb - 40)	10010000	10010000	ppm	100




10010000

Page No. 1/1

Plot No. 10, Block B, Mangal Vihar, Jaipur - 302020, Rajasthan
 Tel: 0141-2848000, 0141-2848001, 0141-2848002
 E-mail: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
 Multi & IT Integrated | ISO 9001 | ISO 14001 | ISO 45001



Test Report

Sample Number : 00000001
 Name & Address of the Party : M/s. Eagle Infra Infra Limited
 Manufacturing Address: Plot No. 1, Sector 10, Gurgaon
 Postage No: 122001 (Gurgaon) Haryana
 Office: 40/100A, Sector 10, Gurgaon, Haryana
 Phone: 9999999999 (Gurgaon)
 Service Description : Asphalting Job

Report No. : SKS/0000000001
 Format No. : 1.0.0-01
 Party Reference No. : Nil
 Report Date : 11/05/2020
 Period of Analysis : 00/05/2020 - 11/05/2020
 Revision Date : 01/05/2020

General Information
 Sampling Location : Industrial Estate (Gurgaon) Haryana
 Sample Collected by : SKS Team (Gurgaon)
 Sampling Equipment used : 1000ml
 Instrument Code : SKS/0000000001
 Instrument Calibration Status : Calibrated
 Latitude : 29°34'30"
 Longitude : 76°34'30"
 Meteorological condition during sampling : Clear Sky
 Date of Monitoring : 01/05/2020 To 11/05/2020
 Time of Monitoring : 07:00 hrs. to 17:00 hrs.
 Ambient Temperature (°C) : Min: 17°C, Max: 30°C
 Surrounding Activity : Heavy Vehicle & Other Activities
 Scope of Monitoring : Regulatory Required
 Sampling & Analysis Protocol : IS 5100
 Sampling Duration : 01-Hrs
 Remarks/Request : As per Work Order

S.No.	Parameters	Test Method	Result	Unit	NAAC 2018
1	Carbon Monoxide (ppm)	By Analyzer	0.07	ppm	5.0




000000000000

Page No. 1/1

Plot No. 25, Block-B, Naraina Vihar, Jaipur - 302015, Rajasthan
 Tel: 0141-2545432, 9810266006, 9812167299
 E-mail: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
 100/1 & 12, Ring Road, 100/1001, 100/1002, 100/1003



Test Report

Report Number: 100/1001 Name & Address of the Party: Mr. Dhanu Info Tech Pvt. Ltd. 100/1001, Ring Road, 100/1001, 100/1002, 100/1003 100/1001, Ring Road, 100/1001, 100/1002, 100/1003 100/1001, Ring Road, 100/1001, 100/1002, 100/1003 Sample Description: Ambient Noise	Report No.: 100/1001 Formed By: 100/1001 Party Reference No.: 100/1001 Report Date: 100/1001 Revised or Rejected: 100/1001 Revised Date: 100/1001

General Information	
Sampling Location	100/1001, Ring Road
Sample Collected by	100/1001, Ring Road
Sampling Equipment used	100/1001, Ring Road
Instrument Code	100/1001, Ring Road
Instrument Calibration Status	100/1001, Ring Road
Latitude	100/1001, Ring Road
Longitude	100/1001, Ring Road
Microclimatic condition during monitoring	100/1001, Ring Road
Size of Monitoring	100/1001, Ring Road
Time of Monitoring	100/1001, Ring Road
Relative Humidity (%)	100/1001, Ring Road
Surrounding Activity	100/1001, Ring Road
Scope of Monitoring	100/1001, Ring Road
Sampling & Analysis Protocol	100/1001, Ring Road
Sampling Duration	100/1001, Ring Road
Operator/Inspector	100/1001, Ring Road

S. No.	Parameter	Test Method	Results	Units	Range/Std
1	Ambient Noise Level (dB)	By Standard	5.27	dB(A)	5.5




100/1001, Ring Road

Page No. 10

Plot No. 25, Ring Road, Ring Road, Ring Road : 100/1001, Ring Road
 Tel: 100/1001, Ring Road, 100/1001, Ring Road : 100/1001, Ring Road
 E-mail: info@skstestlabs.com

www.skstestlabs.com



SKS Test Labs Private Limited
MKT & IT Building / 101-102 / 103-104 / 105-106



Test Report

Sample Number: 101010101
Name & Address of the Party: M/s. Kaps Infra Tech Limited
(Qualifying Engineer: Mr. P. S. Deshpande)
Particulars: 101010101 (Qualifying Engineer: Mr. P. S. Deshpande)
101010101 (Qualifying Engineer: Mr. P. S. Deshpande)
101010101 (Qualifying Engineer: Mr. P. S. Deshpande)
Sample Description: 101010101
Scope of Monitoring: 101010101
Project Name: 101010101
Instrument Used: 101010101
Document Code: 101010101
Report No.: 101010101
Project No.: 101010101
Sample Reference No.: 101010101
Report Date: 101010101
Report Time: 101010101
Sampling Location: 101010101
Sample Collected By: 101010101
Instrument: 101010101
Collection Report: 101010101

Sample Information:
Sampling Location: 101010101
Instrument Code: 101010101
Meteorological condition during monitoring: 101010101
Date of Monitoring: 101010101
Time of Monitoring: 101010101
Ambient Temperature (°C): 101010101
Surrounding Activity: 101010101
Parameter Required: 101010101

S. No.	Test Parameters	Request	Test Results (dB)	
			Day Time	Night Time
1	L _{eq}	101010101	101010101	101010101

Category of Zone	L _{eq} (dB(A))	
	Day	Night
Industrial	10	10
Commercial	10	10
Residential	10	10
Class Zone	10	10

1. Day Time is from 06:00 AM to 10:00 PM
2. Night Time is defined between 10:00 PM to 06:00 AM
3. Class Zone is defined as an area up to 100m around premises of hospitals, educational institutions and Courts. Use of vehicle near hospital and vicinity of courts is defined in these zones.
Note: Every category of zone is defined on the basis of the data above mentioned categories by the competent authority and the corresponding standards shall apply.



101010101010101

Page No. 1/1

Plot No. 25, Block-B, Narayan Vihar, Jaipur - 302005, Rajasthan
Tel: 0141-2644452, 9616555588, 9957147280
E-mail: info@skstestlabs.com

www.skstestlabs.com

Sample Number	00000000000000000000	Report No.	00000000000000000000
Name & Address of the Party	100 Eagle Lake Drive (Supermarket Building) - 100 Eagle Lake Drive Building No. - 10000000000000000000 10000000000000000000, Apt. - 1st Floor 10000000000000000000, 10000000000000000000	Formet No.	10000000000000000000
Sample Description	Antacid Tablets	Party Reference No.	10000000000000000000
Date of Monitoring	10/00/2000	Report Date	10/00/2000
Project Lead	10000000000000000000	Monitor Date	10/00/2000
Instrument Used	GLM	Sampling Duration	10000000000000000000
		Sample Collected by	10000000000000000000
		Instrument	10000000000000000000
		Collection Status	10000000000000000000
General Information	10000000000000000000		
Sampling Location	10000000000000000000		
Instrument Type	10000000000000000000		
Monitoring condition during monitoring	10000000000000000000		
Date of Monitoring	10/00/2000		
Time of Monitoring	10000000000000000000		
Ambient Temperature (°C)	10000000000000000000		
Monitoring Activity	10000000000000000000		
Preparation Required	10000000000000000000		

Date	Test Assessment	Response	Test Result (Min)	
			Day Time	Night Time
5	3-40	20 0000 / 1000	60.00	60.00

Category of Device	Users in Study	
	Male	Female
Industrial	75	70
Commercial	65	60
Residential	55	45
Private Care	30	40

[illegible]

本公司地址：廣東省佛山市順德區均安鎮均安大道東100號

Page 44 of 50

Ref No: 25, Block-B, Newpark West, Japur - 02020, Firozabad
Tel: 0127-2942422, 0120351386, 0981317292
E-mail: info@newparkwest.com

A Safety training and orientation programme at was conducted in Dungarpur town after the award of the contract and was attended by contractor's staff , RUIDP-PIU staff on 06.04.2023. Details safety training and orientation programme is given below along with photographs and attendance sheet.

B- Safety Training Orientation Programme at Dungarpur Town

Location: Contractor Meeting Hall, Dungarpur

Date: 06.04.2023

- a. Environmental, Health and Safety Training Orientation to RUIDP-PHE Staff, Eagle Infra India Pvt. Ltd. Contractor Staff and CMSC-II Dungarpur Staff:

Orientation was given by Dr. Mahaveer Saini (Environment Safeguard Professional-CMSC-II, Jodhpur) and Mr. Rajeev Sharma (Gender and Social Safeguard Professional, CMSC-II)

Topics Discussed:

- ◆ AIO SPS 2009 and RUIDP safeguards requirements;
- ◆ Safeguards implementation arrangements and roles & responsibility of different functionaries in the project;
- ◆ Safety during working at height;
- ◆ Safety during working in Trenches;
- ◆ Safety during working in pit excavation
- ◆ Safety during Casting
- ◆ Personal Safety Equipment's
- ◆ Possible accidents and safety measures;
- ◆ Safety during iron bar & steel cutting;
- ◆ Occupational and community health and safety;
- ◆ Labour and public safety and labour laws;
- ◆ Solid waste (domestic, construction, and spoils) management;
- ◆ Periodical environmental monitoring requirements for air, noise, water and soil;
- ◆ Areas of safety concerns in construction works;
- ◆ Public consultations and grievance redress mechanism of RUIDP;
- ◆ Probable pollutions during construction works and their mitigation measures and;
- ◆ Photos and Signature Sheet of Training sheet are given below:


Dr. MAHAVEER SAINI
 Environment Safeguard
 Professional
 CMSC-II, Jodhpur

Photographs of safety training and orientation programme



by line
DR. MANAVJEER SAINI
 Environment Safeguards
 Professional
 CHSC-II, Jodhpur

P. C. Chouhan
 PE + E - 14013
P. C. CHOUHAN
 Team Leader
 CHSC-I, Jodhpur

Attendance sheet of safety training and orientation programme

ATTENDANCE SHEET
TRAINING ORIENTATION PROGRAM REGARDING ENVIRONMENT
AND SAFETY

PROJECT CODE: - 001/001/001/001/001/001

DATE: 06/04/2022

VENUE: CONTRACTOR MEETING HALL, BANGALORE

S.NO.	NAME	DESIGNATION	PHONE NUMBER	SIGNATURE
1	Amal Kumar	CTO	9896120001	
2	Dr. Prabhu A. Saini	Environment Manager	9896120001	
3	RAJESH CHANDRA	Project Engineer	9896120001	
4	Ravi Singh	Technical Officer	9896120001	
5	Vijayesh Reddy	PP-Engineer	9896120001	
6	Prakash Reddy	PP-Engineer	9896120001	
7	Prakash Reddy	PP-Engineer	9896120001	
8	Prakash Reddy	PP-Engineer	9896120001	
9	Prakash Reddy	PP-Engineer	9896120001	
10	Prakash Reddy	PP-Engineer	9896120001	
11	Prakash Reddy	PP-Engineer	9896120001	
12	Prakash Reddy	PP-Engineer	9896120001	
13	Prakash Reddy	PP-Engineer	9896120001	
14	Prakash Reddy	PP-Engineer	9896120001	
15	Prakash Reddy	PP-Engineer	9896120001	
16	Prakash Reddy	PP-Engineer	9896120001	
17	Prakash Reddy	PP-Engineer	9896120001	
18	Prakash Reddy	PP-Engineer	9896120001	
19	Prakash Reddy	PP-Engineer	9896120001	
20	Prakash Reddy	PP-Engineer	9896120001	

Dr. HARVEER SAINI
 Environment Safeguard
 Professional
 CHSC-IT, Jaipur


 Dr. MAHAVEER SINGH
 Environment Safeguard
 Professional
 CMSC-II, Jodhpur

S.NO.	NAME	DESIGNATION	MOBILE NUMBER	REMARKS
01	Dr. Mahaveer Singh	Dr. Mahaveer Singh	9829012345	Dr. Mahaveer Singh
02	Dr. Mahaveer Singh	Dr. Mahaveer Singh	9829012345	Dr. Mahaveer Singh
03				
04				
05				
06				
07				
08				
09				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				

Appendix 12: Biodiversity assessment of Dimiya Dam Dungarpur with special reference to presence of Marsh Crocodile and its mitigation measures

Biodiversity assessment of Dimiya Dam Dungarpur with special reference to presence of Marsh Crocodile and its mitigation measures



September -November, 2023

Manoj Kulshreshtha

Field biologist and Ornithologist

'Sneh-Deep', B-33, Sethi Colony, Jaipur-302004

Email. kulshmanoj21@gmail.com

Contact No. +91 9314880887

Introduction

1. Dungarpur is one of the project towns, and improvement of water supply and sewerage system in Dungarpur is proposed under the Rajasthan Secondary Towns Development Sector Project (RSTDSP, Funder by Asian Development Bank). Following are the proposed components for water supply :

- **Water supply.** (i) Refurbishment of existing Intake well and pump house 3.2 MLD at Vijay Chakra Sagar (Dimiya) Dam (ii) Raw water pump house-01 no (iii) clear Water Pump House (5 nos.) (iv) Clear Water Reservoir (2 nos., 550 KL & 600 KL) (v) Raw water rising main of 10.082 km and clear water rising main of 14.95 km (vi) Distribution networks of 160.29 km (vii) House service connection- 12067 nos. (viii) Refurbishment of pump house (7 nos.), RWR (235 KL), WTPs- 2 nos. (4.54 MLD and 3.25 MLD), CWRs (2nos.), OHSRs (8nos.), GLSRs (4 nos.), (ix) Rehabilitation of 2 TWs and 2 open wells, (x) Construction of CRMC (2 nos.) and MCC (1no.).

Background

2. **Intake well site at Vijay Chakra Sagar (Dimiya dam, Dungarpur):** During the Joint site visit to Intake well at Vijay Chakra Sagar (Dimiya dam, Dungarpur) by ADB, PMU, PIU and Contractor team in month of August 2023, a Marsh Crocodile (Mugar); *Crocodylus palustris* (Vulnerable species as per IUCN Red List) was observed in the reservoir.

3. After this finding PMU decided to conduct a biodiversity assessment in reference to present of Marsh Crocodile in the Dimiya dam and thus an external biodiversity expert was assigned this Job. PMU asli revise the scope of work to cause least disturbance to natural habitat of crocodile which is mentioned red list species by IUCN as vulnerable. After revision the final scope of work is as follows.

Scope of work at Dimiya dam site includes.

- Installation of SCDA system
- Refurbishment of existing intake structure.
- Replacement of raw water rising mains (Intake to WTP)

Project area the Vijay Chakra Sagar (Dimiya) Dam

4. **Vijay Chakra Sagar Dam:** Situated on Moran River, tributary to mahi river near Dimiya village, Dungarpur is a drinking water reservoir owned by WRD, GOR water of this reservoir is reserved only for drinking water supply for Dungarpur. Capacity of this dam is 44.87 MCFT including dead storage and 40 MCFT (1.27 MCM) is live storage. The PHED has allocated 3.1 MLD (1.18 MCM) water for Dungarpur water supply subproject (but currently only 1 MLD has been abstracted), which is about 93.40% of total water available in dam. The existing water abstraction of water from dam is 3.25 MLD and proposed capacity is 3.1 MLD. The water from dam is not used for irrigation or any other activity. The PHED has recorded yearly water level data of dam and as per water level data of past 12-year, the dam was filled fully up to its storage capacity in all 12 years.

5. **Objective of study:** To conduct thorough ecological surveys to identify crocodile habitats and nesting sites to Implement impact assessments and to understand potential consequences on the local crocodile population, flora and faunal biodiversity was also studied during the assessment. This was done by Communicating with local people and gathering available information and meeting government agencies. Assessment of biodiversity in and around Dimiya Dam with special reference to Environmental safeguards pointed out by ADB

team due to presence of IUCN red list species Marsh crocodiles. To assess the area in and around Dimiya dam where crocodiles exist and other fauna and flora three visits were made for the following objective

Field visit by biodiversity expert

First visit during Monsoon on 19 and 20th September, 2023

6. A site visit along with some project engineers was made to gather details on Dimiya Dam, local people's dependence over it, to observe presence of crocodiles in the dam and its adverse impact if recorded or observed any on local cattle or on human beings.

7. A family of Shiv Lal Meena who has a small piece of agriculture land where he grows Maize crop in routine and Wheat if rain is good. Shiv Lal lives there in his earthen hut just located next to a dam over a hill. He uses water from the dam for day today. We approached him to take his viewpoint on the presence of mugger/Broad Snouted or Marsh Crocodile (*Crocodylus palustris*) in this area. He specifically mentioned that crocodiles have been there but its presence does not make his family uncomfortable while going to the edge of water with his cattle which are mainly Cows and goats, though there have been some sporadic incidences of attack on goat which went to the dam unaccompanied by the owner..

8. The vegetation recorded over that hill was predominantly Teak (*Tectona grandis*), Khakhra (*Butea monosperma*), Ronjh (*Acacia leucophloea*), Papdi (*Holoptelia integrifolia*), Thoor (*Euphorbia* sp.), Khajoor (*Phoenix sylvestris*), Ardu (*Ailanthus excelsa*), Babool (*Acacia nilotica*) and some planted Mango (*Mangifera indica*) trees. There were some seasonal grasses and other seasonal vegetation observed which will find a place in flora listing.

9. Some birds were also observed dependent upon water and insects like Pond Heron, Median Egret, Little Egret, Indian Cormorant, White Breasted Kingfisher, Pied Kingfisher, Red Naped Ibis and some terrestrial birds like Ashy Prinia, Common Hawk Cuckoo, Red Vented Bulbul mainly which are resident birds.

10. A visit to Lolakpur Panchayat Samiti in Dungarpur District was also made to collect facts related to people occupying surrounding hills along the dam who may be directly or indirectly dependent on this dam for water. There were about 5000 people recorded in the last census mainly from the Bheel Meena tribe besides some other people belonging to Yadav community and some from other communities. Out of total population as told by the panchayat Sarpanch, Sh. Dinesh Rot about 80% of people were vegetarian. They keep animals like Goats, sheep, Cows and buffaloes mainly and some people rear poultry birds.

11. Crops grown mainly are Maize, Paddy/Rice, Urad pulse, MP Chari (fodder crop) and Soya bean during monsoon and Wheat (*Triticum aestivum*), Gram (*Cicer arietinum*) and Sarson (*Brassica campestris*) in winter season.

12. Dimiya Dam made over Moran river flows into Margiya Dam then Lodisar Dam and then finally merges into Mahi river suggests that the Moran river has a seasonal flow during monsoon.

13. A meeting was done with the Executive Engineer Ms. Ashwini Ahari in Water Resource Development Project, Dungarpur who handed over a document furnishing information on past history and physical parameters related to Dimiya Dam. In continuation Assistant Engineer Mr. Shankar Lal Rot was also contacted who informed me that in the year 2009 the depth near embankment near spillover site was about 3 meter with a stretch of about just 250 meter long near the dam wall.

14. Since the project relates to bio-diversity assessment so the District Fisheries Officer Mr. Aqueel Ahmed having charge of Dungarpur was also contacted on phone to know about the Ichthyofauna of dam waters around Dungarpur informed that major carps are Rohu (*Labeo rohita*), Catla (*Catla catla*), Mrigal (*Cirrhinus mrigala*) and Minor carps like *Labeo gonius*, *Puntius cirrhatus*, weed fishes like *Gudusia chapra*, *Oxygaster* sp., *Bacaila morar*, *Aspidopelia* sp. Besides these some catfishes like *Mystus cavacius*, *Mystus seenghala*, *Heteropneustus fossilis* and *Channa punctatus*, *Channa striatus* are recorded from lakes, dams and rivers around. He also stated that no fishing activities are conducted in Dimiya dam.

15. Lastly a wild life guard Sh. Yogesh Kumar Purohit in Wild life wing of Forest Department was contacted to know presence of crocodiles in and around Dungarpur who informed that Marsh or Broad Snouted Crocodile (*Crocodylus palustris*) is recorded from Mahi Dam, Margiya Dam, Lodisar Dam and Kadana Backwaters. Whenever a crocodile is rescued from human habitation where they sometimes reach they are scientifically caught and released in Mahi Dam.

16. Some butterflies observed around the dam area are Blue Pansy, Plain Tiger, Small Pierot, Orange butterfly.

17. This first visit was made with an objective to collect general information on presence of crocodiles, people's reaction about its presence and to collect available information with government agencies directly or indirectly involved in maintenance of dam its fauna and local self governing body in the village besides the actual governmental custodian which is 'Water Resource Development Department' or 'Public Health and Engineering Department' (PHED)

Second Visit was made on 18th - 19th October, 2023

18. **Objective:** Special Focus on searching crocodile nesting sites, enriching list of birds and vegetation to assess habitat of crocodile in relation to existing intake and alternatively proposed intake.

19. We reached directly to the site where the suggested alternative water intake was considered temporarily owing to the fact that water remains present there all the year round so that an uninterrupted supply of water could be made to Dungarpur even in summer months. This required Bathymetric survey to substantiate it as informed by engineers to finally take a decision on new intake.

20. Met a local family living there in Kalji Hiraji alone to understand the presence of Crocodile (*Crocodylus palustris*) and if they were affected in some way by its presence. I saw some ladies washing kitchen utensils at the edge of dam water and their goats drinking water comfortably while there were two crocodiles lying just 15 meters away over an exposed mound.

21. Some time was spent asking them questions related to their day today life, problems related to water, agriculture, cattle rearing and access to the city to fetch ration and other requirements. Once they became comfortable I requested a grown up boy called Asheesh from that family to accompany me on my exploration visit along the edge of the hill which he happily agreed. While looking for signs of nesting I came across some 14-16 sites where the soil was scraped and some cavities were observed, I found them very interesting. On asking about them the local boy Asheesh accompanying me confirmed that the crocodile in breeding season dig these cavities on sloping edges located at a distance of 5-10 m in my observation for that specific site. I took a round of the whole hill wherever it was practically possible and then visited the edge of the adjacent hill to look for more nesting sites which were not found there.

22. Selection of nesting sites largely depends upon direction of Sun, duration of sunlight availability in a day and access of breeding crocodiles to the nesting site from water so that crocodiles may guard their nests during breeding season. When the hatchlings come out they can be taken to drop in the main water body easily in the mouth by female crocodiles.

23. Two crocodiles **were** observed near the mound out of which one was 8-10 ft large while the other was young about 4-5 ft long only just opposite the hut of the local family in the water. Later while surveying the edge of the dam for nesting sites I came across 3 more large crocodiles floating in the dam water.

24. Birds observed near Kal ji Hiraji's house were Spotted Fantail Warbler, flock of some Eurasian Thick Knee just next to crocodile nesting site, Ashy Crowned Sparrow Lark, Red Wattled Lapwing, Woolly necked Stork in flight over the water, Great White Egret.

25. Aquatic Vegetation observed on return at the old existing intake presently in use was Trapa, Reeds (*Typha angustata*), Polygonum glabra with pink flowers, water lilies with white flowers, Ipomea sp.

Third visit was made on 20-21st November to finally revisit the nesting site and to take observations on habitat , vegetation, birds and crocodiles.

26. The visit was done with ADB's Environmental Safeguard specialist Sh. Govind Singh Rathore and along the team of engineers with whom detailed discussions were done on preserving the crocodile habitat and nesting site, to assess the proposed impact of water intake if any on surroundings and to document some more bio-diversity parameters.

27. It was observed that with the decreasing temperature about 20 Crocodiles were seen at different spots including a sand bar opposite the present water intake and at edges of the dam basking in the sun from morning till afternoon. Many of them were large, about 3-4 mtr long.

28. The nesting site explored in the last visit was shown to ADB Environment safeguard specialist which was plotted on Google earth for its precise location.

29. Vegetation observed this side was mainly Teak (*Tectona grandis*), Papdi (*Holoptelia integerrima*), Khakhra (*Butea monosperma*), Ratanjot (*Jatropha* sps), Ronjh (*Acacia leucophloea*), Khajoor (*Phoenix* sps), Babol (*Acacia nilotica*), Mango, Lantana and *Polygonum glabra* at the edge and large stretch of edge covered by Ipomea sp. which was well used by birds to perch and feed on insects dwelling over it. Though we recommend to manage its spread.

30. Birds observed here along water were Purple heron, Pond heron, Lily trotters like Grey headed Swamphen, White Breasted Waterhen, Bronze Winged Jacana, Great white Egret, Little Egret, Cattle Egret, Asian Openbill, Red Wattled Lapwing, Common Sandpiper, Green Sandpiper, Wood Sandpiper, Common Red Shank, Glossy ibis, River Tern, Red Naped Ibis, Black Headed Ibis, White Breasted Kingfisher, Pied Kingfisher, Wire Tailed Swallow, Dusky Craig Martin, Green Bee Eater.

31. Other birds recorded were Green Bee Eater, Purple Sunbird, Ashy Prinia, Great Tit, Common Iora, Long Tailed Shrike, Little Minivet, Asian Paradise Flycatcher, White browed Fantail, Indian Robin, Verditer Flycatcher, Wood Shrike, Shikra, Oriental White eye and migratory Lesser White throat and Black Red Start

IUCN Status of Mugger or Broad snout Crocodile (*Crocodylus palustris*)

* It has been listed as vulnerable in IUCN red list : Vulnerable

*Listed in Cites Appendix 1 so commercial Trade is prohibited.

*In India it has been protected since 1972 under provisions of Wildlife Protection Act in Schedule 1

IUCN -SSC - Crocodile specialist Group

32. The 23 living species of alligators, crocodiles, caimans and Gharials around the world are actively being conserved by IUCN-SSC Crocodile Specialist Group (CSG), a global network of biologists, wildlife managers, government officials, independent researchers, non-government (NGO) representatives, farmers, traders, tanners, fashion industry leaders and private companies. It was established in 1971. The mission of the IUCN_SSC crocodile specialist group is to assist the International Union for Conservation of Nature (IUCN) and the Species Survival Commissions (SSC) in meeting their missions with regard to the conservation, management and sustainable use of crocodilians.

33. A total of 1193 Muggers (Broad Snouted Crocodile) were released to restock the population in 28 protected areas in between 1978-1992.

Mugger Crocodiles are medium sized crocodiles found in the Indian subcontinent.

34. They are opportunistic predators that eat a variety of prey, including fish, birds, mammals and reptiles. Mugger Crocodiles live in a variety of habitats, including rivers, lakes, marshes and even coastal areas. They prefer slow-moving water with plenty of vegetation.

35. Reproduction cycle starts earliest at the onset of cold season with courtship and mating. Between February and June females dig 35-56 cm holes between 1 to 2000M away from waterside based on their preference of safety, ease to carry hatchlings, direction of Sun, soil profile type and intensity of intrusion and disturbance availability of food and water in the vicinity.

36. They lay upto two clutches with 8-46 eggs each It takes about half an hour to complete the laying process. Thereafter the female scrapes sand over its nest to close it. Hatching season is 2 months later, between April and June which may slightly vary due to seasonal variations.

37. Females excavate the young and pick them up in their snout and take them to water. Both male and female protect young for up to one year. Healthy hatchlings develop at the temperature between 28-33 degree Celsius. They are 26-31 Cm and weigh about 75 gm.

38. Hatchlings grow 4.25 cm per month and reach body length of 90-170 cm when 2 years old.

Findings

Flora of the area

39. Dungarpur, located in the southern part of Rajasthan, India, is characterized by a semi-arid climate, and its vegetation often falls under the category of Southern Tropical Dry Deciduous forest. In such ecosystems, the dominant tree species are adapted to the dry conditions and typically shed their leaves during the dry season. These forests play a crucial role in supporting biodiversity and providing habitat for various flora and fauna adapted to arid and semi-arid environments.

40. The forest is described as having various characteristics. It is indicated that the forest is primarily composed of 'teak trees, and the ecosystem supports diverse flora and fauna.

41. The second category within this classification is the (Southern Tropical Dry Deciduous). Within this category, there are subcategories, such as (C1a) (Very dry teak forest).

In the context of 5B,' it discusses the (Northern Tropical Dry Deciduous Forest). The details suggest a classification system for different types of dry deciduous forests, emphasizing specific characteristics and features of each."

42. Common tree species that may be found in Southern Tropical Dry Deciduous forests in Dungarpur, Rajasthan, include:

- **Teak (*Tectona grandis*):** A prominent and economically important tree known for its high-quality timber.
- **Salai (*Boswellia serrata*):** Also known as Indian frankincense, this tree is valued for its resin.
- **Anogeissus pendula (Dhawada):** A deciduous tree that is well-adapted to dry conditions.
- **Babul (*Acacia nilotica*):** A thorny tree commonly found in arid and semi-arid regions.
- **Khair (*Acacia catechu*):** Another species of Acacia known for its hard and durable wood.
- **Bamboo (*Dendrocalamus strictus*):** Some species of bamboo are present in these forests.

43. The specific composition of plant species can vary based on factors such as soil type, water availability, and human activities. These forests are crucial for maintaining ecological balance, supporting wildlife, and providing various ecosystem services.

Trees noted near Dimiya dam area and association with birds

1. **Teak (*Tectona grandis*):** While teak may not directly provide food for birds, its large canopy and sturdy branches can offer perching and nesting sites.
2. **Khakhra (*Butea monosperma*):** The Flame-of-the-Forest produces bright orange to scarlet flowers, which can attract nectar-feeding birds like sunbirds. The tree also provides perching and nesting opportunities.
3. **Ronjh (*Acacia leucophloea*):** Acacia trees, including *Acacia leucophloea*, are known for providing habitat and food for various bird species. Birds may use the branches for perching, and some species may feed on insects associated with the tree.
4. **Papdi (*Holoptelia integrifolia*):** The Papdi tree may provide food and shelter for birds. Insects help in pollination and also attract insect-eating birds.
5. **Thoor (*Euphorbia* sp.):** birds may be attracted to the plant for shelter or potential nesting sites. However, many *Euphorbia* species are toxic and should be handled with care.
6. **Khajoor (*Phoenix sylvestris*):** Date Palm trees produce dates, which can attract fruit-eating birds. Additionally, the palm fronds may offer nesting sites for certain bird species.
7. **Ardu (*Ailanthus excelsa*):** Ailanthus trees may attract insects, and birds that feed on insects may be found in the vicinity. The tree's canopy can provide perching and nesting opportunities.
8. **Babool (*Acacia nilotica*):** Acacia trees are known for their thorns, which can provide protection for birds nesting in their branches. Birds may also feed on insects associated with the tree.
9. **Azadirachta indica (Neem):** Neem trees provide shelter and attract insects. Birds, especially insectivores, may feed on the insects found on neem trees. Some bird species may consume neem seeds.
10. **Prosopis cineraria (Khejri):** Khejri trees are a valuable resource for birds in arid regions. They provide shade, and the foliage is browsed by herbivorous birds. The seeds are also consumed by various bird species. Insects attracted to the tree can attract insectivorous birds.

11. **Ziziphus spp.** (Jujube): Jujube trees produce small, edible fruits that are attractive to birds, including bulbuls and barbets. The dense foliage provides shelter and nesting sites for birds.
12. **Mangifera indica** (Mango): Mango trees produce large, fleshy fruits that are attractive to a variety of birds, including Parrots, Mynas, and Bulbuls. The robust branches and thick foliage of mango trees can serve as nesting sites for birds.
13. **Lantana**: Lantana flowers attract butterflies and hummingbirds, contributing to the overall biodiversity in your garden.
14. **Polygonum glabra**: Birds may be attracted to this plant if it produces seeds or provides shelter for insects that birds feed on.


Other terrestrial flora includes –

44. *Sterculia urens*, *Datura metel*, *Croton bonplandianus*, *Ipomoea carnea*, *Parthenium hysterophorus*, *tribulus terrestris*, *Lindenbergia indica*, *Tridax procumbens*, *Evolvulus sps*, *Rungia sps*,

45. Aquatic flora in dam includes - *Ludwigia sedoides*, *Nymphoides indica*, *Nymphaea alba*, *Eclipta abla* and *Ipomoea aquatica*



Teak (Tectona grandis) flowering



Nymphoides indica



Acacia leucophloea



Croton bonplandianus

*Euphorbia caducifolia**Khajoor (Phoenix sylvestris)**Ratan Jot (Jatropha sp.)**Sterculia urens*

46. Aquatic flora in dam includes - *Ludwigia sedoides*, *Nymphoides indica*, *Nymphaea alba*, *Eclipta alba* and *Ipomoea aquatica*

47. **Avifauna observed in area:** - The avifaunal profile recorded during the site visits is dominated by wetland-associated species were recorded near the dam. They include resident species such as Indian Pond-heron, Red-naped Ibis, White-throated Kingfisher, White-breasted Water hen, Red-wattled Lapwing, Common Kingfisher, Purple Heron and migratory species such as Common Sandpiper,, Asian Woollyneck. It is beginning of winter so more winter migration will be observed and many new species of birds will be seen here.

48. A good range of open scrub such as Grey Francolin, Green Bee-eater, Laughing Dove, Long-tailed Shrike, Black Drongo, Indian Robin, Brahminy Starling, Babblers and Ashy-crowned Sparrow Lark.

49. Another significant component comprises birds associated with habitation, cultivation and gardens, including Indian Peafowl, Common Hoopoe, Jungle Babbler, Common Myna, Red-vented Bulbul, Ashy Prinia, Common Tailorbird, Purple Sunbird and House Sparrow.

50. There is also a distinct component comprising birds showing a preference for forests, plantations, groves or orchards, including Alexandrine Parakeet, Indian Grey Hornbill, Southern Coucal etc.

51. Raptors sighted include Shikra. Appendix 2 present the photo log of some birds sighted during the site survey

Resident and Migratory Avifauna

52. The area is part of the massive avian migratory channel called the Central Asian Flyway (CAF), which spans the entire Indian subcontinent. Thus, the area lies in the path of various winter migratory birds entering the Indian subcontinent from the north and headed farther south. With its diversity of habitats, the area is very likely to be providing seasonal habitats or staging-points to many of these visitors. The dam is well-known to be the winter-habitats of a number of visiting water-birds. The area is also known to be a destination for a few summer visitors, as also, part of the passage traversed by migratory birds headed elsewhere. Migratory bird species known to be associated with the area are listed in Appendix

IUCN listed avifauna

Scientific Name	Common Name	Red Category	List	Movement pattern
<i>Sterna aurantia</i>	River Tern	VU		Not a Migrant
<i>Threskiornis melanocephalus</i>	Black-headed Ibis	NT OR LR/NT		Full Migrant
<i>Ciconia episcopus</i>	Asian Woollyneck	NT OR LR/NT		Not a Migrant
<i>Palaeornis eupatria</i>	Alexandrine Parakeet	NT OR LR/NT		Nomadic



53. **River Tern:** River Tern is a widespread resident bird usually seen flying over rivers and lakes in Southern Rajasthan. It has Vulnerable status (VU) in IUCN red list. It had pointed wings, orangish bill, black cap, greyish white upper parts. Behaviour of feeding is to take plunge in water and pick up a fish or sometimes an object. They nest on islands or sand bars located in the middle of water bodies. Many River Terns were observed sitting and flying over the water of Dimiya Dam. This bird species uses sand bars or islands for nesting which are located far from our work site so it does not seem to be affected.

54. **Black Headed Ibis:** Widespread resident bird mainly white. The breeding adult had naked black head, white lower neck plumes. Feeds in agriculture land scape shallow canals and at the edge of water bodies over tubers, crustaceans, frogs, snakes etc. The IUCN red list status is Near Threatened (NT). It nest on big tree which are not there in the middle of water bodies. No nesting was observed in September when first visit was made which is its breeding season.

55. **Asian Woollyneck Stork :** Widespread resident bird with black body and white woolly white neck, black skull cap. Listed in IUCN red list as near Threatened. Seen feeding over fresh water wetlands. Some Woolly Necked Storks were seen individually at the dam site but no breeding was observed here.

56. **Alexandrine Parakeet :** Widespread resident bird seen in forest and wooded areas and cultivation. A very large parakeet with maroon shoulder patch. Male with a black chin stripe and pink collar. Can mimic human voice well so were under threat since it was caged at pet bird at home before the legal protection was given under Wildlife Protection Act 1972. These birds mainly nest in big trees in forest areas, but no nesting was observed in area near dam.

The crocodiles of Dimiya dam

57. Crocodilians, encompassing Crocodiles, Alligators, and Gavials/Gharials, caimans stand as well-known inhabitants widely distributed across tropical and subtropical ecosystems. The global count of Crocodilian species totals 23. Within the Order Crocodylia, three families exist: (1) Alligatoridae, represented by Caimans/Alligators, (2) Crocodylidae, featuring *Crocodylus palustris*, commonly known as the Mugger Crocodile, and (3) Gavilidae, home to the Gavial.

58. The mugger, a medium size crocodile with a maximum length of approximately 5-7 meters. In their juvenile stage, these muggers typically exhibit a light tan coloration, adorned with distinctive black cross banding along their body and tail. Upon reaching adulthood, their coloration transitions to a predominantly grey to brown colours, with minimal banding remains.

59. Notably, enlarged scutes around the throat area in adults may serve a protective function, particularly when navigating through shallow, swampy regions. Described as a medium to large species, muggers attain sizes ranging from 5 to 7 meters.

Mugger Crocodile Reproductive Behaviour

60. Mugger crocodiles, known as hole-nesting species, exhibit a unique nesting behaviour characteristic of other species that lay eggs in concealed locations. The egg-laying ritual aligns with the annual dry season, a period when environmental conditions are conducive to the survival of the offspring. Female muggers attain sexual maturity at approximately 1.82 meters and typically lay clutches comprising 25-30 eggs, as documented by Whitaker and Whitaker (1989). Intriguingly, these nests are found in a diverse array of habitats, with instances of females nesting at the entrances or even inside burrows..

61. Notably, mugger crocodiles are known to lay two clutches within a single year. The incubation period spans 55-75 days.

Aestivation Practices in Crocodiles

62. Crocodiles also exhibit a fascinating habit of aestivation, a period of reduced activity during the summer season. During this time, crocodiles seek refuge in deep burrows that naturally clear out. As a result, crocodiles are compelled to bury themselves in the mud to maintain adequate humidity levels.

63. Similarly, as the dry season commences, females select nesting sites strategically positioned in damp, warm locations near bushes or trees. Under the cover of darkness, they meticulously dig a hole half a meter deep into the sand to deposit their eggs, as described by Groombridge and Wright (1982). The eggs of the Marsh Crocodile measure 9×6 cm, possess an equal dimension at both ends, and feature a hard calcareous shell. After covering the nest, the female may linger on the site to dampen the soil. Hatchlings employ a small, sharp piece of lime on the top of their snouts to facilitate their emergence from the soil. Subsequently, the young crocodiles undergo rapid growth, adapting to their surroundings.

Figure 2:: Map Showing nesting sites of crocodiles in relation to intake site



Figure 3: Google earth map showing points where Crocodiles were sighted during site visit



Dietary Preferences Across Life Stages

64. The dietary preferences of mugger crocodiles evolve with their life stages. Juveniles primarily subsist on a diet comprising crustaceans, insects, and small fish. In contrast, adults consume a broader range of prey, including larger fish, amphibians, reptiles (particularly snakes and possibly turtles), birds, and even mammals such as monkeys. Notably, large adult crocodiles have been documented preying on sizable animals like deer and buffalo species, demonstrating the impressive adaptability and predatory prowess of these formidable creatures.

Impact of Crocodiles on Construction Activities in Lakes and Mitigation Measures

65. Construction activities in Demiya dam can have significant impacts on the resident crocodile populations. Understanding these impacts and implementing effective mitigation measures is crucial to ensure the coexistence of human development and wildlife conservation.

Impacts:

66. **Habitat Disruption:** Construction activities may lead to habitat disruption, affecting the natural nesting and basking sites of crocodiles. Excavation, dredging, land reclamation and use of heavy machinery can alter the shoreline and vegetation cover, impacting the crocodiles' habitat.

67. **Disturbance during Nesting Season:** Construction activities may coincide with the crocodile nesting season, causing disturbances that can lead to the abandonment of nests. Vibrations, noise, and human presence can be stressful for nesting females, potentially affecting egg viability.

68. **Increased Human-Crocodile Conflict:** Construction activities near lakes may attract crocodiles to new areas, increasing the potential for human-crocodile conflicts. Encounters between construction workers and crocodiles can pose risks to both parties.

Mitigation Measures:

69. There may be temporary impacts during construction. Works of pump replacement, refurbishment of intake structure and laying of rising mains from intake to WTP are planned. Potential impacts are due to soil erosion, water pollution, noise, and dust pollution. Worker's camp should not be located near dam, no storage of construction materials and equipment storage near dam, hauling activity during day time only & construction only during dry season, and education about protecting the flora and fauna should be provided. Ultimately, it is important to ensure that the construction is carried out in an environmentally responsible manner to minimize the impact on the ecosystem. The DBO contractor will be required to:

Mitigation measures

- Prepare Environment management plan before starting any work.
- ***Schedule the construction works during low water level period – late winter months to pre monsoon (November - May); ensure that works are completed during the same period to prior to onset of monsoon;***

Mitigation measures during Construction phase

- All project related site staff, construction workers and supervisors, shall be made aware of the sensitive sites, and prevent any harm or damage or disturbance to trees, vegetation, wildlife, birds etc.,

- Schedule works during dry season to avoid contaminated runoff from the work sites entering lake; clear the sites of materials, debris, and consolidated the refilled trenches prior to onset of monsoon
- No construction camps (workers accommodation, material / waste / soil storage) should be established within 200 m from the boundary of dam; camps should not be located close to drainage lines/streams that flow into dam
- Movement of workers and staff should be confined to work site, and not be allowed in dam area which may disturb the sensitive area; ensure via strict supervision no poaching, fishing, cutting / damaging trees/vegetation or wildlife, birds etc.,
- Proper accommodation and facilities shall be provided within the camps, and workers shall not use the lake or surroundings for open defecation, bathing, or fishing / hunting, collecting firewood etc. Contractor should put in place, a proper system to monitor the staff and workers to prevent damage/disturbance.
- ***Implement sediment and erosion control measures to prevent soil erosion and sedimentation in the dam. Prevent entry of silt-laden / contaminated runoff into dam or drains leading to dam from the construction sites or construction camps. Appropriate measures such as silt traps, sedimentation ponds, and filtration systems should be installed to prevent sediment and other pollutants from entering the water supply. Soil stabilization measures should also be taken to prevent soil erosion during construction, Construction near dam to be planned in dry seasons only.***
- ***Place storage areas for fuels and lubricants away from any drainage leading to water bodies;***
- ***Store fuel, construction chemicals etc., on an impervious floor, also avoid spillage by careful handling.***
- Do not use equipment that generate heavy noise, ground vibration, dust etc., (such as pneumatic drills, dozers etc.), within 100 m of Dam. Adapt manual excavation as far as possible
- ***Construction sites often generate significant amounts of dust that can impact nearby habitats. Dust suppression measures, such as watering down exposed soil, can help to reduce dust levels.***
- ***Dispose any wastes generated by construction activities in designated sites; and***
- ***Monitor the project closely throughout construction to ensure that all mitigation measures are being implemented effectively and that any issues are identified and addressed promptly.***
- ***Conduct surface quality inspection according to the environmental management plan (EMP).***
- ***Conduct continuous consultations with the local people during the works***
- ***Install inlet of intake pipe in the dam with appropriate screen to avoid entry of aquatic organisms into inlet***
- ***Select a construction methodology that is least disturbing, and appropriate for the in-situ soil condition, and able to complete the construction work prior to onset of monsoon.***
- ***Erect temporary barriers to form enclosed construction area with least disturbance***
- ***Implement work site safety at works in water body***

Mitigation measures during operation phase

- ***Clear the work site after completion at least to pre project conditions, ensure that there are no materials, debris, spills etc., and prior to removal of temporary barriers / coffer dam***

Recommendations

70. **Seasonal Restrictions:** Schedule construction activities to avoid critical periods in the crocodile's life cycle, such as nesting and hatching seasons. Implement seasonal restrictions to minimize disturbances during sensitive times.

71. **Buffer Zones:** Establish buffer zones around known crocodile habitats where construction activities are restricted. This helps maintain undisturbed areas crucial for crocodile nesting and other essential behaviour.

72. **Maintain dead storage in dam :-** Do not utilize the dead storage of dam for supply; ensure that dead storage is always available in the dam all times; limit the abstraction to allowable limits

73. **Educational Programs:** Conduct educational programs for construction workers, local communities, and relevant stakeholders. Raise awareness about the presence of crocodiles, their behaviour, and the importance of coexisting with these species.

74. **Secure Construction Sites:** Implement measures to secure construction sites, such as fencing and signage, to prevent crocodile ingress. Restrict access to areas where crocodile presence is likely, minimizing the risk of encounters.

75. **Wildlife Monitoring and Rescue Teams:** Establish wildlife monitoring teams to track crocodile movements during construction. Implement rescue teams trained to safely relocate crocodiles away from construction sites if necessary.

76. **Environmental Best Practices:** Adopt environmentally friendly construction practices to minimize habitat disturbance. Use silt fences and erosion control measures to prevent sedimentation in water bodies, maintaining water quality for crocodile habitats.


77. **Collaboration with Conservation Agencies:** Collaborate with local wildlife conservation agencies like forest department, NGOs to develop and implement effective mitigation measures. Engage in research and conservation efforts to better understand and protect crocodile populations in the area. Further this site can be developed as bird and Crocodile conservation and watching site



Appendix 1- Photos



1. Dam and its surround pictures

	
General view of Demiya dam	General view of Demiya dam
	
Present Intake close-up	Intake from other side of lake
	
Dam embankment	Dam – Spilover
	

Spilover from downstream side	Huts of local villagers
	
Domestic cattle and poultry	Typical local mud hut
	
Great Egret (<i>Casmerodius albus</i>)	Little Egret (<i>Egretta garzetta</i>)
	
Little Cormorant (<i>Microcarbo niger</i>) and Black-winged Stilt (<i>Himantopus himantopus</i>)	Purple Heron (<i>Ardea purpurea</i>)
	
Indian Pond-heron (<i>Ardeola grayii</i>)	River Tern (<i>Sterna aurantia</i>)

	
Asian openbill stork (<i>Anastomus oscitans</i>)	Glossy Ibis (<i>Plegadis falcinellus</i>)
	
Black-headed ibis (<i>Threskiornis melanocephalus</i>)	Indian thick-knee (<i>Burhinus indicus</i>)
	
Common Kingfisher (<i>Alcedo atthis</i>)	White-breasted Kingfisher (<i>Halcyon smyensis</i>)
	

	
Purple Sunbird (<i>Cinnyris asiaticus</i>) - female	Purple Sunbird (<i>Cinnyris asiaticus</i>)
	
Ashy prinia (<i>Prinia socialis</i>)	Yellow-eyed Babbler (<i>Chrysomma sinense</i>)
	
Great tit (<i>Parus major</i>)	Long tail shrike (<i>Lanius Schach</i>)
	
Common lora (<i>Aegithina tiphia</i>)	Asian Paradise-flycatcher (<i>Terpsiphone paradisi</i>)

	
Black Redstart (<i>Phoenicurus ochruros</i>) male	Spotted Dove (<i>Stigmatopelia chinensis</i>)
	
Indian White-eye (<i>Zosterops palpebrosus</i>)	Small Minivet (<i>Pericrocotus cinnamomeus</i>)
	
White-bellied Drongo (<i>Dicrurus caerulescens</i>)	Yellow Footed Green Pigeon (<i>Treron phoenicopterus</i>)
	
Island in front of present intake	Basking Crocodile along edge of Dam



Crocodile basking along with Ipomoea vegetation

Crocodile basking at an island at Dimiya Dam

Appendix -2 - List of Birds observed in site visits

S. No	Scientific Name	Common Name	Red Category	List	Movement pattern
1.	<i>Sterna aurantia</i>	River Tern	VU		Not a Migrant
2.	<i>Threskiornis melanocephalus</i>	Black-headed Ibis	NT OR LR/NT		Not a Migrant
3.	<i>Ciconia episcopus</i>	Asian Woollyneck	NT OR LR/NT		Not a Migrant
4.	<i>Dendrocygna javanica</i>	Lesser Whistling-duck	LC OR LR/LC		Not a Migrant
5.	<i>Leiopicus maharattensis</i>	Woodpecker	LC OR LR/LC		Not a Migrant
6.	<i>Alcedo atthis</i>	Common Kingfisher	LC OR LR/LC		Not a Migrant
7.	<i>Ceryle rudis</i>	Pied Kingfisher	LC OR LR/LC		Not a Migrant
8.	<i>Alexandrinus krameri</i>	Rose-ringed Parakeet	LC OR LR/LC		Not a Migrant
9.	<i>Spilopelia senegalensis</i>	Laughing Dove	LC OR LR/LC		Not a Migrant
10.	<i>Amaurornis phoenicurus</i>	White-breasted Waterhen	LC OR LR/LC		Not a Migrant
11.	<i>Porphyrio porphyrio</i>	Purple Swampphen	LC OR LR/LC		Not a Migrant
12.	<i>Tringa totanus</i>	Common Redshank	LC OR LR/LC		Full Migrant
13.	<i>Tringa ochropus</i>	Green Sandpiper	LC OR LR/LC		Full Migrant
14.	<i>Tringa glareola</i>	Wood Sandpiper	LC OR LR/LC		Full Migrant
15.	<i>Actitis hypoleucos</i>	Common Sandpiper	LC OR LR/LC		Full Migrant
16.	<i>Vanellus indicus</i>	Red-wattled Lapwing	LC OR LR/LC		Not a Migrant
17.	<i>Microcarbo niger</i>	Little Cormorant	LC OR LR/LC		Not a Migrant
18.	<i>Phalacrocorax fuscicollis</i>	Indian Cormorant	LC OR LR/LC		Not a Migrant
19.	<i>Ardea purpurea</i>	Purple Heron	LC OR LR/LC		Not a Migrant
20.	<i>Ardea alba</i>	Great White Egret	LC OR LR/LC		Not a Migrant
21.	<i>Bubulcus ibis</i>	Cattle Egret	LC OR LR/LC		Not a Migrant
22.	<i>Ardeola grayii</i>	Indian Pond-heron	LC OR LR/LC		Not a Migrant
23.	<i>Plegadis falcinellus</i>	Glossy Ibis	LC OR LR/LC		Not a Migrant
24.	<i>Pseudibis papillosa</i>	Red-naped Ibis	LC OR LR/LC		Not a Migrant
25.	<i>Anastomus oscitans</i>	Asian Openbill	LC OR LR/LC		Not a Migrant
26.	<i>Lanius schach</i>	Long-tailed Shrike	LC OR LR/LC		Not a Migrant

S. No	Scientific Name	Common Name	Red List Category	Movement pattern
27.	<i>Hirundo smithii</i>	Wire-tailed Swallow	LC OR LR/LC	Not a Migrant
28.	<i>Prinia socialis</i>	Ashy Prinia	LC OR LR/LC	Not a Migrant
29.	<i>Prinia inornata</i>	Plain Prinia	LC OR LR/LC	Not a Migrant
30.	<i>Chrysomma sinense</i>	Yellow-eyed Babbler	LC OR LR/LC	Not a Migrant
31.	<i>Cinnyris asiaticus</i>	Purple Sunbird	LC OR LR/LC	Not a Migrant
32.	<i>Ploceus philippinus</i>	Baya Weaver	LC OR LR/LC	Not a Migrant
33.	<i>Halcyon smyrnensis</i>	White-breasted Kingfisher	LC OR LR/LC	Not a Migrant
34.	<i>Merops orientalis</i>	Asian Green Bee-eater	LC OR LR/LC	Not a Migrant
35.	<i>Ardea intermedia</i>	Intermediate Egret	LC OR LR/LC	Not a Migrant
36.	<i>Himantopus himantopus</i>	Black-winged Stilt	LC OR LR/LC	Not a migrant Migrant
37.	<i>Curruca curruca</i>	Lesser Whitethroat	LC OR LR/LC	Full Migrant
38.	<i>Streptopelia chinensis</i>	Spotted Dove	LC OR LR/LC	Full Migrant
39.	<i>Gallinula chloropus</i>	Common Moorhen	LC OR LR/LC	Not a Migrant
40.	<i>Egretta garzetta</i>	Little Egret	LC OR LR/LC	Not a Migrant
41.	<i>Passer domesticus</i>	House Sparrow	LC OR LR/LC	Not a Migrant
42.	<i>Copsychus saularis</i>	Oriental Magpie-robin	LC OR LR/LC	Not a Migrant
43.	<i>Palaeornis eupatria</i> <i>Francolinus</i>	Alexandrine Parakeet	NT OR LR/NT	Nomadic resident
44.	<i>pondicerianus</i>	Grey Francolin	LC OR LR/LC	Not a Migrant
45.	<i>Pavo cristatus</i>	Indian Peafowl	LC OR LR/LC	Not a Migrant
46.	<i>Ocyrceros birostris</i>	Indian Grey Hornbill	LC OR LR/LC	Not a Migrant
47.	<i>Upupa epops</i>	Common Hoopoe	LC OR LR/LC	Full Migrant
48.	<i>Hierococcyx varius</i>	Common Hawk-cuckoo	LC OR LR/LC	Full Migrant
49.	<i>Treron phoenicopterus</i>	Yellow-footed Green-pigeon	LC OR LR/LC	Not a Migrant
50.	<i>Accipiter badius</i>	Shikra	LC OR LR/LC	Not a Migrant
51.	<i>Dendrocitta vagabunda</i>	Rufous Treepie	LC OR LR/LC	Not a Migrant
52.	<i>Corvus splendens</i> <i>Pericrocotus</i>	House Crow	LC OR LR/LC	Not a Migrant
53.	<i>cinnamomeus</i>	Small Minivet	LC OR LR/LC	Not a Migrant
54.	<i>Rhipidura aureola</i>	White-browed Fantail	LC OR LR/LC	Not a Migrant
55.	<i>Dicrurus macrocercus</i>	Black Drongo	LC OR LR/LC	Not a Migrant
56.	<i>Dicrurus caerulescens</i>	White-bellied Drongo	LC OR LR/LC	Not a Migrant
57.	<i>Aegithina tiphia</i>	Common Iora	LC OR LR/LC	Not a Migrant
58.	<i>Eumyias thalassinus</i>	Verditer Flycatcher	LC OR LR/LC	Full Migrant
59.	<i>Saxicoloides fulicatus</i>	Indian Robin	LC OR LR/LC	Not a Migrant
60.	<i>Phoenicurus ochruros</i>	Black Redstart	LC OR LR/LC	Full Migrant
61.	<i>Sturnia pagodarum</i>	Brahminy Starling	LC OR LR/LC	Not a Migrant
62.	<i>Acridotheres tristis</i>	Common Myna	LC OR LR/LC	Not a Migrant
63.	<i>Ptyonoprogne concolor</i>	Dusky Crag Martin	LC OR LR/LC	Not a Migrant
64.	<i>Pycnonotus cafer</i>	Red-vented Bulbul	LC OR LR/LC	Not a Migrant
65.	<i>Prinia hodgsonii</i>	Grey-breasted Prinia	LC OR LR/LC	Not a Migrant

S. No	Scientific Name	Common Name	Red List Category	Movement pattern
66.	<i>Orthotomus sutorius</i>	Common Tailorbird	LC OR LR/LC	Not a Migrant
67.	<i>Eremopterix griseus</i>	Ashy-crowned Sparrow-lark	LC OR LR/LC	Not a Migrant
68.	<i>Streptopelia decaocto</i>	Eurasian Collared-dove	LC OR LR/LC	Not a Migrant
69.	<i>Parus major</i>	Great Tit	LC OR LR/LC	Not a Migrant
70.	<i>Burhinus indicus</i>	Indian Thick-knee	LC OR LR/LC	Not a Migrant
71.	<i>Tephrodornis pondicerianus</i>	Common Woodshrike	LC OR LR/LC	Not a Migrant
72.	<i>Terpsiphone paradisi</i>	Indian Paradise-flycatcher	LC OR LR/LC	Not a Migrant
73.	<i>Argya striata</i>	Jungle Babbler	LC OR LR/LC	Not a Migrant
74.	<i>Zosterops palpebrosus</i>	Indian White-eye	LC OR LR/LC	

Source : Birds observed during site visit

Appendix -3 - List of Flora observed in site visits

1. Teak (*Tectona grandis*)
2. Salai (*Boswellia serrata*)
3. Dhawada (*Anogeissus pendula*)
4. Babul (*Acacia nilotica*)
5. Khair (*Acacia catechu*)
6. Bamboo (*Dendrocalamus strictus*)
7. Teak (*Tectona grandis*)
8. Khakhra (*Butea monosperma*)
9. Ronjh (*Acacia leucophloea*)
10. Papdi (*Holoptelia integrifolia*)
11. Thoor (*Euphorbia sp.*)
12. Khajoor (*Phoenix sylvestris*)
13. Ardu (*Ailanthus excelsa*)
14. Babool (*Acacia nilotica*)
15. Neem (*Azadirachta indica*)
16. Khejri (*Prosopis cineraria*)
17. Jujube (*Ziziphus spp.*)
18. Mango(*Mangifera indica*)
19. *Lantana camera*
20. *Polygonum glabra*
21. Kadaya (*Sterculia urens*)
22. Dhatura (*Datura metel*)
23. *Croton bonplandianus*
24. Congress grass (*Parthenium hysterophorus*)
25. Gokharu (*Tribulus terrestris*)
26. *Lindenbergia indica*
27. *Tridax procumbens*
28. *Evolvulus sps*
29. *Rungia sps*
30. *Ludwigia sedoides*
31. *Nymphoides indica*
32. *Nymphaea alba*
33. *Eclipta abla*
34. *Ipomoea aquatica*

प्राकृष- 1

दूँगरपुर जिले के जलाशयों का मत्स्य टेका एवं इनसे प्राप्त आय का वर्षवार विवरण

वर्ष	जलाशय का नाम	टेका राशि	टेकेदार/फर्म का नाम
2019-20	1. बंध सोम कमला आंबा	2,13,88,955/-	श्री डेविड नारैद बदारकर, नई दिल्ली
	2. बंध अमरपुरा	06,03,000/-	श्री नरेन्द्र शील, जयपुर
	3. बंध मारगिया	05,37,600/-	श्री शंकर लाल चौधरी, उदयपुर
	4. बंध डीमिया	-	टेका सूची में सम्मिलित नहीं है।
2020-21	1. बंध सोम कमला आंबा	2,39,33,220/-	श्री डेविड नारैद बदारकर, नई दिल्ली
	2. बंध अमरपुरा	06,75,360/-	श्री नरेन्द्र शील, जयपुर
	3. बंध मारगिया	06,02,112/-	श्री शंकर लाल चौधरी, उदयपुर
	4. बंध डीमिया	-	टेका सूची में सम्मिलित नहीं है।
2021-22	1. बंध सोम कमला आंबा	टेका नहीं हुआ।	-
	2. बंध अमरपुरा	07,58,403/-	श्री नरेन्द्र शील, जयपुर
	3. बंध मारगिया	05,45,454/-	श्री राजवीर बागड़ी, उदयपुर
	4. बंध डीमिया	-	टेका सूची में सम्मिलित नहीं है।
2022-23	1. बंध सोम कमला आंबा	टेका नहीं हुआ।	-
	2. बंध अमरपुरा	08,19,009/- (टेका अवधि 31.03.2023 तक)	श्री भुन्नीलाल, सीकर
	3. बंध मारगिया	06,10,508/- टेका अवधि (31.03.2026 तक)	श्री राजवीर बागड़ी, उदयपुर
	4. बंध डीमिया	-	टेका सूची में सम्मिलित नहीं है।

Ravi R.H.
मत्स्य विकास अधिकारी
दूँगरपुर

Appendix 5: References

Bustard, H. R. (1981). Crocodile breeding project. In *Wildlife in India*, ed. by V. B. Saharia, 147-64. New Delhi, Department of Agriculture & Cooperatives, Government of India. Choudhury, B. C. (1982).

Rehabilitating the endangered mugger crocodile (*Crocodylus palustris* Lesson) in India-case histories and future. Symposium on Milestones in Biological Research, Utkal University, Bhubaneshwar. Choudhury, B. C. & Bustard, H. R. (1980).

“Observations on feeding behaviour of a wild population of marsh crocodile in Baghdarrah Lake, Udaipur, Rajasthan”. *Reptile Rap*. 10:16–18.

(Bhatnagar, C., Mahur, M. (2010). “Observations on feeding behavior of a wild population of marsh crocodile in Baghdarrah Lake, Udaipur, Rajasthan”, *Reptile Rap* 10, p. 16–18.)

Whitaker, R. and Whitaker, Z.. (1989) “Ecology of the mugger crocodile”, *Crocodiles, their ecology, management, and conservation*. Gland: IUCN Crocodile Specialist Group, p. 276–

(1984) “Reproductive biology of the Mugger (*Crocodylus palustris*)”, *Journal of the Bombay Natural History Society* 81 (2), p. 297–317.

(1989) “Sex determination and sex ratios in *Crocodylus palustris*”, *American Zoologist* 29 (3), p. 935–952. doi:10.1093/icb/29.3.935.

Da Silva, A. (2010) “Mugger Crocodile *Crocodylus palustris*”, *Crocodiles: Status Survey and Conservation Action Plan*, 3-a edition, Darwin: IUCN Crocodile Specialist Group, p. 94–98.


Inland Wetlands of India : Conservation Priorities


V S Vijayan, S Narendra Prasad, Lalitha Vijayan and S Muralidharan

ISBN 10: 8190213601 /ISBN 13: 9788190213608

Published by Salim Ali Centre for Ornithology and Natural History, 2004

Appendix 13: Letter of Nagar Parishad to WRD to provide no-objection certificate for intake well and pump house

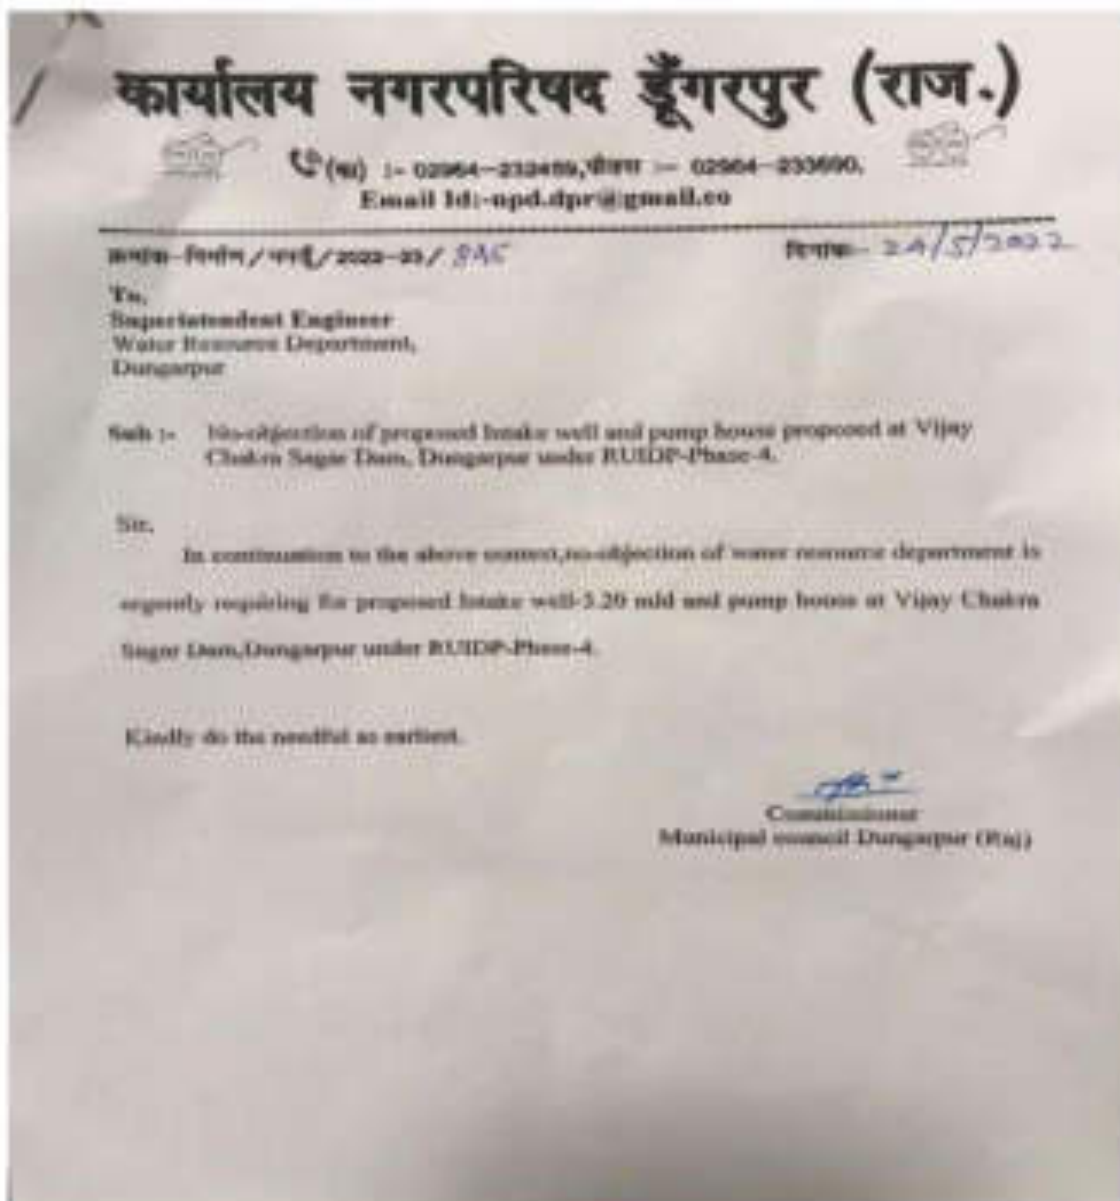

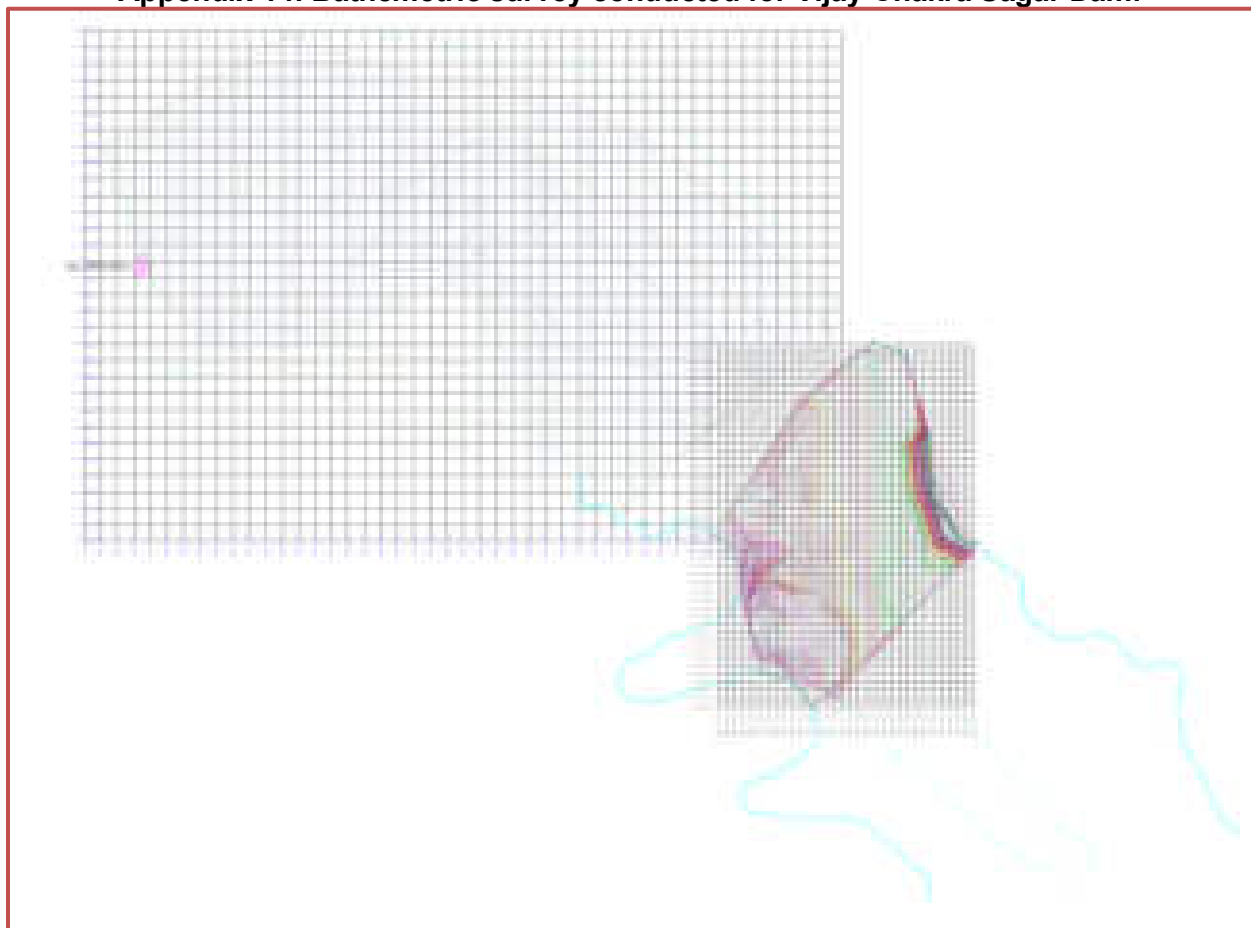Appendix 14: Bathymetric survey conducted for Vijay Chakra Sagar Dam.

Initial Environmental Examination

PUBLIC

Document Stage: Updated
Project Number: 42267-034
January 2024

India: Rajasthan Secondary Towns Development
Sector Project – Additional Financing (PART B)

Dungarpur Town Water Supply and Sewerage Works

Common Appendices

Prepared by Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Limited-
External Aided Project (RUDSICO-EAP) for the Asian Development Bank (ADB). This is an
updated version of the draft originally posted in July 2023 available on
<https://www.adb.org/projects/documents/ind-42267-034-iee-17>

This updated initial environmental examination is a document of the borrower. The views expressed herein do not necessarily represent those of ADB's Board of Directors, Management, or Staff, and may be preliminary in nature. Your attention is directed to the "terms of use" section of ADB's website.

In preparing any country program or strategy, financing any project, or by making any designation of or reference to a particular territory or geographic area in this document, ADB does not intend to make any judgments as to the legal or other status of any territory or area.

APPENDICES:

Appendix C-1: Drinking Water Standards.....	1
Appendix C-2: Ambient Air Quality Standards	2
Appendix C-3: Emission limits for New DG sets up to 800 KW.....	4
Appendix C-4: Stack Height Requirement of DG set.....	5
Appendix C-5: Vehicle Exhaust Emission Norms	6
Appendix C-6: Ambient Noise Quality Standards	7
Appendix C-7: Noise Limits for DG Set.....	8
Appendix C-8 ; Effluent Discharge Standards for STPs order by NGT 30.04.2019.....	10
Appendix C-9: Pages from Rajasthan State Sewerage and Waste Water Policy for reuse of treated effluent and sludge.....	11
Appendix C-10: Guidelines for Reuse of Treated Effluent and Sludge from STP for Beneficial Purposes.....	15
Appendix C-11: Guidelines for compensatory tree plantation in RUIDP works	18
Appendix C-12: Salient Features of Laws applicable to Construction Works including Labor Laws	20
Appendix C-13: Sample Outline Spoil Management Plan	24
Appendix C-14: Sample Outline Traffic Management Plan	25
Appendix C-15: Sample Six Monthly Reporting Format	34
Appendix C-16: Sample Environmental Site Inspection Report	37
Appendix C-17: Sample Grievance Registration Form.....	39
Appendix C-18: Management Plan for Night works at Project Sites.....	40
Appendix C-19: Guidelines for Safety during Monsoon/Heavy rainfall	42
Appendix C-20: Sample ACM Management Plan	44
Appendix C-21: Guidelines for Workers Camps	70
Appendix C-22: Guidelines for Safety in Chlorine Usage	72
Appendix C-23: Guidelines for Prevention and Control of COVID-19.....	79
Appendix C-24: RUDSICO-EAP Guidelines for implementation of Prevention and Control Measures for COVID-19	85
Appendix C-25: Management of Work Plan during Festivals and Melas	98

Appendix C-1: Drinking Water Standards

Group	National Standards for Drinking Water ^a			WHO Guidelines for Drinking-Water Quality, 4 th Edition, 2011 ^b	Applicable Per ADB SPS ^{c, d}
	Parameter	Unit	Max. Concentration Limits ^d		
Physical	Turbidity	NTU	1 (5)	-	1 (5)
	pH		6.5 – 8.5	none	6.5 – 8.5
	Color	Hazen units	5 (15)	none	5 (15)
	Taste and Odor		Agreeable	-	Agreeable
	TDS	mg/l	500 (2,000)	-	500 (2,000)
	Iron	mg/l	0.3	-	0.3
	Manganese	mg/l	0.1 (0.3)	-	0.1 (0.3)
	Arsenic	mg/l	0.01 (0.05)	0.01	0.01
	Cadmium	mg/l	0.003	0.003	0.003
	Chromium	mg/l	0.05	0.05	0.05
	Cyanide	mg/l	0.05	none	0.05
	Fluoride	mg/l	1 (1.5)	1.5	1 (1.5)
	Lead	mg/l	0.01	0.01	0.01
	Ammonia	mg/l	0.5	none established	0.5
Chemical	Chloride	mg/l	250 (1,000)	none established	250 (1,000)
	Sulphate	mg/l	200 (400)	none	200 (400)
	Nitrate	mg/l	45	50	45
	Copper	mg/l	0.05 (1.5)	2	0.05 (1.5)
	Total Hardness	mg/l	200 (600)	-	200 (600)
	Calcium	mg/l	75 (200)	-	75 (200)
	Zinc	mg/l	5 (15)	none established	5 (15)
	Mercury	mg/l	0.001	0.006	0.001
	Aluminum	mg/l	0.1 (0.3)	none established	0.1 (0.3)
	Residual Chlorine	mg/l	0.2	5	0.2
Micro Germs	E-coli	MPN/100ml	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample
	Total Coliform	MPN/100ml			

Note-

^a Bureau of India Standard 10500: 2012.

^b Health-based guideline values.

^c Per ADB SPS, the government shall achieve whichever of the standards is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the executing agency of the government will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in ADB SPS.

^d Figures in parenthesis are maximum limits allowed in the absence of alternate source.

Appendix C-2: Ambient Air Quality Standards

Parameter	Location ^a	India Ambient Air Quality Standard ^b (µg/m ³)	WHO global air quality guidelines 2021 (µg/m ³)	Applicable Per ADB SPS ^e (µg/m ³)
PM ₁₀	Industrial Residential, Rural and Other Areas	60 (Annual) 100 (24-hr)	15 (Annual) 45 (24-hr)	15 (Annual) 45 (24-hr)
	Sensitive Area	60 (Annual) 100 (24-hr)	15 (Annual) 45 (24-hr)	15 (Annual) 45 (24-hr)
PM ₂₅	Industrial Residential, Rural and Other Areas	40 (Annual) 60 (24-hr)	5 (Annual) 15 (24-hr)	5 (Annual) 15 (24-hr)
	Sensitive Area	40 (Annual) 60 (24-hr)	5 (Annual) 15 (24-hr)	5 (Annual) 15 (24-hr)
SO ₂	Industrial Residential, Rural and Other Areas	50 (Annual) 80 (24-hr)	40 (24-hr) 500 (10-min)	40 (24-hr) 500 (10-min)
	Sensitive Area	20 (Annual) 80 (24-hr)	20 (24-hr) 500 (10-min)	20 (Annual) 20 (24-hr) 500 (10-min)
NO ₂	Industrial Residential, Rural and Other Areas	40 (Annual) 80 (24-hr)	10 (Annual) 200 (1-hr)	10 (Annual) 80 (24-hr) 200 (1-hr)
	Sensitive Area	30 (Annual) 80 (24-hr)	10 (Annual) 200 (1-hr)	10 (Annual) 80 (24-hr) 200 (1-hr)
CO	Industrial Residential, Rural and Other Areas	2,000 (8-hr) 4,000 (1-hr)	4000 (24 hour)	2,000 (8-hr) 4,000 (1-hr) 100,000 (15-min)
	Sensitive Area	2,000 (8-hr) 4,000 (1-hr)		2,000 (8-hr) 4,000 (1-hr) 100,000 (15-min)
Ozone (O ₃)	Industrial Residential, Rural and Other Areas	100 (8-hr) 180 (1-hr)	100 (8-hr)	100 (8-hr) 180 (1-hr)
	Sensitive Area	100 (8-hr) 180 (1-hr)	100 (8-hr)	100 (8-hr) 180 (1-hr)
Lead (Pb)	Industrial, Residential, Rural and Other Areas	0.5 (Annual) 1.0 (24-hr)		0.5 (Annual) 1.0 (24-hr)
	Sensitive Area	0.5 (Annual) 1.0 (24-hr)		0.5 (Annual) 1.0 (24-hr)
Ammonia (NH ₃)	Industrial Residential,	100 (Annual) 400 (24-hr)		100 (Annual) 400 (24-hr)

Parameter	Location ^a	India Ambient Air Quality Standard ^b (µg/m ³)	WHO global air quality guidelines 2021 (µg/m ³)	Applicable Per ADB SPS ^e (µg/m ³)
	Rural and Other Areas			
	Sensitive Area	100 (Annual) 400 (24-hr)		100 (Annual) 400 (24-hr)
Benzene (C ₆ H ₆)	Industrial Residential, Rural and Other Areas	5 (Annual)		5 (Annual)
	Sensitive Area	5 (Annual)		5 (Annual)
Benzo(o)pyrene (BaP) particulate phase only	Industrial Residential, Rural and Other Areas	0.001 (Annual)		0.001 (Annual)
	Sensitive Area	0.001 (Annual)		0.001 (Annual)
Arsenic (As)	Industrial Residential, Rural and Other Areas	0.006 (Annual)		0.006 (Annual)
	Sensitive Area	0.006 (Annual)		0.006 (Annual)
Nickel (Ni)	Industrial Residential, Rural and Other Areas	0.02 (Annual)		0.02 (Annual)
	Sensitive Area	0.02 (Annual)		0.02 (Annual)

Note-

^a Sensitive area refers to such areas notified by the India Central Government.

^b Notification by Ministry of Environment and Forests, Government of India Environment (Protection) Seventh Amendment Rules, 2009

^c WHO Air quality guidelines for particulate matter, ozone, nitrogen dioxide and sulfur dioxide. *Global update 2005*. WHO. 2006

^d Air Quality Guidelines for Europe Second Edition. WHO 2000.

^e Per ADB SPS, the government shall achieve whichever of the ambient air quality standards is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the executing agency of the government will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in ADB SPS

**Appendix C-3: Emission limits for New DG sets up to 800 KW
(As per Environment (Protection) (Third Amendment) Rules, 2013)**

TABLE

Power Category	Emission Limits (g/kW-hr)			Smoke Limit (light absorption coefficient, m ⁻¹)
	NOx+HC	CO	PM	
Upto 19 KW	≤ 7.5	≤ 3.5	≤ 0.3	≤ 0.7
More than 19 KW upto 75 KW	≤ 4.7	≤ 3.5	≤ 0.3	≤ 0.7
More than 75 KW upto 800 KW	≤ 4.0	≤ 3.5	≤ 0.2	≤ 0.7

Note:

1. The abbreviations used in the Table shall mean as under: NO_x – Oxides of Nitrogen; HC – Hydrocarbon; CO – Carbon Monoxide; and PM – Particulate Matter.
2. Smoke shall not exceed above value throughout the operating load points of the test cycle.
3. The testing shall be done as per D2 – 5 mode cycle of ISO: 8178- Part 4.
4. The above mentioned emission limits shall be applicable for Type Approval and Conformity of Production (COP) carried out by authorised agencies.
5. Every manufacturer, importer or, assembler (hereinafter referred to as manufacturer) of the diesel engine (hereinafter referred to as 'engine') for genset application manufactured or imported into India or, diesel genset (hereinafter referred to as 'product'), assembled or imported into India shall obtain Type Approval and comply with COP of their product(s) for the emission limits which shall be valid for the next COP year or, the date of implementation of the revised norms specified above, whichever earlier.

Explanation. - The term 'COP year' means the period from 1st April to 31st March.

6. Stack height (in metres), for genset shall be governed as per Central Pollution Control Board (CPCB) guidelines.

Appendix C-4: Stack Height Requirement of DG set

DIESEL GENERATOR SETS : STACK HEIGHT

The minimum height of stack to be provided with each generator set can be worked out using the following formula :

$$H = h + 0.2 \times \text{KVA}$$

H = Total height of stack in metre

h = Height of the building in metres where the generator set is installed

KVA = Total generator capacity of the set in KVA

Based on the above formula the minimum stack height to be provided with different range of generator sets may be categorised as follows:

For Generator Sets	Total Height of stack in metre
50 KVA	Ht. of the building + 1.5 metre
50-100 KVA	Ht. of the building + 2.0 metre
100-150 KVA	Ht. of the building + 2.5 metre
150-200 KVA	Ht. of the building + 3.0 metre
200-250 KVA	Ht. of the building + 3.5 metre
250-300 KVA	Ht. of the building + 3.5 metre

Similarly for higher KVA ratings a stack height can be worked out using the above formula.

Source : Evolved By CPCB
[Emission Regulations Part IV:COINDS/26/1986-87]

Appendix C-5: Vehicle Exhaust Emission Norms

1. Passenger Cars

Norms	CO(g/km)	HC+ NOx(g/km)
1991Norms	14.3-27.1	2.0(Only HC)
1996 Norms	8.68-12.40	3.00-4.36
1998Norms	4.34-6.20	1.50-2.18
India stage 2000 norms	2.72	0.97
Bharat stage-II	2.2	0.5
Bharat Stage-III	2.3	0.35 (combined)
Bharat Stage-IV	1.0	0.18 (combined)

2. Heavy Diesel Vehicles

Norms	CO(g/kmhr)	HC (g/kmhr)	NOx (g/kmhr)	PM(g/kmhr)
1991Norms	14	3.5	18	-
1996 Norms	11.2	2.4	14.4	-
India stage 2000 norms	4.5	1.1	8.0	0.36
Bharat stage-II	4.0	1.1	7.0	0.15
Bharat Stage-III	2.1	1.6	5.0	0.10
Bharat Stage-IV	1.5	0.96	3.5	0.02

Source: Central Pollution Control Board

CO = Carbon Monoxide; g/kmhr = grams per kilometer-hour; HC = Hydrocarbons; NOx = oxides of nitrogen; PM = Particulates Matter

Appendix C-6: Ambient Noise Quality Standards

Receptor/ Source	India National Noise Level Standards ^a (dBA)		WHO Guidelines Value For Noise Levels Measured Out of Doors ^b (One Hour LA _q in dBA)		Applicable Per ADB SPS ^c (dBA)	
	Day	Night	07:00 – 22:00	22:00 – 07:00	Day time	Night time
Industrial area	75	70	70	70	70	70
Commercial area	65	55	70	70	65	55
Residential Area	55	45	55	45	55	45
Silent Zone	50	40	55	45	50	40

Note-

^a Noise Pollution (Regulation and Control) Rules, 2002 as amended up to 2010.

^b Guidelines for Community Noise. WHO. 1999

^c Per ADB SPS, the government shall achieve whichever of the ambient quality standards is more stringent. If less stringent levels or measures are appropriate in view of specific project circumstances, the executing agency of the government will provide full and detailed justification for any proposed alternatives that are consistent with the requirements presented in ADB SPS.

Appendix C-7: Noise Limits for DG Set

(Noise Limit for Generator Sets run with Diesel were notified by Environment (Protection) second Amendment Rules vide GSR 371(E), dated 17th May 2002 at serial no.94 and its amendments vide GSR No 520(E) dated 1st July 2003; GSR 448(E), dated 12th July 2004; GSR 315(E) dated 16th May 2005; GSR 464(E) dated 7th August 2006; GSR 566(E) dated 29th August 2007 and GSR 752(E) dated 24th October 2008; G.S.R. 215 (E), dated 15th March, 2011 under the Environment (Protection) Act, 1986)

Noise Limit for Generator Sets run with Diesel

- 1. Noise limit for diesel generator sets (upto 1000 KVA) manufactured on or after the 1st January, 2005**

The maximum permissible sound pressure level for new diesel generator (DG) sets with rated capacity upto 1000 KVA, manufactured on or after the 1st January, 2005 shall be 75 dB(A) at 1 metre from the enclosure surface.

The diesel generator sets should be provided with integral acoustic enclosure at the manufacturing stage itself.

The implementation of noise limit for these diesel generator sets shall be regulated as given in paragraph 3 below.

- 2. Noise limit for DG sets not covered by paragraph 1.**

Noise limits for diesel generator sets not covered by paragraph 1, shall be as follows:-

- 2.1 Noise from DG set shall be controlled by providing an acoustic enclosure or by treating the room acoustically, at the users end.
- 2.2 The acoustic enclosure or acoustic treatment of the room shall be designed for minimum 25 dB (A) insertion loss or for meeting the ambient noise standards, whichever is on the higher side (if the actual ambient noise is on the higher side, it may not be possible to check the performance of the acoustic enclosure/acoustic treatment. Under such circumstances the performance may be checked for noise reduction upto actual ambient noise level, preferably, in the night time). The measurement for Insertion Loss may be done at different points at 0.5 m from the acoustic enclosure/ room, then averaged.
- 2.3 The DG set shall be provided with proper exhaust muffler with insertion loss of minimum 25 dB (A).

2.4 These limits shall be regulated by the State Pollution Control Boards and the State Pollution Control Committees.

2.5 Guidelines for the manufacturers/ users of Diesel Generator sets shall be as under:-

01. The manufacturer shall offer to the user a standard acoustic enclosure of 25 dB (A) insertion loss and also a suitable exhaust muffler with insertion loss of 25 dB(A).
02. The user shall make efforts to bring down the noise levels due to the DG set, outside his premises, within the ambient noise requirements by proper citing and control measures.
03. Installation of DG set must be strictly in compliance with the recommendations of the DG set manufacturer.
04. A proper routine and preventive maintenance procedure for the DG set should be set and followed in consultation with the DG set manufacturer which would help prevent noise levels of the DG set from deteriorating with use.

3.0 Limits of Noise for DG Sets (upto 1000 KVA) Manufactured on or after the 1st January, 2005

3.1 Applicability

01. These rules apply to DG sets upto 1000 KVA rated output, manufactured or imported in India, on or after 1st January, 2005.
02. These rules shall not apply to –
 - a) DG sets manufactured or imported for the purpose of exports outside India; and
 - b) DG sets intended for the purpose of sample and not for sale in India.

3.2 Requirement of Certification

Every manufacturer or assembler or importer (hereinafter referred to as the "manufacturer") of DG set (hereinafter referred to as "product") to which these regulations apply must have valid certificates of Type Approval and also valid certificates of Conformity of Production for each year, for all the product models being manufactured or assembled or imported from 1st January, 2005 with the noise limit specified in paragraph 1.

3.3 Sale, import or use of DG sets not complying with the rules prohibited

No person shall sell, import or use of a product model, which is not having a valid Type Approval Certificate and Conformity of Production certificate.

Appendix C-8: Effluent Discharge Standards for Sewage Treatment Plant

Discharge Standards to be achieved as per NGT order dtd. 30.04.2019

Sl. No.	Parameters	Parameters Limit
1	pH	5.5-9.0
2	BOD (mg/l)	Not more than 10 mg/l
3	COD (mg/l)	Not more than 50 mg/l
4	TSS (mg/l)	Not more than 20 mg/l
5	P-Total (mg/l)- for discharge into ponds/lakes	Not more than 1.0 mg/l
6	N-Total (mg/l)	Not more than 10 mg/l
7	Fecal Coliform (MPN/100ml)	Desirable- Less than 100 MPN/100ml Permissible- 230 MPN/100ml

Note: These parameters are being followed under RSTDSP works

Appendix C-9: Pages from Rajasthan State Sewerage and Waste Water Policy for reuse of treated effluent and sludge

STATE SEWERAGE AND WASTE WATER POLICY- 2016

- viii. Design and performance specifications of wastewater treatment plants shall be as per guidelines given in the manual on sewerage treatment systems published by CPHEEO. Sufficient room in tendering for the construction of new plants shall be provided for competition to take place in both technologies and costs.

5.4. On Reuse of Treated Effluent and Sludge

1. Treated wastewater effluent is considered a water resource and is added to the water stock for reuse.
2. Priority shall be given to agricultural reuse of treated effluent for unrestricted irrigation. Blending of treated wastewater with fresh water shall be made to improve quality where possible. Crops to be irrigated by the treated effluent or blend thereof with freshwater resources shall be selected to suit the irrigation water, soil type and chemistry, and the economics of the reuse operations.
3. Crop nutrient requirements shall be determined taking into consideration the prevailing effluent quality. Overuse of nutrients shall be avoided.
4. Accumulation of heavy metals and salinity shall be monitored, managed and mitigated. Leaching of soils shall be advocated by the irrigation authorities.
5. Farmers shall be encouraged to determine the rate of water application needed for different crops, taking into consideration the value of nutrients in the treated water and other parameters.
6. Farmers shall be encouraged to use modern and efficient irrigation technologies. Protection of on-farm workers and of crops against pollution with wastewater shall be ensured.
7. Treated effluent quality should be monitored and users alerted to any emergency causing deterioration of the quality so that they will not use such water unless corrective measures are taken.
8. Studies should be conducted and projects designed and implemented to store the excess treated wastewater in surface reservoirs but artificial recharge is not permitted. Due attention shall be given to the quality of treated and groundwater and the characteristics of the strata.
9. Plans and studies for power generation from sludge, if proven technically, economically and financially feasible, shall be made with due attention to environment impacts.
10. Sludge produced from the treatment process would be processed so it may be used as fertilizer and soil conditioner. Care shall be taken to conform to the regulations of public health and environment protection norms.

11. **Industry:** Industrial reuse of reclaimed wastewater represents major reuse next only to irrigation in both developed and developing countries. Reclaimed wastewater is ideal for many industrial purposes. Where effluent is to be used in the industrial processes, it should be the responsibility of the industry to treat it to the quality standards required. Pilot scale feasibility studies carried out in Australia have concluded that it is possible to economically treat the domestic wastewater to achieve adequate quality for reuse as cooling water. Based on the conclusions of the feasibility study, a full-scale treatment plant employing cross-flow membrane microfiltration system may be installed. The membrane filtration system can remove all suspended solids, fecal coliforms, and giardia cysts. It could also significantly reduce human enteric viruses such as *reovirus* and *enterovirus*. The water reclamation plant at Eraring Power Station demonstrates the potential for reuse of wastewater in power generation and other industrial manufacturing facilities.

Industrial uses for reclaimed water include:

- (i) Evaporative cooling water:-
 - (a) Once-through cooling system.
 - (b) Re-circulating cooling system.
 - (c) Cooling water quality requirements.
 - (ii) Boiler –Feed water- The use of reclaimed water differs little from use of conventional public supplies for boiler-feed water, as both require extensive additional treatment. Quality requirements for boiler feed make up water are dependent upon pressure at which boiler is operated.
 - (iii) Industrial process water-
Suitability of reclaimed water for use in industrial process depends upon particular use like-
 - (a) Pulp and paper.
 - (b) Chemical industry.
 - (c) Textile industry.
 - (d) Petroleum and coal.
12. Whenever possible, other end uses of treated effluents; such as recycling, cooling, power generation, etc. shall be considered.
13. **Re-use Options:** The following options for re-use of effluent have been identified: In general, public health concern is the major issue in any type of reuse of wastewater, be it for irrigation or non-irrigation utilization, especially long term impact of reuse practices. It is difficult to delineate acceptable health risks and is a matter that is still hotly debated. Potential reuse of wastewater depends on the hydraulic and biochemical characteristics of wastewater, which determine the methods and degree of treatment required. While agricultural irrigation reuses, in general, require lower quality levels of treatment, domestic reuse options (direct or indirect potable and non-potable) reuses need the highest treatment level. Level of treatment for other

reuse options lie between these two extremes. The reuse options may be (artificial recharge of aquifers is not permitted):

- i. Irrigation
 - (a) Agriculture and forestry
 - (b) Landscaping
- ii. Fish – farming
- iii. Industry
- iv. Non-potable Domestic Reuse.

The detailed project report should clearly define the best reuse option particular to town and strategy to obtain it. Action plan with clarity should be the part of Detailed Project Report (DPR), while preparing sewerage projects. Before deciding the reuse of treated waste water, authorities must full fill the water quality norms and its legal implications.

14. Governing local body can sell the treated waste water and digested sludge to generate the revenue.

5.5. On Pricing, Financing and Investment

1. In view of increasing marginal cost of wastewater collection and treatment, wastewater charges, connection fees, sewerage taxes and treatment fees shall be set to cover at least the operation and maintenance costs. It is also highly desirable that part of the capital cost of the services shall be recovered. The ultimate aim is for a full cost recovery.
2. Appropriate criteria in order to apply the "polluter pays" principle shall be established.
3. Different charges for different areas may be applied. This shall be assessed for each geographical area as a function of end users and effluent quality and will be subject to economic and social considerations.
4. Because of the limited financial resources available to Government of Rajasthan, setting investment priorities in wastewater will be compatible with government investment plans.
5. Criteria for prioritizing investments in the wastewater sector shall take into account the current and future needs of the state, needs to expand wastewater systems in urban areas and to provide wastewater systems to smaller towns and villages.
6. Priorities of wastewater projects shall not be disconnected from water supply projects and urbanization in general. Decisions will be made concerning them to attain optimum solutions to the need for services, availability of finance and availability of trained manpower.

7. Treated effluent shall be priced and sold to end users at a price covering at least the operation and maintenance costs of delivery.
8. It is the intention of the Government, through private sector participation, to transfer management of infrastructure and services from the public to the private sector, in order to improve performance and upgrade the level of service.
9. The role of the private sector will expand with management contracts, concessions and other forms of private sector participation in wastewater management.
10. The concepts of BOO/BOT shall be entertained, and the impact of such concepts on the consumers shall be continually addressed and negative impacts mitigated.
11. The private sector role in reuse of treated effluent shall be encouraged and expanded.
12. As per urban reforms (under various schemes by MOUD) 100% cost of O&M of sewerage system shall be recovered from consumer. The costs will depend on the system/technology adopted for collection of sewerage and treatment and the administration costs. It is important that the full cost of the service is assessed for each urban area instead of adopting a typical cost assessment. The full cost shall cover the following:
 - (i) Institutional aspect of the sanitation service e.g. the management information systems, accountancy and finance management, billing and collection, customer services, etc. and oversight activities.
 - (ii) Operating, maintaining (on a planned maintenance basis), repairing replacing and extending sanitation service physical infrastructure.
 - (iii) Keeping updated infrastructure and customer data on a GIS base.
 - (iv) Managers, staff, vehicles, equipment and consumables associated with the above.
 - (v) Consumable like chemicals etc.
 - (vi) Power charges.
 - (vii) Spare Parts.
 - (viii) Any other O&M contract amount

5.6. Source of Funds for Sewerage Project

- (A) In general, implementation of reuse facility requires substantial capital expenses. In addition to capital cost associated with reclaimed water facility, there are also additional operation, maintenance, and replacement and administrative costs. Hence responsible agencies may consider following sources of 'Funds for Construction of Sewerage Project':

Appendix C-10: Guidelines for Reuse of Treated Effluent and Sludge from STP for Beneficial Purposes

(Source: Manual on Sewerage and Sewage Treatment Systems, CPHEEO, Ministry of Urban Development, Govt. of India)

Health Hazards during Sewage Operations

Labourers working on the sewage treatment and operations may suffer from a number of ailments directly attributed to handling of sewage. In view of this it is desirable to disinfect sewage and where feasible mechanize sewage operations.

The staff of sewage operations must be well educated in the sanitary rules on the utilization of sewage for irrigation as well as with personal hygiene. All persons working in sewage farms must undergo preventive vaccination against enteric infections and annual medical examination for helminthiasis and be provided treatment if necessary.

Sewage treatment plants should be provided with adequate space for canteens with proper sanitation, wash-stands and lockers for irrigation implements and protective clothing. Safe drinking water must be provided for the workers and for population residing within the effective range of the sewage treatment plants.

All workers should be provided with gum boots and rubber gloves, which must compulsorily be worn while at work. They should be forced to observe personal hygiene such as washing after work as well as washing before taking food. The use of antiseptics in the water used for washing should be emphasized. The farm worker should be examined medically at regular intervals and necessary curative measures enforced.

Mitigation measures to avoid Health Hazards

Personal Hygiene against Pathogen

The worker should take precautions because a large number of coliform groups, various kinds of micro-organisms, and egg parasites exist in sewage. The workers should strive to maintain good health by taking care of the following points:

- Wear clean uniform, work boots, etc.
- After work and before having a meal, always wash hands and disinfect them.
- After work, take a shower if possible.
- Do not enter the offices and lounges wearing dirty clothes.
- If necessary, take vaccinations against tetanus, leptospirosis fever and so on

Maintaining Cleanliness The worker should maintain each facility in a clean and neat condition.

- The floors of workrooms, stairs and corridors should be cleaned at the appropriate frequency to maintain them in a clean condition
- Disinfection of relevant locations is to be carried out periodically.

Health Check Workers should receive health check once a year to maintain their health, and prevent illnesses or detect them at an early stage. The results of the health check should be maintained as records. Recommended items to be inspected during the health check are as given below.

- Examine medical history.
- Examine subjective symptoms and other objective symptoms.
- Check height, weight, vision and hearing ability.
- Chest X-ray examination.
- Blood pressure measurement.
- Check for anaemia.
- Check for liver functions.
- Check for lipids in blood.
- Check blood sugar level
- Urine analysis.
- Electrocardiogram analysis

Welfare Measures The Sanitation Workers (Regulation of Employment and Conditions of Service) Act 2012 proposes constitution of a Sanitation Workers State Welfare Board to exercise powers conferred on it and to perform welfare functions such as the following for sanitation workers:

- Provide immediate assistance to a beneficiary in case of an accident
- Sanction of loan and advances
- Medical expenses for treatment of major ailments
- Financial assistance for education of children
- Payment of maternity benefits
- Make provision and improvement of welfare measures and facilities as may be prescribed

Corrective Measures When a worker has symptoms of an illness listed above, the plant engineer should ensure that the worker is checked-up by a specialist doctor and receives proper treatment and care and should take the following actions considering the content of work done by the worker:

- Change the workplace if necessary
- Change the content of the work
- Shorten the working hours
- Perform relevant measurements of the working environment
- Maintain the facility or equipment

Risks in use of treated effluent and sludge in agriculture practices

Cultivation of crops that are eaten raw should be banned. Cultivation of paddy in bunded fields is likely to give rise to sanitation problems and hence is undesirable. Growing of non-edible commercial crops like cotton, jute, fodder, milling varieties of sugarcane and tobacco would be suitable. Cultivation of grasses and fodder legumes, medicinal and essential oil yielding plants like menthol and citronella may be allowed. Cultivation of cereals, pulses, potatoes and other crops that are cooked before consumption may be permitted, if sewage is treated and care is taken in handling the harvests to ensure that they are not contaminated. Cultivation of crop exclusively under seed multiplication programmes would be advantageous as these are not consumed. As an additional safeguard, sewage irrigation should be discontinued at least two months in advance of harvesting of fruits and berries, one month for all kinds of vegetables and a fortnight for all other crops. Direct grazing on sewage irrigated farms should be prohibited.

Risks of Nutrient Loading in Agriculture

Crops receiving excessive dosage of nitrogen show superfluous vegetative growth and decrease in grain or fruit yield. The phosphate deficit of sewage, therefore, should be made good by supplementing with phosphate fertilizers, the extent of phosphate fortification depending upon the nature of crop and its phosphate requirements. As the availability of phosphate is low in the irrigation water it would be desirable to apply the required quantity of phosphatic fertilizer at the time or even (about a fortnight) before the sowing or planting of the crop. Even when sewage nutrients are balanced by fortification, irrigation with such sewage may supply excessive amount of nutrients resulting in waste or unbalanced growth of plants with adverse effects on yields. It may therefore be necessary to dilute the sewage. Dilution also helps in reducing the concentration of dissolved salts and decomposable organic matter in the sewage thus, decreasing hazards to the fertility of the soil. It is desirable to limit the BOD and total suspended solids of sewage to be disposed on land for irrigation, as per relevant standards. There is a need to take caution on describing nutrient supply capacity of sewage particularly in the case of availability of phosphorus because there is a possible conversion of available phosphorus in unavailable mode in the presence of heavy metals present in the sewerage. This happens commonly in high as well as low pH soils.

Alternative Arrangement during Non-irrigating Periods

During rainy and non-irrigating seasons, agricultural practices may not need any water for irrigation. Even during irrigating season, the water requirement fluctuates significantly. Hence,

satisfactory alternative arrangements have to be made for the disposal of sewage on such occasions either by storing the excess sewage or discharging it elsewhere without creating environmental hazards. The following alternatives are generally considered: a) Provision of holding lagoons for off-season storage. They enable irrigation of a fixed area of land to varying rates of crop demand. They may also serve as treatment units such as aerated or stabilization lagoons, provided the minimum volume required for treatment is provided beyond the flow-balancing requirement. b) Provision of additional land where treated sewage is not required on the main plot of land c) Discharge of surplus treated sewage to river or into sea with or without additional treatment. Combining surface discharge facilities with irrigation system is quite common and often quite compatible. d) Resorting to artificial recharge in combination with an irrigation system where feasible.

Treated Sewage into Perennial Rivers

When sewage is treated and discharged into perennial flowing rivers and the blended river water is drawn downstream of the point of such blending as raw water for treatment in public water supply schemes. This is indirect potable use after blending. This is historical and ongoing all around. However, of late, the organic load due to the discharged treated, partially treated and non-point sewage becomes in excess of the self-purifying capacity of the river. Thus, the river water is not actually fresh water. The water quality of Yamuna river for Agra water supply scheme requires to be first treated in MBBR to purify the river water to a level as raw water for the downstream WTP. When it passes through flowing surface water it has the potential disadvantages of contamination by human and animal activities adding organic matter and waterborne pathogens unless the river stretch is protected from such activities. The guiding principle in such cases for the ULBs will be to at least intercept the sewage outfalls and provide adequate STPs and follow the recommended quality criteria for the treated sewage.

Treated Sewage into Non-Perennial / Dry River Courses

There are locations where the rivers are not perennial or almost dry throughout the year except some monsoon runoff. In this case the discharged treated sewage sinks into the aquifer zone and is extracted by infiltration wells or galleries. The advantage of direct dilution from surface water is lost, but the additional purification in the soil and dilution from the aquifer water are happening. An example is the case of the Palar river course in Tamilnadu. The surface water flow in this occurs only for about a week if the monsoon is normal and if the water spills beyond the upstream impoundments. The aquifer however supports the public water supply of over 30 habitations along its dry tract of nearly 80 km before the sea. The partly treated sewage of the en-route habitations does reach this river course as intervals. So far, no epidemics have been met with. This may be due to the above said additional purification in the soil and dilution by aquifer water. However, if these are exceeded by the contamination load, there can be immediate health problems. The guiding principle in such cases for the ULBs will be (a) to keep a check on the raw water quality from the infiltration wells to detect sudden increase in contaminants and (b) at least intercept the sewage outfalls and provide adequate STPs.

Appendix C-11: Guidelines for compensatory tree plantation in RUIDP works

RUIDP Office of RUDSICO, External Aided Project (RUIDP)
Rajasthan Urban Drinking Water Sewerage and Infrastructure Corporation Ltd (RUDSICO)
{Erstwhile Rajasthan Urban Infrastructure Finance and Development Corporation Ltd}
Head Quarter Address:- Old Working Women Hostel, Behind Nehru Palace, Tonk Road Jaipur
Branch Address:- AVS Building, Jawahar Circle, JLN Marg, Jaipur - 302017
Ph. - 141 2721966 Fax No. 141 2721919,
E-mail:- mailruidp@gmail.com, mail.ruidp@rajasthan.gov.in Website:- www.ruidp.rajasthan.gov.in

No. F3 (201)(57)/RUIDP/PMU/Ph-III/CMS/ 556 Date: 3.04.2018

Sub: Construction Management System: Circular - 10
Ref: Guidelines for Compensatory Tree Plantation in RUIDP works.

RUIDP being a responsible organization in the sector of Urban Infrastructure understands the need & responsibility towards protection and conservation of Environment. It is mandatory in all RUIDP projects to avoid tree cutting during construction activities, however, in some unavoidable cases tree cutting may be allowed subjected to following conditions :-

1. Submission of detailed proposal by contractor indicating number of trees required to be cut with justification and details of efforts made to avoid/minimize tree cutting.
2. Tree cutting should be allowed by PIU/Employer Representative only after permission from concerned authorities (Administration/ Tahsildar/ Forest Department as the case may be).
3. Compensatory plantations should be ensured/ done by contractor in sufficient number of trees so that final survived trees should meet criteria of 1:3 (three trees should be planted for every one tree cut). This ratio is a minimum requirement; additional plantation by contractor should be encouraged. The ratio shall also be got approved by concerned permitting authority.
4. Compensatory plantations can be done in any of project sites (if space available) or any other place in the town after due permission from land owner/concerned department and PIU.
5. Tree species selected for compensatory plantations should be native (local) species and list of such species should be obtained/ verified from Forest Department of concerned town prior to submission of proposal for tree cutting.
6. Trees proposed to be planted should be at least of 3 mtrs height and in healthy condition.
7. It shall be responsibility of contractor to ensure the survival of planted trees upto 5/10 years i.e. for entire O&M period.
8. After completion of Contract period and before handing over project for O&M, all the trees should be counted by PIU through consultants and handed over to Municipality/asset owner/concerned department through PIU.

Circular 10

 1

9. Compensatory plantation is an additional obligation (deemed to be accepted by all parties) and should not be considered as replacement/substitution of any pre-existing contractual obligation/conditions. Compensatory plantation obligations will be additional to Pre defended mandatory plantations for sites in contract.
10. Payments for this Compensatory plantation shall be done from provisional sum of contract and rates shall be taken from RUIDP SOR for the available items and market rate analysis for other items.

This circular shall be strictly abided by all the members of PIU, PMDSC, PSC & Contractor.



(Dr. Preetam B Yashvant)
Project Director

No. F3 (201)(57)/RUIDP/PMU/Ph-III/CMS/ 557-91

Date: 13.04.2018

Copy to following for information and necessary action:

1. PA to PD/Addl. PD/ FA/ CE/ ACE/SE-I/SE-II/SE-III/ POs/APOs, PMU, RUIDP, Jaipur
2. SE, PIU, Pali/Tonk/Sriganaganagar/Jhunjhunu/Bhilwara/Hanumangarh/Kota
3. EE, PIU, Sawai Madhopur/ Bikaner/ Udaipur/ Jhalawar/ Mt. Abu/Banswara
4. Team Leader/ Project Coordinator/CM/ Dy. CM/ACM, PMDSC/ PSC, Jaipur, Pali/Tonk/ Sriganaganagar/ Jhunjhunu/ Bhilwara/ Hanumangarh/ Kota/ Sawai Madhopur/ Bikaner/ Udaipur/ Jhalawar/ Mt. Abu/Banswara
5. ACP, RUIDP, Jaipur to send by e-mail and put up the Guidelines on the website.


Addl. Chief Engineer

Appendix C-12: Salient Features of Laws applicable to Construction Works including Labor Laws

- (i) Workmen Compensation Act, 1923 - The Act provides for compensation in case of injury by accident arising out of and during the course of employment.
- (ii) Payment of Gratuity Act, 1972 - Gratuity is payable to an employee under the Act on satisfaction of certain conditions on separation if an employee has completed 5 years' service or more or on death at the rate of 15 days wages for every completed year of service. The Act is applicable to all establishments employing 10 or more employees.
- (iii) Employees' PF and Miscellaneous Provisions Act, 1952 - The Act provides for monthly contributions by the employer plus workers @10 % or 8.33 %. The benefits payable under the Act are: (a) Pension or family pension on retirement or death as the case may be; (b) deposit linked insurance on the death in harness of the worker; (c) payment of PF accumulation on retirement/death etc.
- (iv) Maternity Benefit Act, 1951 (as amended up to 2017) - The Act provides for leave and some other benefits to women employees in case of confinement or miscarriage etc.
- (v) Contract Labour (Regulation and Abolition) Act, 1970 - The Act provides for certain welfare measures to be provided by the Contractor to contract labor and in case the Contractor fails to provide, the same are required to be provided by the Principal Employer by Law. The principal employer is required to take Certificate of Registration and the Contractor is required to take a License from the designated Officer. The Act is applicable to the establishments or Contractor of principal employer if they employ 20 or more contract labor.
- (vi) Minimum Wages Act, 1948 - The employer is supposed to pay not less than the Minimum Wages fixed by appropriate Government as per provisions of the Act if the employment is a scheduled employment. Construction of Buildings, Roads, Runways are scheduled employment.
- (vii) Payment of Wages Act, 1936 - It lays down as to by what date the wages are to be paid, when it will be paid and what deductions can be made from the wages of the workers.
- (viii) Equal Remuneration Act, 1979 - The Act provides for payment of equal wages for work of equal nature to Male and Female workers and not for making discrimination against Female employees in the matters of transfers, training and promotions etc.
- (ix) Payment of Bonus Act, 1965 - The Act is applicable to all establishments employing 20 or more workmen. The Act provides for payments of annual bonus subject to a minimum of 8.33 % of wages and maximum of 20 % of wages to employees drawing Rs. 3,500/- per month or less. The bonus to be paid to employees getting Rs. 2,500/- per month or above up to Rs.3,500/- per month shall be worked out by taking wages as Rs.2,500/- per month only. The Act does not apply to certain establishments. The newly set up establishments are exempted for five years in certain circumstances. Some of the State Governments have reduced the employment size from 20 to 10 for the purpose of applicability of the Act.
- (x) Industrial Disputes Act, 1947 - The Act lays down the machinery and procedure for resolution of industrial disputes, in what situations a strike or lock-out becomes illegal and what are the requirements for laying off or retrenching the employees or closing down the establishment.
- (xi) Industrial Employment (Standing Orders) Act, 1946 - It is applicable to all establishments employing 100 or more workmen (employment size reduced by some of the States and Central Government to 50). The Act provides for laying down rules governing the conditions of employment by the employer on matters provided in the Act and get the same certified by the designated Authority.
- (xii) Trade Unions Act, 1926 - The Act lays down the procedure for registration of trade unions of workmen and employees. The trade unions registered under the Act have been given certain immunities from civil and criminal liabilities.

(xiii) Child Labor (Prohibition and Regulation) Act, 1986 - The Act prohibits employment of children below 14 years of age in certain occupations and processes and provides for regulation of employment of children in all other occupations and processes. Employment of child labor is prohibited in Building and Construction Industry.

(xiv) Inter-State Migrant Workmen's (Regulation of Employment and Conditions of Service) Act, 1979 - The Act is applicable to an establishment which employs 5 or more inter-state migrant workmen through an intermediary (who has recruited workmen in one state for employment in the establishment situated in another state). The inter-state migrant workmen, in an establishment to which this Act becomes applicable, are required to be provided certain facilities such as housing, medical aid, traveling expenses from home up to the establishment and back, etc

(xv) **Construction and Demolition Waste Management Rules 2016**- This Rule stipulate that-

- Every waste generator shall segregate construction and demolition waste and deposit at collection centre or handover it to the authorized processing facilities
- Shall ensure that there is no littering or deposition so as to prevent obstruction to the traffic or the public or drains.
- Large generators (who generate more than 20 tons or more in one day or 300 tons per project in a month) shall submit waste management plan and get appropriate approvals from the local authority before starting construction or demolition or remodelling work,
- Large generators shall have environment management plan to address the likely environmental issues from construction, demolition, storage, transportation process and disposal / reuse of C & D Waste.
- Large generators shall segregate the waste into four streams such as concrete, soil, steel, wood and plastics, bricks and mortar,
- Large generators shall pay relevant charges for collection, transportation, processing and disposal as notified by the concerned authorities;

(xvi) **Solid Waste Management Rules 2016**- As per this Rule, responsibility of Solid Waste Generator is as below-

- segregate and store the waste generated in three separate streams namely bio-degradable, non-biodegradable and domestic hazardous wastes in suitable bins and handover segregated wastes to authorized waste pickers or waste collectors as per the direction or notification by the local authorities from time to time;
- store separately construction and demolition waste, as and when generated, in his own premises and shall dispose off as per the Construction and Demolition Waste Management Rules, 2016; and
- No waste generator shall throw, burn or bury the solid waste generated by him, on streets, open public spaces outside his premises or in the drain or water bodies.

(xvii) **The Building and Other Construction Workers (Regulation of Employment and Conditions of Service) Act, 1996 and the Cess Act of 1996** - All the establishments who carry on any building or other construction work and employ 10 or more workers are covered under this Act. All such establishments are required to pay Cess at rate not exceeding 2% of the cost of construction as may be notified by the Government. The employer of the establishment is required to provide safety measures at the building or construction work and other welfare measures, such as canteens, first-aid facilities, ambulance, housing accommodation for workers near the workplace etc. The employer to whom the Act applies has to obtain a registration certificate from the Registering Officer appointed by the Government. Following are the major requirements under this Act, applicable to this project-

Employer shall-

- Provide and maintain, at suitable point, sufficient quantity of wholesome drinking water, such point shall be at least 6 meters away from any washing areas, urinals or toilets
- Provide sufficient urinals and latrines at convenient place, easily accessible by workers
- Provide free of charge, temporary living accommodations near to work sites with separate cooking place, bathing and lavatory facilities and restore the site as pre conditions after completing the construction works
- Provide crèche with proper accommodation, ventilation, lighting, cleanliness and sanitation if more than fifty female workers are engaged
- Provide first aid facilities in all construction sites

For safety of workers employer shall provide-

- Safe access to site and work place
- Safety in demolition works
- Safety in use of explosives
- Safety in operation of transporting equipments and appoint competent person to drive or operate such vehicles and equipments
- Safety in lifting appliance, hoist and lifting gears
- Adequate and suitable lighting to every work place and approach
- Prevention of inhalation of dust, smoke, fumes, gases during construction works and provide adequate ventilation in work place and confined space
- Safety in material handling and stacking/un stacking
- Safeguarding the machinery with fly-wheel of moving parts
- Safe handling and use of plants operated by compressed air
- Fire safety
- Limit of weight to be lifted by workers individually
- Safety in electric wires, apparatus, tools and equipments
- Provide safety net, safety sheet, safety belts while working at height (more than 1.6 mtrs as per OSHA)
- Providing scaffolding, ladders and stairs, lifting appliances, chains and accessories where required
- Safety in pile works, concrete works, hot asphalt, tar, insulation, demolition works, excavation, underground construction and handling materials
- Provide and maintain medical facilities for workers
- Any other matters for the safety and health of workers

(xviii) **The Occupational Safety, Health and Working Conditions Code, 2020:** The Occupational Safety, Health And Working Conditions Code, 2020 is a code to consolidate and amend the laws regulating the Occupational safety and health and working conditions of the persons employed in an establishment and for matters connected therewith or incidental thereto. This Code simplifies, amalgamates and rationalises the provisions of the different enactments with certain important changes which, inter alia, are as under:—

- To impart flexibility in adapting technological changes and dynamic factors, in the matters relating to health, safety, welfare and working conditions of workers;
- To apply the provisions of the proposed Code for all establishments having ten or more workers, other than the establishments relating to mines and docks;
- To provide the concept of “one registration” for all establishments having ten or more employees. However, for the applicability of all other provisions of the Code in respect of factories, except registration, the threshold has been fixed twenty workers in a factory (with power) and forty workers (without power);

- To include the journalist working in electronic media such as in e-paper establishment or in radio or in other media in the definition of “working journalists”;
- To provide for issuing of appointment letter mandatorily by the employer of an establishment to promote formalisation in employment;
- To provide free of cost annual health check-ups for employees above the specified age in all or certain class of establishments by which it would be possible to detect diseases at an early stage for effective and proper treatment of the employees;
- To make the provisions relating to Inter-State Migrant Workers applicable on the establishment in which ten or more migrant workers are employed or were employed on any day of the preceding twelve months and also provide that a Inter-State Migrant may register himself as an Inter-State Migrant Worker on the portal on the basis of self-declaration and Aadhaar;
- An Inter-State Migrant Worker has been provided with the portability to avail benefits in the destination State in respect of ration and availing benefits of building and other construction worker cess;
- To constitute the National Occupational Safety and Health Advisory Board to give recommendations to the Central Government on policy matters, relating to occupational safety, health and working conditions of workers;
- To constitute the State Occupational Safety and Health Advisory Board at the State level to advise the State Government on such matters arising out of the administration of the proposed Code;
- To make a provision for the constitution of Safety Committee by the appropriate Government in any establishment or class of establishments;
- To employ women in all establishments for all types of work. They can also work at night, that is, beyond 7 PM and before 6 AM subject to the conditions relating to safety, holiday, working hours and their consent;
- To make provision of “common license” for factory, contract labour and beedi and cigar establishments and to introduce the concept of a single all India license for a period of five years to engage the contract labour;
- To enable the courts to give a portion of monetary penalties up to fifty per cent. to the worker who is a victim of accident or to the legal heirs of such victim in the case of his death;
- To provide overriding powers to the Central Government to regulate general safety and health of persons residing in whole or part of India in the event of declaration of epidemic or pandemic or disaster;
- To make provision for Social Security Fund for the welfare of unorganised workers; and
- To make provision for adjudging the penalties imposed under the Code.

Appendix C-13: Sample Outline Spoil Management Plan

- The Spoil Management Plan should be site specific and be part of the monthly Construction Management Plan.
- The contractor, in consultation with the ULB, has to find out appropriate location/s for the disposal of the excess soil generated. The spoils should be deposited only at these sites.
- Further precautions need to be taken in case of the contaminated spoils.
- The vehicle carrying the spoil should be covered properly.
- The spoils generating from each site should be removed on the same day or immediately after the work is complete. The site / road should be restored to the original condition.

I. Spoils information

The spoil information contains the details like a) The type / material, b) Potential contamination by that type, c) Expected volume (site / component specific), d) Spoil Classification etc.

II. Spoils management

The Spoil Management section gives the details of a) Transportation of spoil b) disposal site details c) Precautions taken d) Volume of contaminated spoil, if present, d) Suggested reuse of disposal of the spoil

III. Documentation

The volume of spoil generated (site specific, date wise), site disposed, reuse / disposal details should be documented properly.

Appendix C-14: Sample Outline Traffic Management Plan

A. Principles for TMP around the Water Pipes/Sewer Construction Sites

1. One of the prime objectives of this TMP is to ensure the safety of all the road users along the work zone, and to address the following issues:

- the safety of pedestrians, bicyclists, and motorists travelling through the construction zone;
- protection of work crews from hazards associated with moving traffic;
- mitigation of the adverse impact on road capacity and delays to the road users;
- maintenance of access to adjoining properties; and
- addressing issues that may delay the project.

B. Operating Policies for TMP

2. The following principles will help promote safe and efficient movement for all road users (motorists, bicyclists, and pedestrians, including persons with disabilities) through and around work zones while reasonably protecting workers and equipment.

- Make traffic safety and temporary traffic control an integral and high-priority element of project from planning through design, construction, and maintenance.
- Inhibit traffic movement as little as possible.
- Provide clear and positive guidance to drivers, bicyclists, and pedestrians as they approach and travel through the temporary traffic control zone.
- Inspect traffic control elements routinely, both day and night, and make modifications when necessary.
- Pay increased attention to roadside safety in the vicinity of temporary traffic control zones.
- Train all persons that select, place, and maintain temporary traffic control devices.
- Keep the public well informed.
- Make appropriate accommodation for property owners, residents, businesses, emergency services, railroads, commercial vehicles, and transit operations.

3. **Figure A2 to Figure A12** illustrates the operating policy for TMP for the construction of water pipes and the sewers along various types of roads.

C. Analyze the impact due to street closure


4. Apart from the capacity analysis, a final decision to close a particular street and divert the traffic should involve the following steps:

- approval from the ULB/Public Works Department (PWD) to use the local streets as detours;
- consultation with businesses, community members, traffic police, PWD, etc, regarding the mitigation measures necessary at the detours where the road is diverted during the construction;
- determining of the maximum number of days allowed for road closure, and incorporation of such provisions into the contract documents;
- determining if additional traffic control or temporary improvements are needed along the detour route;
- considering how access will be provided to the worksite;
- contacting emergency service, school officials, and transit authorities to determine if there are impacts to their operations; and
- developing a notification program to the public so that the closure is not a surprise. As part of this program, the public should be advised of alternate routes that commuters can take or will have to take as result of the traffic diversion.

5. If full road-closure of certain streets within the area is not feasible due to inadequate capacity of the detour street or public opposition, the full closure can be restricted to weekends

with the construction commencing on Saturday night and ending on Monday morning prior to the morning peak period.

Figure A1: Policy Steps for the TMP

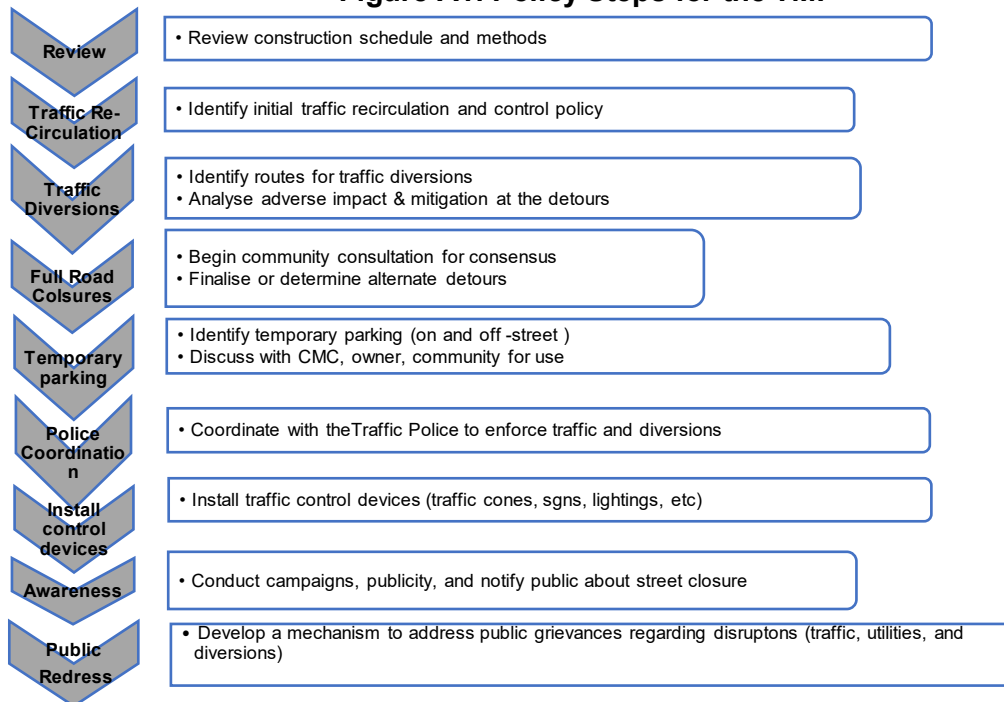

D. Public awareness and notifications

6. As per discussions in the previous sections, there will be travel delays during the constructions, as is the case with most construction projects, albeit on a reduced scale if utilities and traffic management are properly coordinated. There are additional grounds for travel delays in the area, as most of the streets lack sufficient capacity to accommodate additional traffic from diverted traffic as a result of street closures to accommodate the works.

6. The awareness campaign and the prior notification for the public will be a continuous activity which the project will carry out to compensate for the above delays and minimize public claims as result of these problems. These activities will take place sufficiently in advance of the time when the roadblocks or traffic diversions take place at the particular streets. The reason for this is to allow sufficient time for the public and residents to understand the changes to their travel plans. The project will notify the public about the roadblocks and traffic diversion through public notices, ward level meetings and city level meeting with the elected representatives.

7. The PIU will also conduct an awareness campaign to educate the public about the following issues:

- traffic control devices in place at the work zones (signs, traffic cones, barriers, etc.);
- defensive driving behaviour along the work zones; and
- reduced speeds enforced at the work zones and traffic diversions.

8. It may be necessary to conduct the awareness programs/campaigns on road safety during construction.

9. The campaign will cater to all types of target groups i.e. children, adults, and drivers. Therefore, these campaigns will be conducted in schools and community centres. In addition, the project will publish a brochure for public information. These brochures will be widely circulated around the area and will also be available at the PIU, and the contractor's site office. The text of the brochure should be concise to be effective, with a lot of graphics. It will serve the following purpose:

- explain why the brochure was prepared, along with a brief description of the project;
- advise the public to expect the unexpected;
- educate the public about the various traffic control devices and safety measures adopted at the work zones;
- educate the public about the safe road user behaviour to emulate at the work zones;
- tell the public how to stay informed or where to inquire about road safety issues at the work zones (name, telephone, mobile number of the contact person; and
- indicate the office hours of relevant offices.

E. Install traffic control devices at the work zones and traffic diversion routes

10. The purpose of installing traffic control devices at the work zones is to delineate these areas to warn, inform, and direct the road users about a hazard ahead, and to protect them as well as the workers. As proper delineation is a key to achieve the above objective, it is important to install good traffic signs at the work zones. The following traffic control devices are used in work zones:

- Signs
- Pavement Markings
- Channelizing Devices
- Arrow Panels
- Warning Lights

11. Procedures for installing traffic control devices at any work zone vary, depending on road configuration, location of the work, construction activity, duration, traffic speed and volume, and pedestrian traffic. Work will take place along major roads, and the minor internal roads. As such, the traffic volume and road geometry vary. The main roads carry considerable traffic; internal roads in the new city areas are wide but in old city roads very narrow and carry considerable traffic. However, regardless of where the construction takes place, all the work zones should be cordoned off, and traffic shifted away at least with traffic cones, barricades, and temporary signs (temporary "STOP" and "GO").

12. **Figure A2 to Figure A12** illustrates a typical set-up for installing traffic control devices at the work zone of the area, depending on the location of work on the road way, and road geometrics:

- Work on shoulder or parking lane
- Shoulder or parking lane closed on divided road
- Work in Travel lane
- Lane closure on road with low volume
- Lane closure on a two-line road with low volume (with yield sign)
- Lane closure on a two-line road with low volume (one flagger operation)
- Lane closure on a two lane road (two flagger operation)
- Lane closure on a four lane undivided Road
- Lane closure on divided roadway
- Half road closure on multi-lane roadway
- Street closure with detour

13. The work zone should take into consideration the space required for a buffer zone between the workers and the traffic (lateral and longitudinal) and the transition space required for delineation, as applicable. For the works, a 30 cm clearance between the traffic and the temporary STOP and GO signs should be provided. In addition, at least 60 cm is necessary to install the temporary traffic signs and cones.

14. Traffic police should regulate traffic away from the work zone and enforce the traffic diversion result from full street closure in certain areas during construction. Flaggers/ personnel should be equipped with reflective jackets at all times and have traffic control batons (preferably the LED type) for regulating the traffic during night time.

16. In addition to the delineation devices, all the construction workers should wear fluorescent safety vests and helmets in order to be visible to the motorists at all times. There should be provision for lighting beacons and illumination for night constructions.

Figure A2 & A3: Work on shoulder or parking lane & Shoulder or parking lane closed on divided road

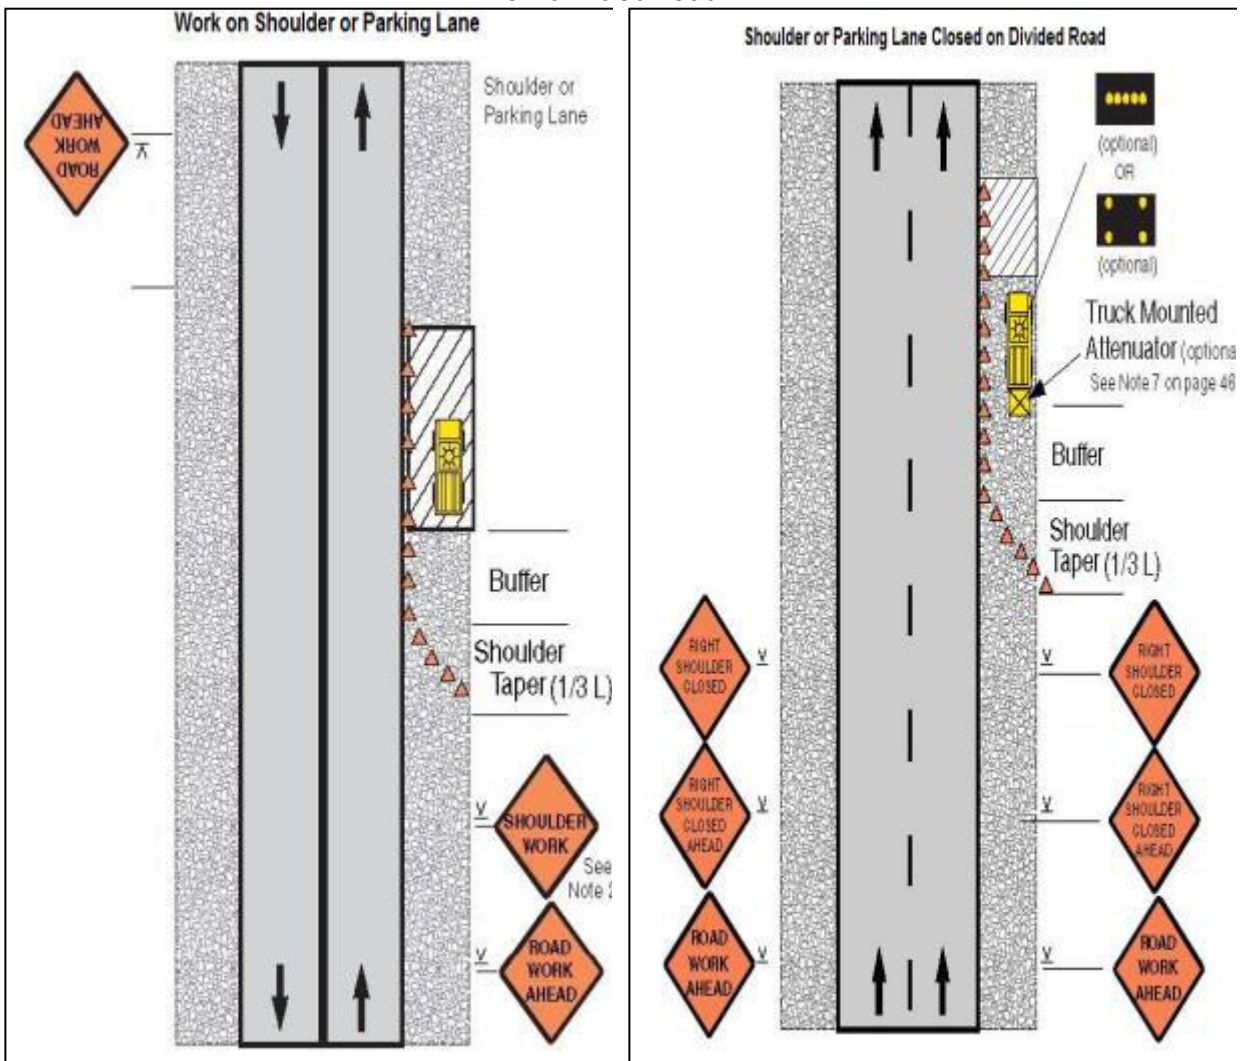


Figure A4 & A5: Work in Travel Lane & Lane closure on road with low volume

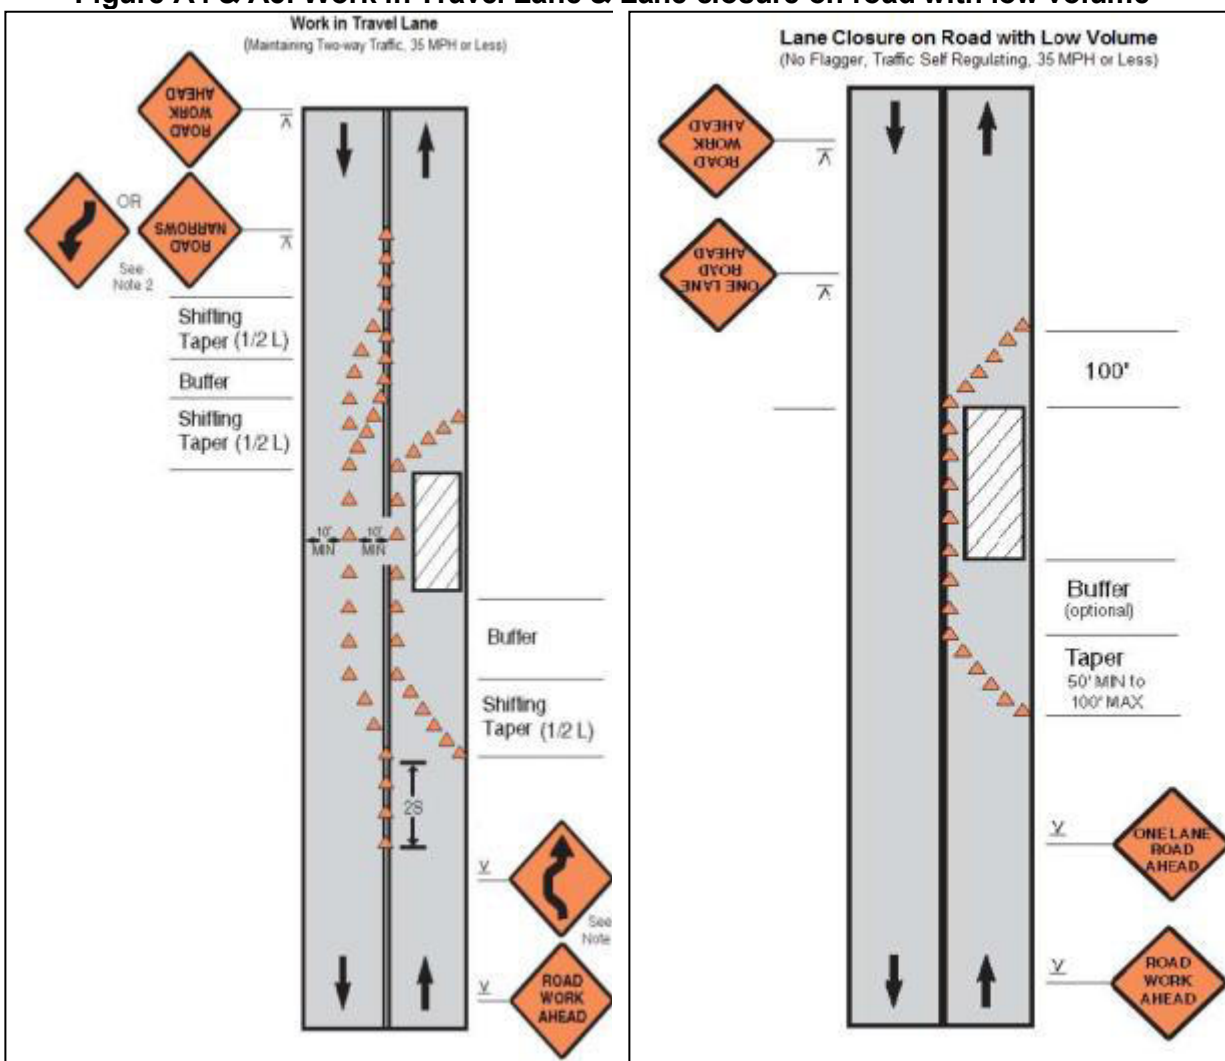


Figure A6 & A7: Lane closure on a two-line road with low volume (with yield sign) & Lane closure on a two-line road with low volume (one flagger operation)

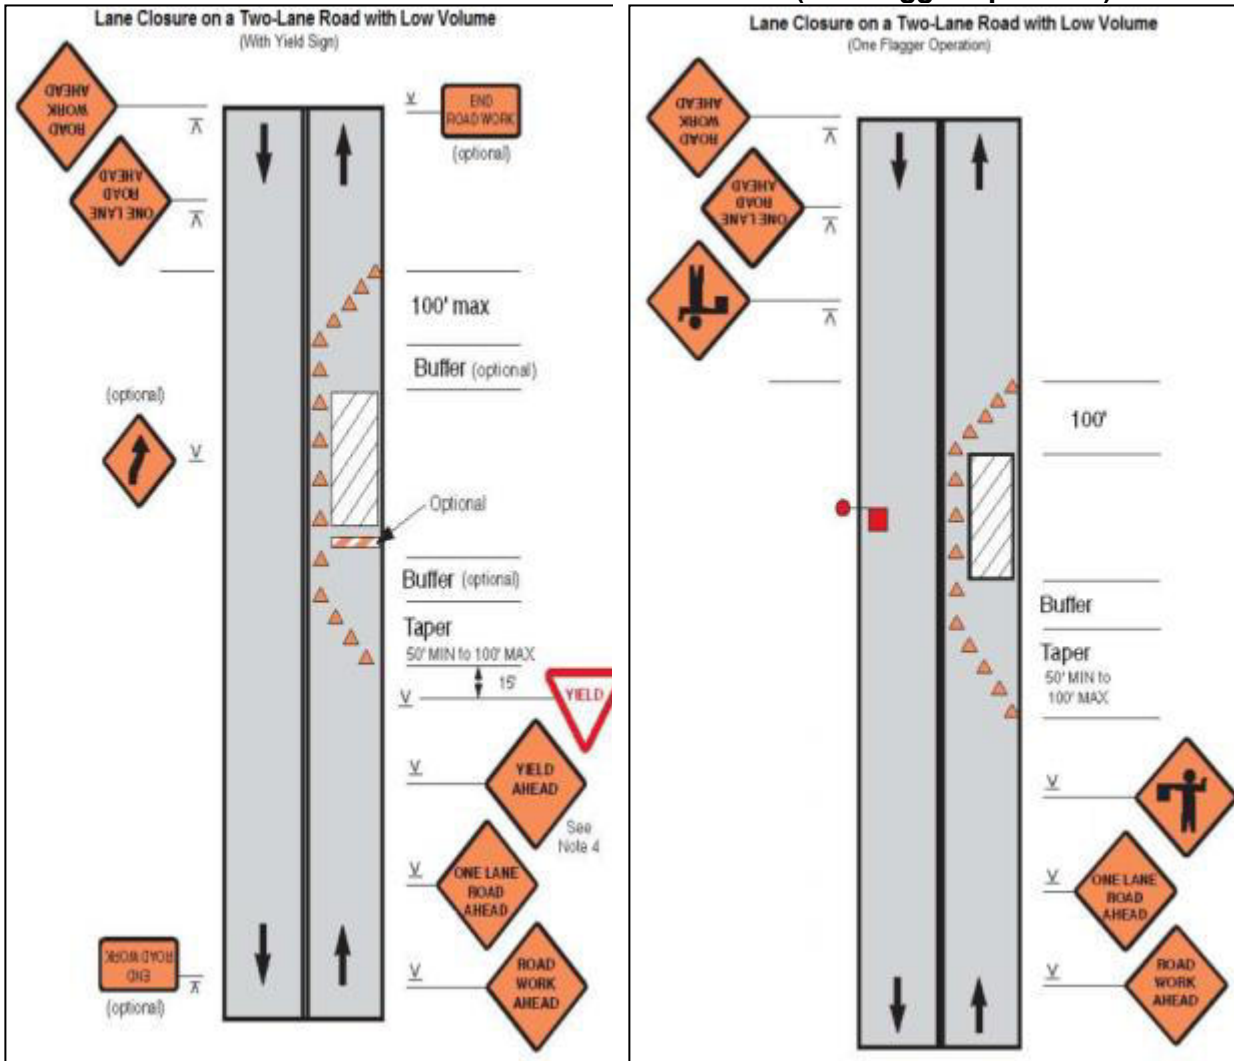


Figure A8 & A9: Lane Closure on a Two-Lane Road (Two Flagger Operation) & Lane Closure on a Four-Lane Undivided Road


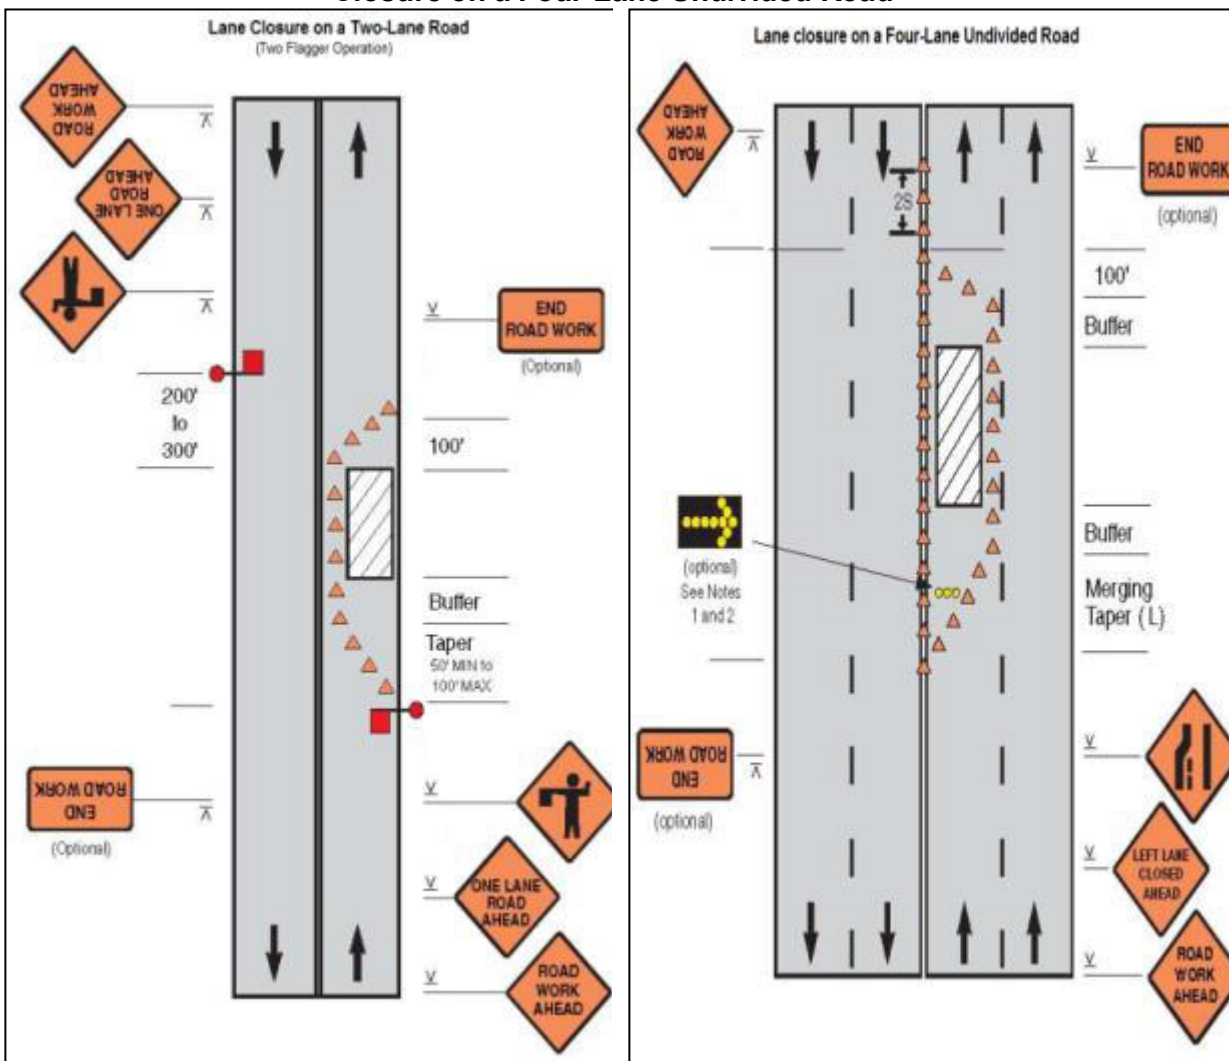


Figure A10 & A11: Lane Closure On Divided Roadway & Half Road Closure On Multi-Lane Roadway

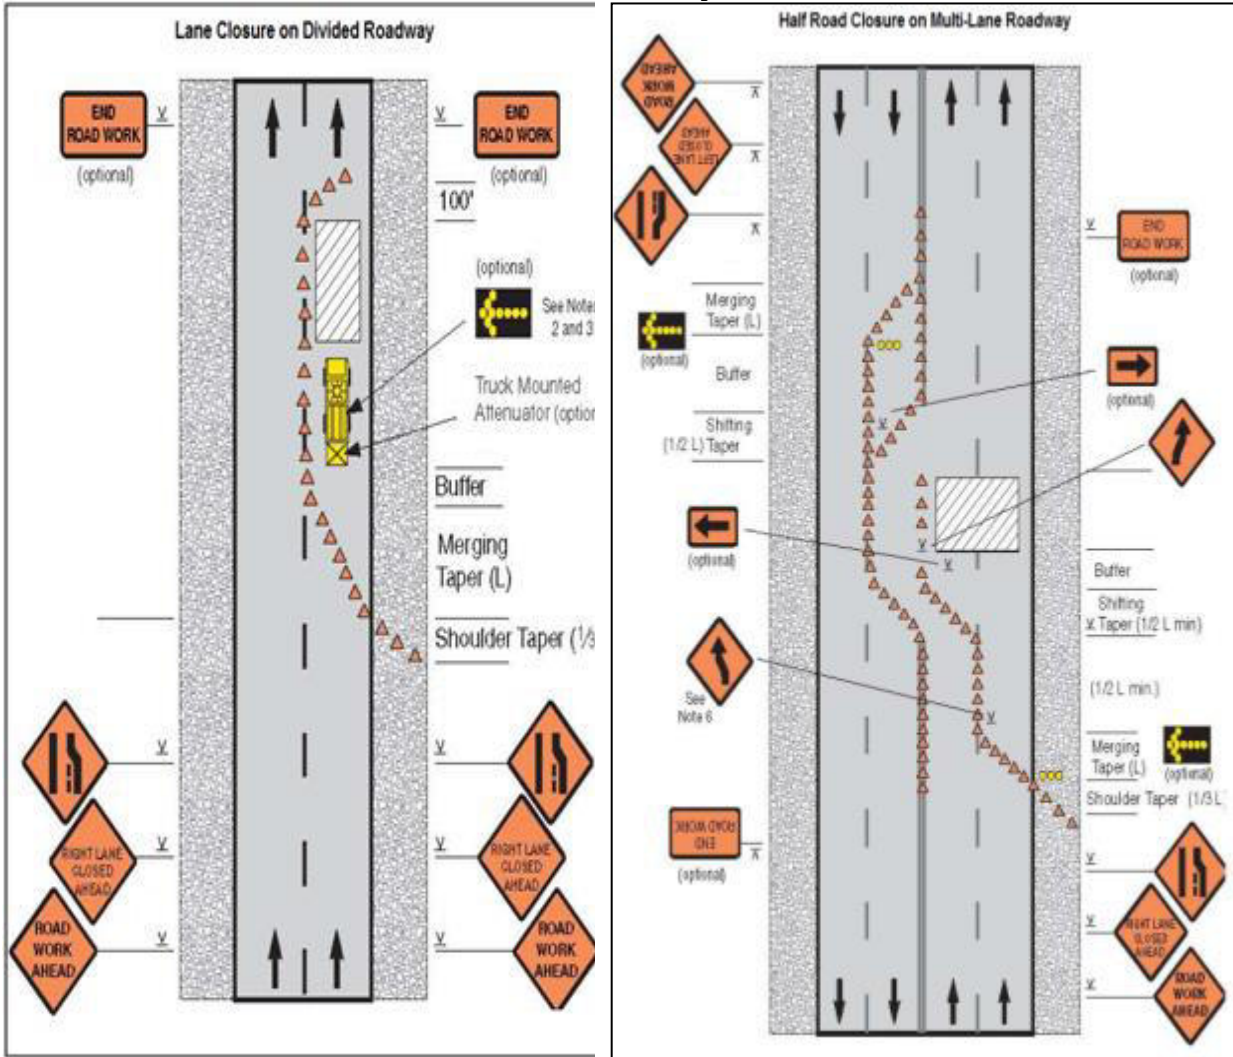

Appendix C-15: Sample Six Monthly Reporting Format

1. Introduction

- Overall project description and objectives
- Description of sub-projects
- Environmental category of the sub-projects
- Details of site personnel and/or consultants responsible for environmental monitoring
- Overall project and sub-project progress and status

No.	Sub-Project Name	Status of Sub-Project				List of Works	Progress of Works
		Design	Pre-Construction	Construction	Operational Phase		
		┐	┐	┐	┐		
		┐	┐	┐	┐		
		┐	┐	┐	┐		

2. Compliance status with National/ State/ Local statutory environmental requirements

No.	Sub-Project Name	Statutory Environmental Requirements	Status of Compliance	Action Required

3. Compliance status with environmental loan covenants

No.(List schedule and paragraph number of Loan Agreement)	Covenant	Status of Compliance	Action Required

4. Compliance status with the environmental management and monitoring plan

5. Provide the monitoring results as per the parameters outlined in the EMP. Append supporting documents where applicable, including Environmental Site Inspection Reports.
6. There should be reporting on the following items which can be incorporated in the checklist of routine Environmental Site Inspection Report followed with a summary in the semi-annual report send to ADB. Visual assessment and review of relevant site documentation during routine site inspection needs to note and record the following:
 - What are the dust suppression techniques followed for site and if any dust was noted to escape the site boundaries;
 - If muddy water was escaping site boundaries or muddy tracks were seen on adjacent roads;
 - adequacy of type of erosion and sediment control measures installed on site, condition of erosion and sediment control measures including if these were intact following heavy rain;
 - Are their designated areas for concrete works, and refuelling;
 - Are their spill kits on site and if there are site procedure for handling emergencies;
 - Is there any chemical stored on site and what is the storage condition?
 - Is there any dewatering activities if yes, where is the water being discharged;
 - How are the stockpiles being managed;
 - How is solid and liquid waste being handled on site;
 - Review of the complaint management system;
 - Checking if there are any activities being under taken out of working hours and how that is being managed.

Summary Monitoring Table

Impacts (List from IEE)	Mitigation Measures (List from IEE)	Status Compliance	of	Responsibility of mitigation	Responsibility of monitoring	Cost and Source of Funds	Remarks
Design Phase							
Pre-Construction Phase							
Construction Phase							
Operational Phase							

Overall Compliance with CEMP/ EMP

No.	Sub-Project Name	EMP/CEMP Part of Contract Documents(Y/N)	CEMP/EMP Being Implemented (Y/N)	Status of Implementation (Excellent/Satisfactory/Partially Satisfactory/Below Satisfactory)	Action Proposed and Additional Measures Required

5. Approach and methodology for environmental monitoring of the project

- Brief description on the approach and methodology used for environmental monitoring of each sub-project

6. Monitoring of environmental impacts on project surroundings (ambient air, water quality and noise levels)

- Brief discussion on the basis for monitoring
- Indicate type and location of environmental parameters to be monitored
- Indicate the method of monitoring and equipment to be used
- Provide monitoring results and an analysis of results in relation to baseline data and statutory requirements

As a minimum the results should be presented as per the tables below.

Air Quality Results

Site No.	Date of Testing	Site Location	Parameters (Government Standards)			
			PM ₁₀ µg/m ³	PM _{2.5} µg/m ³	SO ₂ µg/m ³	NO ₂ µg/m ³

Water Quality Results

Site No.	Date of Sampling	Site Location	Parameters(Government Standards)					
			pH	Conductivity μS/cm	BODm g/L	TSSmg /L	TNmg/ L	TPmg/ L

Noise Quality Results

Site No.	Date of Testing	Site Location	LAeq (dBA) (Government Standard)	
			DayTime	NightTime

7. Summary of key issues and remedial actions

- Summary of follow up time-bound actions to be taken within a set timeframe.

8. Appendixes

- Photos
- Summary of consultations
- Copies of environmental clearances and permits
- Sample of environmental site inspection report
- Other

Appendix C-16: Sample Environmental Site Inspection Report

Project Name Contract Number

NAME: DATE: TITLE: DMA: LOCATION: ____ GROUP:

WEATHER:	Project Activity Stage	Survey	
		Design	
		Implementation	
		Pre-Commissioning	
		Guarantee Period	

	Compliance
Compliance marked as Yes / No / Not applicable(NA) / Partially Implemented (PI)	
EHS supervisor appointed by contractor and available on site	
Construction site management plan (spoils, safety, schedule, equipment etc.,) prepared	
Traffic management plan prepared	
Dust is under control	
Excavated soil properly placed within minimum space	
Construction area is confined; no traffic/pedestrian entry observed	
Surplus soil/debris/waste is disposed without delay	
Construction material (sand/gravel/aggregate) brought to site as & when required only	
Tarpaulins used to cover sand & other loose material when transported by vehicles	
After unloading , wheels & undercarriage of vehicles cleaned prior to leaving the site	
No chance finds encountered during excavation	
Work is planned in consultation with traffic police	
Work is not being conducted during heavy traffic	
Work at a stretch is completed within a day (excavation, pipe laying & backfilling)	
Pipe trenches are not kept open unduly	
Road is not completely closed; work is conducted on edge; at least one line is kept open	
Road is closed; alternative route provided & public informed, information board provided	
Pedestrian access to houses is not blocked due to pipe laying	
Spaces left in between trenches for access	
Wooden planks/metal sheets provided across trench for pedestrian	
No public/unauthorized entry observed in work site	
Children safety measures(barricades, security)in place at works in residential areas	
Prior public information provided about the work, schedule and disturbances	
Caution/warning board provided on site	
Guards with red flag provided during work at busy roads	
Workers using appropriate PPE (boots, gloves, helmets, ear muffs etc)	
Workers conducting or near heavy noise work is provided with ear muffs	
Contractor is following standard & safe construction practices	
Deep excavation is conducted with land slip/protection measures	
First aid facilities are available on site and workers informed	
Drinking water provided at the site	
Toilet facility provided at the site	
Separate toilet facility is provided for women workers	
Workers camps are maintained cleanly	
Adequate toilet & bath facilities provided	
Contractor employed local workers as far as possible	

Workers camp set up with the permission of PIU	
Adequate housing provided	
Sufficient water provided for drinking/washing/bath	
No noisy work is conducted in the nights	
Local people informed of noisy work	
No blasting activity conducted	
Pneumatic drills or other equipment creating vibration is not used near old/risky buildings	

Signature

Name
Position

Name
Position

Appendix C-17: Sample Grievance Registration Form

(To be available in Hindi and English)

The _____ Project welcomes complaints, suggestions, queries, and comments regarding project implementation. We encourage persons with grievance to provide their name and contact information to enable us to get in touch with you for clarification and feedback.

Should you choose to include your personal details but want that information to remain confidential, please inform us by writing/typing ***(CONFIDENTIAL)*** above your name. Thank you.

Date	Place of registration	Project Town			
		Project:			
Contact information/personal details					
Name		Gender	* Male * Female	Age	
Home address					
Place					
Phone no.					
E-mail					
Complaint/suggestion/comment/question Please provide the details (who, what, where, and how) of your grievance below:					
If included as attachment/note/letter, please tick here:					
How do you want us to reach you for feedback or update on your comment/grievance?					

FOR OFFICIAL USE ONLY

Registered by: (Name of official registering grievance)	
Mode of communication: Note/letter E-mail Verbal/telephonic	
Reviewed by: (Names/positions of officials reviewing grievance)	
Action taken:	
Whether action taken disclosed:	Yes No
Means of disclosure:	

Appendix C-18: Management Plan for Night works at Project Sites

Following requirements should be fulfilled for construction works at night hours-

1. Night works should be avoided at construction sites specially in residential areas and should be performed only when day works are not possible due to excessive traffic/public/pedestrian movement, site of cultural or religious importance, where there is huge crowd during day hours or any other unavoidable circumstances.
2. Contractor should plan for night works only after directions from PMU/PIU/CMSC
3. Contractor should submit plan for night works for approval from PIU.
4. PIU should ensure that prior written information should be given to local authorities such as district administration, Police/traffic police, line agencies concerned, residents welfare association/business association/vyapar of the affected areas and their consents/permissions should be taken prior to start of night works.
5. PIU/CMSC engineers should check and ensure that all the preparation as per management plan is done by contractor and contractor is having all the necessary equipments and materials for night works.
6. Contractor is required to have following equipments/arrangements for night works-
 - Contractors should have hand held noise level meter for measurement of noise during night hours
 - Contractors should have hand held lux meter for the measurement of illumination during night hours
 - Preferably electrical connections is available for running equipments otherwise sound proof/super silent Diesel Generator set should be available
 - Sound level should not increase as per following-

Type of area of work	Maximum noise level dB(A)
Industrial	70
Commercial	55
Residential	45
Silence zone	40

- Illumination should be as follows-

Minimum illumination (lx)	Areas to be illuminated	Type of work activity
54	Illumination throughout the work area	General work area lighting, and performance of visual tasks of large size, or medium contrast, or low require accuracy
108	Illumination of work area and areas adjacent to equipment	Performance of visual tasks of medium size, or low to medium contrast, or medium required accuracy
216	Illumination of task	Performance of visual tasks of small size, or low contrast or high required accuracy or fine finish

- As far as possible ready mix concrete from batching plant to be used, otherwise the concrete should be prepared away from residential areas and brought to the site
- All the noise activity like hammering, cutting, crushing, running of heavy equipments should be done in day time and avoided in night time

- Workers engaged in night works should have adequate rest/sleep in day time before start of night works
 - Worker engaged for night works should have previous experience of night works and should be physically fit for such works including clear vision in night
 - All the necessary provisions of traffic aids such as traffic signals, road signage, barricades, cautions boards, traffic diversion boards etc. should be available with fluorescent/retro-reflective arrangements
 - Workers should be trained before start of night works about risks and hazards of night works and their mitigation measures and should be provided all the protective aids (PPEs) including fluorescent/retro-reflective vests
 - Horns should not be permitted by equipment's and vehicles
 - Workers should not shout and create noise
 - First aid and emergency vehicles should be available at site
 - Emergency preparedness plan should be operative during night works
 - Old persons and pregnant women and women having small kids should not work in night time
 - All the vehicles and equipment's being used at night works should have adequate type of silencers/enclosures/mufflers to reduce noise
 - All the vehicles should be checked for working head lamps, tail lamps, inner lights etc. before start of night works
7. PIU/CMSC site engineers and contractor's safety personnel should closely monitor the safety of works continuously and noise and illumination levels on hourly basis and maintain photographic and videographic records as well as register the observations
 8. Night works should be stopped early in the morning at least one hour before start of pedestrian/traffic movement
 9. After completion of night works all the site should be cleaned and maintained obstruction free for day time movement of vehicles and pedestrians
 10. Drivers and workers should be alert and responsive during night works
 11. All the wages to workers working in night hours should be as per the applicable labour acts
 12. Avoid any nuisance which may create problems to nearby habitants and work peacefully during night hours
 13. Night works should not be conducted near hospitals and during peak seasons such as peak tourist season, students' exam times etc.

Appendix C-19: Guidelines for Safety during Monsoon/Heavy rainfall

Excavation and refilling of earth are common activities, which, if not carefully executed may pose problems to the safety of works as well as passers-by and road users during the impending Monsoon.

Normal and heavy rainfall event affect our ongoing works, It should be our conscientious effort to ensure that such events do not prove to be problematic to people and structures in town. During monsoon PIU/PMCBC should ensure that any further excavation work is taken up only after ensuring that the earlier work is in safe stage. It is desired that DCM/ACM & Ex En PIU should inspect all sites during rains and take proactive actions.

Some of the precautions and mitigation measures to be taken are discussed below-

1. The execution of works having deep excavation in smaller lanes and congested areas should be completed well before monsoon. The works of deep excavation during monsoon should not be preferably taken up or extensive care should be taken for execution of such works.
2. The settlement in refilled trenches of sewerage and water supply lines may occur during monsoon. PMCBC and PIU team should inspect all sites after a storm to identify such reaches and take immediate corrective action by proper refilling and compacting. It is responsibility of all engineers to look after this activity during monsoon and ensure corrective actions from Contractor's side.
3. The contractor's crew should be equipped with vehicle, gum boots, raincoats, torch etc. to tackle such situation during and after rains. Adequate quantities of earth, debris and gravel should be stacked at strategic places so that no time is lost in procuring such material.
4. In trenches where pipe laying has been done and duly tested and approved, refilling should be done and all surplus material relocated to safe disposal sites such that it does not obstruct traffic or waterways.
5. All open ends of WS and WW pipelines should be firmly plugged to prevent debris from entering the pipeline. Manhole covers of sewer lines should be fixed in place to avoid any harm to road users.
6. Drains are primary or secondary carriers of storm water. Any unutilized construction material should be relocated to allow free passage of storm water. Surplus earth should be suitably and immediately be relocated to avoid earth from falling into the drain so that choking does not occur.
7. Overhead works should not be carried on in-weather conditions that threaten the safety of workers. More frequent checks on scaffold and bracings should be done during monsoon season.
8. Additional precautions should be taken of the power lines, ignorance and carelessness can cause major accidents and casualty.
9. Take preventive measures for water logging in working areas by providing dewatering pumps. Place bright and reflective warning signs.
10. Inspection should also be carried out before resumption of work after a shower/rain.
11. Storage of Construction Material: Steel & Cement are vital ingredients for quality construction work but in absence of proper storage, especially during monsoon, cement and steel may rapidly decline in quality and strength. Care should be taken to protect these materials and use of any exposed material should be allowed only after conducting fresh tests. Improper storage of such material should be reported to SE PIU/ACM PMCBC and use of any apparently affected material should be done after permission of SE PIU/DCM/ACM.

Additional Precautions

1. Adequate set up and resources such as dewatering pumps, electrical routings etc should be planned ahead. Water logging on main roads to be avoided, where construction works are going on.
2. Ensuring the monsoon specific PPE's issued in adequate and are used during monsoon.
3. Use of electric extension box should be avoided; extension cables (if used) should not be wet and damaged. Cables connections should be only weatherproof/waterproof. Electrical and HSE personnel of contractor should visit permanent and running sites regularly. Transparent protective sheets/rain sheds should be placed for the power distribution boards.
4. Welding machines, bar cutting machines etc. should be kept in dry conditions; should not stand in water logged area. Brakers and Drill machines should not be used when raining; dirt/mud should be scrubbed with cloth.
5. Special Trainings to all drivers and operators on safe practices and all vehicles/ equipment's maintenance checks to be more frequent.
6. High boom equipment to be stopped during blowing of high speed wind and rain storm. Arresting of parked vehicles, equipment during monsoon should be done.
7. All chemicals should be stored as per MSDS, chemicals to be protected from water ingress. Chemical waste should be disposed for preventing overflow of chemicals.
8. At labor camps following precautions should be taken:-
 - Maintaining hygiene & proper housekeeping.
 - Additional health checkup camp to identify seasonal diseases
 - Preventive measures on mosquito/parasite breeding mainly in work locations and camps
 - Frequent cleaning of toilets
 - To avoid water borne diseases, high level of cleanliness to be maintained, drinking water containers need to be cleaned and kept covered. Walk areas and pathways to be covered with Murom and soft rock particles (to avoid soft soil conditions).
 - Obstacle free approach to rest sheds, camp and toilets.
 - Proper illumination, provision of battery operated emergency lights
 - No bonfires inside resting sheds. No use of wood.

Note-

SE-PIU and ACM-PMCBC should oversee the arrangements to effectively deal with the eventuality.

EHS officer of contractor should visit each site and camps more frequently. Contractor/EHS officer will also impart training on safe working methods during Monsoon and will keep a daily watch on weather conditions to share with site team to act accordingly.

Contractor should organize Monsoon Health Camps and Monitor Workmen Habitat and Hygiene.


Appendix C-20: Sample ACM Management Plan

BACKGROUND OF ASBESTOS

1. The purpose of this Asbestos Management Plan (AMP) is to identify, use appropriate methodology and scientifically handling /disposal of the Asbestos Containing Materials (ACM) in order to comply with the applicable National legislation and International standards in sync with norms of ADB's SPS 2009. ADB has mandated as per Appendix 5 - prohibit the investment activities list - production of, trade in, or use of un-bonded asbestos fibers is deliberated. As per SPS 2009 Safeguard Requirement 1, it is emphasized "that the borrower/client will provide workers with a safe and healthy working environment" in the work areas with accounted risks inherent to the work zone and defined safety instructions and standard operating procedures identifying roles and responsibilities.
2. Asbestos is a collective name given to a group of minerals that occur naturally as fiber bundles and possess high tensile strength, flexibility, heat resistance, non-biodegradability with chemical and physical durability. Asbestos is hydrated silicates with complex crystal structures. It is found in two configurations: chrysotile (derived from serpentine minerals) and amphibole is a naturally occurring mineral with long thin fibers. The most abundant asbestos used in the world is chrysotile. The use of ACM propagated due to its economic viability.
3. The purpose of this AMP is to identify, use appropriate methodology and scientifically handling /disposal of the Asbestos Containing Materials (ACM) in order to comply with the applicable National legislation and International standards in sync with norms of ADB's SPS 2009.. As per SPS 2009 Safeguard Requirement 1, it is emphasized "that the borrower/client will provide workers with a safe and healthy working environment" in the work areas with accounted risks inherent to the sector and defined safety instructions and standard operating procedures identifying roles and responsibilities.

Table 1: REGULATORY FRAMEWORK, STANDARDS AND PROTOCOL

Government of India Laws, Regulations and standards on Asbestos Applicable to the projects	Requirements for the project
IS 11768: 1986/2005: Recommendations for disposal of asbestos waste material	The standard emphasis that every employer who undertakes work which is liable to generates asbestos containing waste, shall undertake adequate steps to prevent and /or reduce the generation of airborne dust during handling, storing, transportation and final disposal of final disposal of asbestos and asbestos containing products. • The crux is waste avoidance: the practice inculcated should focus the on minimal waste generation. • Waste Collection: In the project circumstance, the waste is referred to the damaged powered asbestos which will be collected in the Permissible plastic bags to be disposed off to the nearest TSDF facilities.
IS 12081: Pictorial Warning to be implemented on equipment containing Asbestos Contaminated Products.	The objective of the caution is to make the person handling to take all pre-cautionary measures and make them aware of all the possible risk.

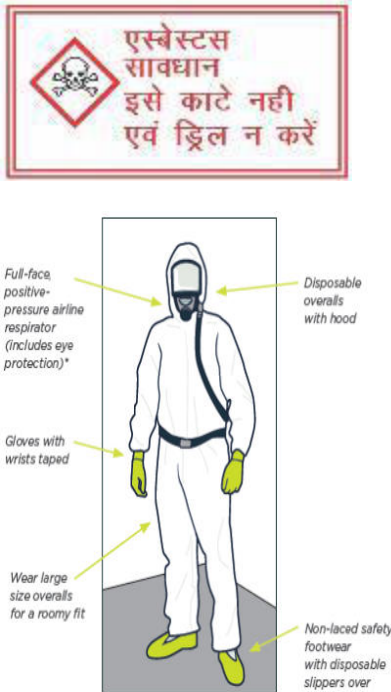	
IS 11451: Safety and Health Requirements related to Occupational Exposure to Asbestos contaminated Products.	In the project the norms pertaining to limiting number of hours working with ACM will be 8.0 hrs/48 hrs a week and the medical examination has to be periodic, the environmental monitoring has to be done as per the protocol. The safety at work place shall be enforced.
IS 11768: Waste Disposal Procedure for Asbestos Containing Products.	The protocol pertaining to disposal of the waste is emphasized, the collection of ACM powered will be in permissible plastic bags, which will be twisted tight at the neck so that the wear and tear due to abrasion will be minimum and the transportation of the asbestos waste has to be done by the authorized vendor to the approved landfill site that in the project case id TSDF.
Sampling of asbestos fiber (as per BIS-11450) has to be done regularly using personal sampler and determined using phase contrast microscope.	The Sampling and analysis protocol is emphasized. Details are given as above.

4. Further, there are several legislations that regulate the use and handling of asbestos as applicable, namely:

- The Supreme Court of India – Banned ACM use in January 21 2011.
- National Green Tribunal - In pursuant to the above order, in 2015, NGT issued an order- “that there is no asbestos mining presently operational anywhere in the country and the operations of the mines of associated minerals with asbestos has also been halted.”
- Environmental (Protection) Act (1986)-Environmental monitoring.

RISK ASSESMENT:

5. The process of evaluation of risk at all the working sites was evaluated with the

inventorization of the unscientific storage pipes-in case of worst scenario. The site identified and evaluated was Sardarshar. Site visit was conducted to evaluate the risk associated with the ACM handling and re- handling. Working with or handling AC pipes in manner that produces dust, fibers, air borne particles etc., is very harmful and hazardous to the workers and general public in and around the work sites. The condition of existing underground AC pipes are not known, however, as these are old certain pipes will be in deteriorated conditions. So the Conditions were presumed if it is in friable form or in a condition in which it can release fibers before it is subjected any disturbance or removal, all safeguard measures needs to be adopted. There were certain areas where the AC pipes were subjected to shear and are powered, and AC Pipe ends were damaged these were the high risk zones in the campus. The probability of the air borne asbestos fibers in the areas cannot be over ruled.

6. Thus it is necessitated to draft standard operating procedure for disposal of ACM. The purpose of this standard operating procedure (SOP) is to ensure the safe handling of AMC including protection from hazards associated with uncontrolled distribution, encounter and removal of Asbestos Cement (AC) Pipes and pipe fittings. The scope of this SOP encompasses all aspects of safe AC pipe handling including identification of site, re-handling and encountering of ACM, site selection and proper identification for storage, inventorization, monitoring, final disposal, training and maintenance of records.

7. The fatal health hazard with inhalation of air borne asbestos fibers and its adverse health impact are known and needs a proper attention and planning with defined roles and responsibilities to ensure the work zone is at minimal risk and safe for the workers. It is also necessary to mandate the standard operating procedures with implementation of all requisite safety gears.

8. The assessment of the ACM disposal will be vested with the DBO Operator. The undamaged pipe-where the pipe ends are intact that there is no damaged on the entire length of pipe-to be stored in isolated storage with secured pipe ends either by wrapping the ends with permissible plastic bags. The damaged/broken pipes/powered pipes will be disposed off, by bagging the same in permissible plastic bags. All the records pertaining to the inventorization has to be kept by the DBO Contractor. The same shall be cross verified by RUIDP.

EMERGENCY RESPONSE PLAN & CHANCE FIND PROTOCOL

9. The emergency procedures should include managing an uncontrolled release of asbestos materials into the workplace. The onus of the same shall be ensured with immediate action of the field staff-DBO Operator/ HSE Staff. Steps should be taken to:

- Warn anybody who may be affected.
- Exclude from the area anyone not needed to deal with the release.
- Identify the cause of the uncontrolled release.
- Regain adequate control as soon as possible.
- Make sure anyone in the work area affected, who is not wearing personal protective equipments (PPEs), including respiratory protective equipment (RPE), leaves the affected area immediately.
- Minimize the spread of asbestos by ensuring they are suitably decontaminated.
- Clean up dust and debris.
- Decontaminate anyone who is contaminated with dust and debris.
- Ensure rags, clothing or PPE is decontaminated or disposed of as contaminated

- waste.
- Consider alone and/or remote workers to ensure they can alert someone if necessary.

Check what you're working on before you start:

- Avoid using a sweeping brush as this can spread asbestos.
- Make sure no unauthorised personnel enter the area.
- The clean-up of any accidental release of higher risk materials, eg asbestos cuttings, powered asbestos that may release the asbestos fibers, to be done by authorized person

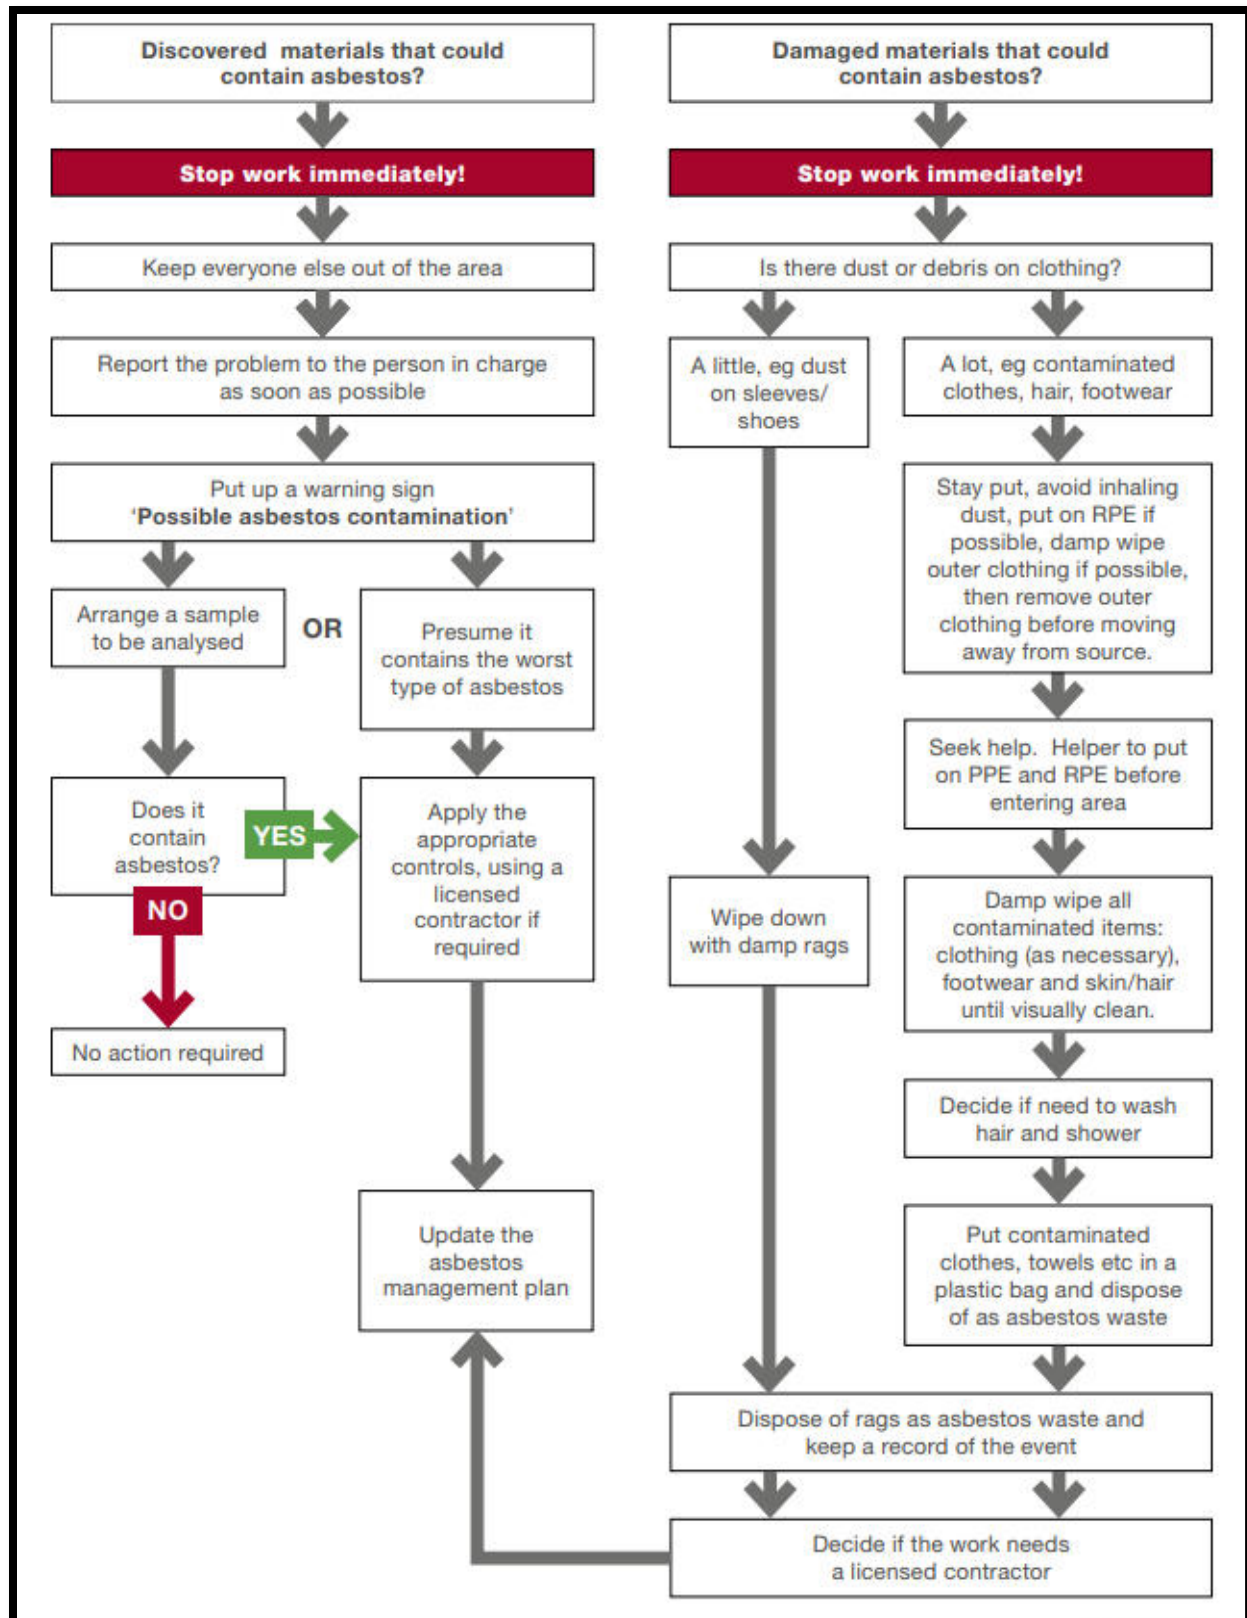


Fig.No.1-Showing Flow chart of ERP

Table 2-Roles and Responsibilities

PRE-CONSTRUCTION				
Activities	Responsibilities	Associated Documents	Estimated Cost	Remark
Design to encounter minimal ACM, and then Identification & Inventorization ACM - AC pipes & fittings	RUIDP & DBO CONTRACTOR	Form-I	Rs.100/km	The onus of the minimal encounter of ACM is vested upon the RUIDP and inventory will be with the DBO Operator and has to be annually verified by RUIDP.
Define & confine ACM storage area-in-situ			Rs.65/Sq.m	The storage area made available will be confined and fenced.
Warning signage near the ACM work site, storage and on AC pipes in local language**			Rs.500/label	The signage labels can be printed, sticker pamphlets or painted.
Training of personals handling the AC pipes and fittings	DBO CONTRACTOR	Form-II	Rs.1000/Person	All requisite safety gears should be made available at all sites.
Use of safety Gears			Rs.6000/Person	All the safety gears should be silicon based and suitable for Asbestos protection.
Briefing of Emergency Response Plan			Rs.500/Person	All the risk zones with respect to white card has to be briefed.
Confined storage with access control plan			Rs.5000/site	Inward and outward movement of authorized person must be allowed and has to be guarded or should be under key control.
Pre-history medical records of the ACM handling team			Rs.3000/Person	All requisite medical test, Respiratory test, lungs /Chest X-ray/CT Scan, Blood Test, Lower Abdomen examination etc
CONSTRUCTION PHASE				
Monthly Inspection & Annual Environmental Monitoring.	DBO CONTRACTOR	Form-III	Rs.40,000/sample	The sampling zone should be 500 m from the storage site and personal sampling has to be as per SOP-2
Reporting in SEMR	RUIDP/ DBO CONTRACTOR	None	Nil	As per ADB Format
Collection of Health records in compliance to the local laws	DBO CONTRACTOR/RUIDP/PHED/LSG	Form-IV	Nil	For regular evaluation & identification of any abornomality.

Ensure adoption of all standard operating procedure		SOP-1&2	Nil	As revision desired on basis of Site specific information may be upgraded in the SOP 1&2 if required
Collection, Segregation, Reception and Disposal as per National norms of ACM		Form-V	Nil	Standard Regulatory format has to be filled and disposed off within 90 days.
Use of safety gears prior to handling of ACM based on White Card.		White Card-Page-11	Nil	Periodic training can be site specific
Disposal of ACM to the identified TSDF Facility to be done as per procedure within or prior to 90 days		SOP-2	1500/ton of waste plus freight as per actual.	Within 90 days from the generation of waste, in case of existing waste it has to be disposed off within 90 days from the Project Start.
To inform and fill the returns in the prescribed manifest as per HWMR.		Form-V(Form-10 of the Rule HWMR	Nil	90 days from the start of work
To facilitated a restricted confined storage space with access control with proper inventorization.		Form-II	Nil	Site Specific
In-situ storage of ACM.	DBO CONTRACTOR	Form-VI		The storage of existing and encountered ACM pipes (more than 4.0 ft) will be stacked end to end at 90 deg. With vertical stacks, 8 inches above the ground, covered with permissible plastic sheet. The campus custodian-viz PHED etc should also be informed about the In-situ storage of ACM and its impact.
ACM removal	DBO CONTRACTOR	--	--	Follow ACM Removal
Record maintenance of ACM in-situ and disposed off to TSDF	DBO CONTRACTOR	Form-I & Form-IV	Nil	The copies of inventory generated and collected will have to be shared with Land Custodian (LC), RUIDP and DBO Operator. To distinguish the forms they can be

				numbered. FORM-I(LC),Form-IV(LC)
Transits ACM storage of waste to be disposed off to TSDF	DBO Contractor	Form-IV	50,000/room	An isolated storage room should be constructed with 10x10 with height of 3.5 ft roofed properly for transit disposal of ACM to TSDF. DISPOSABLE ASBESTOS WASTE STORAGE ROOM HAZARDOUR WASTE CATEGORY-15.2 (as per Hazardous waste management & Handling Rules 2015).
POST CONSTRUCTION PHASE				
Compliance of AAQM, Asbestos Fiber monitoring and Soil Quality monitoring and Periodic Work zone monitoring(Asbestos fiber count) records to be maintained	DBO Contractor	SOP-2	Rs.40,000/sample	The Asbestos Fiber count monitoring has to be conducted prior to ACM handling operation and after ACM Handling operation by an Accredited Laboratory. List of accredited laboratory will be available at Rajasthan State Pollution Control Board website- rspcb.nic.in
Health records &Periodic Medical Checkup of the personals handling ACM to be maintained.	PHED/LSG/DBO CONTRACTOR	Form-II	Rs.3000/Person	All the concerned employees deputed to handle or deal with ACM has to have Pre medical history and periodic medical examination done

Permissible Levels

10. Permissible Exposure Limit (PEL) for asbestos is 0.1 fibers per cubic centimeter of air as an eight hour time weighted average (TWA), with an excursion limit (EL) of 1.0 asbestos fiber per cubic centimeter over a 30 minutes period.

ACM REMOVAL

11. ACM Removal has to be checked in sync with the design and emphasis has to be laid to avoid the removal of ACM, in case it is unavoidable, then all the requisite safety gears are to be adopted:

- Inform the Asbestos Expert/HSE Expert prior to removal.

- Isolate the area with access to only trained staff/employees under supervision of Asbestos /HSE Expert.
- Exhibit all warnings

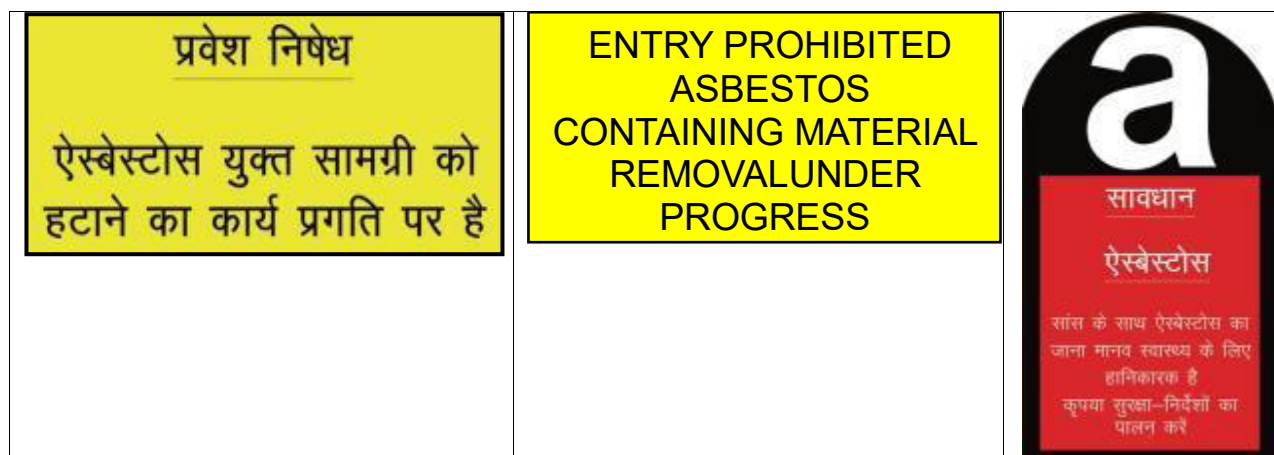


Fig. 2 Asbestos warning signage

- Undertaken Asbestos fibre Monitoring
- The trained Employees have to be deputed for removal of ACM.
- The removal ACM material has to be check with the status and extent of damage.
- Efforts should be made to remove the ACM as minimal as possible.
- The ACM removal has to be manual; it should neither be cut nor drilled.
- All removal operation should be undertaken with ACM in wet condition.
- The removed ACM will then be labeled and placed on permissible plastic sheet. It should not be put on ground directly.
- The dimension of plastic sheet should be larger than the ACM placed.
- If the ACM pipe is not damaged as about 4.0 ft and above, the ACM will be subjected for in-situ disposal.
- If the ACM is damaged and broken then it has to be packed in permissible plastic bags and disposed off to TSDF.
- Prior to disposal it can be stored in isolated room-showing board of –Hazardous waste storage room.
- The hazardous waste to be disposed off to TSDF should not be stored over 90 days after the removal date of ACM at site.
- All the safety procedures and safety gears should be worn by all the employees engaged in the ACM Removal operation.
- The Asbestos fiber monitoring, soil monitoring has to be undertaken during the operation as well.
- The process of removal of ACM will be completed after the removed ACM and its suitably disposed off either in -situ or to the isolated room prior to disposal at TSDF.
- Post ACM Removal asbestos fiber monitoring has to be undertaken to ensure the work zone is safe to resume further operations.

Safe Practices in Handling ACM

12. Proper handling and PPE:

- a. Cover up and wear PPE (Personal Protection Equipment). including respirator or

dust mask

- b. Make sure the mask has two straps to hold it firmly in place. Don't use masks that only have one
 - c. Also wear a Hard hat, gloves, disposable coveralls with a hood, and safety glasses or goggles to protect eyes
 - d. Do not eat, drink or smoke in the work area as you may inhale or eat dust. Wash your hands and face with soap and water before meal breaks and when finished work for the day.
 - e. Do not use power tools Asbestos fibers can be released if power tools are used for anything other than the removal of screws.
 - f. Do not water blast or scrub with a stiff broom or brush. It is illegal to water blast asbestos cement sheets. If the material has been accidentally water blasted or has suddenly deteriorated in some way, you should call a licensed asbestos removal DBO Operator
 - g. Wet gently with water when removing asbestos cement pipes, use a pump spray to lightly dampen the pipes and keep the dust down. Remember: Not to waterblast asbestos cement materials.
 - h. Avoid drilling and cutting into asbestos products.
 - i. Do not drill holes through and never cut Instead remove the entire product and replace it with a non-asbestos product
 - j. Don't drop fiber pipes remove them carefully, Lower them to the ground, don't drop them, to minimize breakage.
 - k. Lay plastic sheeting under the work area to prevent any dust contaminating the ground. Use 200 micron thick plastic sheeting or bags or as permissible these must not be made from recycled materials or re-used for any other purpose.
 - l. The work area has to be barricaded and there should be no un-authorized person allowed. Only Trained ACM expert should be allowed to handle the ACM along with EHS Expert.
 - m. Close windows and doors and seal vents to stop dust getting into the house; ask neighbors' to do the same.
 - n. Seal off other places where dust can get in.
 - o. Remove soft furnishings like rugs, clothes, jute bags from the work area, and seal anything with plastics if it cannot be moved.
 - p. All the AC broken pipes have to collected and stacked properly with 200micron plastic wrapping with winning signage.
 - q. Do not leave plastic sheet lying about where they may be further broken or crushed by people or traffic.
 - r. Remove all ACM by the trained handler.
 - s. Since we are amidst of dry climatic conditions due care must be taken to see that no waste broken pipes or fittings are left loose and outside the confined area and may be dampened as required.
 - t. Mark and add signage.
13. Due care has to be taken to collect the dampened waste in a permissible standard bags with proper warning signage's.
14. The wastages packed have to be disposed off to Treatment, Storage or Disposal Facility

(TSDF). The plastic bags must have legible note:

- d. Waste Type:
- e. Date of packing:
- f. Qty/Numbers:
- g. Packed by:
- h. Warning Signage:
- i. Disposal



Fig. 3- ACM: In-situ storage warning

15. The AMP procedures-**Standard Operating Procedure-01-** are as follows and are summarized as above

- j. Objectives – to keep the work zone safe and secured.
- k. Requirements – identify all the requirements needed for handling AC in the specific site and project
- l. Conduct and ensure awareness and vocational training to ACM handlers
- m. Conduct a comprehensive identification and risk assessment of ACMs
- n. Apply restriction / re-handling of ACM on ground-use of PPE. Ensure that workers handling ACM have the right PPEs as follows:
 - i. Hard helmet
 - ii. Overall suit
 - iii. Gloves
 - iv. Mask to be strapped tight
 - v. Safety goggles
 - vi. Safety shoes
 - vii. Ear plugs
- o. Avoid underground encountering of ACM
 - i. Ensure that an authorized person (HSE) are supervising the work
 - ii. Barricade the area with signage
 - iii. Damp ACM
 - iv. Use safety gears
 - v. Dismantle ACM to be labeled, kept on plastic grounding and packed in permissible bags
 - vi. Label the bags properly
 - vii. Ensure shipping to proper disposal sites
- p. Site selection – the disposal site should be ready to handle ACM and protect the nearby people as well The site selection criteria are as follows:
 - i. Away from habitation
 - ii. Avoid low lying areas
 - iii. Away from water storage
 - iv. To be enveloped with minimum of 8-feet height enclosure
 - v. Avoid high vertical stacks
 - vi. Access controlled
 - vii. Proper signage enclosure
- q. Proper re-handling of AMC, labeling and packing

- r. Control access and ensure proper monitoring of records, specifically:
- Environment
 - Health
 - Reporting to regulators
- s. Dispose the ACM through qualified DBO Operators up to the Total Sanitary Disposal Facility (TSDf)

Table 3: LIST OF APPROVED TSDf OPERATORS IN RAJASTHAN

S.No	Operator	Address	Remark
1.	Rajasthan Waste Management Project (M/s Ramky Enviro Engineers Ltd)	Survey 1018/13, Vill-Gudli, Tehsil-Mavli, Zinc Choraha to Debari Railway Station Road, Dist Udaipur (Rajasthan).	This TSDf is for all kind of hazardous waste as listed in the hazardous waste (Management & Handling) Rules.
2.	Ramky Enviro Engineers Ltd, Balotra	Ramky BWMP Rd, Rajasthan 344032.	This TSDf is for all kind of hazardous waste as listed in the hazardous waste (Management & Handling) Rules
3.	Continental Petroleum Ltd	Bheror, Distt- Alwar	Only for Incineration

16. Label/display for TSDf disposal bags has to have clear display of the content in both English and local language as displayed under:

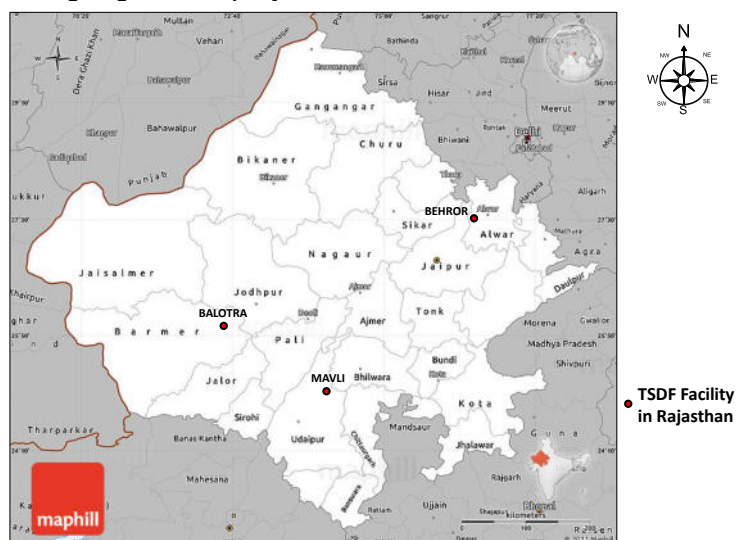


Fig 4: Map of the locations of approved TSDf in Rajasthan.

IN-SITU STORAGE ACM PIPES AREA

17. The removed undamaged ACM pipes have to be stacked properly as shown below to avoid any rolling of the pipes and eventual damage. The existing ACM Pipe stacking has to be

re-handled to stack the ACM pipes properly. If the removed ACM Pipes is less than the full length of the ACM pipes, then separate stack of the same should be done with proper pre-caution and safety measures and gears.

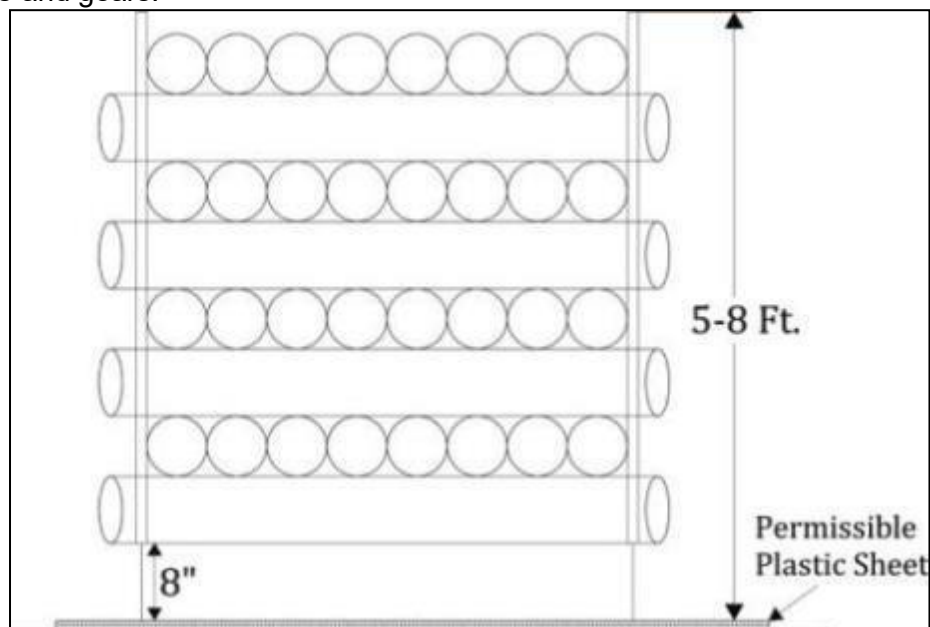


Fig. 5: Schematic diagram showing ACM Pipes stacking

18. The ACM stack has to be enveloped with proper fencing showing internal movement of person with 4.0ft corridor all around the stack. The Storage area will have display of all requisite warning and access control of the authorized person's entry and exit.

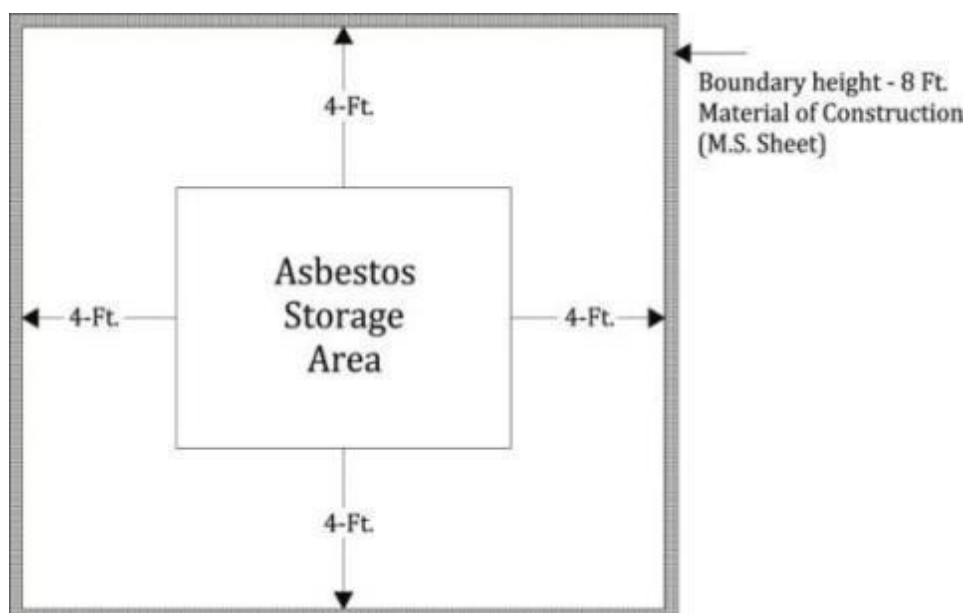


Fig. 6: Schematic diagram showing ACM Pipes storage area

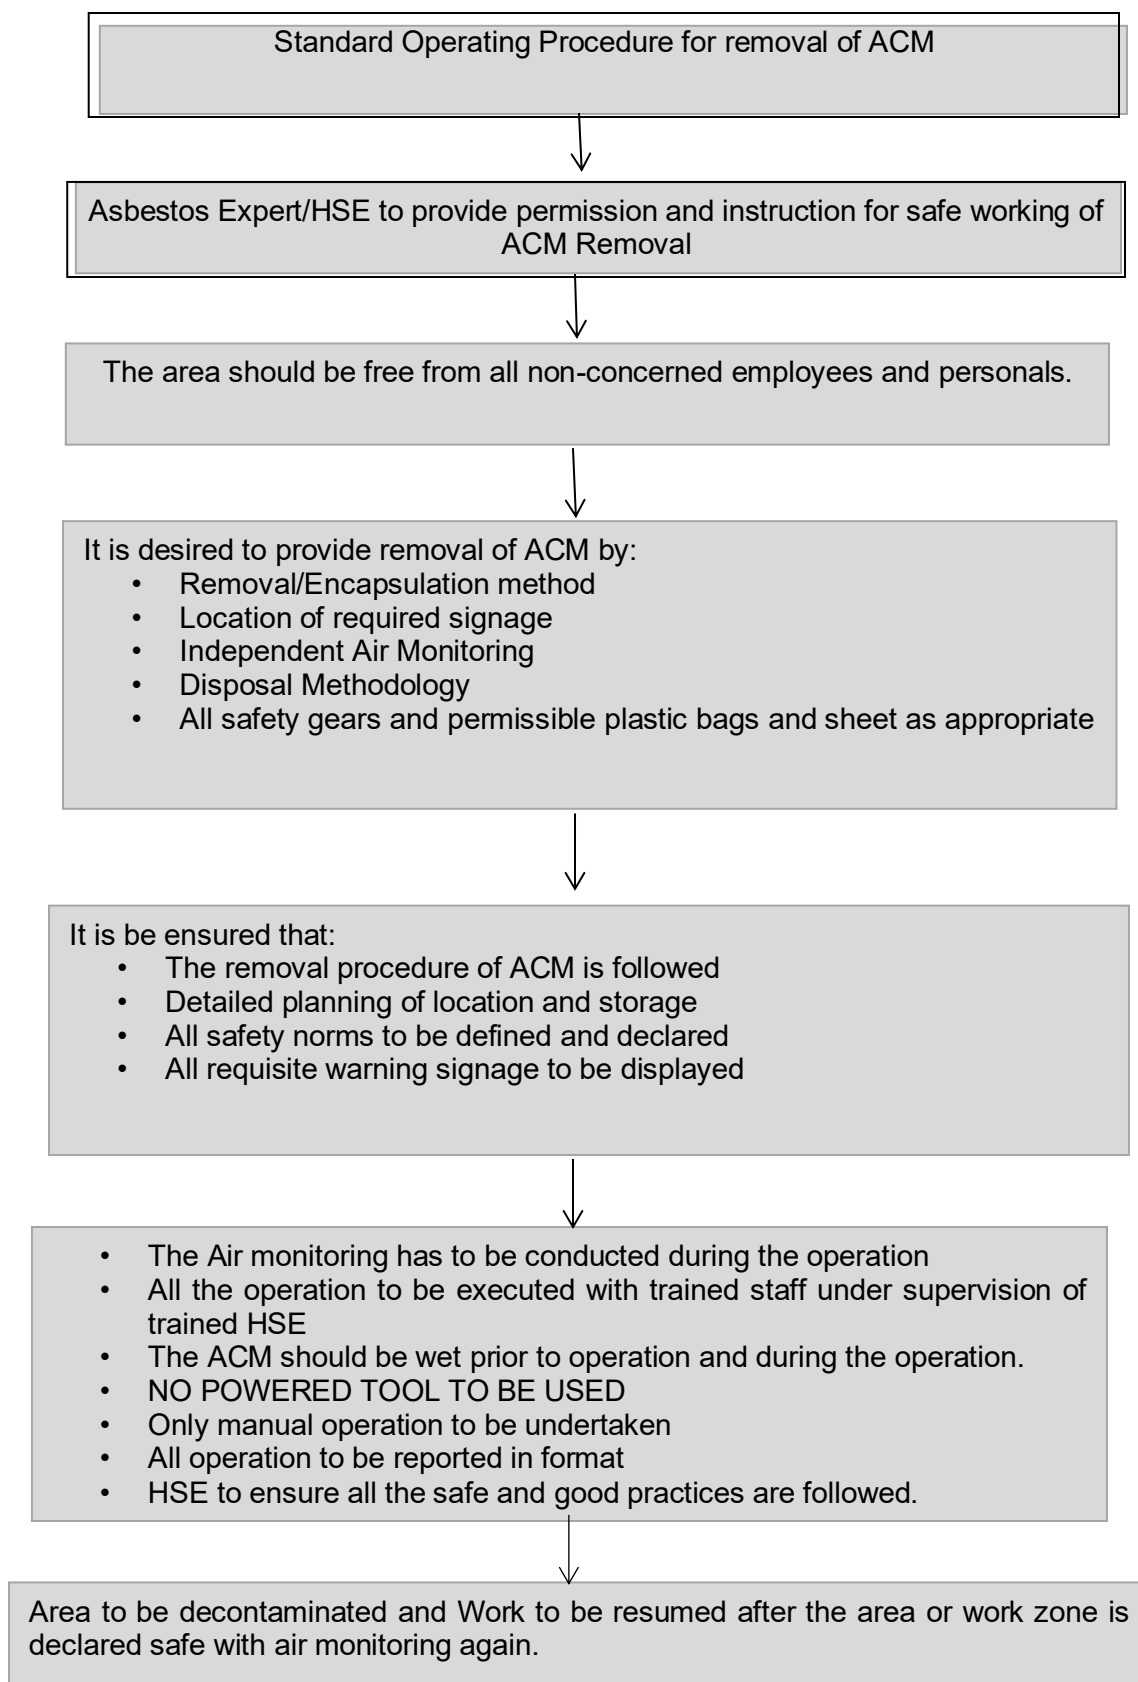


Fig. 6 -Standard Operating Procedure Flow Sheet

19. All the records in the pre-determined format are to be maintained and the disposal as stated in the applicable National legislation is to be followed. Any innovative use of the discarded ACM with the permissible law frame must be approved by respective Regulators prior to practice.

20. The format of Inventorization & records at all locations must be maintained irrespective of generation of ACM waste. The format of documentation must be uniform in order to track and trace the details as desired.

21. Based on the outcome of the workshop it was essential to enumerate the standard operating procedure & define the roles and responsibilities (already discussed as above) and the re-handling cost of the ACM as stated below:

Table 4- Suggestive Protective measures & Estimation of the cost of Re-Handling of ACM

1	Re-Handling			
	Re-handling of AC Pipes scattered/used in the premises.	- Re-Handling of the old AC Pipes in the premises needs to be quantified and a proper inventorization has to be prepared. - The isolated enveloped storage sites should be away from the habitation, the pipes used for fencing, tree guard needs to be re-handled & stored in the nearest isolated storage site and the damaged pipes/broken pipes have to be disposed off to the TSDF with all pre-cautionary measures. NOTE: Only powered/grounded ACM will have to be disposed off to TSDF.	Manpower engaged: Trained labor, Supervisor, HSE Experts/Asbestos Expert	The re-handling cost will be part of the laying program. The disposal cost is Rs.1500/MT plus freight as per actual
	Removal of encountered AC Pipes	The damaged / broken AC Pipes have to be cautiously handled with prior moistening and packed in plastic bags (permissible plastic bags) and sent for re-use in road making or to TSDF with all signage and precautionary measures as suggested above.	Manpower engaged: Trained labor, Supervisor, HSE Experts/Asbestos Expert	As stated above
	Storage	The existing storage stacks have to be shielded with 8.0 ft height and above ground (min1.0 ft) The Pipes shall be stored in stacks with stoppers provided at the bottom layer to keep the pipe stack stable. The stack, particularly of smaller diameter pipes, shall be in pyramid shape. Pipes shall not be stacked more than 1.5 m high. Each stack shall have pipes of the same type and size only. Removal of pipes shall start from the top layer and by pulling from one end, if required, with all safety precautions. A pipe shall not be stored inside another pipe. The pipes	Manpower engaged: Trained labor, Supervisor, HSE Experts/Asbestos Expert	As on daily wages

		may also be placed alternately length and crosswise. They shall be stored on horizontal racks supported throughout their lengths on a reasonably flat surface free from stones and sharp projections. They should not be stacked in large piles, especially under warm conditions. Open ends of pipes to be sealed with permissible polythene.		
	Transportation	• Full length pipes • Damaged/Broken Pipes	Authorised agency	As per actual.
Disposal				
	Isolated storage	The storage area should be twice the area required for storage of ACM	Manpower engaged: Trained labor, Supervisor, HSE Experts/Asbestos Expert. Authorised vendor. Boundary, signage, safety aspects etc	As stated in Table 1.1.
	Sent to TSDF	The damaged/broken pipes will be packed in permissible Poly bags and has to be stored in defined location within the isolated storage. The records pertaining to the disposal (within 90 days of generation) have to be made systematic. Possibilities of using the broken pipes in wet conditions in road making in order to bind the asbestos fibers can be explored.	Authorised agency	Freight as per actual.
Estimation of suggestive protective and preventive measures				
	Air Quality sampling & Analysis- Asbestos fiber count	Personal sampler, phase contrast microscope, In case of asbestos dust, the same shall not exceed 2 mg/Nm ³ . Per the OSHA standards for asbestos, exposure monitoring and medical surveillance of workers is required when the Workers are or will be exposed to airborne concentrations of fibers of asbestos at or above OSHA's exposure limits for a combined total of 30 or more days per year; Workers perform work that disturbs asbestos-containing material (ACM) or presumed asbestos-containing material (PACM) for a combined total of 30 or more days per year. Minimum 3 locations (@120deg from each location) at min 500 m from the isolated storage of ACM and one sampling near the encountered site. The frequency of monitoring should be bi-annually.	Approved/accredited laboratory	As stated above.

	PPE's	Hard helmet, double strapped mask, safety tapes, boots(non laced), gloves, safety suits, goggles, ear plugs,	Standard make, minimum-4 sets at each site	As stated Above
	Education & Training	Awareness, New induction training and inspections	Asbestos expert/HSE Experts	As stated Above
	Medical Check up	As per norms or in consultation with Medical Practitioner.	Medical Doctor	As stated Above

Note:

Efforts should be made to minimize the existing AC water pipes. In areas where ACM are stored, it is required to have induction training of AMP, complete the formats and maintain the records.

Removals of used AC Pipes for fencing, boundary wall etc have to be carefully removed from use and stored in isolated storage.

At certain locations, it was observed that the discarded pipes was used as tree guard, when the sapling was planted as on date the tree is fully grown, in that case the removal of ACM has to be done with all precautions and use of total safety gears. Hand tools or slow-running tools producing coarse dust or chips should be used where practicable rather than high-speed machines or those which cut by abrading the material after wetting. Alternatively, the same can also be bounded properly by bitumen paint.

The coarse dust and pieces in wet conditions will have to be collected in permissible plastic bags with use of all safety gears.

The collected wastes are to be labeled as stated above and disposed off to TSDF. The records of the same will have to be kept on daily basis and summarized to monthly basis.

FORM I – ASBESTOS INVENTORY, INSPECTION AND ACTION FORM

Format: RUIDP/IIA/ LOCATION/NAME OF DBO CONTRACTOR/HSE 002/YEAR		
Location:		
Site co-ordinates:		
Elevation:	Team:	
Date of visit	Sign:	
Present Status		Indicate if installed, operational, in storage, etc.
Original age		Months or years since installation
Diameter		mm or inches
Length		meters
Volume		
Total packet		
Packing date		
Disposal date		
Existing Site (Photo or illustrations):		
Illustration/ Design of Activities On-site with respect to existing asbestos (include details such as size of new pipes, distance from existing AC pipes, other notable observations)		
DBO Contractor Handling Asbestos:		
Number of persons handling waste		
Medical Records		

Safety Gears	
Vocational Training Last Conducted:	
Number of attendees:	
Conducted by Schedule:	
Required Actions:	
Remarks	
Conclusion/Remark	
HSE Signatory	

FORM-II – MATRIX FOR TRAINING & RECORDS

Format: RUIDP/INSP.MATRIX/LOCATION/NAME OF DBO CONTRACTOR/HSE 001/YEAR			
S. No.	Aspects of ACM	Check points	Remarks
Training Schedule:			
Trainer Details:			
Date/Location of Training:			
Number of attendees:			
Training Schedule, Training Materials & Attendance Sheet, Feedback of Trainees.			
Understanding of:			
A. DOCUMENTS AND RECORDS			
1.	Site Inventory		
2.	List of ACM storage and installation points		
3.	Structure of ACM management committee		
B. INVENTORY			
1.	Inventorization of ACM		
	Number of ACM/ pipes		
	Dimensions of ACM/ pipes		
	Total volume of ACM/ pipes		
2.	Storage facility/ installation location:		
A.	In-use	Location	
		Condition	Intact/ damaged
		Purpose	
		Accessibility by the workers	
		Evidence of physical damage and approximate size (length, width, volume) without coming into contact with The damaged ACM	
		Impacts on the environment (Based on Asbestos fiber Monitoring)	
3.	LABELING AND SIGNAGE		
	Notification to workplace safety and health		
	Working instruction		
	The risks associated with exposure to asbestos fibers		
	Cautionary statement to not disturb materials containing asbestos		
4.	PERSONAL PROTECTIVE EQUIPMENT (PEP)		
	Record of pep		
	Mask		

	Eye glasses	
	Gloves	
	Ear muffs	
	Others	
	Training	
	On occupational risks of asbestos to the workers	Date: Time: In-house/ external: Faculty: No of workers attended:
	Training for maintenance, repair and renovation	Date: Time: In-house/ external: Faculty: No of workers attended:
	Training for workers working with asbestos	Date: Time: In-house/ external: Faculty: No of workers attended:
Periodic air quality monitoring records	• Within the permissible limits • Not within the permissible limits (specify the reason)	
Workers medical check-up records	Date: In-house/ external: Performed by: Remarks: No of workers attended:	
Conclusion/Remark HSE Signatory		

The all the data required in Form-II will be filled by the DBO Operator (HSE-Officer), the records of this document has to be maintained for a pre-decided life. Details of training imparted have to be file with appropriate evidence like photographs, feedback form, videos etc. There has to be a proper documentation of the records kept with highest level of transparencies to retrieve, trace and track the records as necessary. The records maintained by the DBO Operator, has to be audited regularly by the ACM-Expert.

Form-I has to be accompanied with Form-II. Defined period of Air Quality monitoring and health will have to be minimum twice a year. Where ever the fiber counts are found/ recorded beyond the permissible norms, corrective action, like:

- Cordon off the area of ACM
- HSE team with trained experts to be deputed for the task
- Moisten the ACM prior to handling
- Storage area of the ACM stacks to be covered
- The damaged/deteriorated ACM to be re-handled in presence of Asbestos Expert/ HSE (Trained) with all defined norms and safety gears.
- Disposal of damaged/deteriorated ACM to be done as per the Norms.
- Records of disposal to be maintained.
- Keep all requisite evidence in form of documentation, geo-tagged photographs etc
- Frequency of health monitoring at such locations to be increased.

Form-III-AIR QUALITY MONITORING AND RESULTS

Format: RUIDP/AQMR/ LOCATION/NAME OF DBO CONTRACTOR/HSE 003/YEAR				
Vendor details				
Approvals				
S.No	Location	Agency	Results& Norms	Permissible
Conclusion/Remark				
HSE Signatory				

FORM-IV-MEDICAL HISTORY

Format: RUIDP/MH/ LOCATION/NAME OF DBO CONTRACTOR/HSE 004/YEAR							
Employee code:							
Employer Details:							
PPE Used:							
Insurance/ESI							
S. No	Name	Age/Sex/D BO	Address/ Contact details:	Period of Employment/ Job Title	Pre-History	Doctor's comments	HSE Remarks
					Height		
					Weight/B MI		
					Blood group		
					X-Ray		
					CT Scan		
					others		
					Smoker: Tobacco: Alcohol Consumption: Family History: Medication if any: Eye sight: Hearing: Others:		

FORM -V

[FORM-10- as per rule 19 (1) of Hazardous waste Handling & Management Rules-2016]
MANIFEST FOR HAZARDOUS AND OTHER WASTE

1.	Sender's name and mailing address (including Phone No. and e-mail)					
2.	Sender's authorisation No.		•			
3.	Manifest Document No.		•			
4.	Transporter's name and address: (including Phone No. and e-mail)					
5.	Type of vehicle		•			(Truck/Tanker/Special Vehicle)
6.	Transporter's registration No.		•			
7.	Vehicle registration No.		•			
8.	Receiver's name and mailing address (including Phone No. and e-mail)					
9.	Receiver's	Authorisation No.				
10.	Waste description		•			
11.	Total quantity No. of Containers		•			m ³ or MT Nos.
12.	Physical form				(Solid/Semi-Solid/Sludge/Oily/Tarry/Slurry/Liquid)	
13.	Special handling instructions and additional information					
14.	Sender's Certificate				I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised, packed, marked, and labeled, and are in all respects in proper conditions for transport by road according to applicable National Government regulations.	
	Name and stamp:	Signature:			Month	Day
						Year
15.	Transporter acknowledgement of receipt of Wastes					
	Name and	Signature:			Mont	Day
						Year

	stamp:			h										
1			Receiver's certification for receipt of hazardous and other waste											
6.	Name stamp:	and Signature:		Mont h	Day			Year						

FORM –VI: IN-SITU STORAGE OF ACM

S. No	Activity	Number of Stacks	Area occupied	Details of ACM Pipes		Day/month/year Of storage
Site History						
For existing Stacks, details of re-handling of pipes in number or volume to be mentioned under supervision of Authorized Experts.						
Details of Location of re-handled ACM storage, new area should be • Minimum 10-15 ft away from campus habitation. • 250m away from the water sources • 500-800m away from Children play area • The area should be isolated and covered from all the sides with restricted Access for Authorised Experts Only. • Register to be maintained for Entry& Exit of personals. • Register to be maintained for Entry & Exit of ACM • Labels to be displayed in legible format • Specific training of ACM to be inducted in the ACM storage area for residing population in the campus.						
Details of transit storage of ACM to be maintained as per norms in an isolated storage room full covered						

Standard Operating Procedure-02

Asbestos Fiber Monitoring, Analysis and Identification

Principle

1. The collection of environmental samples including air must follow an appropriate sampling procedure. A review of method for sampling of asbestos fibers has been published (IPCS, 1986). The most commonly used analytical method involves phase contrast optical microscopy (PCOM) in the work place and transmission electron microscopy (TEM) in the general environment. The phase contrast optical microscopy (POCM) is universally recommended for asbestos analysis (Eache and Groff, 1997; Dion and Perrault, 1994) including Bureau of Indian Standard. POCM coupled with polarized light is largely used for asbestos analysis in solid samples (USEPA, 1993). The fiber monitoring has to be done by any NABL/MOEF&CC accredited laboratory either in-house or by third party.

Monitoring of Asbestos Fiber in Air

2. A general survey of inside and outside the storage sites of the work zone has to be conducted to choose the sampling sites. Sampling is to be carried out at visually selected locations appeared more prone to emission or possibility of release of asbestos fiber. The sample

collected by drawing a measured quantity of air through cellulose ester a membrane filter by a battery operated sampling pump that was fully charged to operate continuously over the chosen sampling time. The exposed filters will then be placed into plastic petri dishes and transferred carefully to the laboratory.

3. Two types of samples are to be taken, one within the workers breathing zone that is 300 mm radius extending in front of the face, and measured from the midpoint of a line bisecting the ears called personal samples. The samples taken at a fixed location mostly near to the source point called area or static samples. Personal sampler model "XX 5700000" and low volume vacuum/pressure pump model "XX5622050" attached with monitor or cowl model "MAWP025AC" of Millipore Corporation, USA are to be used for the collection of personal and area samples, respectively. The flow rate of pump is to be adjusted to 1litre per minute. The flow rate checked before and after in each monitoring, those samples showing the difference by >10 percent from the initial flow rate are to be rejected. In both the samples filter holder (Cowl) always pointed downward position to avoid the deposition of heavy particles. An ester cellulose membrane filters "AAWP02500" having 0.8 µm-1.2 µm pore size diameter are to be used throughout the sampling for asbestos counts at work environment.

Mounting Procedure

4. Complete filter is to be placed on clean microscopic slide, dust side up at room temperature. Electrostatic force keeps the filter usually on the slide. Filters are to be exposed to acetone fumes and triacetin (Glycerol triacetate, Sigma). In this procedure a small quantity of acetone in round bottom flask (500-1000ml) heated at the boiling point underwater bath, the vapors condensed in a simple condensing column. When the sufficient fumes of acetone become ready then pass it throughout on the filter for 3-5 seconds at a distance of 15-25 mm. put the 1-3 drops of Glycerol Triacetate (Triacetin) on the acetone-cleared filter. Place a cover slip on cleared filter by avoiding the air bubbles. Heat the cleared filter at 50°C for 15 minutes and leave it at room temperature for 24 hours under the action of triacetin to clear entire filter. Alternatively, membrane filter can also be made transparent with immersion oil (Leica Microsystems Wetzlar GmbH, Wetzlar). Using a phase contrast microscope with polarized light, Laborlux S (of M/s Leica, Germany) and then counting has to be done at magnification 400X-500x

$$C = A/a \times N/n \times 1/r \times 1/t$$

Where:

C= concentration in fibers per cubic centimeter rounded to first place of decimal,

N = total no. of fiber counted,

n = number of graticule areas observed,

A= effective filter area in mm²

a= graticule counting area in mm²,

r= flow rate of air through filter in cm³/min., and

t= single sample duration in minutes

5. To rule out the probability of the air borne asbestos in the existing scenario at the said site as well as other similar sites at the different work zones, it is necessary to have the asbestos fiber monitoring and sampling counts to be recorded at regular intervals. The environmental air sampling stations will have to be minimum three at 120 degree angle, within 1000-500 m from the ACM. The sampling frequency has to be in all three stages-Pre-Construction, Construction and Post Construction, while the personal sampling has to be done as stated above.

6. Bureau of Indian Standards (BIS) Guidelines for Safe Use of Products containing Asbestos states that "Asbestos cement products (such as AC pipes) generally contain about 10-

15% asbestos fibers in a cement matrix that comprises the rest of the materials and are termed as locked in asbestos products as these products have the asbestos fibers bound in cement. The possibilities of air borne asbestos fiber will be in case of mishandling of encountered pipes with unsafe practice. During storing and installation; recommended work practices shall be followed to avoid harmful exposure". According to Hazardous and Other Wastes (Management and Trans-boundary Movement) Rules, 2016, any waste with asbestos concentration limit of 10,000 mg/kg (i.e. 1%), however this will apply only if the asbestos containing substances are in a friable, powdered or finely divided state. Under the Basel Convention¹, asbestos or asbestos waste in the form of dust and fibers is classified as hazardous waste. The applicable legislation under the present scenario are:

¹ Basel Convention on the Control of Trans-boundary Movements of Hazardous Wastes and their Disposal, adopted in 1989

Summary of Asbestos Management Plan

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Remark
Clearing, transfer and disposal of ACM pipes	Possibilities of air borne asbestos if handled unsafely, cut, drilled or broken into pieces that may cause: ☐ Inflammation of the lungs ☐ Mesothelioma ☐ Peritoneal mesothelioma ☐ Pleural plaques ☐ Asbestosis ☐ Bronchogenic Carcinoma ☐ Second hand-exposure	Implement the AMP strictly that includes identification of hazards, the use of proper safety gear and disposal methods.	DBO Contractor /RUIDP	There has to be a suitable call to be taken for in-situ disposal if the removed ACM pipes are not damaged, full length or 4.0 ft length not damaged.
Work in narrow streets	Possibilities of air borne asbestos if handled unsafely cut, drilled or broken into pieces that may cause: ☐ Inflammation of the lungs ☐ Mesothelioma ☐ Peritoneal mesothelioma ☐ Pleural plaques ☐ Asbestosis ☐ Bronchogenic Carcinoma Second hand-exposure	Conduct awareness program on safety during the construction work Undertake the construction work stretch-wise; excavation, pipe laying and trench refilling should be completed on the same day Provide barricades, and deploy security personnel to ensure safe movement of people and also to prevent unnecessary entry and to avoid accidental fall into open trenches Identify risk of intervention with existing AC pipes. If there is significant risk, implement the AMP strictly that includes identification of hazards, the use of proper safety gear and disposal methods.	DBO Contractor/RUIDP	All provision of safe working with proper signage has to be undertaken prior to work initiation, during the work and after the work.
Interventions in existing AC pipelines	Possibilities of air borne asbestos if handled unsafely cut, drilled or broken into pieces that may cause: ☐ Inflammation of the lungs ☐ Mesothelioma	Appropriate actions as defined in the Asbestos Management Plan will have to be adhered to	DBO Contractor/RUIDP	Measure to avoid the encounter & removal has to be prioritized and if the same is not avoided then the

Field	Anticipated Impact	Mitigation Measures	Responsible for Implementation/ Monitoring	Remark
	☐ Peritoneial mesothelioma ☐ Pleural plaques ☐ Asbestosis ☐ Bronchogenic Carcinoma Second hand-exposure			measures stated have to be strictly followed.
Documentation /record	Unmonitored ACM might be handled incorrectly and can cause release of airborne asbestos	To be formatted and kept as mentioned in the Asbestos Management Plan	DBO Contractor/RUIDP	To be kept intact for easy tracking and reference in legible format. The same can be kept in soft format as well.

Appendix C-21: Guidelines for Workers Camps

(Based on IFC benchmark standards for workers accommodation)

Guidelines for Workers' Accommodation

1. Availability of sufficient number of clean rooms for the workers with adequate facilities of ventilation, Drinking water, Electricity/fan/light (natural and artificial lighting) etc. in each room.
2. Camps should not be subjected to periodic flooding nor located within 200 feet of swamps, pools, sink holes or other surface collections of water. All sites should be graded, ditches and rendered free from depressions in which water may become a nuisance.
3. Accessibility to an adequate and convenient supply of potable water to the workers. Depending upon the climate, weather conditions and accommodation standards, 80 to 180 litres per persons per day water should be available and drinking water should meet the national/WHO drinking water standards.
4. Camp site should be adequately drained to avoid the accumulation of stagnant water.
5. All tanks used for the storage of drinking water should be constructed and covered as to prevent water stored therein from becoming polluted or contaminated.
6. All sites should be adequate in size to prevent overcrowding of necessary structures.
7. Camps should have Crèche facility for children with necessary arrangements.
8. The grounds and open areas surrounding the shelters should be maintained in a clean and sanitary condition free from rubbish, debris, waste papers, garbage or other refuse.
9. Beds, cots, or bunks, and suitable storage facilities such as wall lockers for clothing and personal articles should be provided in every room used for sleeping purposes.
10. A separate bed for each worker should be provided. Double deck bunks are not advisable for the safety and hygiene reasons and their use should be minimized. If they are used there must be enough clear space between the lower and upper bunk of the bed. Standard range is 0.7 to 1.10 meters. Triple deck bunks are prohibited.
11. All heating, cooking, and water heating equipment should be installed in accordance with State and local ordinances, codes, and regulations governing such installations. If a camp is used during cold weather, adequate heating equipment should be provided.
12. If food is provided, it should cater for different cultural needs. Kitchens should be provided with facilities to maintain adequate personal hygiene including a sufficient number of washbasins designated for cleaning hands with clean running water and materials for hygiene drying.
13. All kitchen floors, ceiling and wall surface adjacent to or above food preparation and cooking areas should be built using durable, non-absorbent, easily cleanable, non-toxic materials.
14. No person with any communicable disease shall be employed or permitted to work in the preparation, cooking, serving, or other handling of food, foodstuffs, or materials used therein, in any kitchen or dining room operated in connection with a camp or regularly used by persons living in a camp.
15. There should be recreation facilities for the camp workers i.e. TV/sports/newspaper/magazine etc.
16. There should be facility of mosquitoes prevention and control i.e. use of mosquito net/coil/electric repellent/pesticide etc.
17. Sanitary and toilet facilities should be constructed of the materials that are easily cleanable. Standard range of the toilets varies from 1 unit for 6 persons to 15 persons. For urinals, standards are 1 unit for 15 persons.
18. There is no need to provide separate urinals in any place where less than 50 workers are employed or where the latrines are connected to water borne sewage system.
19. Sanitary and toilet facilities should be designed to provide workers with adequate privacy including ceiling to floor partitions and lockable doors.

20. Separate toilet and bathing facilities should be available for Men and women. These facilities shall be distinctly marked "for men" and "for women" by signs printed in English and in the native language of the persons using the facilities, and/or marked with easily understood pictures or symbols.
21. Workers' gender, religious, cultural and social backgrounds should be respected. In particular, workers should be provided with the possibility of celebrating religious holidays and observances.
22. No pets, birds or livestock should be kept or fed unless approved by management or camp operator.
23. There should be proper arrangement of colour coded dustbins i.e. Green for wet/biodegradable wastes, blue for dry/non-biodegradable waste and red for safe disposal of domestic hazardous waste i.e. sanitary napkins and diapers.
24. There should be adequate facility for waste water management (i.e. septic tanks/soak pits) and for disposal of Municipal solid waste (i.e. composting).
25. The person in charge of managing the accommodations has a specific duty to report to the health authorities the outbreak of any contagious diseases, food poisoning and any other important casualties.
26. Guidance on the detrimental effects of the abuse of alcohol and drugs and other potentially harmful substances and the risk, concerns related to HIV/AIDS and other health risk related activities should be provided to the workers through group/individual orientations and should also be displayed at camps as visual boards.
27. Workers should have easy access to medical facilities and medical staff where possible female doctors/nurses should be available for female workers. Regular health check up should be done for the workers. First-AID Kit/Health care facilities should be available in the camps. There should be proper demarcation/display of First Aid facility and First Aider.
28. A specific fire safety plan should be prepared including training of fire wardens, periodic testing and monitoring of fire safety equipments.
29. All key contacts, emergency contact number, including nearby hospital should be posted in a prominent place and in all languages present e.g., at camp gate and throughout the camp.

Appendix C-22: Guidelines for Safety in Chlorine Usage

Instructions for Storage and Handling of Chlorine Cylinders

(Based on the 'Manual on Operation and Maintenance of Water Supply Systems' published by the Central Public Health and Environmental Engineering Organization (CPHEEO) in 2005)

1.1 Storage Area

- Obtain storage license from controller of explosives under Gas Cylinder Rules 2004 if the quantity of Cl₂ containers to be stored is more than 5 Nos.
- Storage area should be cool, dry, well ventilated, and clean of trash and protected from external heat sources. Please refer to Manual on "Water Supply and Treatment", (1999 Edition), for further details.
- Ventilation must be sufficient to prevent accumulation of vapour pockets. The exhaust should be located either near the floor or duct be provided extending to the floor. All fan switches should be outside the storage area.
- Do not store container directly under the sun.
- Weather cock should be installed near the storage to determine wind direction.
- The storage building should be of non-combustible construction with at least two exits opening outside.
- Neutralization system should be provided.
- Continuous monitoring of chlorine leak detection equipment with alarm should be installed in the storage area.
- The area should be free and remote from elevators, gangways or ventilating system to avoid dangerous concentration of Chlorine during leak.
- Two portable foam type fire extinguishers should be provided in the premises.
- Corrosive substances shall not be stored nearby which react violently with each other.
- Unauthorized person should not be allowed to enter into the storage area.
- The floor level of storage shed should be preferably 30 cms (at least one foot) higher from the ground level to avoid water logging.
- Ensure that all containers are properly fitted with safety caps or hooks.

1.2. Cylinder & Drum Containers

- Store chlorine cylinders upright and secure them so that they do not fall.
- Drum containers should be stored on their sides on rails, a few inches above the floor. They should not be stacked one upon the other. They should be stored such that the valves are in vertical plane.
- Keep enough space between containers so as to have accessibility in case of emergency.
- Store the containers in a covered shed only. Keep them away from any source of heat as excessive heat may increase the pressure in container which will result into burst.
- Do not store explosives, acids, turpentine, ether, anhydrous ammonia, finely divided metals or other flammable material in the vicinity of Chlorine.
- Do not store containers in wet and muddy areas.
- Store filled and empty containers separately.
- Protective covers for valves are secured even when the containers are empty, except during use in the system.
- Never use containers as a roller to move other equipment.
- Never tamper with fusible plugs of tonners.
- Check leakages every day by means of ammonia torch. However, it should not be touched to brass components like valves of container for safety.
- Never carry out any welding work on the chlorine system as combustion of steel takes place at 2510C in presence of chlorine.

- The boxes containing emergency kit, safety applications and self contained breathing apparatus should be kept in working order in an easily approachable area.

1.3. Use of Cylinders & Drum Containers in Process System

- Use containers in the order of their receipt, as valve packing can get hardened during prolonged storage and cause gas leaks.
- Do not use oil or lubricant on any valve of the containers.
- Badly fitting connections should not be forced and correct tool should always be used for opening and closing valves. They should never be hammered.
- The area should be well ventilated with frequent air changes.
- Transport the cylinders to the process area by using crane, hoist or railings etc.
- The drum containers should be kept in a horizontal position in such a way that the valves are in a vertical plane. The upper valve gives out gas and the lower one gives out liquid chlorine.
- The cylinder should be kept in upright position in order to release gas from the valve. For liquid chlorine withdrawal, it should be inverted with the help of an inverted rack.
- Connect the containers to the system by using approved accessories.
- Use copper flexible tube, with lead washer containing 2 to 4% antimony or bonded asbestos or teflon washer. Use yoke clamp for connecting chlorine container.
- Never use rubber tubes, PVC tubes etc. for making connections.
- Use the right spanner for operating the valve. Always keep the spanner on the valve spindle. Never use ill fitting spanner.
- After making the flexible connection, check for the leakage by means of ammonia torch but it should not come in contact with a valve.
- Keep minimum distance between the container valve and header valve so that during change-over of the container, minimum amount of gas leaks.
- The material of construction of the adapter should be same as that of valve outlet threads. o. The valve should not be used as a regulator for controlling the chlorine. During regulation due to high velocity of Chlorine, the valve gets damaged which in turn can cause difficulty in closing.
- The tools and other equipment used for operating the container should be clean and free of grease, dust or grit.
- Wear breathing apparatus while making the change-over of the container from the process header.
- Do not heat the container to withdraw more gas at faster rate.
- Use pressure gauge and flow measuring device to control the flow and to know the quantity of gas left in the container.
- Use an inverted U type barometric leg or vacuum breaking arrangement for connecting the container to the process piping.
- Withdrawal of the gas should be stopped when the gas pressure inside the container is between 0.1 to 0.5 kg/cm² approximately.
- If withdrawal of the gas from the container connected to the process system has to be suspended for long intervals, it should be disconnected from the system, and the valve cap and hood replaced.
- Gas containers should be handled by trained persons only.

1.4. Disconnecting Containers from Process System

- Use breathing apparatus before disconnecting the container.
- First close the container valve fully. After removal of chlorine the process valve should be closed.
- Remove the flexible connection, plug the flexible connection in order to avoid entry of humid air. Replace the valve cap or hood on the container.

- Put the tag on the empty container & bring it to storage area marked for empties. e. Check for the leakage.

1.5. Loading and Unloading of Containers

- The handling of containers should be done under the supervision of trained and competent person.
- It should be done carefully with a crane, hoist or slanted ramp. Do not use magnet or sharp object for lifting the containers.
- Small cylinders should not be lifted by means of valve caps as these are not designed to carry the weight.
- The containers should not be allowed to strike against each other or against any hard object.
- Vehicles should be braked and isolated against any movement.
- After loading, the containers should be secured properly with the help of wooden wedges, rope or sling wire so that they do not roll away.
- The containers should never be dropped directly to the ground or on the tyre from the vehicle.
- There should be no sharp projection in the vehicle.
- Containers must have valve caps and plugs fitted properly.
- Check containers for leakage before loading/unloading.

1.6. Transportation of Container

- The name of the chemical along with diamond pictorial sign denoting the dangerous goods should be marked on the vehicle.
- The name of the transporter, his address and telephone number should be clearly written on the vehicle.
- The vehicle should not be used to transport any material other than what is written on it. d. Only trained drivers and cleaners should transport hazardous chemical
- The driver should not transport any leaking cylinder.
- The cylinder should not project outside the vehicle.
- The transporter must ensure that every vehicle driver must carry "Trem Card" (Transport Emergency Card) and 'Instructions in writing booklet' and follow them.
- Every driver must carry safety appliances with him, viz; Emergency kit, breathing apparatus etc.
- The vehicles must be driven carefully, especially in crowded localities and on bumpy roads. Do not apply sudden brakes.
- Check for the leakage from time to time.
- In the case of uncontrollable leakage, the vehicle should be taken to an open area where there is less population.

1.7. Emergency Kit: It consists of various tools and appliances like gaskets, yokes, studs, tie rods hoods, clamps, spanners, mild steel channels, screws, pins, wooden pegs etc. of standard sizes. Separate kits are used for cylinders and tonners. All the gadgets are designed for using in controlling or stopping the leakages from valves, fusible plug and side walls of cylinders and containers used for handling chlorine.

- Leakage may occur through the valve. There are basically four types of valve leaks.
 - Valve packing
 - Valve seat
 - Defective inlet thread
 - Broken valve thread

- Leakage may occur through container wall. For controlling such leakages, clamps are used for cylinders and chain and yoke arrangement is used for tonner. Sometimes wooden peg is used by driving into the leaking hole as a temporary arrangement.
- Leakage may occur through fusible plug.
 - If the leakage is through the threads of fusible plug, yoke, hood and cap nut arrangement is used to control the leak.
 - If fusible metal itself in the plug is leaking, yoke and stud arrangement is used to control the leak.

2. First Aid to be Provided for a Person Affected by Chlorine

a. General Remove the affected person immediately to an uncontaminated area. Remove contaminated clothing and wash contaminated parts of the body with soap and plenty of water. Lay down the affected person in cardiac position and keep him warm. Call a physician for medical assistance at the earliest. Caution: Never attempt to neutralize chlorine with other chemicals.

b. Skin Contact Remove the contaminated clothes, wash the affected skin with large quantity of water. Caution: No ointment should be applied unless prescribed by the physician.

c. Eye Contact If eyes get affected with liquid chlorine or high concentration of chlorine gas, they must be flushed immediately with running water for atleast 15 minutes keeping the eyelids open by hand. Caution: No ointment should be used unless prescribed by an eye specialist.

d. Inhalation If the victim is conscious, take him to a quiet place and lay him down on his back, with head and back elevated (cardiac position). Loosen his clothes and keep him warm using blankets. Give him tea, coffee, milk, peppermint etc. for making good effect on breathing system. If the victim is unconscious, but breathing, lay him down in the position mentioned above and give oxygen at low pressure until the arrival of doctor. If breathing has stopped, quickly stretch him out on the ground or a blanket if available, loosen his collar and belt and start artificial respiration without delay. Neilson arm lift back pressure method is useful. Automatic artificial respiration is preferable if available. Continue the respiration until the arrival of the doctor. Amboo bag can also be used for this purpose.

3. On-Site Emergency Plan to Cover the Leakage of Chlorine

3.1. Introduction As chlorine is a hazardous chemical, handling and storage of it demand adequate precautions to avoid possible hazards. Leakage of chlorine may develop into a major emergency. Therefore, the emergency procedure to cover this eventuality is essential. It is drawn in the form of on-site emergency plan. The elements of onsite emergency plan are as follows:

3.2. Identification of Hazard Chart

In this case the site risk is evaluated by the expert and the extent of the probable damage is calculated on the basis of stored chlorine quantity, nearby population, wind direction, type of equipment failure etc. For this purpose, hazard analysis is conducted in which case all the hazardous properties of chlorine are considered. If evacuation is required, the range of it is calculated.

3.3. Appointing Key Persons In order to control the incident like chlorine leakage, it is essential to appoint various persons with their well-defined responsibilities. Taking into account the various activities likely to be involved, the following key persons are

appointed (i) Site Controller, (ii) Incident controller, (iii) Shift Executive In charge, (iv) Communication Officer, (v) Safety Officer, (vi) Fire and Security Officer, (vii) Utilities and Services In charge, (viii) Traffic Controller, (ix) First Aider

3.4. Assembly Points These points are set up where persons from the plant would assemble in case of chlorine leakage. At these points the in-charge for counting the heads will be available.

3.5. Emergency Control Centre

The control centre is the focal point in case of an emergency from where the operations to handle the emergency from are directed and coordinated. It contains site plan, telephone lines, public address system, safety equipment, first aid boxes, loud speaker, torches, list of essential telephone numbers, viz. fire brigade, police, hospital, civil defence, collector, factory inspector, organizational authorities, chlorine suppliers, mutual aid group, social workers, list of key persons and their addresses, copy of chemical fact sheet, location plan of fire hydrant, details of dispersion model of chlorine gas, population distribution pattern, location of alarm system.

3.6. Procedure to Meet Emergency

The actions to be taken by the staff and authority are given below; Emergency Alarm: An audible emergency alarm system is installed throughout the plant. On hearing the alarm the incident controller will activate the public address system to communicate with the staff about the emergency and give specific instructions for evacuations etc. anyone can report the occurrence of chlorine leakage to section in-charge or incident controller through telephone or intercom or in person.

3.7. Communication

Communication officer shall establish the communication suitable to that incident.

3.8. Services

For quickness and efficient operation of emergency plan the plant is divided into convenient number of zones and clearly marked on the plan. These are emergency services viz. firefighting, first aid, rescue, alternative source of power supply, communication with local bodies etc. The incident controller will hand over the charge to the site controller of all these coordinating activities, when the site controller appears on the site. The site controller will coordinate all the activities of the key persons. On hearing the emergency alarm system all the key persons will take their charge. In case of their absence other alternatives are nominated. The person nominated for personnel and administration purposes will be responsible for informing all statutory authorities, keeping account of all persons in the plant including contract labour, casual workers and visitors. He will be responsible for giving information to press or any outside agencies. He is also responsible for organizing canteen facilities and keeping informed the families of affected persons. The person nominated as security officer should guide police, fire fighting and control the vehicle entries. The site controller or any other nominated person will announce resumption of normalcy after everything is brought under control. The onsite emergency plan needs to be evaluated by mock drill. Any weaknesses noticed during such drills should be noted and the plan is modified to eliminate the weaknesses.

3.9. Emergency

Measures In case of leakage or spillage of Chlorine, the following emergency measures should be taken:

- Take a shallow breath and keep eyes opened to a minimum.
- Evacuate the area.

- Investigate the leak with proper gas mask and other appropriate Personal protection.
- The investigator must be watched by a rescuer to rescue him in emergency.
- If liquid leak occurs, turn the containers so as to leak only gas.
- In case of major leakage, all persons including neighbours should be warned.
- As the escaping gas is carried in the direction of the wind all persons should be moved in a direction opposite to that of the wind. Nose should be covered with wet handkerchief.
- Under no circumstances should water or other liquid be directed towards leaking containers, because water makes the leak worse due to corrosive effect.
- The spillage should be controlled for evaporation by spraying chilled water having temperature below 9.4oC. With this water crystalline hydrates are formed which will temporarily avoid evaporation. Then try to neutralize the spillage by caustic soda or soda ash or hydrated lime solution carefully. If fluoroprotein foam is available, use for preventing the evaporation of liquid chlorine.
- Use emergency kit for controlling the leak.
- On controlling the leakage, use the container in the system or neutralize the contents in alkali solution such as caustic soda, soda ash or hydrated lime. Caution: Keep the supply of caustic soda or soda ash or hydrated lime available. Do not push the leaking container in the alkali tank. Connect the container to the tank by barometric leg.
- If container commences leak during transport, it should be carried on to its destination or manufacturer or to remote place where it will be less harmful. Keeping the vehicle moving will prevent accumulation of high concentrations.
- Only specially trained and equipped workers should deal with emergency arising due to major leakage.
- If major leak takes place, alert the public nearby by sounding the siren.
- Any minor leakage must be attended immediately or it will become worse.
- If the leakage is in the process system, stop the valve on the container at once.

3.10. Safety Systems Required at Chlorination Plant

The following safety systems should be kept ready at the chlorination plant:

- Breathing apparatus.
- Emergency kit.
- Leak detectors.
- Neutralisation tank.
- Siren system.
- Display of boards in local language for public cautioning, first aid and list of different authorities with phone numbers.
- Communication system.
- Tagging system for equipment's.
- First aid including tablets and cough mixtures.
- Exhaust fans.
- Testing of pressure vessels, chlorine lines etc. every year as per factory act.
- Training & mock drill.
- Safety showers.
- Eye fountain.

- Personal protective equipment.
- Protecting hoods for ton-containers.
- Fire extinguishers.
- Wind cock.

Appendix C-23: Guidelines for Prevention and Control of COVID-19 WHO Interim Guidance on Water, Sanitation, Hygiene and Waste Management for the COVID-19 virus



Water, sanitation, hygiene, and waste management for the COVID-19 virus

Interim guidance
19 March 2020

Background

This interim guidance supplements the infection prevention and control (IPC) documents by summarizing WHO guidance on water, sanitation and health care waste relevant to viruses, including coronaviruses. It is intended for water and sanitation practitioners and providers and health care providers who want to know more about water, sanitation and hygiene (WASH) risks and practices.

The provision of safe water, sanitation, and hygienic conditions is essential to protecting human health during all infectious disease outbreaks, including the COVID-19 outbreak. Ensuring good and consistently applied WASH and waste management practices in communities, homes, schools, marketplaces, and health care facilities will help prevent human-to-human transmission of the COVID-19 virus.

The most important information concerning WASH and the COVID-19 virus is summarized here:

- Frequent and proper hand hygiene is one of the most important measures that can be used to prevent infection with the COVID-19 virus. WASH practitioners should work to enable more frequent and regular hand hygiene by improving facilities and using proven behavior-change techniques.
- WHO guidance on the safe management of drinking-water and sanitation services applies to the COVID-19 outbreak. Extra measures are not needed. Disinfection will facilitate more rapid die-off of the COVID-19 virus.
- Many co-benefits will be realized by safely managing water and sanitation services and applying good hygiene practices.

Currently, there is no evidence about the survival of the COVID-19 virus in drinking-water or sewage. The morphology and chemical structure of the COVID-19 virus are similar to those of other human coronaviruses for which there are data about both survival in the environment and effective inactivation measures. This document draws upon the evidence base and WHO guidance on how to protect against viruses in sewage and drinking-water. This document will be updated as new information becomes available.

1. COVID-19 transmission

There are two main routes of transmission of the COVID-19 virus: respiratory and contact. Respiratory droplets are generated when an infected person coughs or sneezes. Any person who is in close contact with someone who has respiratory symptoms (sneezing, coughing) is at risk of being exposed to potentially infective respiratory droplets.¹ Droplets may also land on surfaces where the virus could remain viable; thus, the immediate environment of an infected individual can serve as a source of transmission (contact transmission).

Approximately 2–10% of cases of confirmed COVID-19 disease present with diarrhoea,^{2,4} and two studies detected COVID-19 viral RNA fragments in the faecal matter of COVID-19 patients.^{3,6} However, only one study has cultured the COVID-19 virus from a single stool specimen.⁷ There have been no reports of faecal–oral transmission of the COVID-19 virus.

2. Persistence of the COVID-19 virus in drinking-water, faeces and sewage and on surfaces

Although persistence in drinking-water is possible, there is no evidence from surrogate human coronaviruses that they are present in surface or groundwater sources or transmitted through contaminated drinking water. The COVID-19 virus is an enveloped virus, with a fragile outer membrane. Generally, enveloped viruses are less stable in the environment and are more susceptible to oxidants, such as chlorine. While there is no evidence to date about survival of the COVID-19 virus in water or sewage, the virus is likely to become inactivated significantly faster than non-enveloped human enteric viruses with known waterborne transmission (such as adenoviruses, norovirus, rotavirus and hepatitis A). For example, one study found that a surrogate human coronavirus survived only 2 days in dechlorinated tap water and in hospital wastewater at 20°C.⁸ Other studies concur, noting that the human coronaviruses transmissible gastroenteritis coronavirus and mouse hepatitis virus demonstrated a 99.9% die-off in from 2 days⁹ at 23°C to 2 weeks¹⁰ at 25°C. Heat, high or low pH, sunlight, and common disinfectants (such as chlorine) all facilitate die off.

It is not certain how long the virus that causes COVID-19 survives on surfaces, but it seems likely to behave like other coronaviruses. A recent review of the survival of human

coronaviruses on surfaces found large variability, ranging from 2 hours to 9 days.¹¹ The survival time depends on a number of factors, including the type of surface, temperature, relative humidity, and specific strain of the virus. The same review also found that effective inactivation could be achieved within 1 minute using common disinfectants, such as 70% ethanol or sodium hypochlorite (for details, see Cleaning practices).

3. Keeping water supplies safe

The COVID-19 virus has not been detected in drinking-water supplies, and based on current evidence, the risk to water supplies is low.¹² Laboratory studies of surrogate coronaviruses that took place in well-controlled environments indicated that the virus could remain infectious in water contaminated with faeces for days to weeks.¹⁰ A number of measures can be taken to improve water safety, starting with protecting the source water; treating water at the point of distribution, collection, or consumption; and ensuring that treated water is safely stored at home in regularly cleaned and covered containers.

Conventional, centralized water treatment methods that use filtration and disinfection should inactivate the COVID-19 virus. Other human coronaviruses have been shown to be sensitive to chlorination and disinfection with ultraviolet (UV) light.¹³ As enveloped viruses are surrounded by a lipid host cell membrane, which is not robust, the COVID-19 virus is likely to be more sensitive to chlorine and other oxidant disinfection processes than many other viruses, such as coxsackieviruses, which have a protein coat. For effective centralized disinfection, there should be a residual concentration of free chlorine of ≥ 0.5 mg/L after at least 30 minutes of contact time at pH < 8.0 .¹² A chlorine residual should be maintained throughout the distribution system.

In places where centralized water treatment and safe piped water supplies are not available, a number of household water treatment technologies are effective in removing or destroying viruses, including boiling or using high-performing ultrafiltration or nanomembrane filters, solar irradiation and, in non-turbid waters, UV irradiation and appropriately dosed free chlorine.

4. Safely managing wastewater and faecal waste

There is no evidence that the COVID-19 virus has been transmitted via sewerage systems with or without wastewater treatment. Further, there is no evidence that sewage or wastewater treatment workers contracted the severe acute respiratory syndrome (SARS), which is caused by another type of coronavirus that caused a large outbreak of acute respiratory illness in 2003. As part of an integrated public health policy, wastewater carried in sewerage systems should be treated in well-designed and well-managed centralized wastewater treatment works. Each stage of treatment (as well as retention time and dilution) results in a further reduction of the potential risk. A waste stabilization pond (an oxidation pond or lagoon) is generally considered a practical and simple wastewater treatment technology particularly well suited to destroying pathogens, as relatively long retention times (20 days or longer) combined with sunlight, elevated pH levels, biological activity, and other factors serve to accelerate pathogen destruction. A final disinfection step may be considered if existing wastewater treatment plants are not optimized to remove viruses. Best practices for protecting the health of workers at sanitation treatment facilities should

be followed. Workers should wear appropriate personal protective equipment (PPE), which includes protective outerwear, gloves, boots, goggles or a face shield, and a mask; they should perform hand hygiene frequently; and they should avoid touching eyes, nose, and mouth with unwashed hands.

WASH in health care settings

Existing recommendations for water, sanitation and hygiene measures in health care settings are important for providing adequate care for patients and protecting patients, staff, and caregivers from infection risks.¹⁴ The following actions are particularly important: (i) managing excreta (faeces and urine) safely, including ensuring that no one comes into contact with it and that it is treated and disposed of correctly; (ii) engaging in frequent hand hygiene using appropriate techniques; (iii) implementing regular cleaning and disinfection practices; and (iv) safely managing health care waste. Other important measures include providing sufficient safe drinking-water to staff, caregivers, and patients; ensuring that personal hygiene can be maintained, including hand hygiene, for patients, staff and caregivers; regularly laundering bedsheets and patients' clothing; providing adequate and accessible toilets (including separate facilities for confirmed and suspected cases of COVID-19 infection); and segregating and safely disposing of health care waste. For details on these recommendations, please refer to Essential environmental health standards in health care.¹⁴

1. Hand hygiene practices

Hand hygiene is extremely important. Cleaning hands with soap and water or an alcohol-based hand rub should be performed according to the instructions known as "My 5 moments for hand hygiene".¹⁵ If hands are not visibly dirty, the preferred method is to perform hand hygiene with an alcohol-based hand rub for 20–30 seconds using the appropriate technique.¹⁶ When hands are visibly dirty, they should be washed with soap and water for 40–60 seconds using the appropriate technique.¹⁷ Hand hygiene should be performed at all five moments, including before putting on PPE and after removing it, when changing gloves, after any contact with a patient with suspected or confirmed COVID-19 infection or their waste, after contact with any respiratory secretions, before eating, and after using the toilet.¹⁸ If an alcohol-based hand rub and soap are not available, then using chlorinated water (0.05%) for handwashing is an option, but it is not ideal because frequent use may lead to dermatitis, which could increase the risk of infection and asthma and because prepared dilutions might be inaccurate.¹⁹ However, if other options are not available or feasible, using chlorinated water for handwashing is an option.

Functional hand hygiene facilities should be present for all health care workers at all points of care and in areas where PPE is put on or taken off. In addition, functional hand hygiene facilities should be available for all patients, family members, and visitors, and should be available within 5 m of toilets, as well as in waiting and dining rooms and other public areas.

2. Sanitation and plumbing

People with suspected or confirmed COVID-19 disease should be provided with their own flush toilet or latrine that has a door that closes to separate it from the patient's room. Flush toilets should operate properly and have functioning drain traps. When possible, the toilet should be flushed with the lid down to prevent droplet splatter and aerosol clouds. If it is not possible to provide separate toilets, the toilet should be cleaned and disinfected at least twice daily by a trained cleaner wearing PPE (gown, gloves, boots, mask, and a face shield or goggles). Further, and consistent with existing guidance, staff and health care workers should have toilet facilities that are separate from those used by all patients.

WHO recommends the use of standard, well-maintained plumbing, such as sealed bathroom drains, and backflow valves on sprayers and faucets to prevent aerosolized faecal matter from entering the plumbing or ventilation system,²⁰ together with standard wastewater treatment.²¹ Faulty plumbing and a poorly designed air ventilation system were implicated as contributing factors to the spread of the aerosolized SARS coronavirus in a high-rise apartment building in Hong Kong in 2003.²² Similar concerns have been raised about the spread of the COVID-19 virus from faulty toilets in high-rise apartment buildings.²³ If health care facilities are connected to sewers, a risk assessment should be conducted to confirm that wastewater is contained within the system (that is, the system does not leak) before its arrival at a functioning treatment or disposal site, or both. Risks pertaining to the adequacy of the collection system or to treatment and disposal methods should be assessed following a safety planning approach,²⁴ with critical control points prioritized for mitigation.

For smaller health care facilities in low-resource settings, if space and local conditions allow, pit latrines may be the preferred option. Standard precautions should be taken to prevent contamination of the environment by excreta. These precautions include ensuring that at least 1.5 m exists between the bottom of the pit and the groundwater table (more space should be allowed in coarse sands, gravels, and fissured formations) and that the latrines are located at least 30 m horizontally from any groundwater source (including both shallow wells and boreholes).²⁵ If there is a high groundwater table or a lack of space to dig pits, excreta should be retained in impermeable storage containers and left for as long as feasible to allow for a reduction in virus levels before moving it off-site for additional treatment or safe disposal, or both. A two-tank system with parallel tanks would help facilitate inactivation by maximizing retention times, as one tank could be used until full, then allowed to sit while the next tank is being filled. Particular care should be taken to avoid splashing and the release of droplets while cleaning or emptying tanks.

3. Toilets and the handling of faeces

It is critical to conduct hand hygiene when there is suspected or direct contact with faeces (if hands are dirty, then soap and water are preferred to the use of an alcohol-based hand rub). If the patient is unable to use a latrine, excreta should be collected in either a diaper or a clean bedpan and immediately and carefully disposed of into a separate toilet or latrine used only by suspected or confirmed cases of COVID-19. In all health care settings, including those with suspected or confirmed COVID-19 cases, faeces must be treated as a biohazard and handled as little as possible. Anyone handling

faeces should follow WHO contact and droplet precautions¹⁸ and use PPE to prevent exposure, including long-sleeved gowns, gloves, boots, masks, and goggles or a face shield. If diapers are used, they should be disposed of as infectious waste as they would be in all situations. Workers should be properly trained in how to put on, use, and remove PPE so that these protective barriers are not breached.²⁵ If PPE is not available or the supply is limited, hand hygiene should be regularly practiced, and workers should keep at least 1 m distance from any suspected or confirmed cases.

If a bedpan is used, after disposing of excreta from it, the bedpan should be cleaned with a neutral detergent and water, disinfected with a 0.5% chlorine solution, and then rinsed with clean water; the rinse water should be disposed of in a drain or a toilet or latrine. Other effective disinfectants include commercially available quaternary ammonium compounds, such as cetylpyridinium chloride, used according to manufacturer's instructions, and peracetic or peroxyacetic acid at concentrations of 500–2000 mg/L.²⁶

Chlorine is ineffective for disinfecting media containing large amounts of solid and dissolved organic matter. Therefore, there is limited benefit to adding chlorine solution to fresh excreta and it is possible that this may introduce risks associated with splashing.

4. Emptying latrines and holding tanks, and transporting excreta off-site.

There is no reason to empty latrines and holding tanks of excreta from suspected or confirmed COVID-19 cases unless they are at capacity. In general, the best practices for safely managing excreta should be followed. Latrines or holding tanks should be designed to meet patient demand, considering potential sudden increases in cases, and there should be a regular schedule for emptying them based on the wastewater volumes generated. PPE (long-sleeved gown, gloves, boots, masks, and goggles or a face shield) should be worn at all times when handling or transporting excreta off-site, and great care should be taken to avoid splashing. For crews, this includes pumping out tanks or unloading pumper trucks. After handling the waste and once there is no risk of further exposure, individuals should safely remove their PPE and perform hand hygiene before entering the transport vehicle. Soiled PPE should be put in a sealed bag for later safe laundering (see Cleaning practices). Where there is no off-site treatment, in-situ treatment can be done using lime. Such treatment involves using a 10% lime slurry added at 1-part lime slurry per 10 parts of waste.

5. Cleaning practices

Recommended cleaning and disinfection procedures for health care facilities should be followed consistently and correctly.¹⁹ Laundry should be done and surfaces in all environments in which COVID-19 patients receive care (treatment units, community care centres) should be cleaned at least once a day and when a patient is discharged.²⁷ Many disinfectants are active against enveloped viruses, such as the COVID-19 virus, including commonly used hospital disinfectants. Currently, WHO recommends using:

- 70% ethyl alcohol to disinfect small areas between uses, such as reusable dedicated equipment (for example, thermometers);
- sodium hypochlorite at 0.5% (equivalent to 5000 ppm) for disinfecting surfaces.

All individuals dealing with soiled bedding, towels, and clothes from patients with COVID-19 infection should wear appropriate PPE before touching soiled items, including heavy duty gloves, a mask, eye protection (goggles or a face shield), a long-sleeved gown, an apron if the gown is not fluid resistant, and boots or closed shoes. They should perform hand hygiene after exposure to blood or body fluids and after removing PPE. Soiled linen should be placed in clearly labelled, leak-proof bags or containers, after carefully removing any solid excrement and putting it in a covered bucket to be disposed of in a toilet or latrine. Machine washing with warm water at 60–90°C (140–194°F) with laundry detergent is recommended. The laundry can then be dried according to routine procedures. If machine washing is not possible, linens can be soaked in hot water and soap in a large drum using a stick to stir and being careful to avoid splashing. The drum should then be emptied, and the linens soaked in 0.05% chlorine for approximately 30 minutes. Finally, the laundry should be rinsed with clean water and the linens allowed to dry fully in sunlight.

If excreta are on surfaces (such as linens or the floor), the excreta should be carefully removed with towels and immediately safely disposed of in a toilet or latrine. If the towels are single use, they should be treated as infectious waste; if they are reusable, they should be treated as soiled linens. The area should then be cleaned and disinfected (with, for example, 0.5% free chlorine solution), following published guidance on cleaning and disinfection procedures for spilled body fluids.²⁷

6. Safely disposing of greywater or water from washing PPE, surfaces and floors.

Current WHO recommendations are to clean utility gloves or heavy duty, reusable plastic aprons with soap and water and then decontaminate them with 0.5% sodium hypochlorite solution after each use. Single-use gloves (nitrile or latex) and gowns should be discarded after each use and not reused; hand hygiene should be performed after PPE is removed. If greywater includes disinfectant used in prior cleaning, it does not need to be chlorinated or treated again. However, it is important that such water is disposed of in drains connected to a septic system or sewer or in a soakaway pit. If greywater is disposed of in a soakaway pit, the pit should be fenced off within the health facility grounds to prevent tampering and to avoid possible exposure in the case of overflow.

7. Safe management of health care waste

Best practices for safely managing health care waste should be followed, including assigning responsibility and sufficient human and material resources to dispose of such waste safely. There is no evidence that direct, unprotected human contact during the handling of health care waste has resulted in the transmission of the COVID-19 virus. All health care waste produced during the care of COVID-19 patients should be collected safely in designated containers and bags, treated, and then safely disposed of or treated, or both, preferably on-site. If waste is moved off-site, it is critical to understand where and how it will be treated and destroyed. All who handle health care waste should wear appropriate PPE (boots, apron, long-sleeved gown, thick gloves, mask, and goggles or a face shield) and perform hand hygiene after removing it. For more information refer to the WHO guidance, Safe management of wastes from health-care activities.²⁸

Considerations for WASH practices in homes and communities.

Upholding best WASH practices in the home and community is also important for preventing the spread of COVID-19 and when caring for patients at home. Regular and correct hand hygiene is of particular importance.

1. Hand hygiene

Hand hygiene in non-health care settings is one of the most important measures that can prevent COVID-19 infection. In homes, schools and crowded public spaces – such as markets, places of worship, and train or bus stations – regular handwashing should occur before preparing food, before and after eating, after using the toilet or changing a child's diaper, and after touching animals. Functioning handwashing facilities with water and soap should be available within 5 m of toilets.

2. Treatment and handling requirements for excreta.

Best WASH practices, particularly handwashing with soap and clean water, should be strictly applied and maintained because these provide an important additional barrier to COVID-19 transmission and to the transmission of infectious diseases in general.¹⁷ Consideration should be given to safely managing human excreta throughout the entire sanitation chain, starting with ensuring access to regularly cleaned, accessible, and functioning toilets or latrines and to the safe containment, conveyance, treatment, and eventual disposal of sewage.

When there are suspected or confirmed cases of COVID-19 in the home setting, immediate action must be taken to protect caregivers and other family members from the risk of contact with respiratory secretions and excreta that may contain the COVID-19 virus. Frequently touched surfaces throughout the patient's care area should be cleaned regularly, such as bedside tables, bed frames and other bedroom furniture. Bathrooms should be cleaned and disinfected at least once a day. Regular household soap or detergent should be used for cleaning first and then, after rinsing, regular household disinfectant containing 0.5% sodium hypochlorite (that is, equivalent to 5000 ppm or 1-part household bleach with 5% sodium hypochlorite to 9 parts water) should be applied. PPE should be worn while cleaning, including mask, goggles, a fluid-resistant apron, and gloves,²⁹ and hand hygiene with an alcohol-based hand rub or soap and water should be performed after removing PPE.

References

1. Coronavirus disease (COVID-19) advice for the public. Geneva: World Health Organization; 2020 (<https://www.who.int/emergencies/diseases/novel-coronavirus-2019/advice-for-public>, accessed 3 March 2020).
2. Huang C, Wang Y, Li X, Ren L, Zhao J, Hu Y, et al. Clinical features of patients infected with 2019 novel coronavirus in Wuhan, China. *Lancet*. 2020;395:497–506. doi:10.1016/S0140-6736(20)30183-5.

3. Chen N, Zhou M, Dong X, Qu J, Gong F, Han Y, et al. Epidemiological and clinical characteristics of 99 cases of 2019 novel coronavirus pneumonia in Wuhan, China: a descriptive study. *Lancet*. 2020;395:507–13. doi:10.1016/S0140-6736(20)30211-7.
4. Wang D, Hu B, Hu C, Zhu F, Liu X, Zhang J, et al. Clinical characteristics of 138 hospitalized patients with 2019 novel coronavirus-infected pneumonia in Wuhan, China. *JAMA*. 2020. Feb 7. doi:10.1001/jama.2020.1585.
5. Xiao E, Tang M, Zheng Y, Li C, He J, Hong H, et al. Evidence for gastrointestinal infection of SARS-CoV-2. *medRxiv*. doi:10.1101/2020.02.17.20023721.
6. Holshue ML, DeBolt C, Lindquist S, Lofy KH, Wiesman J, Bruce H et al. for the Washington State 2019-nCoV Case Investigation Team. First case of 2019 novel coronavirus in the United States. *N Engl J Med*. 2020. Jan 31. doi:10.1056/NEJMoa2001191.
7. Zhang Y, Chen C, Zhu S et al. [Isolation of 2019-nCoV from a stool specimen of a laboratory-confirmed case of the coronavirus disease 2019 (COVID-19)]. *China CDC Weekly*. 2020;2(8):123–4. (In Chinese.)
8. Wang XW, Li JS, Zhen B, Kong QX, Song N, Xiao WJ et al. Study on the resistance of severe acute respiratory syndrome-associated coronavirus. *J Virol Methods*. 2005;126:171–7. doi:10.1016/j.jviromet.2005.02.005.
9. Gundy P, Gerba CP, Pepper IL. Survival of coronaviruses in water and wastewater. *Food Environ Virol*. 2009;1:10–14. doi:10.1007/s12560-008-9001-6.
10. Casanova L, Rutlall WA, Weber DJ, Sobsey MD. Survival of surrogate coronaviruses in water. *Water Res*. 2009;43(7):1893–8. doi:10.1016/j.watres.2009.02.007.
11. Kampf G, Todt D, Pfaender S, Steinmann E. Persistence of coronaviruses on inanimate surfaces and their inactivation with biocidal agents. *J Hosp Infect*. 2020;104(3):246–51. doi:10.1016/j.jhin.2020.01.022.
12. Guidelines for drinking-water quality, fourth edition, incorporating the first addendum. Geneva: World Health Organization; 2017 (<http://apps.who.int/iris/bitstream/10665/254637/1/9789241549950-eng.pdf>, accessed 3 March 2020).
13. SARS-CoV-2 – water and sanitation. Adelaide: Water Research Australia; 2020 (http://www.waterra.com.au/r9544/media/system/attribfile/2199/WaterRA_FS_Coronavirus_V10.pdf, accessed 3 March 2020).
14. Essential environmental health standards in health care. Geneva: World Health Organization; 2008 (https://apps.who.int/iris/bitstream/handle/10665/43767/9789241547239_eng.pdf?sequence=1&isAllowed=y, accessed 3 March 2020).
15. My 5 moments for hand hygiene. In: WHO/Infection prevention and control [website]. Geneva: World Health Organization; 2020 (<https://www.who.int/infection-prevention/campaigns/clean-hands/5moments/en/>, accessed 3 March 2020).
16. Siddharta A, Pfaender S, Vielle NJ, Dijkman R, Friesland M, Becker B, et al. Virucidal activity of World Health Organization-recommended formulations against enveloped viruses, including Zika, Ebola, and emerging coronaviruses. *J Infect Dis*. 2017;215(6):902–6. doi:10.1093/infdis/jix046.
17. WHO guidelines on hand hygiene in health care settings. Geneva: World Health Organization; 2009 (https://apps.who.int/iris/bitstream/handle/10665/44102/9789241597906_eng.pdf?sequence=1&isAllowed=y, accessed 3 March 2020).
18. Infection prevention and control during health care when novel coronavirus (nCoV) infection is suspected: interim guidance, 25 January 2020. Geneva: World Health Organization ([https://www.who.int/publications-detail/infection-prevention-and-control-during-health-care-when-novel-coronavirus-\(ncov\)-infection-is-suspected-20200125](https://www.who.int/publications-detail/infection-prevention-and-control-during-health-care-when-novel-coronavirus-(ncov)-infection-is-suspected-20200125), accessed 3 March 2020).
19. Q&A on infection prevention and control for health care workers caring for patients with suspected or confirmed 2019-nCoV. In: WHO/Newsroom [website]. Geneva: World Health Organization; 2020 (<https://www.who.int/news-room/q-a-detail/q-a-on-infection-prevention-and-control-for-health-care-workers-caring-for-patients-with-suspected-or-confirmed-2019-ncov>, accessed 3 March 2020).
20. Health aspects of plumbing. Geneva: World Health Organization; 2006 (<https://apps.who.int/iris/handle/10665/43423>, accessed 3 March 2020).
21. Guidelines on sanitation and health. Geneva: World Health Organization; 2018 (<https://apps.who.int/iris/bitstream/handle/10665/274939/9789241514705-eng.pdf?ua=1>, accessed 3 March 2020).
22. Yu ITS, Li Y, Wong TW, Tam W, Chan A, Lee JHW, et al. Evidence of airborne transmission of the severe acute respiratory syndrome virus. *N Engl J Med*. 2004;350(17):1731–9. doi:10.1056/NEJMoa032867.
23. Regan H. How can the coronavirus spread through bathroom pipes? Experts are investigating in Hong Kong. CNN. 12 February 2020 (<https://edition.cnn.com/2020/02/12/asia/hong-kong-coronavirus-pipes-intl-hnk/index.html>).
24. Sanitation safety planning: manual for safe use and disposal of wastewater, greywater and excreta. Geneva: World Health Organization; 2015. (<https://apps.who.int/iris/handle/10665/171753>, accessed 3 March 2020).
25. How to put on and take off personal protective equipment. Geneva: World Health Organization; 2008 (<https://apps.who.int/iris/handle/10665/70066>, accessed 3 March 2020).
26. Chemical disinfectants: guideline for disinfection and sterilization in healthcare facilities (2008). In: CDC/Infection Control [website]. Atlanta: US Centers for Disease Control and Prevention; 2019. (<https://www.cdc.gov/infectioncontrol/guidelines/disinfection/disinfection-methods/chemical.html>, accessed 3 March 2020).

27. Best practices for environmental cleaning in healthcare facilities in resource-limited settings. Atlanta: US Centers for Disease Control and Prevention; 2019.
(<https://www.cdc.gov/hai/pdfs/resource-limited/environmental-cleaning-508.pdf>, accessed 3 March 2020).
28. Safe management of wastes from health-care activities: a summary. Geneva: World Health Organization; 2017.
(<https://apps.who.int/iris/handle/10665/259491>, accessed 3 March 2020).
29. Home care for patients with suspected novel coronavirus (COVID-19) infection presenting with mild symptoms, and management of their contacts: interim guidance, 4 February 2020.
([https://www.who.int/publications-detail/home-care-for-patients-with-suspected-novel-coronavirus-\(ncov\)-infection-presenting-with-mild-symptoms-and-management-of-contacts](https://www.who.int/publications-detail/home-care-for-patients-with-suspected-novel-coronavirus-(ncov)-infection-presenting-with-mild-symptoms-and-management-of-contacts), accessed 3 March 2020).

US Centers for Disease Control and Prevention, United States of America; David Berendes, US Centers for Disease Control and Prevention, United States of America; Lisa Casanova, Georgia State University, United States of America; David Cunliffe, SA Health, Australia; Rick Gelting, US Centers for Disease Control and Prevention, United States of America; Dr Thomas Handzel, US Centers for Disease Control and Prevention, United States of America; Paul Hunter, University of East Anglia, United Kingdom; Ana Maria de Roda Husman, National Institute for Public Health and the Environment, the Netherlands; Peter Maes, Médecins Sans Frontières, Belgium; Molly Patrick, US Centers for Disease Control and Prevention, United States of America; Mark Sobsey, University of North Carolina-Chapel Hill, United States of America.

WHO continues to monitor the situation closely for any changes that may affect this interim guidance. Should any factors change, WHO will issue a further update. Otherwise, this interim guidance document will expire 2 years after the date of publication.


Contributors

This interim guidance was written by staff from WHO and UNICEF. In addition, a number of experts and WASH practitioners contributed. They include Matt Arduino,

© World Health Organization 2020. Some rights reserved. This work is available under the [CC BY-NC-SA 3.0 IGO](#) licence.

WHO reference number: WHO/2019-nCoV/IPC_WASH/2020.2

Appendix C-24: RUDSICO-EAP Guidelines for implementation of Prevention and Control Measures for COVID-19



Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

Contents

I.INTRODUCTION.....	3
II.PURPOSE.....	3
III.COVID-19 TYPICAL SYMPTOMS.....	4
IV.PRINCIPLES OF WORKER PROTECTION.....	4
V.MAXIMUM PRECAUTION FOR PERSONS/LABOURERS REPORTING TO WORK.....	4
VI.PPEs AND SANITIZATION ARRANGEMENTS.....	4
VII.HEALTH CHECK UP AND THERMAL SCANNING.....	4
VIII.SELF ATTESTATION BY PERSONS/LABOUR PRIOR TO WORK.....	5
IX.GENERAL PRECAUTIONS TO BE FOLLOWED AT PERMANENT SITES/OFFICES.....	5
X.TEMPORARY WORK-SITE (PIPE LAYING SITES) PREVENTION PRACTICES.....	6
XI.WASHING FACILITY.....	7
XII.CLEANING PROCEDURES.....	7
XIII.LABOUR CAMP.....	8
Toilet Facility.....	8
Eating/snacks Arrangements.....	8
Changing Facilities, Bathrooms, Showers and Drying Areas.....	9
XIV.UPDATES ON COVID-19.....	9
XV.TRAINING.....	9
XVI.EMERGENCY CONTACT.....	9

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

Safe Operating Procedure (SOP) and COVID-19 Management Plan for Construction Works during COVID-19 Situation

I. INTRODUCTION

- Coronavirus disease (COVID-19) is an infectious disease caused by a newly discovered coronavirus.
- Most people infected with the COVID-19 virus will experience mild to moderate respiratory illness and recover without requiring special treatment. Older people, and those with underlying medical problems like cardiovascular disease, diabetes, chronic respiratory disease, and cancer are more likely to develop serious illness.
- The COVID-19 virus spreads primarily through droplets of saliva or discharge from the nose when an infected person coughs or sneezes, so it's important that you also practice respiratory etiquette (for example, by coughing into a flexed elbow) and maintain social distancing
- At this time, there are no specific vaccines or treatments for COVID-19. However, there are many ongoing clinical trials evaluating potential treatments

II. PURPOSE

- This document¹ is intended to supplement formal EH&S policies, procedures and plans that the contractor has in place for its employees and staff working in RSTDSP projects. Hence, this document is not intended to replace any formalized procedures currently in place for the Contractor. Where this guideline does not meet or exceed the standards put forth by the Contractor, the Contractor shall abide by the most stringent procedure available.
- In addition to prevailing EH&S Plan in all projects, Safe Operating Procedures specific to COVID-19 are prepared by working contractors and being followed in all work sites.
- Existing EH&S Officer of contractor to be given additional responsibility of COVID-19 Officer² to implement and monitor the COVID-19 SOPs. The EH&S officer cum COVID-19 Officer² at the Contractor's worksite (appointed by Contractor and agreed by PIU) will submit a written weekly report to the Client's Representative (PIU Head). The EH&S Officer cum COVID-19 Officer shall certify that the Contractor and all subcontractors are in full compliance with these guidelines.
- The EH&S Officer cum COVID-19 officer should monitor all sites on daily basis.
- Any issue of non-compliance with these guidelines shall be a basis for the suspension of work. The Contractor will be required to submit a corrective action plan (on the next day or immediately as per the nature of issue) detailing each issue of non-conformance and a plan to rectify the issue(s). The Contractor will not be allowed to resume work until the plan is approved by the Client (PIU). Any additional issues of non-conformance may be subject to action against the Contractor's as health & safety/safeguard clauses of the contract.
- Construction sites operating during the Covid-19 pandemic need to ensure they are

¹ This document may be made available in the local language, and the salient features would be displayed through signages at the appropriate locations throughout work sites and stretches by the Contractor for wider dissemination and awareness

² The existing safeguards officer OR health & safety officer OR supervisor of the contractor can be designated as COVID-19 officer by undergoing the training available at

(a) <https://www.who.int/emergencies/diseases/novel-coronavirus-2019/training/online-training>

(b) <https://openwho.org/courses/eprotect-acute-respiratory-infections>

(c) <https://openwho.org/courses/COVID-19-IPC-EN>

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

protecting their workforce and minimizing the risk of spread of infection.

- This guidance is intended to introduce consistent measures on sites of all sizes in line with the Government's recommendations on social distancing.
- These are exceptional circumstances and the contractor and PIU must remain abreast of and comply with the latest Government advice on COVID-19 at all times.
- The health and safety requirements of any construction activity must also not be compromised at this time. If an activity cannot be undertaken safely due to a lack of suitably qualified personnel being available or social distancing being implemented, it should not take place.
- It is to be noted that emergency services/medical services are also under great pressure and may not be in a position to respond as quickly as usual.
- Sites should remind the workforce at every opportunity of the Worksite Procedures which are aimed at protecting them, their colleagues, their families and the nearby population.

If a worksite is not consistently implementing the measures in this document, it may be required to shut down.

III. COVID-19 TYPICAL SYMPTOMS

- Fever
- Cough
- Shortness of Breath
- Sore Throat

IV. PRINCIPLES OF WORKER PROTECTION

- Consistently practice social distancing
- Cover coughs and sneezes
- Maintain hand hygiene
- Clean surfaces frequently

V. MAXIMUM PRECAUTION FOR PERSONS/LABOURERS REPORTING TO WORK

- IF SICK, STAY HOME!
- IF SICK DURING WORK, GO HOME!
- IF SOMEONE SICK, SEND THEM HOME!

VI. PPEs AND SANITIZATION ARRANGEMENTS

Contractor to provide face masks (of the type approved by Government for use to protect persons from COVID-19) to all persons working in or visiting the worksite. At each worksite hand sanitizers/soap shall be kept and workers will be required to regularly sanitize/wash hands with soap. If any object is to be used by several workers, all workers shall be provided hand gloves. Full sanitization of worksite and work objects shall be done every day before start of works. This along with procedures set out in this document is for maximum precaution to protect all persons/labourers at all times.

VII. HEALTH CHECK UP AND THERMAL SCANNING

All persons at the worksite should have their temperature screened by COVID-19 officer with Infrared Thermometer (handheld non-contact).

Health checkup of all workers and staff shall be done by a medical practitioner on weekly basis. If any suspected COVID-19 infected person is found, he shall immediately reported to local authority/govt. recognized COVID-19 hospital. Thermal scanning shall be done of each worker and staff before entering to site and office and if any person has more than normal

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

temperature, he shall not be allowed to enter site/office. Such person shall be sent back to home/work camp and regular daily monitoring of his temperature shall be done and if temperature remains high he shall be reported to local authority/govt. recognized COVID-19 hospital for further treatment/quarantine.

VIII. SELF ATTESTATION BY PERSONS/LABOUR PRIOR TO WORK

Prior to starting a work (on daily basis), each labour /worker will self-attest to the supervisor:

- no signs of COVID-19 symptoms within the past 24 hours.
- No contact with an individual diagnosed with COVID-19. (contact means living with a positive person, being within 6 ft of positive person OR sharing things of positive person)
- Not undergone quarantine or isolation (in case of any labourer /worker who has been quarantined or isolated previously, the engagement shall be only after obtaining the requisite clearance)

The engagement of workers falling in the high-risk category such as workers over the age of 55 years, with underlying medical conditions or health issues, etc. should be done only after obtaining the requisite clearance from trained and registered medical practitioners.

The self-attestation would be verified in collaboration with trained and registered medical practitioners deployed at site through discussions with laborers /workers and/or preliminary checks such as temperature checks, etc. prior to their engagement at site.

In addition, the Contractor shall mandatorily follow all medical test requirements for the workers prior to their engagement and/or mobilization at site as per the guidelines issued by the Central and State government agencies and WHO from time to time.

Persons/Labourers showing COVID-19 symptoms or not providing self-attestation shall be directed to leave the work site and report to the Govt. recognized hospital/quarantine centre immediately. Labour not to return to the work site until cleared by Govt. recognized hospital /quarantine centre.

IX. GENERAL PRECAUTIONS TO BE FOLLOWED AT PERMANENT SITES/OFFICES

- No handshake, Only Namaste
- Non-essential physical work that requires close contact between workers should not be carried out
- Work requiring physical contact should not be carried out
- Plan all other work to minimise contact between workers
- Wash hands often (every 1-2 hrs or frequently as possible) with soap for at least 20 seconds
- Use hand sanitizer
- No person should enter the work site other than the authorized persons mentioned by supervisor during start of work
- All must implement social distancing³ by maintaining a minimum distance of 6-feet from others³ at all times to eliminate the potential of cross contamination.
- Avoid face to face meetings – critical situations requiring in-person discussion must follow social distance i.e., 6 ft from others.
- Conduct all meetings via conference calls, if possible. Do not convene meetings of

³ Social distancing may not be practical for undertaking certain specific activities within the workplace. It is therefore important to review the work method statements for these types of activities to assess impact and how to find safe ways of doing in line with best available guidance.

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

more than 10 people. Recommend use of cell phones, texting, web meeting sites and conference calls for project discussion

- All individual work group meetings/ talks should follow social distancing
- At each job briefing /toolbox talk, employees are asked if they are experiencing any symptoms, and are sent home if they are
- Each worksite should have displayed laminated COVID-19 safety guidelines and handwashing instructions (seen Annexure for display pictographs)
- All restroom /toilet facilities should be cleaned (min twice a day), and handwashing facility must be provided with soap, hand sanitizer and paper towels
- All surfaces should be regularly cleaned, including mobiles, tabletops /surfaces, door handles, laptops, records, etc.
- All common areas and meeting areas are to be regularly cleaned (min twice a day) and disinfected at least twice a day
- All persons to maintain their own water bottle, and should not be shared.
- To avoid external contamination, it is recommended everyone bring food from home
- Maintain Social Distancing separation during breaks and lunch.
- Cover coughing or sneezing with a tissue, then throw the tissue in the trash and wash hands, if no tissue is available then cough /sneeze into your upper sleeves or elbow. Do not cough or sneeze into your hands.
- Clean your hands after coughing or sneezing thoroughly by using soap and water (minimum for 20 seconds). If soap and water are not available, please use a hand sanitizer. The Contractor shall ensure adequate quantities of sanitizer and soap are made available at all locations including site offices, meeting rooms, corridors, washrooms /toilets, etc. as appropriate.
- Avoid touching eyes, nose, and mouth with your hands
- To avoid sharing germs, please clean up after Yourself. DO NOT make others responsible for moving, unpacking and packing up your personal belongings
- If you or a family member is feeling ill, stay home!⁴
- Work schedules are adjusted to provide time for proper cleaning and disinfecting as required.

X. TEMPORARY WORK-SITE (PIPE LAYING SITES) PREVENTION PRACTICES

- At the start of each shift, confirm with all employees that they are healthy and inform all workers of reusable and disposable PPE.
- Outside person(s) should be strictly prohibited at worksite
- All construction workers will be required to wear cut-resistant gloves or the equivalent.
- Use of eye protection (reusable safety goggles/face shields) is recommended. The supply of eye protection equipment to the workers is considered as a standard part of PPE during construction works.
- In work conditions where required social distancing is impracticable to achieve, such employees shall be supplied with standard face mask, gloves, and eye protection.
- All employees shall drive to work site in a single occupant vehicle. Staff shall not ride together in the same vehicle
- When entering a machine or vehicle which you are not sure you were the last person to enter, make sure that you wipe down the interior and door handles with disinfectant (with 1% sodium hypochlorite solution) prior to entry. Adequate quantity of the disinfectant shall be provided by the Contractor at all such site-specific locations.
- Workers should maintain separation of 6 feet from each other.
- Multi person activities will be limited where feasible (two persons lifting activities)
- Gathering places on the site such as sheds and/or break areas will be eliminated, and

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

- instead small break areas will be used with seating limited to ensure social distancing.
- Contact the cleaning person of the worksite and ensure proper COVID-19 sanitation processes. Increase cleaning/disinfection visits to at least 2 times a day. Cleaning person(s) to be provided with gloves, gown and face mask for each cycle of cleaning. The Contractor shall make available adequate supply of PPE and chemicals while the threat of COVID-19 continues.
- Clean all high contact surfaces a minimum of twice a day in order to minimize the spread of germs in areas that people touch frequently. This includes but is not limited to desks, laptops and vehicles
- All employees to maintaining good health by getting adequate sleep; eating a balanced, healthy diet, avoid alcohol; and consume plenty of fluids.
- Continuation of works in construction project with workers available on site and no workers to be brought in from outside
- The site offices shall have adequate ventilation. The air conditioning or ventilation systems installed at the site offices would have high-efficiency air filters to reduce the risk of infection. The frequency of air changes may be increased for areas where close personal proximity cannot be fully prevented such as control rooms, elevators, waiting rooms, etc.
- The Contractor shall carry out contactless temperature checks for the workers prior to site entrance, during working hours and after site works to identify persons showing signs of being unwell with the COVID-19 symptoms

XI. WASHING FACILITY

- All worksites should have access to toilet and hand washing facility.
- Providing hand cleaning facilities at entrances and exits. This should be soap and water wherever possible or hand sanitizer if water is not available
- Washing facility with hot water, and soap at fire hydrants or other water sources to be used for frequent handwashing for all onsite employees
- All onsite workers must help to maintain and keep stations clean
- If a worker notices soap or towels are running low or out, immediately notify supervisors. Proactively supervisor should make sure shortage situation never occurs.
- Garbage bins will be placed next to the hand wash facility for discarding of used tissues/towels with regular removal and disposal facility (end of each day)

XII. CLEANING PROCEDURES

Increase cleaning/disinfection visits to at least 2 times a day. Cleaning person(s) to be provided with gloves, gown and face mask for each cycle of cleaning.

Each worksite should have enhanced cleaning and disinfection procedures that are posted and shared including sheds, gates, equipment, vehicles, etc. and shall be posted at all entry points to the sites, and throughout the project site. These include common areas and high touch points like

- Taps and washing facilities
- Toilet flush and seats
- Door handles and push plates
- Handrails on staircases and corridors
- Lift and hoist controls
- Machinery and equipment controls
- Food preparation and eating surfaces
- Telephone equipment / mobiles
- Keyboards, photocopiers and other office equipment



Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

Re-usable PPEs⁴ should be thoroughly cleaned after use and not shared between workers

XIII. LABOUR CAMP

Contractor shall follow a zero-tolerance policy on wearing of masks.

Masks (homemade can be thought of) to be provided to all the persons/labourers for use at the camp site as well as at the worksite. Increase cleaning/disinfection visits to at least 2 times a day. Cleaning person(s) to be provided with disposable gloves, gown and face mask for each cycle of cleaning.

Toilet Facility

- Restrict the number of people using toilet facility at any one time e.g. appoint one welfare attendant among the labours.
- Wash hands before and after using the facilities
- Enhance the cleaning regimes for toilet facilities particularly door handles, locks and the toilet flush
- Portable toilets should be avoided wherever possible, but where in use these should be cleaned and emptied more frequently
- Provide suitable and sufficient rubbish bins for hand towels with regular removal and disposal.

Eating/snacks Arrangements

- Provide permanent (till society is safe from COVID-19) on-camp/off-camp cook/helpers can be implemented. Make sure that the "Guidelines for food handling, preparation and distribution during COVID-19" and its regular updates are being followed.
- Whilst there is a requirement for construction camps to provide a means of heating food and making hot water, these are exceptional circumstances and where it is not possible to introduce a means of keeping equipment clean between use, etc. must be removed from use.
- Contractor to arrange all daily need items and grocery at site itself and no worker is allowed to go to shops for daily need items.
- Dedicated eating areas should be identified on camp to reduce food waste and contamination
- Break times should be staggered to reduce congestion and contact at all times
- Hand cleaning facilities or hand sanitizer should be available at the entrance of any room where people eat and should be used by workers when entering and leaving the area
- Workers should sit 2 metres apart from each other whilst eating and avoid all contact
- Where catering is provided on camp, it should provide pre-prepared and wrapped food only
 - Payments should be taken by contactless options wherever possible
 - Crockery, eating utensils, cups etc. should be avoided wherever possible
- Drinking water should be provided with enhanced cleaning measures of the tap mechanism introduced
- Tables should be cleaned between each use
- All rubbish should be put straight in the bin and not left for someone else to clear up; only covered pedal operated bins should be used and the bins should be cleared and cleaned regularly, with strict adherence to safety protocols for disposal and hygiene maintenance (including proper PPE's such as gloves, mask and apron worn by the

⁴ Advisory on use of Homemade Protective Cover for Face & Mouth by GOI

Safe Operating Procedures (SOP) and COVID-19 Management Plan for Construction works

- waste handler/cleaner and disposal at a designated place);
- All areas used for eating must be thoroughly cleaned at the end of each break and shift, including chairs, door handles, etc.

Changing Facilities, Bathrooms, Showers and Drying Areas

- Introduce staggered start and finish times to reduce congestion and contact at all times
- Introduce enhanced cleaning of all facilities throughout the day and at the end of each day
- Consider increasing the number or size of facilities available on camp if possible
- Based on the size of each facility, determine how many people can use it at any one time to maintain a distance of two metres
- Provide suitable and sufficient garbage bins in these areas with regular removal and disposal.
- Visitor log should be strictly maintained that the labour camp.

COVID-19 officer will ensure compliance with prevention issues at the labour camp(s).

XIV. UPDATES ON COVID-19

The Contractor shall be in touch with the Department of Health & Family Welfare and Labour Department to identify any potential worksite exposures relating to COVID-19, including:

- Strictly follow the guidelines issued by Ministry of Health and Family Welfare
- Other workers, vendors, inspectors, or visitors to the worksite with close contact to the individual
- Labour Camps / Work areas such as designated workstations or rooms /sheds
- Work tools and equipment
- Common areas such as break rooms, tables and sanitary facilities

Also refer the following websites from time to time for regular updates.

<https://www.mohfw.gov.in/>

This document can be updated from time to time based on the advisories or directions of the Govt.

XV. TRAINING

- PIU to ensure all workers get training on above requirements before start of any construction activity
- During construction period frequent visual and verbal reminders to workers can improve compliance with hand hygiene practices and thus reduce rates of infection. Handwashing posters should also be displayed at work site and labour camps

XVI. EMERGENCY CONTACT

- Provide emergency contact number(s) at work site and labour camp for reporting COVID-19 symptoms


Ensure all staff and personal use the Aarogya Setu app, recommended by GOI for tracking COVID-19 patients.


Shakeen
Team Leader
PMCBC, RSTDSP Jaipur


ESS, PMBC
Page 9 of 9

COVID-19 PRECAUTIONS

(To be displayed at sites)









Appendix C-25: Management of Work Plan during Festivals and Melas

1.	Planning Of Fair and Festival	• The date and time should be fixed well in advance so that all requisite preparations can be made. It should be announced at least 60 days in advance. • Information shall be shared with local health authorities'/ health officers of all localities in which fair/festival is being organized. • Health officer shall inform higher officials concerned with the fair/festival
2.	Notification of fairs and festivals	• Notification (by govt. order or otherwise) should specify ➤ The area and duration of the fairs/ festivals ➤ The limits of the area where fairs/ festivals are to be organized should be well defined • Also, festival tax if any being levied by the govt. on vehicles, travellers, etc should be notified. The Govt. should also notify how much tax will be levied
3.	EHS Arrangements	• The site should be demarcated and preparation of the site be done. • Site should be cleaned and drained properly • Roads should be aligned properly • Water sprinkling should be done periodically to avoid dust nuisance. • Sufficient numbers of dustbin container should be placed (Wet & Dry) • Water sufficient in quality and quantity fit for drinking and cooking should be arranged. Also facilities for safe storage of water can be made. • To practically possible extent, accommodation to the pilgrims and visitors be made. • Adequate lighting arrangements be made. • Wholesome food should be made available at reasonable price and yet of necessary quantities. Foods prepared/ offered/ stored has to be properly supervised. • All the food preparation should be hygienic. • Refuse, rubbish, sewage should be collected, removed and disposed off safely. • Suitable latrines should be arranged and maintained • Infectious cases if any should be detected early and segregated. Preventive measures should be started. • Adequate medical staff, medical relief, hospital accommodation be provided. • Any other service deemed necessary can be arranged for. • Health officer be given adequate powers to seize private buildings, private water supply like wells, etc. Same should be informed to public to prevent protest. • There should be good approach to the road. • Sweepers in ratio of 1 per 1000 pilgrims be appointed. • Temporary hospital be set up for management of any infections. District health officer should stay at the site of fair and festival.
4.	Promoting COVID appropriate Behaviour.	• Avoiding physical contact is a responsible behaviour as it prevents the spread of COVID-19 disease and other viruses. • Physical distance Should be maintained minimum 6 feet • Avoid Touching Eyes, Nose and Mouth / Maintain respiratory hygiene / Wash hands frequently and thoroughly
